Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 2/16/2026

Type	Project	Region	Responsible
Construction	Anna, TX	Central	Brendan Blair

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
11/30/2026	11/30/2026	0 Baseline 0 Previous	Remaining Work Compression: -2%

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	1/5/2026	1/5/2026	1/5/2026	0	0	Ntp Start Date	On Track – Gaining
Foundation Complete	3/17/2026	3/17/2026	2/12/2026	33	33	Pour Concrete Slab On Grade- Building A	On Track – Gaining
Hardscape/Landscape Complete	3/26/2026	3/26/2026	3/19/2026	7	7	Paving Staking	On Track – Gaining
Structure Top Out	7/8/2026	7/8/2026	7/8/2026	0	0	Roof Framing And Roof Deck- Building A	On Track – Gaining
Weather Tight	8/11/2026	8/11/2026	8/11/2026	0	0	Tpo Roofing System	On Track – Gaining
1st Floor Finishes Complete	9/29/2026	9/29/2026	9/29/2026	0	0	Hallway System | First Floor- Building A	On Track – Gaining
Conditioned Air	10/15/2026	10/15/2026	10/15/2026	0	0	Setup The Roof Top Condenser Unit	On Track – Gaining
2nd Floor Finishes Complete	10/27/2026	10/27/2026	10/27/2026	0	0	Hallway System | Second Floor- Building A	On Track – Gaining
3rd Floor Finishes Complete	11/26/2026	11/26/2026	11/26/2026	0	0	Hallway System | Third Floor- Building A	On Track – Gaining
Contract Completion	11/30/2026	11/30/2026	11/30/2026	0	0	Tco/Co	On Track – Gaining

Baseline Variance

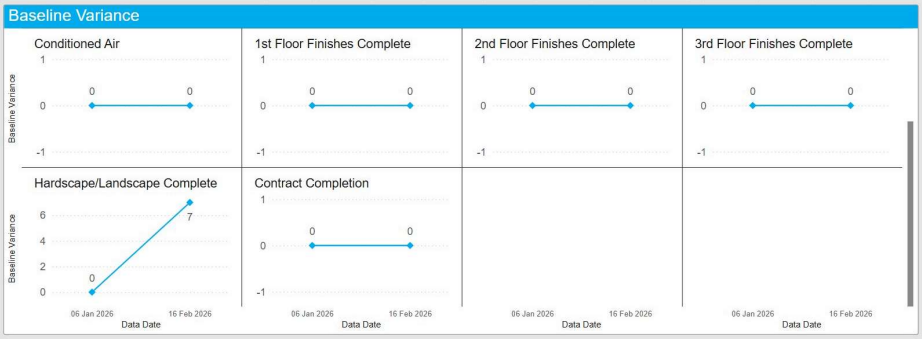

Schedule Performance Summary

Summary

The schedule exhibits multiple risk factors: a critically deficient validation score, frequent schedule changes, and both compression and slippage on the critical path. Immediate attention is required to address technical weaknesses and regain schedule stability. Management should prioritize schedule cleanup, reduce unnecessary changes, and implement strategies to recover lost ground on the critical path, as these issues collectively increase the risk of further delay and diminished schedule reliability.

Schedule Validation Score: 47.00% — ALERT
The SV Score is critically low, indicating significant technical deficiencies, poor logic quality, or unresolved schedule issues. Immediate review and remediation of schedule structure and logic integrity are recommended to restore credibility and forecasting value.

Schedule Change Index: 8.00% — WARNING
The schedule has experienced moderate volatility, with over 8% of activities being modified since the last update. This level of change signals shifting plans, which could undermine stability if not carefully controlled.

Critical Path Compression: 3.00% — WARNING
The project shows signs of deliberate compression on the critical path, with schedule adjustments exceeding best-practice thresholds. While not alarming, sustained compression may heighten execution risk or stress resources.

Critical Path Variance: 17.00% — WARNING
The current critical path is 17% longer than the baseline, suggesting notable slippage against the plan. Unless addressed, this could erode schedule contingency and threaten timely completion

Remaining Work Compression: -2%
Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea... by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Powered By STELIC INSIGHT • ACTION • IMPACT
