	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Public Storage Anna**	**Tue 12/16/25**	**Tue 12/16/25**	**0d**	**Mon 11/30/26**	**Mon 11/30/26**	**0d**
2	**Permitting**	**Tue 12/16/25**	**Tue 12/16/25**	**0d**	**Fri 4/3/26**	**Fri 4/3/26**	**0d**
3	Engineering Permit	Tue 12/16/25	Tue 12/16/25	0d	Tue 12/16/25	Tue 12/16/25	0d
4	Building Permit	Thu 1/8/26	Thu 1/8/26	0d	Thu 1/8/26	Thu 1/8/26	0d
5	NTP Start Date	Mon 1/5/26	Mon 1/5/26	0d	Mon 1/5/26	Mon 1/5/26	0d
6	Fire Department Approval to Go Vertical	Fri 4/3/26	Fri 4/3/26	0d	Fri 4/3/26	Fri 4/3/26	0d
7	**Procurement**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Tue 9/15/26**	**Tue 9/15/26**	**0d**
8	**Elevator | Schendler**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Mon 5/25/26**	**Mon 5/25/26**	**0d**
9	Shop Drawing | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Mon 2/2/26	Mon 2/2/26	0d
10	Fabrication and Material Delivery	Tue 2/3/26	Tue 2/3/26	0d	Mon 5/25/26	Mon 5/25/26	0d
11	**Hallway System | Janus International**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Tue 9/15/26**	**Tue 9/15/26**	**0d**
12	Shop Drawing | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Mon 1/19/26	Mon 1/19/26	0d
13	Fabrication and Material Delivery	Tue 8/25/26	Tue 8/25/26	0d	Tue 9/15/26	Tue 9/15/26	0d
14	**Electrical Gear**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Fri 4/24/26**	**Mon 4/27/26**	**-1d**
15	Submittals | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Fri 2/13/26	Mon 2/16/26	-1d
16	Fabrication and Material Delivery	Mon 2/16/26	Tue 2/17/26	-1d	Fri 4/24/26	Mon 4/27/26	-1d
17	**Electrical Lighting**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Fri 3/6/26**	**Mon 3/9/26**	**-1d**
18	Submittals | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Mon 1/19/26	Mon 1/19/26	0d
19	Fabrication and Material Delivery	Tue 1/20/26	Tue 1/20/26	0d	Fri 3/6/26	Mon 3/9/26	-1d
20	**CMU Split Face Masonry**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Fri 6/5/26**	**Mon 6/8/26**	**-1d**
21	Submittals | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Fri 2/27/26	Mon 3/2/26	-1d
22	Fabrication and Material Delivery	Mon 3/2/26	Tue 3/3/26	-1d	Fri 6/5/26	Mon 6/8/26	-1d
23	**Bi-Parts Sliding Doors | Stanley Door**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Fri 5/22/26**	**Mon 5/25/26**	**-1d**
24	Shop Drawing | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Fri 2/27/26	Mon 3/2/26	-1d
25	Fabrication and Material Delivery	Mon 3/2/26	Tue 3/3/26	-1d	Fri 5/22/26	Mon 5/25/26	-1d
26	**Glass**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Fri 2/27/26**	**Mon 3/2/26**	**-1d**
27	Shop Drawing | Preparation - Review - Approval	Tue 1/6/26	Tue 1/6/26	0d	Mon 1/19/26	Mon 1/19/26	0d
28	Fabrication and Material Delivery	Tue 1/20/26	Tue 1/20/26	0d	Fri 2/27/26	Mon 3/2/26	-1d
29	**Site Work**	**Wed 12/17/25**	**Wed 12/17/25**	**0d**	**Wed 9/16/26**	**Wed 9/16/26**	**0d**
30	**Survey - Staking and SWPPP**	**Wed 12/17/25**	**Wed 12/17/25**	**0d**	**Thu 3/19/26**	**Thu 3/26/26**	**-5d**
31	Property Corner and BM	Wed 12/17/25	Wed 12/17/25	0d	Wed 12/17/25	Wed 12/17/25	0d
32	Building Pad Staking	Fri 1/16/26	Fri 1/16/26	0d	Mon 1/19/26	Mon 1/19/26	0d
33	UG Utility Staking	Fri 1/30/26	Fri 1/30/26	0d	Sat 1/31/26	Mon 2/2/26	-0.5d
34	Paving Staking	Thu 3/19/26	Thu 3/26/26	-5d	Thu 3/19/26	Thu 3/26/26	-5d
35	Silt Fence, Construction Entrance	Thu 12/18/25	Thu 12/18/25	0d	Thu 12/18/25	Thu 12/18/25	0d
36	**Dirt Work | Inside the Property**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Wed 8/5/26**	**Wed 8/5/26**	**0d**
37	**Site Dirtwork**	**Tue 1/6/26**	**Tue 1/6/26**	**0d**	**Wed 8/5/26**	**Wed 8/5/26**	**0d**
38	Dirt Contractor Mobilization	Tue 1/6/26	Tue 1/6/26	0d	Wed 1/7/26	Wed 1/7/26	0d
39	Demo the Additional Trees along Buddy Hayes Street	Thu 1/8/26	Thu 1/8/26	0d	Mon 1/12/26	Mon 1/12/26	0d
40	Strip and Stockpile Topsoil	Mon 1/12/26	Mon 1/12/26	0d	Fri 1/16/26	Fri 1/16/26	0d

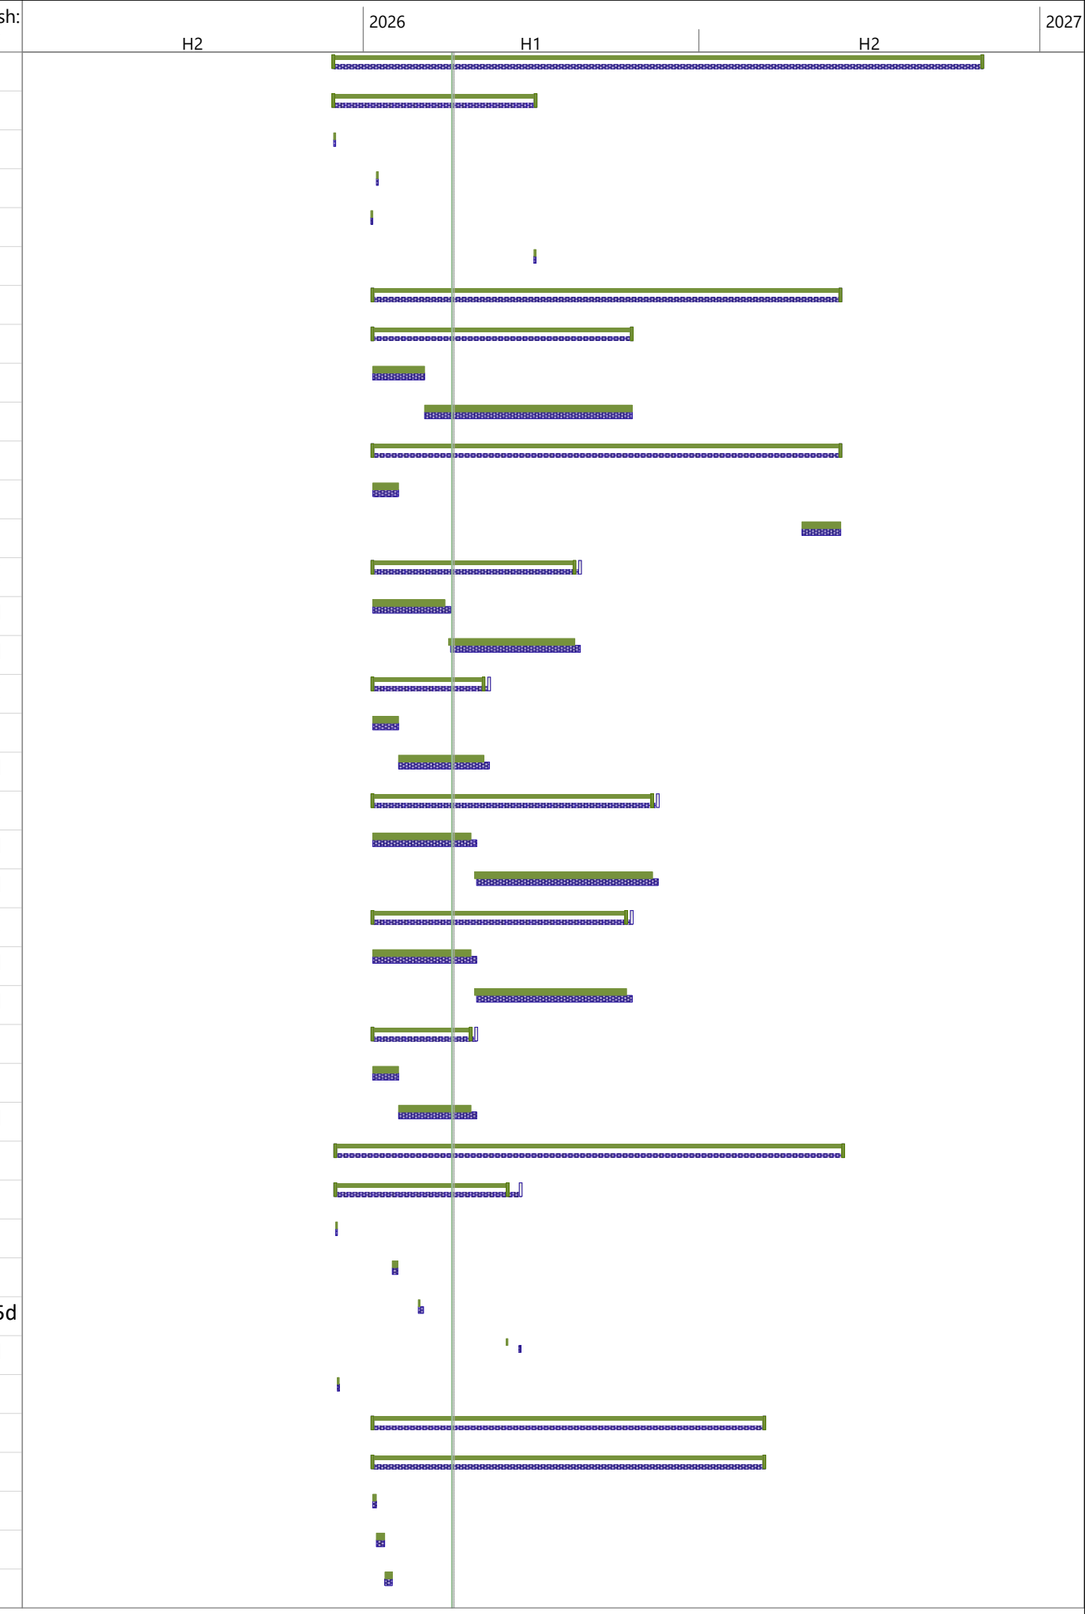

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
41	Site Excavation Cut to Fill	Fri 1/16/26	Fri 1/16/26	0d	Fri 1/23/26	Fri 1/23/26	0d
42	Fine Grade Landscape area +/- .10	Mon 8/3/26	Mon 8/3/26	0d	Wed 8/5/26	Wed 8/5/26	0d
43	**Building Pad Subgrade Preparation**	**Fri 1/23/26**	**Fri 1/23/26**	**0d**	**Thu 2/19/26**	**Thu 2/19/26**	**0d**
44	**Building A**	**Fri 1/23/26**	**Fri 1/23/26**	**0d**	**Wed 2/11/26**	**Wed 2/11/26**	**0d**
45	Excavate Building Pad 7FT Deep and 5 FT over ex	Fri 1/23/26	Fri 1/23/26	0d	Fri 1/30/26	Fri 1/30/26	0d
46	1FT Moisture Condition Building Pad	Fri 1/30/26	Fri 1/30/26	0d	Tue 2/3/26	Tue 2/3/26	0d
47	Import and Place 6FT of Select Fill	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
48	Fine Grade Building Pad	Wed 2/11/26	Wed 2/11/26	0d	Wed 2/11/26	Wed 2/11/26	0d
49	**Building B**	**Fri 1/30/26**	**Fri 1/30/26**	**0d**	**Wed 2/11/26**	**Wed 2/11/26**	**0d**
50	Excavate Building Pad 7FT Deep and 5 FT over ex	Fri 1/30/26	Fri 1/30/26	0d	Wed 2/4/26	Wed 2/4/26	0d
51	1FT Moisture Condition Building Pad	Wed 2/4/26	Wed 2/4/26	0d	Fri 2/6/26	Fri 2/6/26	0d
52	Import and Place 6FT of Select Fill	Fri 2/6/26	Fri 2/6/26	0d	Tue 2/10/26	Tue 2/10/26	0d
53	Fine Grade Building Pad	Tue 2/10/26	Tue 2/10/26	0d	Wed 2/11/26	Wed 2/11/26	0d
54	**Building C**	**Wed 2/4/26**	**Wed 2/4/26**	**0d**	**Mon 2/16/26**	**Mon 2/16/26**	**0d**
55	Excavate Building Pad 7FT Deep and 5 FT over ex	Wed 2/4/26	Wed 2/4/26	0d	Mon 2/9/26	Mon 2/9/26	0d
56	1FT Moisture Condition Building Pad	Mon 2/9/26	Mon 2/9/26	0d	Wed 2/11/26	Wed 2/11/26	0d
57	Import and Place 6FT of Select Fill	Wed 2/11/26	Wed 2/11/26	0d	Fri 2/13/26	Fri 2/13/26	0d
58	Fine Grade Building Pad	Fri 2/13/26	Fri 2/13/26	0d	Mon 2/16/26	Mon 2/16/26	0d
59	**Building D**	**Mon 2/9/26**	**Mon 2/9/26**	**0d**	**Thu 2/19/26**	**Thu 2/19/26**	**0d**
60	Excavate Building Pad 7FT Deep and 5 FT over ex	Mon 2/9/26	Mon 2/9/26	0d	Thu 2/12/26	Thu 2/12/26	0d
61	1FT Moisture Condition Building Pad	Thu 2/12/26	Thu 2/12/26	0d	Mon 2/16/26	Mon 2/16/26	0d
62	Import and Place 6FT of Select Fill	Mon 2/16/26	Mon 2/16/26	0d	Wed 2/18/26	Wed 2/18/26	0d
63	Fine Grade Building Pad	Wed 2/18/26	Wed 2/18/26	0d	Thu 2/19/26	Thu 2/19/26	0d
64	**Pavement Subgrade Prep**	**Wed 3/18/26**	**Wed 3/11/26**	**5d**	**Fri 3/20/26**	**Fri 3/27/26**	**-5d**
65	8" Lime Stabilization		Wed 3/11/26			Tue 3/24/26	
66	Scarify and Recompact Pavement Subgrade	Wed 3/18/26	Wed 3/25/26	-5d	Thu 3/19/26	Thu 3/26/26	-5d
67	Fine Grade Pavement Subgrade	Fri 3/20/26	Fri 3/27/26	-5d	Fri 3/20/26	Fri 3/27/26	-5d
68	**Utility | Inside the Property**	**Fri 1/30/26**	**Fri 1/30/26**	**0d**	**Tue 3/24/26**	**Wed 3/11/26**	**8.5d**
69	Utility Contractor Mobilization	Fri 1/30/26	Fri 1/30/26	0d	Mon 2/2/26	Tue 2/3/26	-1d
70	Public and Private Water	Fri 2/20/26	Fri 2/13/26	5d	Thu 3/5/26	Thu 2/26/26	5d
71	Fire Water and connections	Fri 3/6/26	Fri 2/27/26	5d	Fri 3/13/26	Fri 3/6/26	5d
72	Public Sanitary Sewer	Tue 2/17/26	Fri 2/20/26	-3d	Thu 2/19/26	Mon 2/23/26	-2d
73	Sewer Easement Delay	Thu 2/5/26			Mon 2/16/26		
74	Private Sanitary Sewer	Mon 2/2/26	Tue 2/24/26	-15.5	Thu 2/5/26	Thu 2/26/26	-15.5d
75	Public Storm Drain	Fri 3/6/26	Tue 2/3/26	22.5	Tue 3/17/26	Thu 2/12/26	22.5d
76	Private Storm Drain	Tue 3/17/26	Fri 2/13/26	22.5	Tue 3/24/26	Thu 2/19/26	22.5d
77	Pressure Testing	Mon 3/16/26	Mon 3/9/26	5d	Tue 3/17/26	Tue 3/10/26	5d
78	Get Approval from Fire Department and Public Works	Wed 3/18/26	Wed 3/11/26	5d	Wed 3/18/26	Wed 3/11/26	5d
79	**Site Paving**	**Tue 2/24/26**	**Thu 2/26/26**	**-2d**	**Mon 3/30/26**	**Mon 4/6/26**	**-5d**
80	Paving Contractor Mobilization	Mon 3/23/26	Mon 3/30/26	-5d	Mon 3/23/26	Mon 3/30/26	-5d

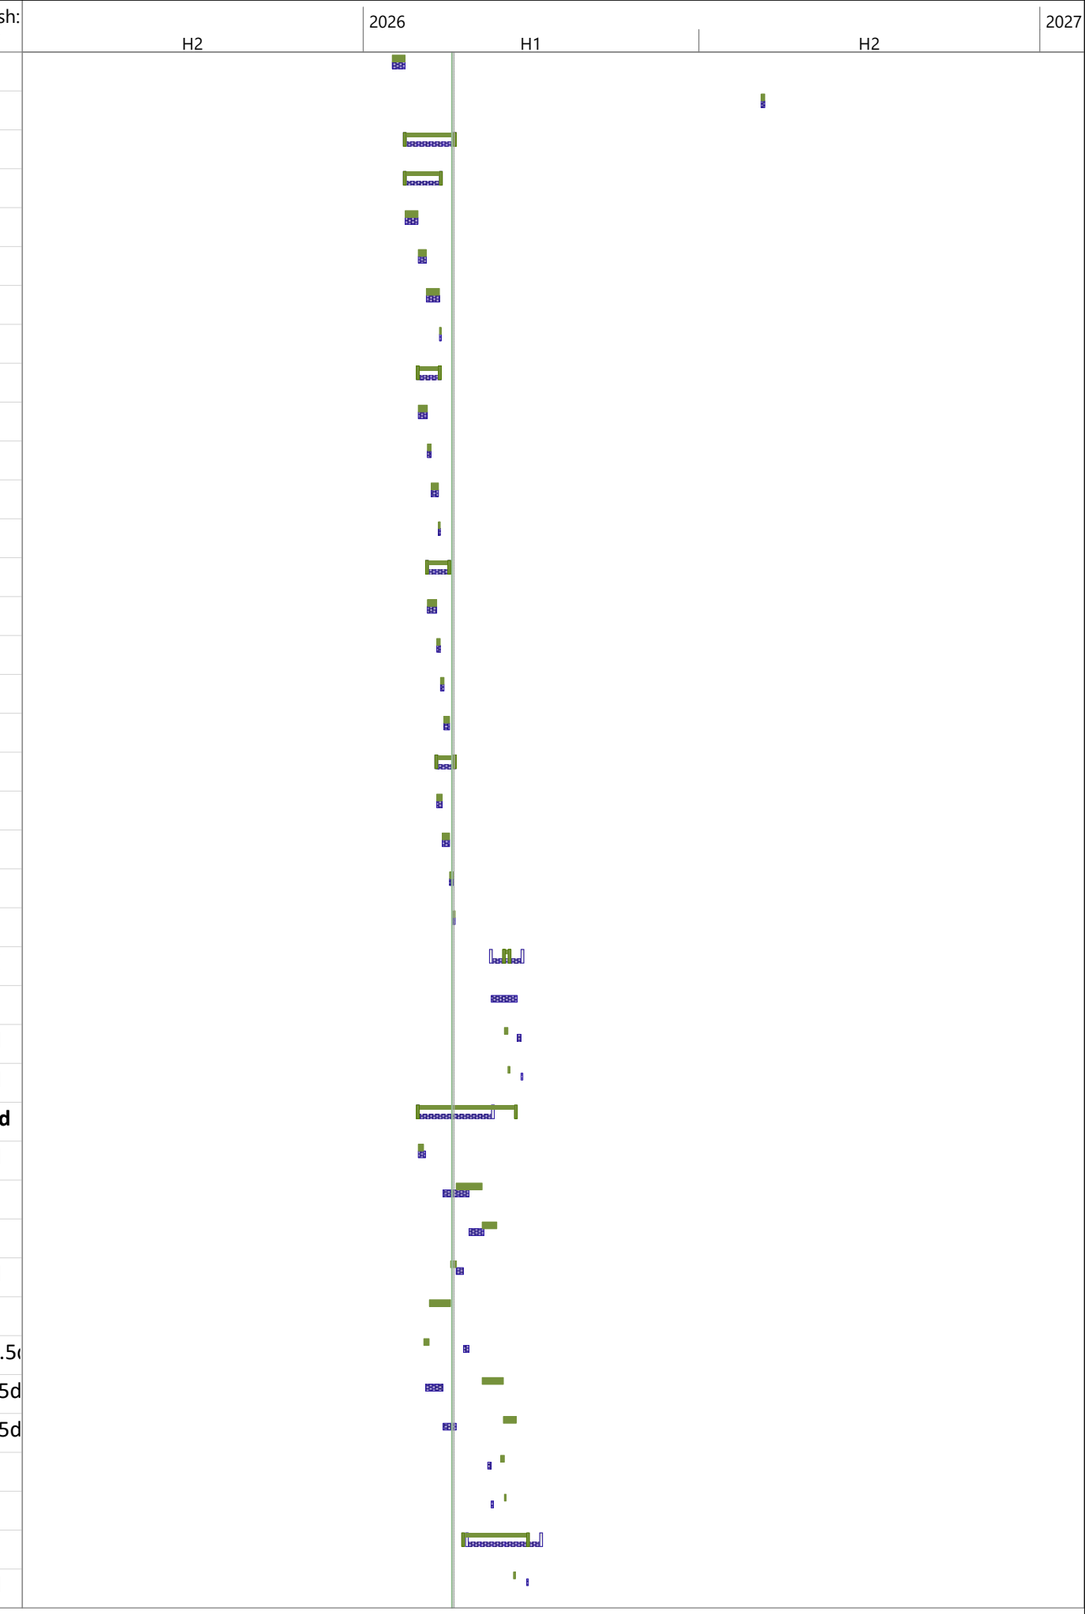

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
81	Concrete Fire Lane Paving	Tue 3/24/26	Tue 3/31/26	-5d	Thu 3/26/26	Thu 4/2/26	-5d
82	Concrete Parking Paving	Fri 3/27/26	Fri 4/3/26	-5d	Mon 3/30/26	Mon 4/6/26	-5d
83	Concrete Pour Back for the Utility Tie-in	Tue 2/24/26	Thu 2/26/26	-2d	Wed 2/25/26	Fri 2/27/26	-2d
84	**Public Street Work | Buddy Hayes Street**	**Fri 2/27/26**	**Fri 2/20/26**	**5d**	**Thu 4/16/26**	**Tue 4/14/26**	**2d**
85	Saw Cut and Demo	Fri 2/27/26	Fri 2/20/26	5d	Mon 3/2/26	Mon 2/23/26	5d
86	12" Water line crossings and Connect with Kroger	Tue 3/3/26	Tue 2/24/26	5d	Mon 3/9/26	Mon 3/2/26	5d
87	Site Excavation Cut to Fill	Tue 3/10/26	Tue 3/3/26	5d	Thu 3/12/26	Thu 3/5/26	5d
88	8" Lime Stabilization	Fri 3/13/26	Wed 3/11/26	2d	Thu 3/26/26	Tue 3/24/26	2d
89	Scarify and Recompact Pavement Subgrade	Mon 3/23/26	Thu 3/19/26	2d	Thu 3/26/26	Tue 3/24/26	2d
90	Blue Top and Proof Roll	Fri 3/27/26	Wed 3/25/26	2d	Mon 3/30/26	Thu 3/26/26	2d
91	Concrete Paving | Buddy Hayes	Wed 4/1/26	Mon 3/30/26	2d	Thu 4/2/26	Tue 3/31/26	2d
92	Asphalt Paving | Buddy Hayes	Wed 4/8/26	Mon 4/6/26	2d	Thu 4/9/26	Tue 4/7/26	2d
93	Pavement Markings	Wed 4/15/26	Mon 4/13/26	2d	Thu 4/16/26	Tue 4/14/26	2d
94	**Site Electrical**	**Fri 3/6/26**	**Fri 2/27/26**	**5d**	**Mon 3/16/26**	**Mon 3/9/26**	**5d**
95	Electrical Primary by GCEC	Fri 3/6/26	Fri 2/27/26	5d	Wed 3/11/26	Wed 3/4/26	5d
96	Electrical Secondry	Thu 3/12/26	Thu 3/5/26	5d	Mon 3/16/26	Mon 3/9/26	5d
97	**Landscape and Irrigation**	**Mon 8/10/26**	**Mon 8/10/26**	**0d**	**Wed 9/2/26**	**Wed 9/2/26**	**0d**
98	Irrigation	Mon 8/10/26	Mon 8/10/26	0d	Mon 8/24/26	Mon 8/24/26	0d
99	Landscape	Mon 8/24/26	Mon 8/24/26	0d	Wed 9/2/26	Wed 9/2/26	0d
100	**Site Amenities**	**Thu 2/5/26**	**Fri 2/6/26**	**-1d**	**Wed 9/16/26**	**Wed 9/16/26**	**0d**
101	Retaining Wall | Permit and Installation	Thu 2/5/26	Fri 2/6/26	-1d	Thu 2/12/26	Fri 2/13/26	-1d
102	7 FT Tall Screening Wall	Thu 3/12/26	Fri 3/13/26	-1d	Thu 3/26/26	Fri 3/27/26	-1d
103	Light Bollard, Keypad Bollard	Thu 9/3/26	Thu 9/3/26	0d	Mon 9/7/26	Mon 9/7/26	0d
104	Wrought Iron Fence	Thu 9/3/26	Thu 9/3/26	0d	Wed 9/9/26	Wed 9/9/26	0d
105	Sliding Gate	Thu 9/10/26	Thu 9/10/26	0d	Wed 9/16/26	Wed 9/16/26	0d
106	Swing Arm Gate	Thu 9/10/26	Thu 9/10/26	0d	Tue 9/15/26	Tue 9/15/26	0d
107	**Building Work**	**Mon 2/2/26**	**Thu 2/19/26**	**-13.!**	**Thu 11/26/26**	**Thu 11/26/26**	**0d**
108	**Building A**	**Mon 2/2/26**	**Thu 2/19/26**	**-13.!**	**Thu 11/26/26**	**Thu 11/26/26**	**0d**
109	**Concrete | Building A**	**Mon 2/2/26**	**Thu 2/19/26**	**-13.!**	**Fri 6/5/26**	**Fri 6/5/26**	**0d**
110	**Slab on Grade | Building A**	**Mon 2/2/26**	**Thu 2/19/26**	**-13.!**	**Thu 2/12/26**	**Tue 3/17/26**	**-23d**
111	Form Board installation	Thu 2/5/26	Thu 2/19/26	-10.!	Fri 2/6/26	Mon 2/23/26	-10.5
112	UG Plumbing Rough-in	Wed 2/4/26	Mon 2/23/26	-13.!	Fri 2/6/26	Mon 3/2/26	-15.5
113	Excavation for the Footing	Mon 2/9/26	Mon 3/2/26	-15.!	Wed 2/11/26	Wed 3/11/26	-20d
114	Excavation for the Elevator Pit	Mon 2/2/26	Mon 2/23/26	-15.!	Wed 2/4/26	Thu 2/26/26	-15.5
115	Pour Concrete wall for the Elevator Pit	Mon 2/9/26	Mon 3/2/26	-15.!	Mon 2/9/26	Tue 3/3/26	-15.5
116	Elevator Pit Waterproofing	Tue 2/10/26	Thu 3/5/26	-17.!	Tue 2/10/26	Fri 3/6/26	-17.5
117	Poly, Termite Control	Tue 2/10/26	Thu 3/12/26	-22d	Wed 2/11/26	Thu 3/12/26	-21d
118	Reinforcement Steel Placement	Tue 2/10/26	Fri 3/13/26	-23d	Wed 2/11/26	Mon 3/16/26	-23d
119	Pour Concrete Slab on Grade	Thu 2/12/26	Tue 3/17/26	-23d	Thu 2/12/26	Tue 3/17/26	-23d
120	Saw Cut for Control Joint	Thu 2/12/26	Tue 3/17/26	-23d	Thu 2/12/26	Tue 3/17/26	-23d

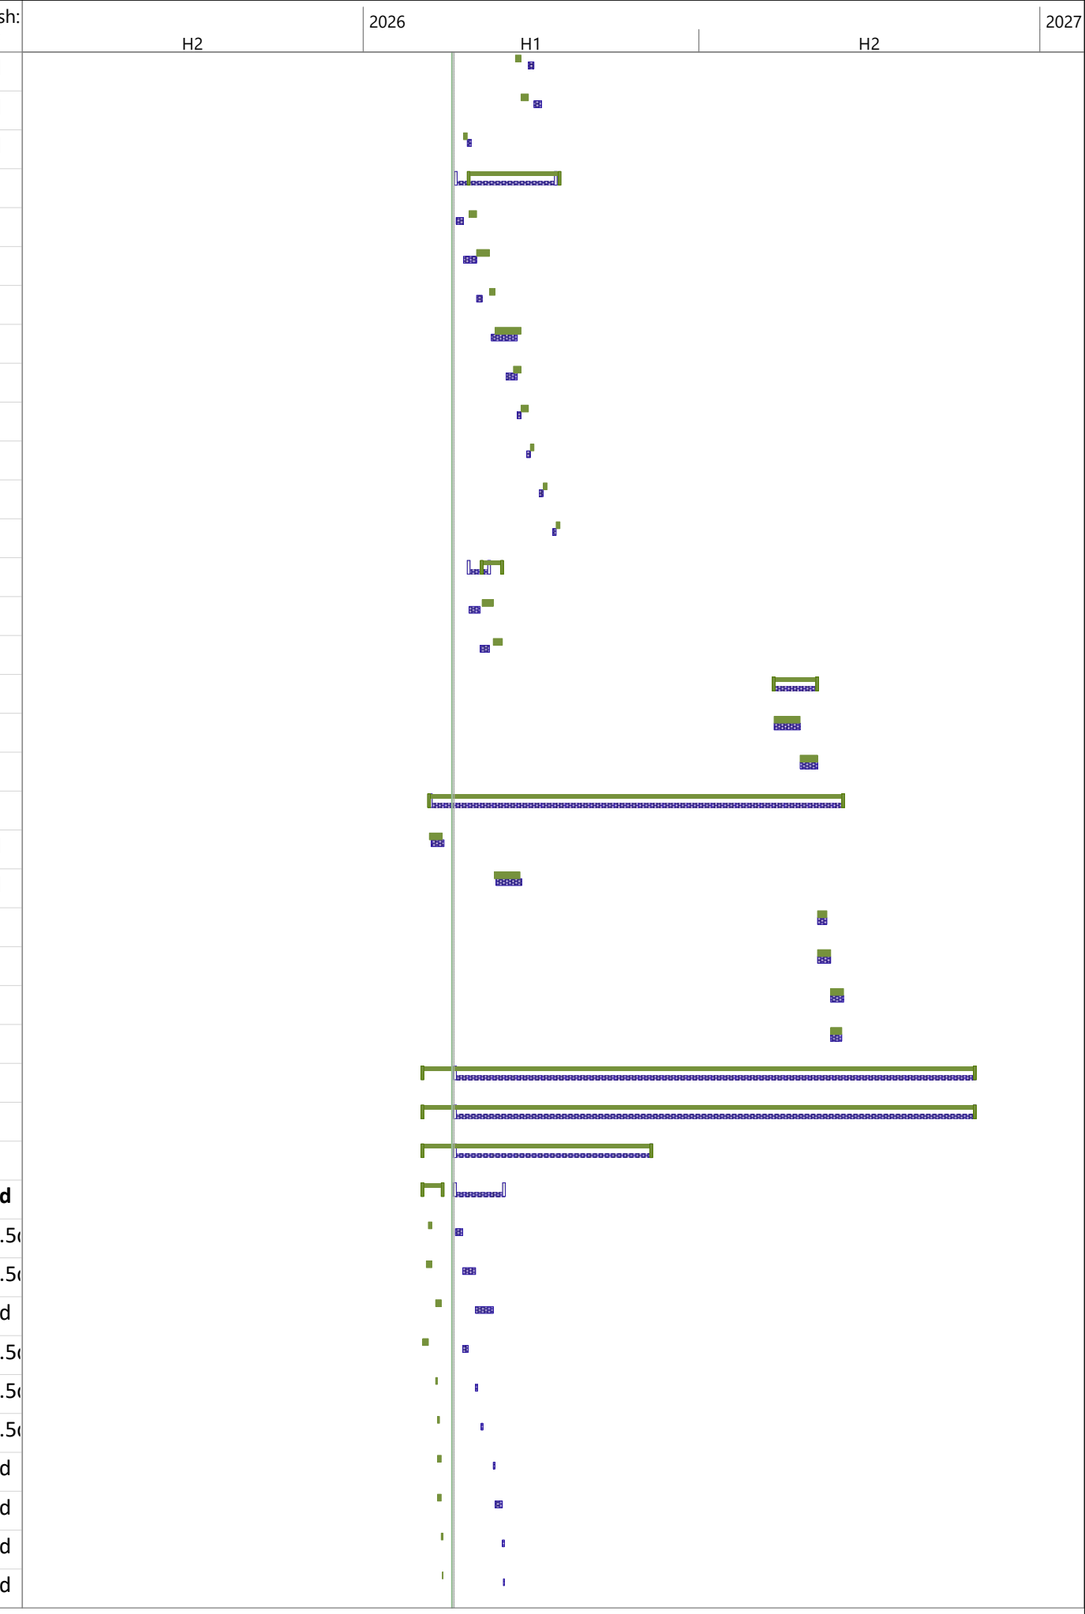

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
121	**Second Floor Slab on Deck | Building A**	**Fri 5/1/26**	**Fri 5/1/26**	**0d**	**Tue 5/5/26**	**Tue 5/5/26**	**0d**
122	Place Wire Mesh	Fri 5/1/26	Fri 5/1/26	0d	Mon 5/4/26	Mon 5/4/26	0d
123	Pour Concrete Slab on Deck	Tue 5/5/26	Tue 5/5/26	0d	Tue 5/5/26	Tue 5/5/26	0d
124	Saw Cut for Control Joint	Tue 5/5/26	Tue 5/5/26	0d	Tue 5/5/26	Tue 5/5/26	0d
125	**Third Floor Slab on Deck | Building A**	**Tue 6/2/26**	**Tue 6/2/26**	**0d**	**Fri 6/5/26**	**Fri 6/5/26**	**0d**
126	Place Wire Mesh	Tue 6/2/26	Tue 6/2/26	0d	Thu 6/4/26	Thu 6/4/26	0d
127	Pour Concrete Slab on Deck	Thu 6/4/26	Thu 6/4/26	0d	Fri 6/5/26	Fri 6/5/26	0d
128	Saw Cut for Control Joint	Thu 6/4/26	Thu 6/4/26	0d	Fri 6/5/26	Fri 6/5/26	0d
129	**Structural Steel Framing | Building A**	**Mon 4/6/26**	**Mon 4/6/26**	**0d**	**Mon 9/14/26**	**Mon 9/14/26**	**0d**
130	First Floor Structural Framing	Mon 4/6/26	Mon 4/6/26	0d	Fri 4/24/26	Fri 4/24/26	0d
131	Second Floor Deck	Mon 4/27/26	Mon 4/27/26	0d	Thu 4/30/26	Thu 4/30/26	0d
132	Second Floor Structural Framing	Mon 5/11/26	Mon 5/11/26	0d	Wed 5/27/26	Wed 5/27/26	0d
133	Third Floor Deck	Wed 5/27/26	Wed 5/27/26	0d	Tue 6/2/26	Tue 6/2/26	0d
134	Third Floor Structural Framing	Wed 6/10/26	Wed 6/10/26	0d	Fri 6/26/26	Fri 6/26/26	0d
135	Roof Framing and Roof Deck	Mon 6/29/26	Mon 6/29/26	0d	Wed 7/8/26	Wed 7/8/26	0d
136	Awning	Mon 8/31/26	Mon 8/31/26	0d	Mon 9/14/26	Mon 9/14/26	0d
137	Stair 1	Wed 5/6/26	Wed 5/6/26	0d	Tue 6/16/26	Tue 6/16/26	0d
138	Stair 2	Wed 5/20/26	Wed 5/20/26	0d	Tue 6/30/26	Tue 6/30/26	0d
139	**Exterior Wall Assembly | Building A**	**Wed 6/17/26**	**Wed 6/17/26**	**0d**	**Mon 8/31/26**	**Mon 8/31/26**	**0d**
140	Exterior Sheathing	Wed 6/17/26	Wed 6/17/26	0d	Wed 7/8/26	Wed 7/8/26	0d
141	Air Moisture Barrier	Wed 7/8/26	Wed 7/8/26	0d	Wed 7/15/26	Wed 7/15/26	0d
142	Rigid Insulation	Wed 7/15/26	Wed 7/15/26	0d	Fri 7/31/26	Fri 7/31/26	0d
143	EIFS	Wed 7/29/26	Wed 7/29/26	0d	Wed 8/26/26	Wed 8/26/26	0d
144	Parapet Wall Assembly	Mon 7/6/26	Mon 7/6/26	0d	Fri 7/10/26	Fri 7/10/26	0d
145	4" Split Face CMU Masonry	Mon 8/10/26	Mon 8/10/26	0d	Mon 8/31/26	Mon 8/31/26	0d
146	**Roof | Building A**	**Fri 7/17/26**	**Fri 7/17/26**	**0d**	**Tue 8/11/26**	**Tue 8/11/26**	**0d**
147	Roofing Insulation	Fri 7/17/26	Fri 7/17/26	0d	Tue 7/28/26	Tue 7/28/26	0d
148	TPO Roofing system	Tue 7/28/26	Tue 7/28/26	0d	Tue 8/11/26	Tue 8/11/26	0d
149	**Interior Wall Assembly | Building A**	**Mon 4/6/26**	**Mon 4/6/26**	**0d**	**Mon 8/24/26**	**Mon 8/24/26**	**0d**
150	Elevator CMU Wall Assembly	Mon 4/6/26	Mon 4/6/26	0d	Fri 6/12/26	Fri 6/12/26	0d
151	Stair CMU Wall Assembly	Wed 4/8/26	Wed 4/8/26	0d	Tue 6/16/26	Tue 6/16/26	0d
152	Lite-Gauge Framing | Office Area	Wed 7/22/26	Wed 7/22/26	0d	Wed 7/29/26	Wed 7/29/26	0d
153	Plumbing and Electrical Wall Rough-in | Office Area	Tue 8/11/26	Tue 8/11/26	0d	Tue 8/18/26	Tue 8/18/26	0d
154	Sheathing | Office Area	Tue 8/18/26	Tue 8/18/26	0d	Mon 8/24/26	Mon 8/24/26	0d
155	**Elevator | Building A**	**Tue 8/18/26**	**Tue 8/18/26**	**0d**	**Tue 10/13/26**	**Tue 10/13/26**	**0d**
156	Elevator 1	Tue 8/18/26	Tue 8/18/26	0d	Tue 9/15/26	Tue 9/15/26	0d
157	Elevator 2	Tue 9/15/26	Tue 9/15/26	0d	Tue 10/13/26	Tue 10/13/26	0d
158	Sump Pump for Elevator	Fri 10/9/26	Fri 10/9/26	0d	Tue 10/13/26	Tue 10/13/26	0d
159	Fire Alarm and Electrical for Elevator	Fri 10/9/26	Fri 10/9/26	0d	Tue 10/13/26	Tue 10/13/26	0d
160	**Fire Supression | Building A**	**Fri 5/15/26**	**Fri 5/15/26**	**0d**	**Mon 8/10/26**	**Mon 8/10/26**	**0d**

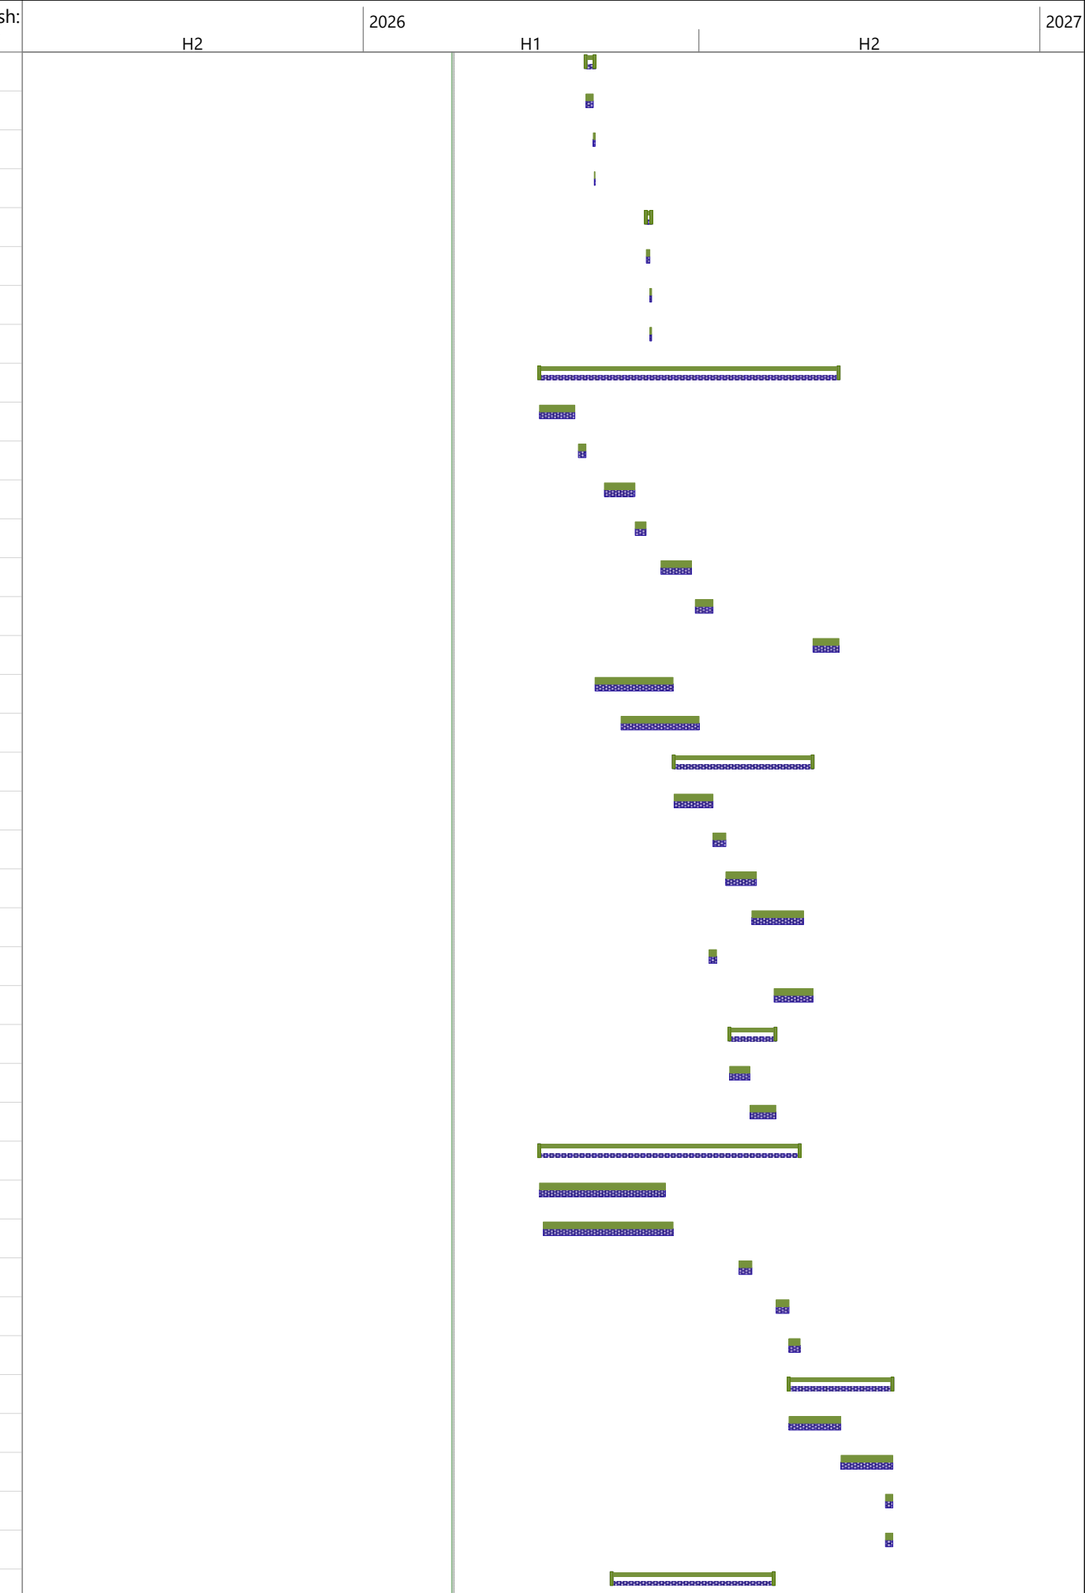

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
161	Fire Sprinkler | First Floor	Fri 5/15/26	Fri 5/15/26	0d	Thu 6/4/26	Thu 6/4/26	0d
162	Fire Sprinkler | Second Floor	Tue 6/16/26	Tue 6/16/26	0d	Tue 7/7/26	Tue 7/7/26	0d
163	Fire Sprinkler | Third Floor	Wed 7/15/26	Wed 7/15/26	0d	Wed 8/5/26	Wed 8/5/26	0d
164	UG Utility Flush Test for the Riser	Wed 6/10/26	Wed 6/3/26	5d	Thu 6/11/26	Thu 6/4/26	5d
165	Riser Room Assembly	Wed 8/5/26	Wed 8/5/26	0d	Mon 8/10/26	Mon 8/10/26	0d
166	**Fire Alarm | Building A**	**Tue 8/11/26**	**Tue 8/11/26**	**0d**	**Fri 9/25/26**	**Fri 9/25/26**	**0d**
167	Fire Alarm rough-in First Floor	Tue 8/11/26	Tue 8/11/26	0d	Tue 8/25/26	Tue 8/25/26	0d
168	Fire Alarm rough-in Second Floor	Tue 8/25/26	Tue 8/25/26	0d	Tue 9/8/26	Tue 9/8/26	0d
169	Fire Alarm rough-in Third Floor	Tue 9/8/26	Tue 9/8/26	0d	Tue 9/22/26	Tue 9/22/26	0d
170	Fire Alarm Panels	Tue 9/22/26	Tue 9/22/26	0d	Fri 9/25/26	Fri 9/25/26	0d
171	**Hallway System | Owner Furnished**	**Tue 9/8/26**	**Tue 9/8/26**	**0d**	**Thu 11/26/26**	**Thu 11/26/26**	**0d**
172	Hallway System | First Floor	Tue 9/15/26	Tue 9/15/26	0d	Tue 9/29/26	Tue 9/29/26	0d
173	Hallway System | Second Floor	Tue 10/13/26	Tue 10/13/26	0d	Tue 10/27/26	Tue 10/27/26	0d
174	Hallway System | Third Floor	Fri 11/13/26	Fri 11/13/26	0d	Thu 11/26/26	Thu 11/26/26	0d
175	Welded Wire Mesh | First Floor	Tue 9/8/26	Tue 9/8/26	0d	Tue 9/15/26	Tue 9/15/26	0d
176	Welded Wire Mesh | Second Floor	Tue 10/6/26	Tue 10/6/26	0d	Tue 10/13/26	Tue 10/13/26	0d
177	Welded Wire Mesh | Third Floor	Fri 11/6/26	Fri 11/6/26	0d	Thu 11/12/26	Thu 11/12/26	0d
178	**HVAC | Building A**	**Tue 8/11/26**	**Tue 8/11/26**	**0d**	**Thu 10/15/26**	**Thu 10/15/26**	**0d**
179	First Floor Rough-in	Tue 8/11/26	Tue 8/11/26	0d	Tue 9/1/26	Tue 9/1/26	0d
180	Second Floor Rough-in	Tue 9/1/26	Tue 9/1/26	0d	Tue 9/22/26	Tue 9/22/26	0d
181	Third Floor Rough-in	Tue 9/22/26	Tue 9/22/26	0d	Tue 10/13/26	Tue 10/13/26	0d
182	Set up the AHU on Three Floors	Fri 10/2/26	Fri 10/2/26	0d	Tue 10/13/26	Tue 10/13/26	0d
183	Setup the Roof Top Condenser Unit	Tue 10/13/26	Tue 10/13/26	0d	Thu 10/15/26	Thu 10/15/26	0d
184	**Electrical | Building A**	**Tue 8/11/26**	**Tue 8/11/26**	**0d**	**Thu 11/12/26**	**Thu 11/12/26**	**0d**
185	First Floor | Conduit, running Wire	Tue 8/11/26	Tue 8/11/26	0d	Tue 9/1/26	Tue 9/1/26	0d
186	First Floor Lighting	Tue 9/1/26	Tue 9/1/26	0d	Tue 9/8/26	Tue 9/8/26	0d
187	Second Floor | Conduit, running wire	Tue 9/8/26	Tue 9/8/26	0d	Tue 9/29/26	Tue 9/29/26	0d
188	Second Floor Lighting	Tue 9/29/26	Tue 9/29/26	0d	Tue 10/6/26	Tue 10/6/26	0d
189	Third Floor | Conduit, running wire	Tue 10/6/26	Tue 10/6/26	0d	Tue 10/27/26	Tue 10/27/26	0d
190	Third Floor Lighting	Tue 10/27/26	Tue 10/27/26	0d	Thu 11/5/26	Thu 11/5/26	0d
191	Gear Installation and Electrical Riser Assembly	Fri 11/6/26	Fri 11/6/26	0d	Thu 11/12/26	Thu 11/12/26	0d
192	Exterior Wall Packs	Thu 8/27/26	Thu 8/27/26	0d	Mon 8/31/26	Mon 8/31/26	0d
193	**Plumbing | Building A**	**Mon 7/6/26**	**Mon 7/6/26**	**0d**	**Tue 10/27/26**	**Tue 10/27/26**	**0d**
194	Second Floor Condenser line	Tue 10/13/26	Tue 10/13/26	0d	Tue 10/20/26	Tue 10/20/26	0d
195	Third Floor Condenser line	Tue 10/20/26	Tue 10/20/26	0d	Tue 10/27/26	Tue 10/27/26	0d
196	Roof Drain	Mon 7/6/26	Mon 7/6/26	0d	Fri 7/10/26	Fri 7/10/26	0d
197	Plumbing Bathroom Fixture	Thu 10/1/26	Thu 10/1/26	0d	Mon 10/5/26	Mon 10/5/26	0d
198	**Opening | Building A**	**Wed 6/17/26**	**Wed 6/17/26**	**0d**	**Mon 9/28/26**	**Mon 9/28/26**	**0d**
199	HMD Frame	Wed 6/17/26	Wed 6/17/26	0d	Mon 6/22/26	Mon 6/22/26	0d
200	HM Door and Hardware	Mon 9/21/26	Mon 9/21/26	0d	Thu 9/24/26	Thu 9/24/26	0d

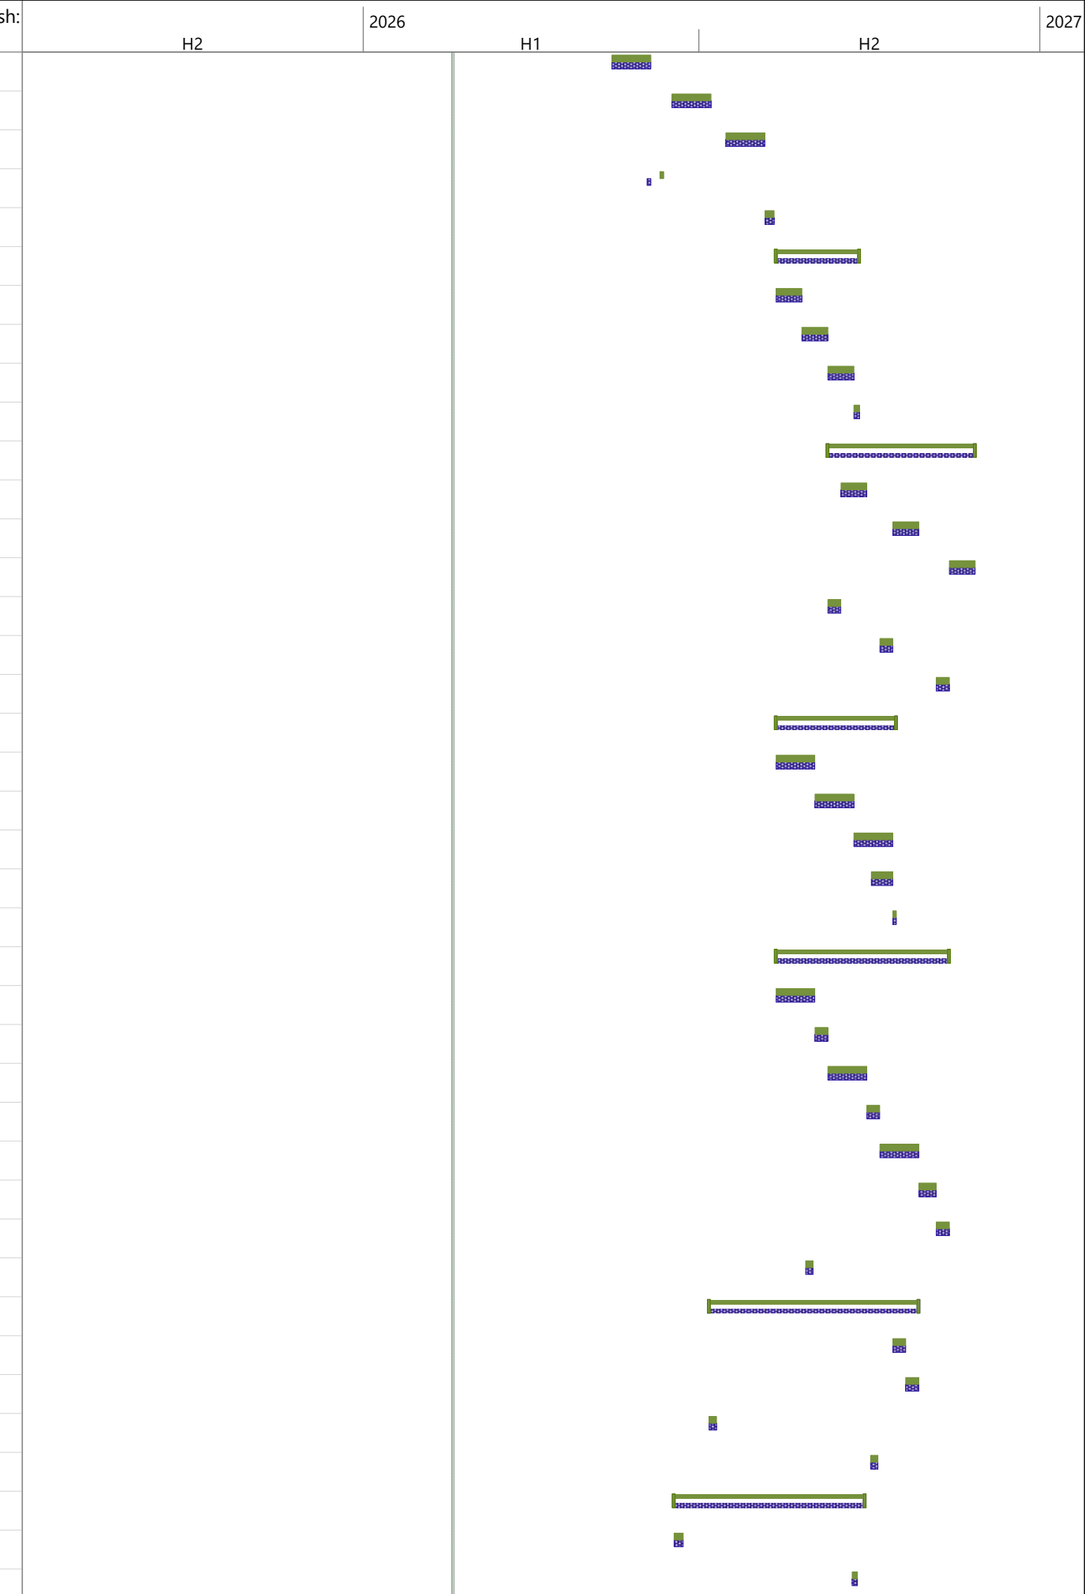

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
201	Glass and Glazing	Mon 9/21/26	Mon 9/21/26	0d	Mon 9/28/26	Mon 9/28/26	0d
202	Automatic Bi-Part Sliding Door	Tue 9/8/26	Tue 9/8/26	0d	Mon 9/14/26	Mon 9/14/26	0d
203	**Finishout | Building A**	**Mon 8/31/26**	**Mon 8/31/26**	**0d**	**Mon 10/5/26**	**Mon 10/5/26**	**0d**
204	Polish Concrete Floor | Restroom and corridor	Mon 8/31/26	Mon 8/31/26	0d	Wed 9/9/26	Wed 9/9/26	0d
205	White FRP for the Rest Room	Mon 9/28/26	Mon 9/28/26	0d	Thu 10/1/26	Thu 10/1/26	0d
206	Bathroom accessories and Signage	Thu 10/1/26	Thu 10/1/26	0d	Mon 10/5/26	Mon 10/5/26	0d
207	Gypsum Board Ceiling and Paint | Bathroom	Mon 9/21/26	Mon 9/21/26	0d	Mon 9/28/26	Mon 9/28/26	0d
208	Tape, Bed and Paint the Stair Wall	Mon 9/21/26	Mon 9/21/26	0d	Mon 9/28/26	Mon 9/28/26	0d
209	Paint HMD	Thu 9/24/26	Thu 9/24/26	0d	Mon 9/28/26	Mon 9/28/26	0d
210	Punch List | Building A	Fri 11/13/26	Fri 11/13/26	0d	Thu 11/19/26	Thu 11/19/26	0d
211	**Building B**	**Thu 3/5/26**	**Wed 3/18/26**	**-9d**	**Wed 7/22/26**	**Tue 8/4/26**	**-9d**
212	**Concrete | Building B**	**Thu 3/5/26**	**Wed 3/18/26**	**-9d**	**Thu 3/19/26**	**Wed 4/1/26**	**-9d**
213	**Slab on Grade | Building B**	**Thu 3/5/26**	**Wed 3/18/26**	**-9d**	**Thu 3/19/26**	**Wed 4/1/26**	**-9d**
214	Form Board installation	Thu 3/5/26	Wed 3/18/26	-9d	Fri 3/6/26	Thu 3/19/26	-9d
215	UG Plumbing Rough-in	Mon 3/9/26	Fri 3/20/26	-9d	Tue 3/10/26	Mon 3/23/26	-9d
216	Excavation for the Footing	Wed 3/11/26	Tue 3/24/26	-9d	Fri 3/13/26	Thu 3/26/26	-9d
217	Poly, Termite Control	Mon 3/16/26	Fri 3/27/26	-9d	Mon 3/16/26	Fri 3/27/26	-9d
218	Reinforcement Steel Placement	Tue 3/17/26	Mon 3/30/26	-9d	Wed 3/18/26	Tue 3/31/26	-9d
219	Pour Concrete Slab on Grade	Thu 3/19/26	Wed 4/1/26	-9d	Thu 3/19/26	Wed 4/1/26	-9d
220	Saw Cut for Control Joint	Thu 3/19/26	Wed 4/1/26	-9d	Thu 3/19/26	Wed 4/1/26	-9d
221	**Structural Steel Framing | Building B**	**Fri 4/17/26**	**Thu 4/30/26**	**-9d**	**Tue 5/5/26**	**Mon 5/18/26**	**-9d**
222	First Floor Structural Framing	Fri 4/17/26	Thu 4/30/26	-9d	Thu 4/23/26	Wed 5/6/26	-9d
223	Roof Framing and Roof Deck	Fri 4/24/26	Thu 5/7/26	-9d	Tue 5/5/26	Mon 5/18/26	-9d
224	**Exterior Wall Assembly | Building B**	**Fri 3/27/26**	**Thu 4/9/26**	**-9d**	**Thu 4/16/26**	**Wed 4/29/26**	**-9d**
225	8" CMU Masonry	Fri 3/27/26	Thu 4/9/26	-9d	Thu 4/16/26	Wed 4/29/26	-9d
226	**Roof | Building B**	**Thu 5/14/26**	**Wed 5/27/26**	**-9d**	**Mon 6/8/26**	**Fri 6/19/26**	**-9d**
227	Roofing Insulation	Thu 5/14/26	Wed 5/27/26	-9d	Mon 5/25/26	Fri 6/5/26	-9d
228	Standing Seam Metal Roof	Mon 5/25/26	Fri 6/5/26	-9d	Mon 6/8/26	Fri 6/19/26	-9d
229	**Interior Wall Assembly | Building B**	**Mon 6/8/26**	**Fri 6/19/26**	**-9d**	**Mon 6/22/26**	**Fri 7/3/26**	**-9d**
230	Fire Riser Room Assembly	Mon 6/8/26	Fri 6/19/26	-9d	Mon 6/22/26	Fri 7/3/26	-9d
231	**Fire Supression | Building B**	**Mon 6/8/26**	**Fri 6/19/26**	**-9d**	**Mon 6/22/26**	**Fri 7/3/26**	**-9d**
232	Fire Sprinkler | Dry System	Mon 6/8/26	Fri 6/19/26	-9d	Wed 6/17/26	Tue 6/30/26	-9d
233	Riser Room Assembly	Thu 6/18/26	Wed 7/1/26	-9d	Mon 6/22/26	Fri 7/3/26	-9d
234	**Fire Alarm | Building B**	**Mon 6/8/26**	**Fri 6/19/26**	**-9d**	**Thu 6/25/26**	**Wed 7/8/26**	**-9d**
235	Fire Alarm rough-in First Floor	Mon 6/8/26	Fri 6/19/26	-9d	Mon 6/22/26	Fri 7/3/26	-9d
236	Fire Alarm Panels	Tue 6/23/26	Mon 7/6/26	-9d	Thu 6/25/26	Wed 7/8/26	-9d
237	**Hallway System | Owner Furnished**	**Wed 7/1/26**	**Tue 7/14/26**	**-9d**	**Wed 7/22/26**	**Tue 8/4/26**	**-9d**
238	Hallway System | First Floor	Wed 7/8/26	Tue 7/21/26	-9d	Wed 7/22/26	Tue 8/4/26	-9d
239	Welded Wire Mesh | First Floor	Wed 7/1/26	Tue 7/14/26	-9d	Wed 7/8/26	Tue 7/21/26	-9d
240	**HVAC | Building B**	**Mon 6/29/26**	**Fri 7/10/26**	**-9d**	**Wed 7/1/26**	**Tue 7/14/26**	**-9d**

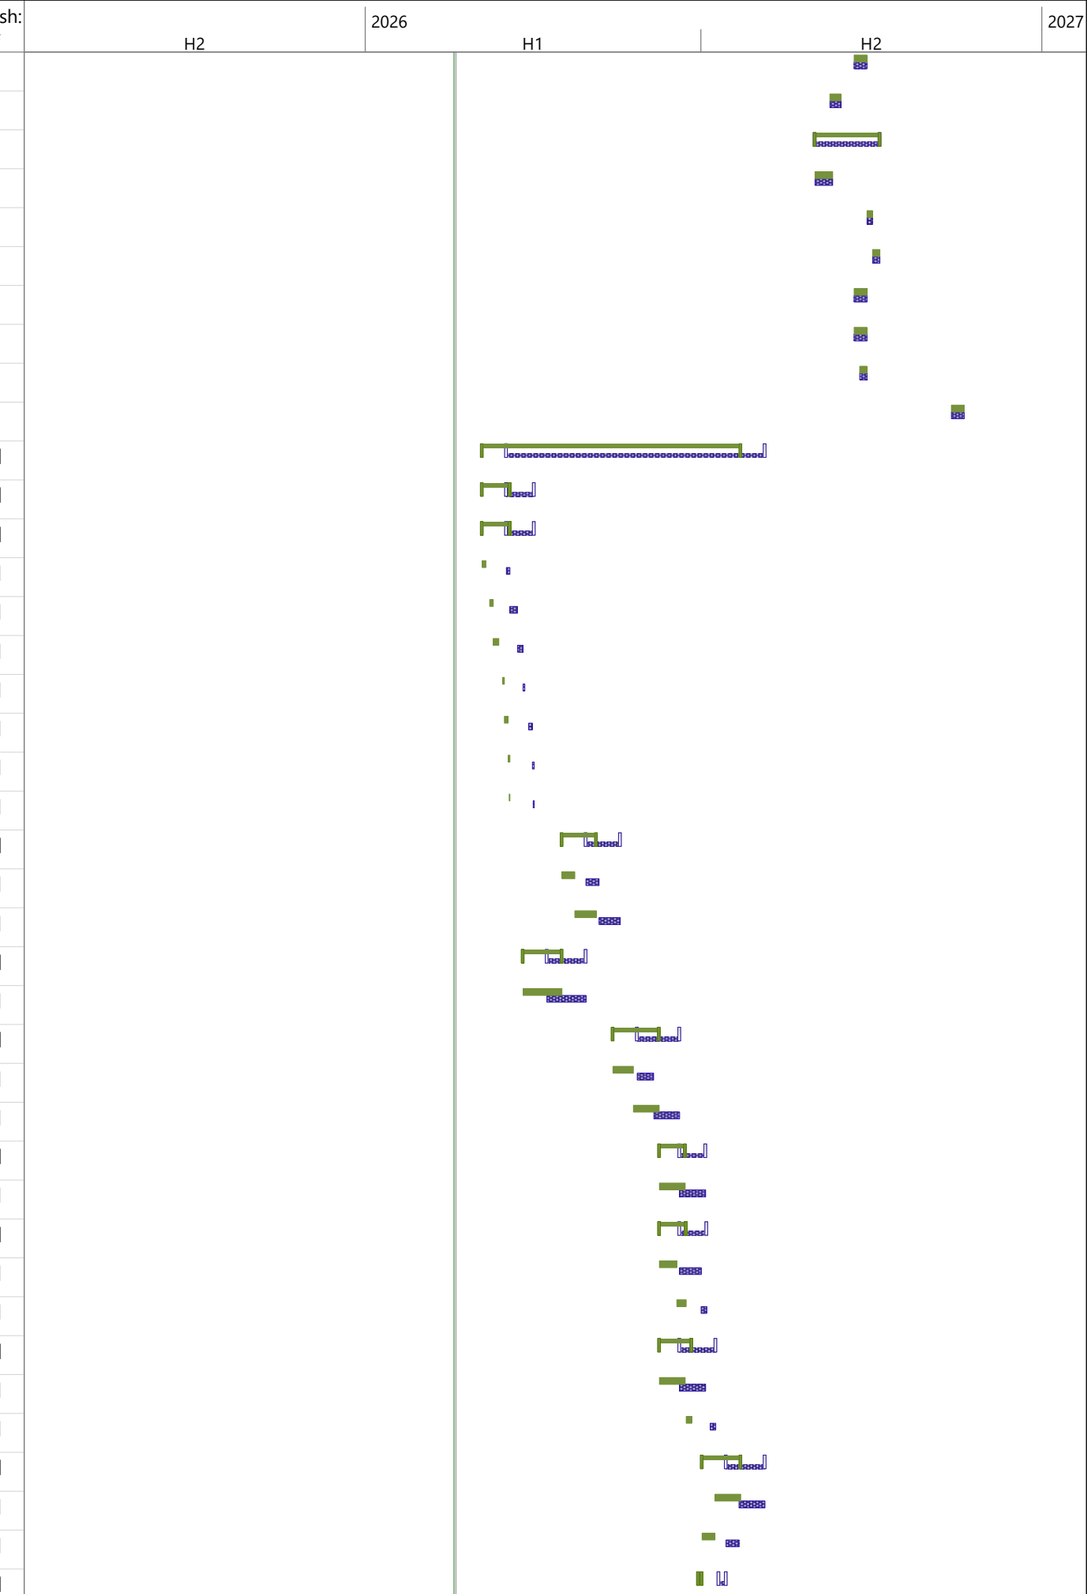

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
241	Riser Room Heater	Mon 6/29/26	Fri 7/10/26	-9d	Wed 7/1/26	Tue 7/14/26	-9d
242	**Electrical | Building B**	**Thu 6/11/26**	**Wed 6/24/26**	**-9d**	**Thu 7/2/26**	**Wed 7/15/26**	**-9d**
243	First Floor | Conduit, running Wire	Thu 6/11/26	Wed 6/24/26	-9d	Thu 6/18/26	Wed 7/1/26	-9d
244	First Floor Lighting	Thu 6/18/26	Wed 7/1/26	-9d	Thu 6/25/26	Wed 7/8/26	-9d
245	Gear Installation and Electrical Riser Assembly	Thu 6/25/26	Wed 7/8/26	-9d	Thu 7/2/26	Wed 7/15/26	-9d
246	Exterior Wall Packs	Thu 6/18/26	Wed 7/1/26	-9d	Mon 6/22/26	Fri 7/3/26	-9d
247	**Plumbing | Building B**	**Wed 5/6/26**	**Tue 5/19/26**	**-9d**	**Thu 5/7/26**	**Wed 5/20/26**	**-9d**
248	Roof Drain	Wed 5/6/26	Tue 5/19/26	-9d	Thu 5/7/26	Wed 5/20/26	-9d
249	**Opening | Building B**	**Tue 3/31/26**	**Mon 4/13/26**	**-9d**	**Thu 6/11/26**	**Wed 6/24/26**	**-9d**
250	HMD Frame	Tue 3/31/26	Mon 4/13/26	-9d	Thu 4/2/26	Wed 4/15/26	-9d
251	HM Door and Hardware	Mon 6/8/26	Fri 6/19/26	-9d	Thu 6/11/26	Wed 6/24/26	-9d
252	Punch List | Building B	Thu 7/2/26	Wed 7/15/26	-9d	Thu 7/9/26	Wed 7/22/26	-9d
253	**Building C**	**Fri 2/20/26**	**Fri 3/20/26**	**-20d**	**Wed 8/12/26**	**Tue 8/25/26**	**-9d**
254	**Concrete | Building C**	**Fri 2/20/26**	**Fri 3/20/26**	**-20d**	**Fri 3/27/26**	**Thu 4/9/26**	**-9d**
255	**Slab on Grade | Building C**	**Fri 2/20/26**	**Fri 3/20/26**	**-20d**	**Fri 3/27/26**	**Thu 4/9/26**	**-9d**
256	Form Board installation	Fri 2/20/26	Fri 3/20/26	-20d	Mon 2/23/26	Mon 3/23/26	-20d
257	UG Plumbing Rough-in	Tue 2/24/26	Tue 3/24/26	-20d	Wed 2/25/26	Wed 3/25/26	-20d
258	Excavation for the Footing	Thu 3/19/26	Wed 4/1/26	-9d	Mon 3/23/26	Fri 4/3/26	-9d
259	Poly, Termite Control	Tue 3/24/26	Mon 4/6/26	-9d	Tue 3/24/26	Mon 4/6/26	-9d
260	Reinforcement Steel Placement	Wed 3/25/26	Tue 4/7/26	-9d	Thu 3/26/26	Wed 4/8/26	-9d
261	Pour Concrete Slab on Grade	Fri 3/27/26	Thu 4/9/26	-9d	Fri 3/27/26	Thu 4/9/26	-9d
262	Saw Cut for Control Joint	Fri 3/27/26	Thu 4/9/26	-9d	Fri 3/27/26	Thu 4/9/26	-9d
263	**Structural Steel Framing | Building C**	**Fri 5/8/26**	**Thu 5/21/26**	**-9d**	**Tue 5/26/26**	**Mon 6/8/26**	**-9d**
264	First Floor Structural Framing	Fri 5/8/26	Thu 5/21/26	-9d	Thu 5/14/26	Wed 5/27/26	-9d
265	Roof Framing and Roof Deck	Fri 5/15/26	Thu 5/28/26	-9d	Tue 5/26/26	Mon 6/8/26	-9d
266	**Exterior Wall Assembly | Building C**	**Fri 4/17/26**	**Thu 4/30/26**	**-9d**	**Thu 5/7/26**	**Wed 5/20/26**	**-9d**
267	8" CMU Masonry	Fri 4/17/26	Thu 4/30/26	-9d	Thu 5/7/26	Wed 5/20/26	-9d
268	**Roof | Building C**	**Thu 6/4/26**	**Wed 6/17/26**	**-9d**	**Mon 6/29/26**	**Fri 7/10/26**	**-9d**
269	Roofing Insulation	Thu 6/4/26	Wed 6/17/26	-9d	Mon 6/15/26	Fri 6/26/26	-9d
270	Standing Seam Metal Roof	Mon 6/15/26	Fri 6/26/26	-9d	Mon 6/29/26	Fri 7/10/26	-9d
271	**Interior Wall Assembly | Building C**	**Mon 6/29/26**	**Fri 7/10/26**	**-9d**	**Mon 7/13/26**	**Fri 7/24/26**	**-9d**
272	Fire Riser Room Assembly	Mon 6/29/26	Fri 7/10/26	-9d	Mon 7/13/26	Fri 7/24/26	-9d
273	**Fire Supression | Building C**	**Mon 6/29/26**	**Fri 7/10/26**	**-9d**	**Mon 7/13/26**	**Fri 7/24/26**	**-9d**
274	Fire Sprinkler | Dry System	Mon 6/29/26	Fri 7/10/26	-9d	Wed 7/8/26	Tue 7/21/26	-9d
275	Riser Room Assembly	Thu 7/9/26	Wed 7/22/26	-9d	Mon 7/13/26	Fri 7/24/26	-9d
276	**Fire Alarm | Building C**	**Mon 6/29/26**	**Fri 7/10/26**	**-9d**	**Thu 7/16/26**	**Wed 7/29/26**	**-9d**
277	Fire Alarm rough-in First Floor	Mon 6/29/26	Fri 7/10/26	-9d	Mon 7/13/26	Fri 7/24/26	-9d
278	Fire Alarm Panels	Tue 7/14/26	Mon 7/27/26	-9d	Thu 7/16/26	Wed 7/29/26	-9d
279	**Hallway System | Owner Furnished**	**Wed 7/22/26**	**Tue 8/4/26**	**-9d**	**Wed 8/12/26**	**Tue 8/25/26**	**-9d**
280	Hallway System | First Floor	Wed 7/29/26	Tue 8/11/26	-9d	Wed 8/12/26	Tue 8/25/26	-9d

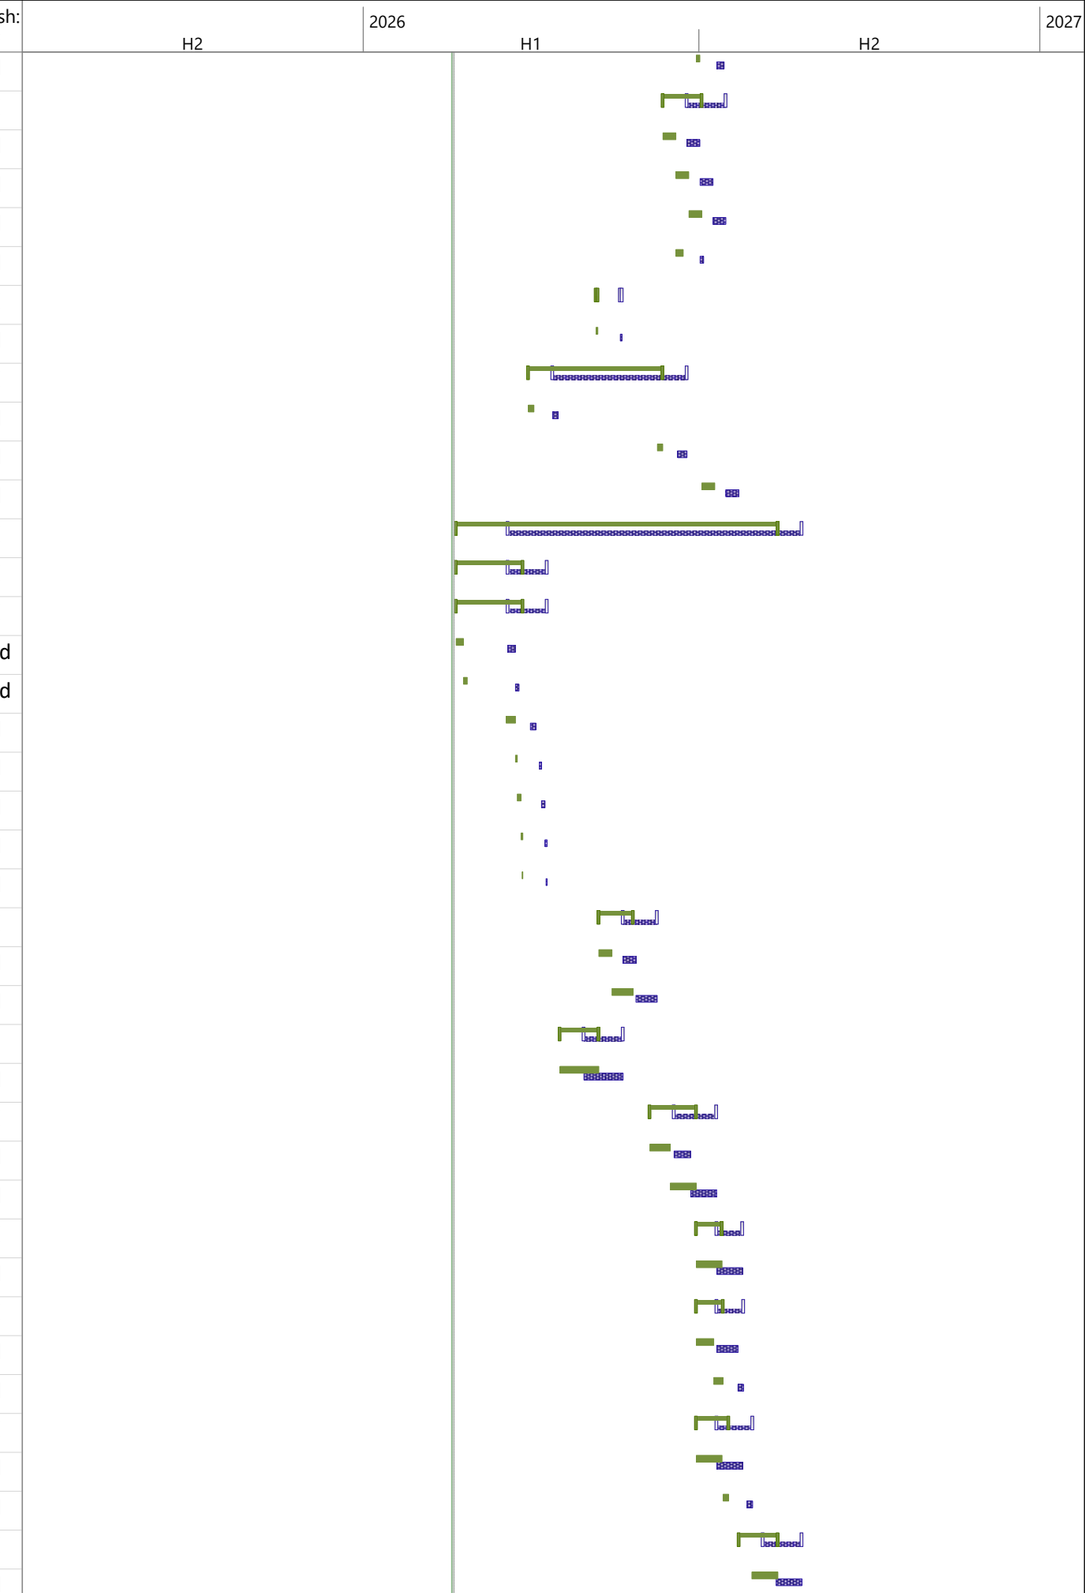

	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
281	Welded Wire Mesh | First Floor	Wed 7/22/26	Tue 8/4/26	-9d	Wed 7/29/26	Tue 8/11/26	-9d
282	**HVAC | Building C**	**Mon 7/20/26**	**Fri 7/31/26**	**-9d**	**Wed 7/22/26**	**Tue 8/4/26**	**-9d**
283	Riser Room Heater	Mon 7/20/26	Fri 7/31/26	-9d	Wed 7/22/26	Tue 8/4/26	-9d
284	**Electrical | Building C**	**Thu 7/2/26**	**Wed 7/15/26**	**-9d**	**Thu 7/23/26**	**Wed 8/5/26**	**-9d**
285	First Floor | Conduit, running Wire	Thu 7/2/26	Wed 7/15/26	-9d	Thu 7/9/26	Wed 7/22/26	-9d
286	First Floor Lighting	Thu 7/9/26	Wed 7/22/26	-9d	Thu 7/16/26	Wed 7/29/26	-9d
287	Gear Installation and Electrical Riser Assembly	Thu 7/16/26	Wed 7/29/26	-9d	Thu 7/23/26	Wed 8/5/26	-9d
288	Exterior Wall Packs	Thu 7/9/26	Wed 7/22/26	-9d	Mon 7/13/26	Fri 7/24/26	-9d
289	**Plumbing | Building C**	**Wed 5/27/26**	**Tue 6/9/26**	**-9d**	**Thu 5/28/26**	**Wed 6/10/26**	**-9d**
290	Roof Drain	Wed 5/27/26	Tue 6/9/26	-9d	Thu 5/28/26	Wed 6/10/26	-9d
291	**Opening | Building C**	**Tue 4/21/26**	**Mon 5/4/26**	**-9d**	**Thu 7/2/26**	**Wed 7/15/26**	**-9d**
292	HMD Frame	Tue 4/21/26	Mon 5/4/26	-9d	Thu 4/23/26	Wed 5/6/26	-9d
293	HM Door and Hardware	Mon 6/29/26	Fri 7/10/26	-9d	Thu 7/2/26	Wed 7/15/26	-9d
294	Punch List | Building C	Thu 7/23/26	Wed 8/5/26	-9d	Thu 7/30/26	Wed 8/12/26	-9d
295	**Building D**	**Tue 2/24/26**	**Tue 3/24/26**	**-20d**	**Wed 9/2/26**	**Tue 9/15/26**	**-9d**
296	**Concrete | Building D**	**Tue 2/24/26**	**Tue 3/24/26**	**-20d**	**Wed 4/1/26**	**Tue 4/14/26**	**-9d**
297	**Slab on Grade | Building D**	**Tue 2/24/26**	**Tue 3/24/26**	**-20d**	**Wed 4/1/26**	**Tue 4/14/26**	**-9d**
298	Form Board installation	Tue 2/24/26	Tue 3/24/26	-20d	Wed 2/25/26	Wed 3/25/26	-20d
299	UG Plumbing Rough-in	Thu 2/26/26	Thu 3/26/26	-20d	Fri 2/27/26	Fri 3/27/26	-20d
300	Excavation for the Footing	Tue 3/24/26	Mon 4/6/26	-9d	Thu 3/26/26	Wed 4/8/26	-9d
301	Poly, Termite Control	Fri 3/27/26	Thu 4/9/26	-9d	Fri 3/27/26	Thu 4/9/26	-9d
302	Reinforcement Steel Placement	Mon 3/30/26	Fri 4/10/26	-9d	Tue 3/31/26	Mon 4/13/26	-9d
303	Pour Concrete Slab on Grade	Wed 4/1/26	Tue 4/14/26	-9d	Wed 4/1/26	Tue 4/14/26	-9d
304	Saw Cut for Control Joint	Wed 4/1/26	Tue 4/14/26	-9d	Wed 4/1/26	Tue 4/14/26	-9d
305	**Structural Steel Framing | Building D**	**Fri 5/29/26**	**Thu 6/11/26**	**-9d**	**Tue 6/16/26**	**Mon 6/29/26**	**-9d**
306	First Floor Structural Framing	Fri 5/29/26	Thu 6/11/26	-9d	Thu 6/4/26	Wed 6/17/26	-9d
307	Roof Framing and Roof Deck	Fri 6/5/26	Thu 6/18/26	-9d	Tue 6/16/26	Mon 6/29/26	-9d
308	**Exterior Wall Assembly | Building D**	**Fri 5/8/26**	**Thu 5/21/26**	**-9d**	**Thu 5/28/26**	**Wed 6/10/26**	**-9d**
309	8" CMU Masonry	Fri 5/8/26	Thu 5/21/26	-9d	Thu 5/28/26	Wed 6/10/26	-9d
310	**Roof | Building D**	**Thu 6/25/26**	**Wed 7/8/26**	**-9d**	**Mon 7/20/26**	**Fri 7/31/26**	**-9d**
311	Roofing Insulation	Thu 6/25/26	Wed 7/8/26	-9d	Mon 7/6/26	Fri 7/17/26	-9d
312	Standing Seam Metal Roof	Mon 7/6/26	Fri 7/17/26	-9d	Mon 7/20/26	Fri 7/31/26	-9d
313	**Interior Wall Assembly | Building D**	**Mon 7/20/26**	**Fri 7/31/26**	**-9d**	**Mon 8/3/26**	**Fri 8/14/26**	**-9d**
314	Fire Riser Room Assembly	Mon 7/20/26	Fri 7/31/26	-9d	Mon 8/3/26	Fri 8/14/26	-9d
315	**Fire Supression | Building D**	**Mon 7/20/26**	**Fri 7/31/26**	**-9d**	**Mon 8/3/26**	**Fri 8/14/26**	**-9d**
316	Fire Sprinkler | Dry System	Mon 7/20/26	Fri 7/31/26	-9d	Wed 7/29/26	Tue 8/11/26	-9d
317	Riser Room Assembly	Thu 7/30/26	Wed 8/12/26	-9d	Mon 8/3/26	Fri 8/14/26	-9d
318	**Fire Alarm | Building D**	**Mon 7/20/26**	**Fri 7/31/26**	**-9d**	**Thu 8/6/26**	**Wed 8/19/26**	**-9d**
319	Fire Alarm rough-in First Floor	Mon 7/20/26	Fri 7/31/26	-9d	Mon 8/3/26	Fri 8/14/26	-9d
320	Fire Alarm Panels	Tue 8/4/26	Mon 8/17/26	-9d	Thu 8/6/26	Wed 8/19/26	-9d
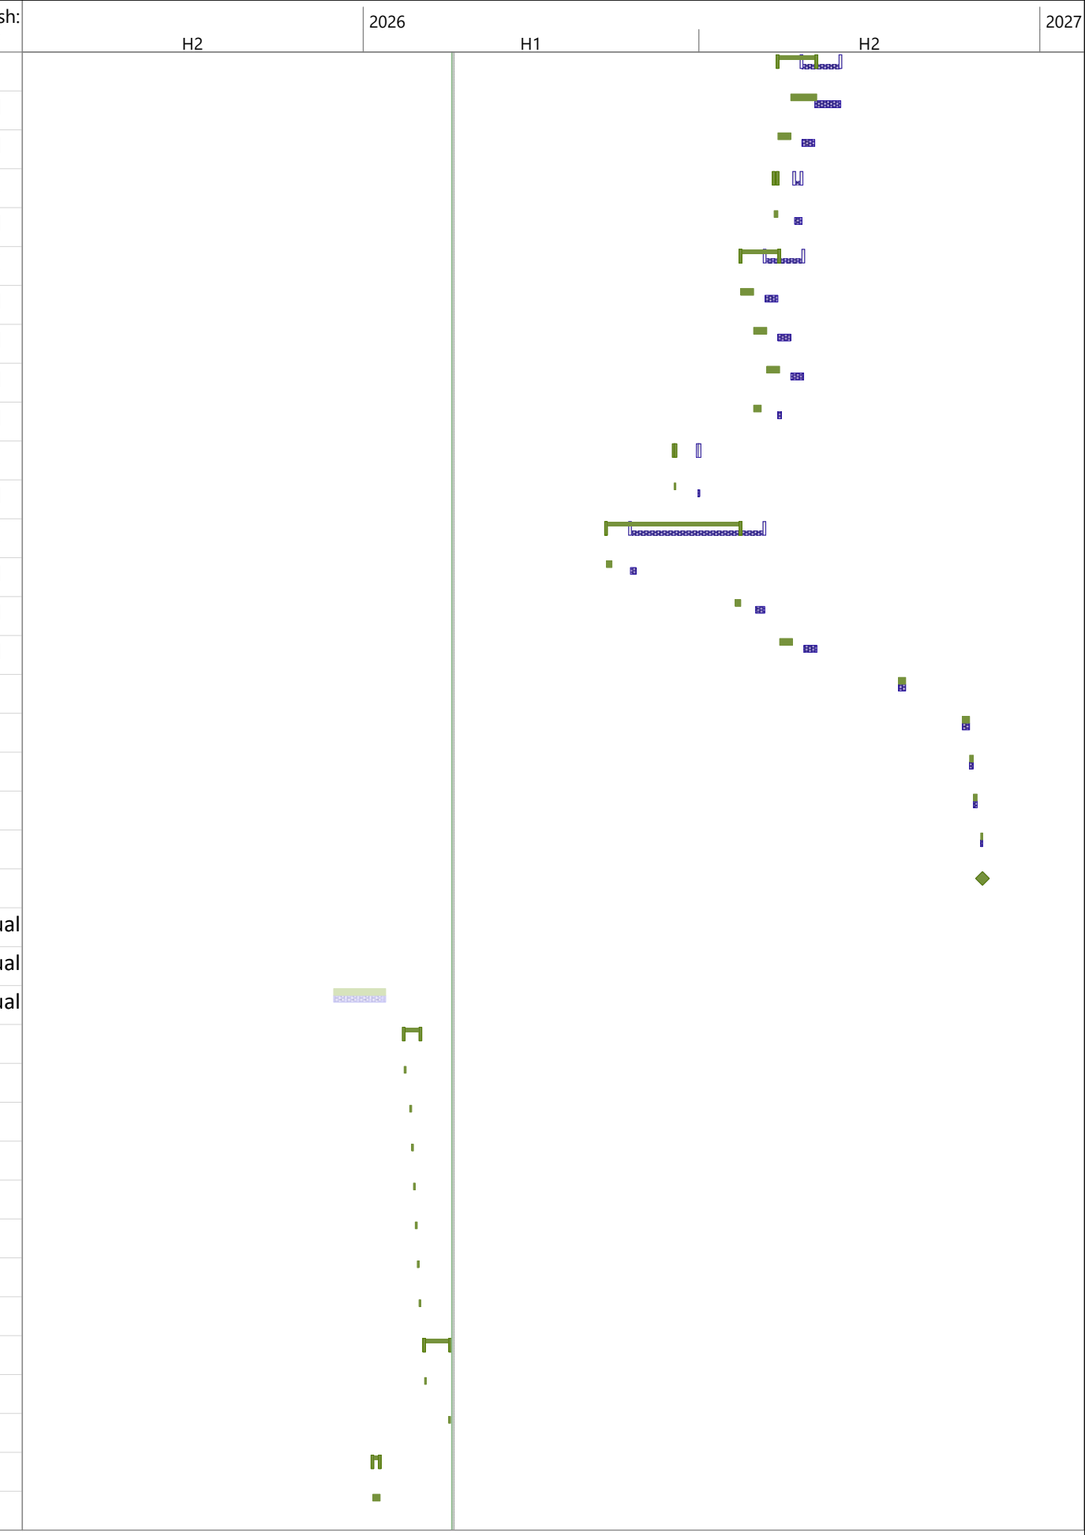
	Name	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
321	**Hallway System | Owner Furnished**	**Wed 8/12/26**	**Tue 8/25/26**	**-9d**	**Wed 9/2/26**	**Tue 9/15/26**	**-9d**
322	Hallway System | First Floor	Wed 8/19/26	Tue 9/1/26	-9d	Wed 9/2/26	Tue 9/15/26	-9d
323	Welded Wire Mesh | First Floor	Wed 8/12/26	Tue 8/25/26	-9d	Wed 8/19/26	Tue 9/1/26	-9d
324	**HVAC | Building D**	**Mon 8/10/26**	**Fri 8/21/26**	**-9d**	**Wed 8/12/26**	**Tue 8/25/26**	**-9d**
325	Riser Room Heater	Mon 8/10/26	Fri 8/21/26	-9d	Wed 8/12/26	Tue 8/25/26	-9d
326	**Electrical | Building D**	**Thu 7/23/26**	**Wed 8/5/26**	**-9d**	**Thu 8/13/26**	**Wed 8/26/26**	**-9d**
327	First Floor | Conduit, running Wire	Thu 7/23/26	Wed 8/5/26	-9d	Thu 7/30/26	Wed 8/12/26	-9d
328	First Floor Lighting	Thu 7/30/26	Wed 8/12/26	-9d	Thu 8/6/26	Wed 8/19/26	-9d
329	Gear Installation and Electrical Riser Assembly	Thu 8/6/26	Wed 8/19/26	-9d	Thu 8/13/26	Wed 8/26/26	-9d
330	Exterior Wall Packs	Thu 7/30/26	Wed 8/12/26	-9d	Mon 8/3/26	Fri 8/14/26	-9d
331	**Plumbing | Building D**	**Wed 6/17/26**	**Tue 6/30/26**	**-9d**	**Thu 6/18/26**	**Wed 7/1/26**	**-9d**
332	Roof Drain	Wed 6/17/26	Tue 6/30/26	-9d	Thu 6/18/26	Wed 7/1/26	-9d
333	**Opening | Building D**	**Tue 5/12/26**	**Mon 5/25/26**	**-9d**	**Thu 7/23/26**	**Wed 8/5/26**	**-9d**
334	HMD Frame	Tue 5/12/26	Mon 5/25/26	-9d	Thu 5/14/26	Wed 5/27/26	-9d
335	HM Door and Hardware	Mon 7/20/26	Fri 7/31/26	-9d	Thu 7/23/26	Wed 8/5/26	-9d
336	Punch List | Building D	Thu 8/13/26	Wed 8/26/26	-9d	Thu 8/20/26	Wed 9/2/26	-9d
337	Elevator State Inspection	Fri 10/16/26	Fri 10/16/26	0d	Tue 10/20/26	Tue 10/20/26	0d
338	MEP Final Inspection	Fri 11/20/26	Fri 11/20/26	0d	Mon 11/23/26	Mon 11/23/26	0d
339	Fire Final Inspection	Tue 11/24/26	Tue 11/24/26	0d	Wed 11/25/26	Wed 11/25/26	0d
340	Engineering Final Inspection	Thu 11/26/26	Thu 11/26/26	0d	Fri 11/27/26	Fri 11/27/26	0d
341	Building Final Inspection	Mon 11/30/26	Mon 11/30/26	0d	Mon 11/30/26	Mon 11/30/26	0d
342	TCO/CO	Mon 11/30/26	Mon 11/30/26	0d	Mon 11/30/26	Mon 11/30/26	0d
343				Equa			Equal
344	Weather Day Log			Equa			Equal
345	Contractor has included 20 Weatherdays in this schedule from 01.			Equa			Equal
346	**Januray 2026 - 7 Days**	**Fri 1/23/26**			**Sat 1/31/26**		
347	01.23.2026 - Freezing Rain	Fri 1/23/26			Fri 1/23/26		
348	01.26.2026 - Snow	Mon 1/26/26			Mon 1/26/26		
349	01.27.2026 - Snow	Tue 1/27/26			Tue 1/27/26		
350	01.28.2026 - Ice	Wed 1/28/26			Wed 1/28/26		
351	01.29.2026 - Ice	Thu 1/29/26			Thu 1/29/26		
352	01.30.2026 - Ice	Fri 1/30/26			Fri 1/30/26		
353	01.31.2026 - Freezing	Sat 1/31/26			Sat 1/31/26		
354	**February 2026**	**Tue 2/3/26**			**Mon 2/16/26**		
355	02.03.2026 - Muddy	Tue 2/3/26			Tue 2/3/26		
356	02.16.2026 - Water Ponding and Muddy	Mon 2/16/26			Mon 2/16/26		
357	**Delay Log**	**Tue 1/6/26**			**Fri 1/9/26**		
358	Material Testing Lab	Tue 1/6/26			Fri 1/9/26
