Public Storage Willis - TX24198

ID	Task Mode	Task Name	Duration	Start	Finish	% Complete
1		**Public Storage Willis - TX 24198**	**207 days**	**Thu 25/09/25**	**Fri 26/07/10**	**0%**
2		**Pre-Construction**	**133 days**	**Thu 25/09/25**	**Mon 26/03/30**	**0%**
3		Contract Signed	1 day	Thu 25/09/25	Thu 25/09/25	0%
4		Building Permit	1 day	Fri 26/01/09	Fri 26/01/09	0%
5		Fire Tank Permit	1 day	Mon 26/03/30	Mon 26/03/30	0%
6		NTP - From PS	1 day	Mon 26/01/12	Mon 26/01/12	0%
7		Approval to go Vertical by AHJ	1 day	Wed 26/03/04	Wed 26/03/04	0%
8		**Procurement**	**70 days**	**Tue 26/02/17**	**Mon 26/05/25**	**0%**
9		Building Structure	2 days	Tue 26/02/17	Thu 26/02/19	0%
10		Hallway System	2 days	Tue 26/05/19	Thu 26/05/21	0%
11		Fire Tank Delivery	1 day	Mon 26/05/25	Mon 26/05/25	0%
12		**Site Work**	**100 days**	**Tue 26/01/13**	**Mon 26/06/01**	**0%**
13		**Earthwork**	**17 days**	**Tue 26/01/13**	**Wed 26/02/04**	**0%**
14		Erosion Control | BMPs	3 days	Tue 26/01/13	Thu 26/01/15	0%
15		Demolition & Haul Off - For Bldg Pad	4 days	Fri 26/01/16	Wed 26/01/21	0%
16		Grading | Cut & Fill	5 days	Thu 26/01/22	Wed 26/01/28	0%
17		Bulding Pad Preparation	5 days	Thu 26/01/29	Wed 26/02/04	0%
18		**Site Utilities**	**93 days**	**Thu 26/01/22**	**Mon 26/06/01**	**0%**
19		Re-adjust existing storm	3 days	Thu 26/01/22	Mon 26/01/26	0%
20		Storm Sewer	5 days	Thu 26/02/05	Wed 26/02/11	0%
21		Sanitary Sewer	6 days	Thu 26/02/12	Thu 26/02/19	0%
22		Water Line	6 days	Fri 26/02/20	Fri 26/02/27	0%
23		Utility Approval by AHJ	2 days	Mon 26/03/02	Tue 26/03/03	0%
24		**Fire Tank (By Others)**	**5 days**	**Tue 26/05/26**	**Mon 26/06/01**	**0%**
25		Fire Tank Installation	5 days	Tue 26/05/26	Mon 26/06/01	0%
26		**Exterior Improvements**	**66 days**	**Mon 26/03/02**	**Mon 26/06/01**	**0%**
27		**Site Paving**	**22 days**	**Mon 26/03/02**	**Tue 26/03/31**	**0%**
28		Paving Subgrade Prep	8 days	Mon 26/03/02	Wed 26/03/11	0%
29		Fire Lane Concrete Paving	8 days	Thu 26/03/12	Mon 26/03/23	0%
30		Light Duty Concrete Paving	6 days	Tue 26/03/24	Tue 26/03/31	0%
31		**Detention Pond Work**	**9 days**	**Thu 26/03/12**	**Tue 26/03/24**	**0%**
32		Grading | Cut	5 days	Thu 26/03/12	Wed 26/03/18	0%
33		Storm Sewer	4 days	Thu 26/03/19	Tue 26/03/24	0%
34		**Landscape & Irrigation**	**11 days**	**Mon 26/05/11**	**Mon 26/05/25**	**0%**
35		Irrigation Installation	6 days	Mon 26/05/11	Mon 26/05/18	0%
36		Landscape Installation	5 days	Tue 26/05/19	Mon 26/05/25	0%
37		**Gates & Fences**	**5 days**	**Tue 26/05/26**	**Mon 26/06/01**	**0%**
38		Chain Link Fence	3 days	Tue 26/05/26	Thu 26/05/28	0%
39		Double Swing Gate	2 days	Fri 26/05/29	Mon 26/06/01	0%
40		**Building Work**	**107 days**	**Thu 26/02/05**	**Fri 26/07/03**	**0%**
41		**SOG | Foundation**	**12 days**	**Thu 26/02/05**	**Fri 26/02/20**	**0%**
42		Form Board	1 day	Thu 26/02/05	Thu 26/02/05	0%
43		Plumbing UG Rough-In	1 day	Fri 26/02/06	Fri 26/02/06	0%
44		Electrical UFER & Service	1 day	Mon 26/02/09	Mon 26/02/09	0%
45		Grade Beam Excavation	3 days	Tue 26/02/10	Thu 26/02/12	0%
46		Set Poly & Termite Control	1 day	Fri 26/02/13	Fri 26/02/13	0%
47		Set Rebar for GB & SOG	2 days	Mon 26/02/16	Tue 26/02/17	0%
48		Pour & Finish SOG	2 days	Wed 26/02/18	Thu 26/02/19	0%

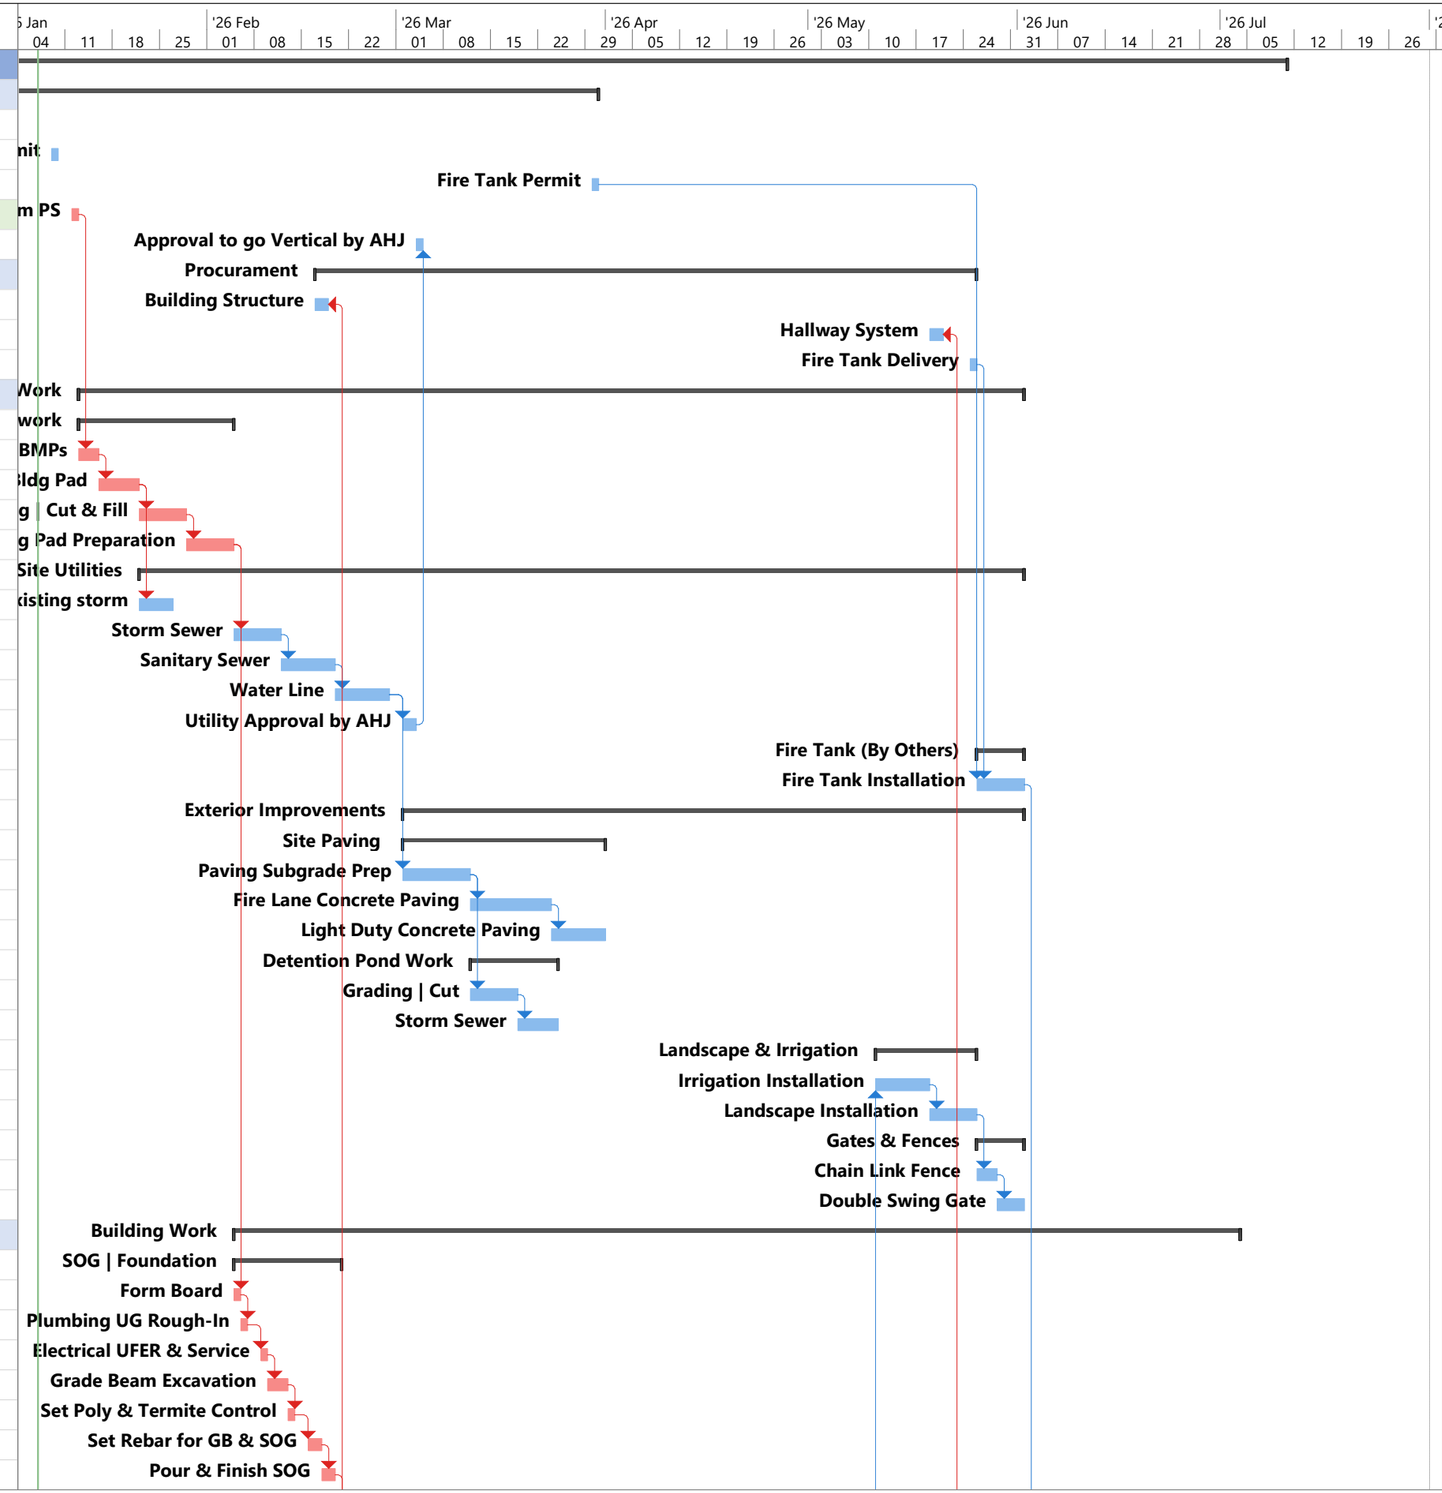

Public Storage Willis - TX24198
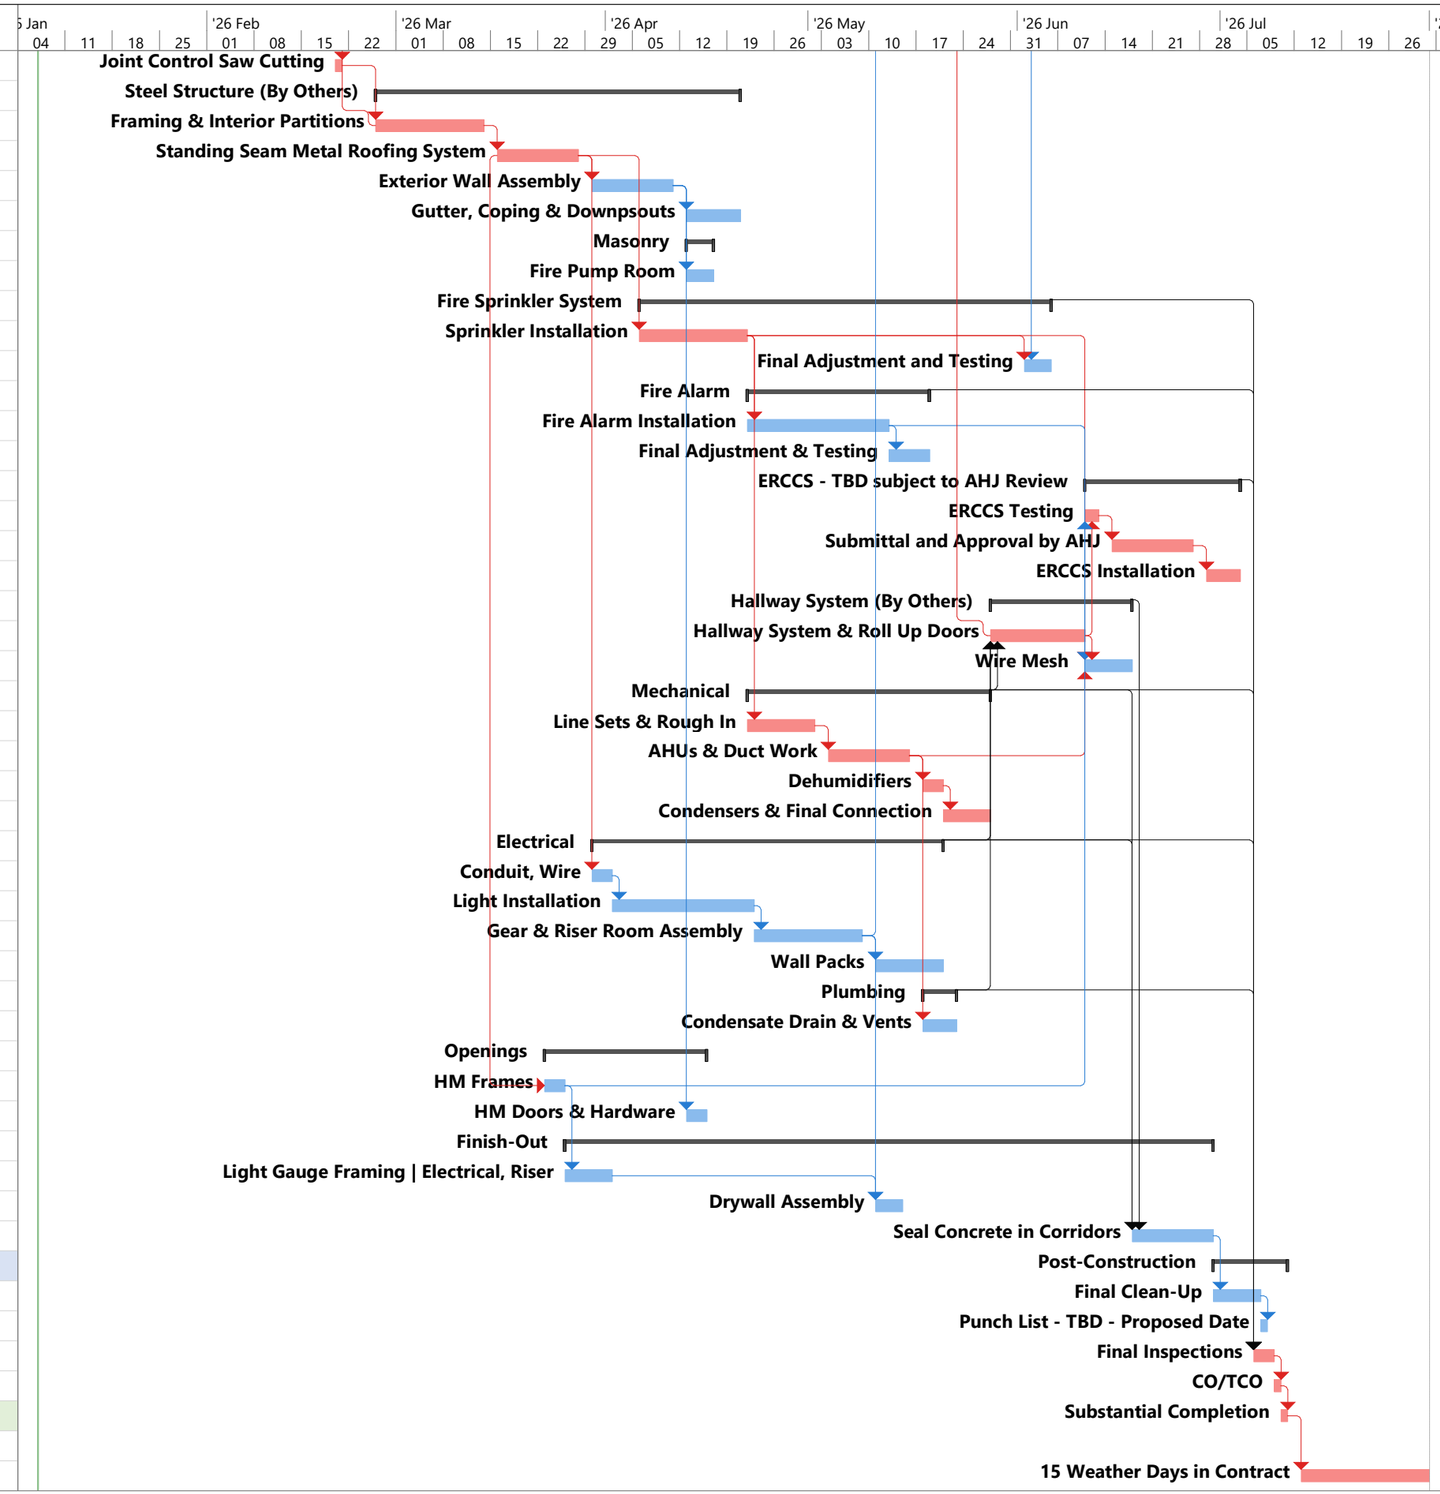
ID	Task Mode	Task Name	Duration	Start	Finish	% Complete
49		Joint Control Saw Cutting	1 day	Fri 26/02/20	Fri 26/02/20	0%
50		**Steel Structure (By Others)**	**38 days**	**Thu 26/02/26**	**Mon 26/04/20**	**0%**
51		Framing & Interior Partitions	12 days	Thu 26/02/26	Fri 26/03/13	0%
52		Standing Seam Metal Roofing System	10 days	Mon 26/03/16	Fri 26/03/27	0%
53		Exterior Wall Assembly	10 days	Mon 26/03/30	Fri 26/04/10	0%
54		Gutter, Coping & Downpsouts	6 days	Mon 26/04/13	Mon 26/04/20	0%
55		**Masonry**	**4 days**	**Mon 26/04/13**	**Thu 26/04/16**	**0%**
56		Fire Pump Room	4 days	Mon 26/04/13	Thu 26/04/16	0%
57		**Fire Sprinkler System**	**45 days**	**Mon 26/04/06**	**Fri 26/06/05**	**0%**
58		Sprinkler Installation	12 days	Mon 26/04/06	Tue 26/04/21	0%
59		Final Adjustment and Testing	4 days	Tue 26/06/02	Fri 26/06/05	0%
60		**Fire Alarm**	**19 days**	**Wed 26/04/22**	**Mon 26/05/18**	**0%**
61		Fire Alarm Installation	15 days	Wed 26/04/22	Tue 26/05/12	0%
62		Final Adjustment & Testing	4 days	Wed 26/05/13	Mon 26/05/18	0%
63		**ERCCS - TBD subject to AHJ Review**	**17 days**	**Thu 26/06/11**	**Fri 26/07/03**	**0%**
64		ERCCS Testing	2 days	Thu 26/06/11	Fri 26/06/12	0%
65		Submittal and Approval by AHJ	10 days	Mon 26/06/15	Fri 26/06/26	0%
66		ERCCS Installation	5 days	Mon 26/06/29	Fri 26/07/03	0%
67		**Hallway System (By Others)**	**15 days**	**Thu 26/05/28**	**Wed 26/06/17**	**0%**
68		Hallway System & Roll Up Doors	10 days	Thu 26/05/28	Wed 26/06/10	0%
69		Wire Mesh	5 days	Thu 26/06/11	Wed 26/06/17	0%
70		**Mechanical**	**26 days**	**Wed 26/04/22**	**Wed 26/05/27**	**0%**
71		Line Sets & Rough In	8 days	Wed 26/04/22	Fri 26/05/01	0%
72		AHUs & Duct Work	10 days	Mon 26/05/04	Fri 26/05/15	0%
73		Dehumidifiers	3 days	Mon 26/05/18	Wed 26/05/20	0%
74		Condensers & Final Connection	5 days	Thu 26/05/21	Wed 26/05/27	0%
75		**Electrical**	**38 days**	**Mon 26/03/30**	**Wed 26/05/20**	**0%**
76		Conduit, Wire	3 days	Mon 26/03/30	Wed 26/04/01	0%
77		Light Installation	15 days	Thu 26/04/02	Wed 26/04/22	0%
78		Gear & Riser Room Assembly	12 days	Thu 26/04/23	Fri 26/05/08	0%
79		Wall Packs	8 days	Mon 26/05/11	Wed 26/05/20	0%
80		**Plumbing**	**5 days**	**Mon 26/05/18**	**Fri 26/05/22**	**0%**
81		Condensate Drain & Vents	5 days	Mon 26/05/18	Fri 26/05/22	0%
82		**Openings**	**18 days**	**Mon 26/03/23**	**Wed 26/04/15**	**0%**
83		HM Frames	3 days	Mon 26/03/23	Wed 26/03/25	0%
84		HM Doors & Hardware	3 days	Mon 26/04/13	Wed 26/04/15	0%
85		**Finish-Out**	**68 days**	**Thu 26/03/26**	**Mon 26/06/29**	**0%**
86		Light Gauge Framing | Electrical, Riser	5 days	Thu 26/03/26	Wed 26/04/01	0%
87		Drywall Assembly	4 days	Mon 26/05/11	Thu 26/05/14	0%
88		Seal Concrete in Corridors	8 days	Thu 26/06/18	Mon 26/06/29	0%
89		**Post-Construction**	**9 days**	**Tue 26/06/30**	**Fri 26/07/10**	**0%**
90		Final Clean-Up	5 days	Tue 26/06/30	Mon 26/07/06	0%
91		Punch List - TBD - Proposed Date	1 day	Tue 26/07/07	Tue 26/07/07	0%
92		Final Inspections	3 days	Mon 26/07/06	Wed 26/07/08	0%
93		CO/TCO	1 day	Thu 26/07/09	Thu 26/07/09	0%
94		Substantial Completion	1 day	Fri 26/07/10	Fri 26/07/10	0%
95						
96		15 Weather Days in Contract	15 days	Mon 26/07/13	Fri 26/07/31	0%
