Public Storage Willis - TX24198

ID	Task Name	% Complete	Duration	Start	Finish
1	**Public Storage Willis - TX 24198**	**9%**	**224 days**	**Thu 9/25/25**	**Tue 8/4/26**
2	**Pre-Construction**	**60%**	**133 days**	**Thu 9/25/25**	**Mon 3/30/26**
3	Contract Signed	100%	1 day	Thu 9/25/25	Thu 9/25/25
4	Building Permit	100%	1 day	Fri 1/9/26	Fri 1/9/26
5	Fire Tank Permit	0%	1 day	Mon 3/30/26	Mon 3/30/26
6	NTP - From PS	100%	1 day	Mon 1/12/26	Mon 1/12/26
7	Approval to go Vertical by AHJ	0%	1 day	Wed 3/25/26	Wed 3/25/26
8	**Procurement**	**0%**	**44 days**	**Tue 3/31/26**	**Mon 6/1/26**
9	Building Structure	0%	2 days	Tue 3/31/26	Thu 4/2/26
10	Hallway System	0%	2 days	Thu 5/28/26	Mon 6/1/26
11	Fire Tank Delivery	0%	1 day	Mon 5/25/26	Mon 5/25/26
12	**Site Work**	**20%**	**116 days**	**Mon 2/2/26**	**Mon 7/13/26**
13	**Earthwork**	**100%**	**17 days**	**Mon 2/2/26**	**Tue 2/24/26**
14	Erosion Control | BMPs	100%	3 days	Mon 2/2/26	Wed 2/4/26
15	Demolition & Haul Off - For Bldg Pad	100%	4 days	Mon 2/9/26	Thu 2/12/26
16	Grading | Cut & Fill	100%	5 days	Fri 2/13/26	Thu 2/19/26
17	Bulding Pad Preparation	100%	3 days	Fri 2/20/26	Tue 2/24/26
18	**Site Utilities**	**0%**	**63 days**	**Thu 3/5/26**	**Mon 6/1/26**
19	Storm Sewer	0%	4 days	Thu 3/5/26	Tue 3/10/26
20	Sanitary Sewer	0%	4 days	Wed 3/11/26	Mon 3/16/26
21	Water Line	0%	5 days	Tue 3/17/26	Mon 3/23/26
22	Utility Approval by AHJ	0%	1 day	Tue 3/24/26	Tue 3/24/26
23	**Fire Tank (By Others)**	**0%**	**5 days**	**Tue 5/26/26**	**Mon 6/1/26**
24	Fire Tank Installation	0%	5 days	Tue 5/26/26	Mon 6/1/26
25	**Exterior Improvements**	**0%**	**93 days**	**Thu 3/5/26**	**Mon 7/13/26**
26	**Site Paving**	**0%**	**12 days**	**Tue 3/24/26**	**Wed 4/8/26**
27	Paving Subgrade Prep	0%	6 days	Tue 3/24/26	Tue 3/31/26
28	Fire Lane Concrete Paving	0%	4 days	Wed 4/1/26	Mon 4/6/26
29	Light Duty Concrete Paving	0%	2 days	Tue 4/7/26	Wed 4/8/26
30	**Detention Pond Work**	**0%**	**14 days**	**Thu 3/5/26**	**Tue 3/24/26**
31	Grading | Cut	0%	10 days	Thu 3/5/26	Wed 3/18/26
32	Storm Sewer	0%	4 days	Thu 3/19/26	Tue 3/24/26

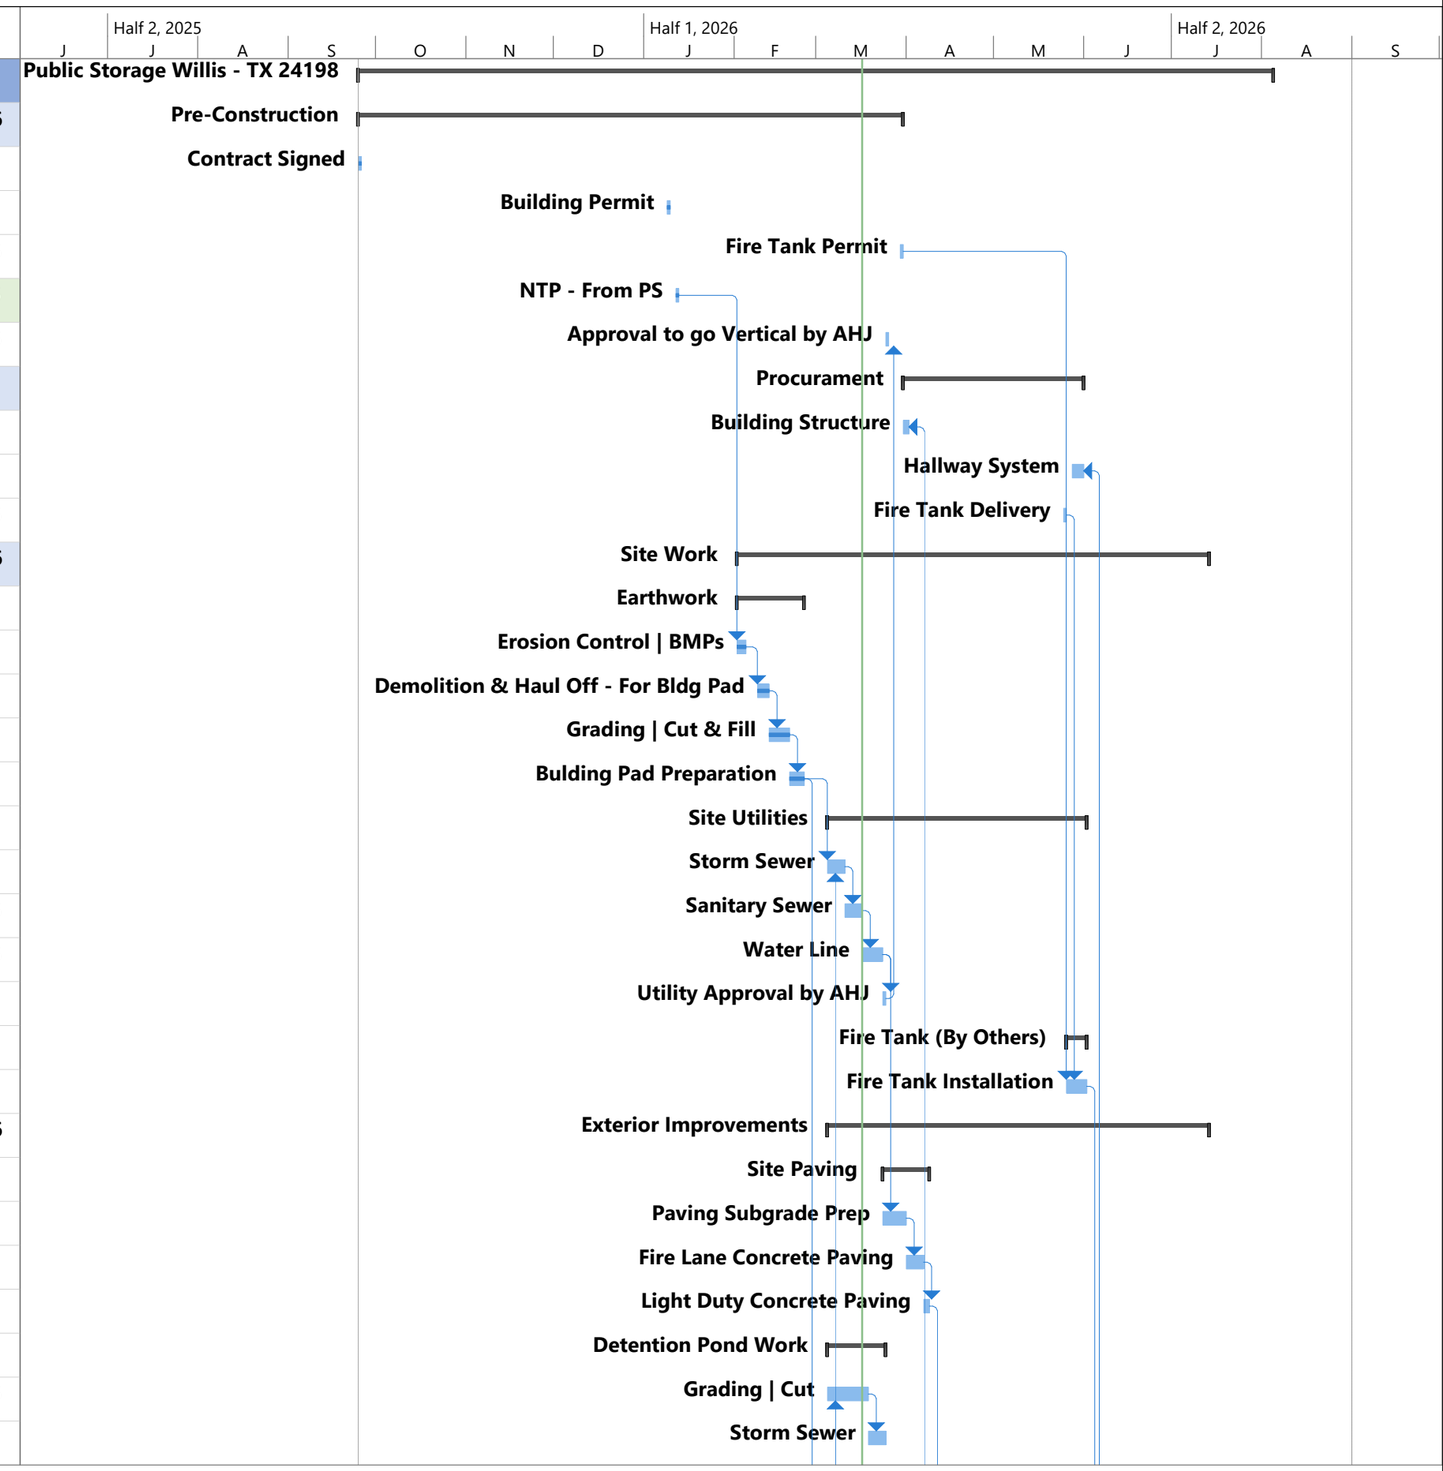

Public Storage Willis - TX24198

ID	Task Name	% Complete	Duration	Start	Finish
33	**Landscape & Irrigation**	**0%**	**11 days**	**Mon 6/22/26**	**Mon 7/6/26**
34	Irrigation Installation	0%	6 days	Mon 6/22/26	Mon 6/29/26
35	Landscape Installation	0%	5 days	Tue 6/30/26	Mon 7/6/26
36	**Gates & Fences**	**0%**	**5 days**	**Tue 7/7/26**	**Mon 7/13/26**
37	Chain Link Fence	0%	3 days	Tue 7/7/26	Thu 7/9/26
38	Double Swing Gate	0%	2 days	Fri 7/10/26	Mon 7/13/26
39	**Building Work**	**5%**	**110 days**	**Wed 2/25/26**	**Tue 7/28/26**
40	**SOG | Foundation**	**100%**	**6 days**	**Wed 2/25/26**	**Wed 3/4/26**
41	Form Board & Grade Beam Excavation	100%	1 day	Wed 2/25/26	Wed 2/25/26
42	Pest Control	100%	1 day	Thu 2/26/26	Thu 2/26/26
43	Set Up Poly & Rebar - Phase 1	100%	2 days	Fri 2/27/26	Mon 3/2/26
44	Place and Finish Slab - Phase 1	100%	1 day	Tue 3/3/26	Tue 3/3/26
45	Undeground Plumbing Rough In	100%	2 days	Thu 2/26/26	Fri 2/27/26
46	Set Up Poly & Rebar - Phase 2	100%	2 days	Mon 3/2/26	Tue 3/3/26
47	Place and Finish Rebar - Phase 2	100%	1 day	Wed 3/4/26	Wed 3/4/26
48	**Steel Structure (Betco/Janus)**	**0%**	**38 days**	**Thu 4/9/26**	**Mon 6/1/26**
49	Framing & Interior Partitions	0%	12 days	Thu 4/9/26	Fri 4/24/26
50	Standing Seam Metal Roofing System	0%	10 days	Mon 4/27/26	Fri 5/8/26
51	Exterior Wall Assembly	0%	10 days	Mon 5/11/26	Fri 5/22/26
52	Gutter, Coping & Downpsouts	0%	6 days	Mon 5/25/26	Mon 6/1/26
53	**Masonry**	**0%**	**4 days**	**Mon 5/25/26**	**Thu 5/28/26**
54	Fire Pump Room	0%	4 days	Mon 5/25/26	Thu 5/28/26
55	**Fire Sprinkler System**	**0%**	**30 days**	**Mon 4/27/26**	**Fri 6/5/26**
56	Sprinkler Installation	0%	12 days	Mon 4/27/26	Tue 5/12/26
57	Final Adjustment and Testing	0%	4 days	Tue 6/2/26	Fri 6/5/26
58	**Fire Alarm**	**0%**	**19 days**	**Wed 5/13/26**	**Mon 6/8/26**
59	Fire Alarm Installation	0%	15 days	Wed 5/13/26	Tue 6/2/26
60	Final Adjustment & Testing	0%	4 days	Wed 6/3/26	Mon 6/8/26
61	**ERCCS - TBD subject to AHJ Review**	**0%**	**17 days**	**Mon 7/6/26**	**Tue 7/28/26**
62	ERCCS Testing	0%	2 days	Mon 7/6/26	Tue 7/7/26
63	Submittal and Approval by AHJ	0%	10 days	Wed 7/8/26	Tue 7/21/26
64	ERCCS Installation	0%	5 days	Wed 7/22/26	Tue 7/28/26

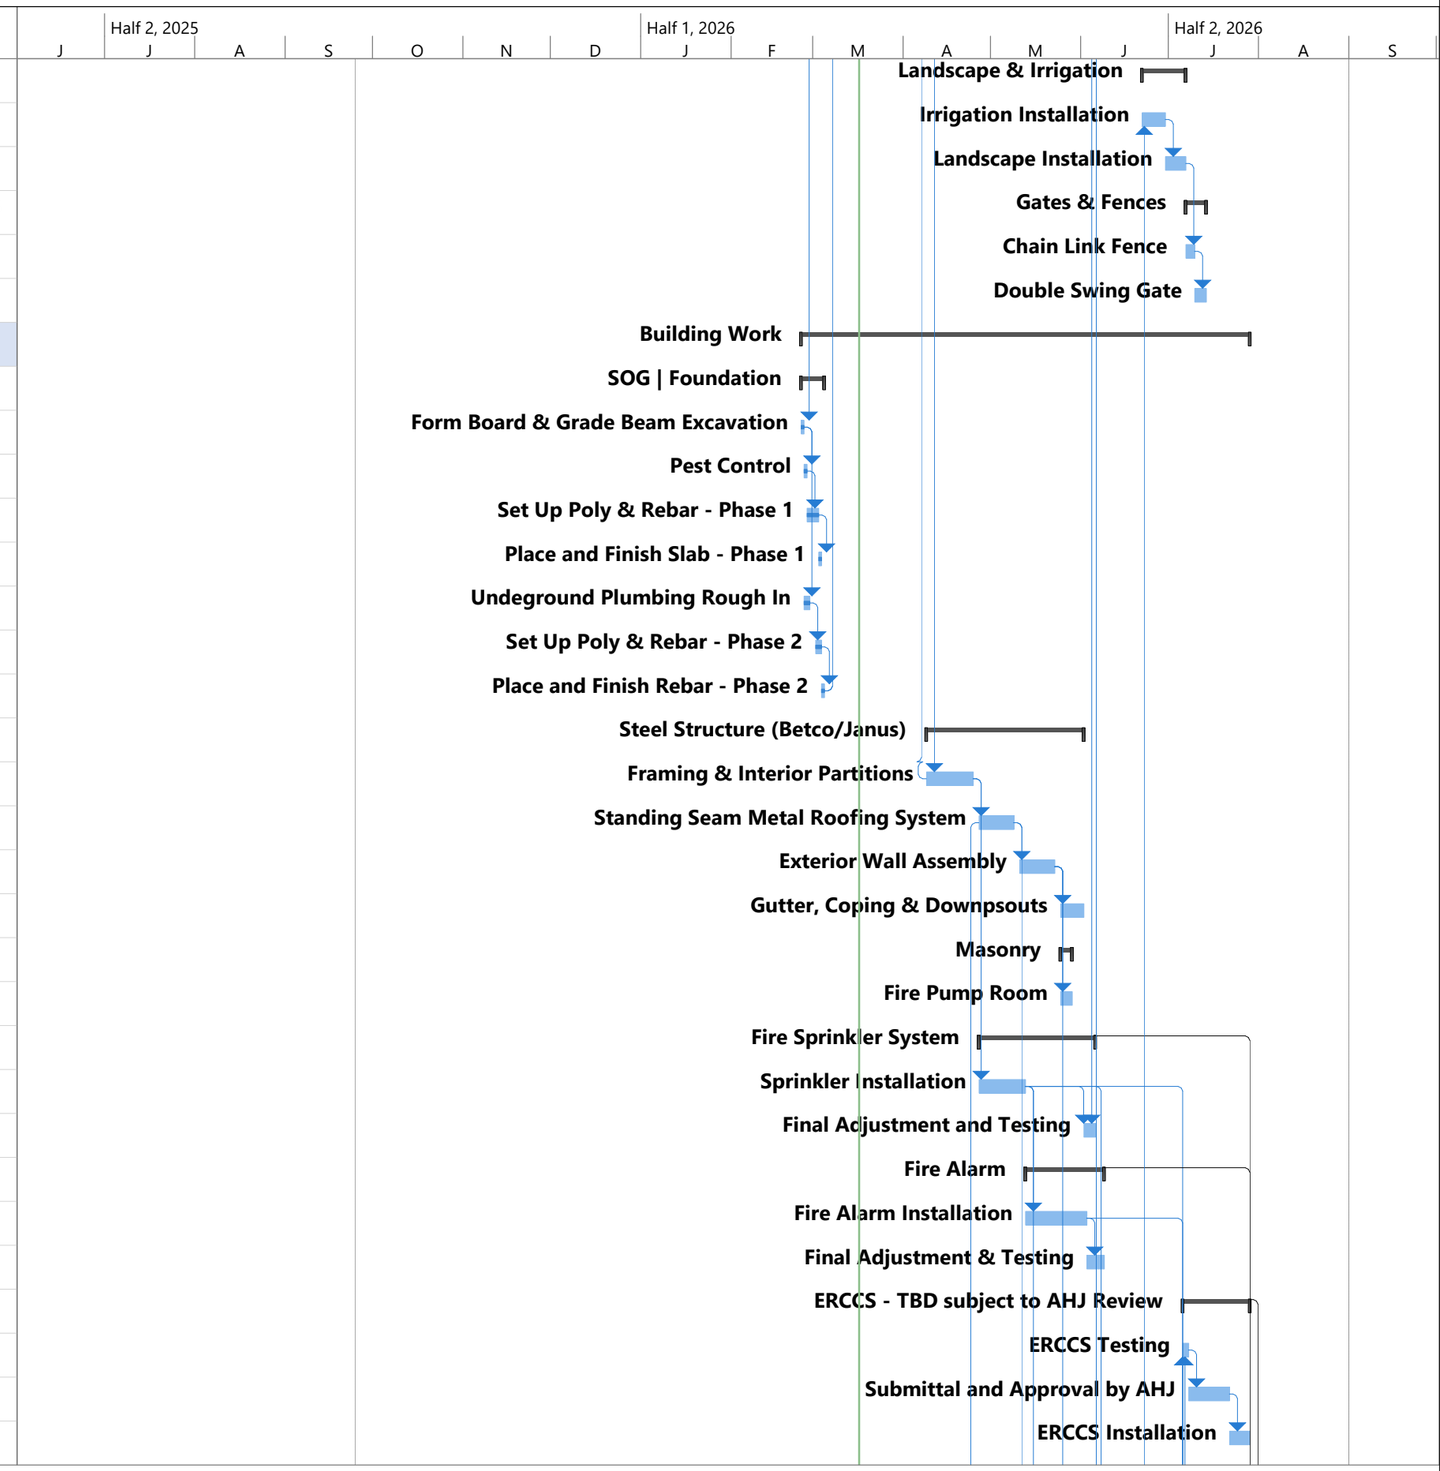

Public Storage Willis - TX24198
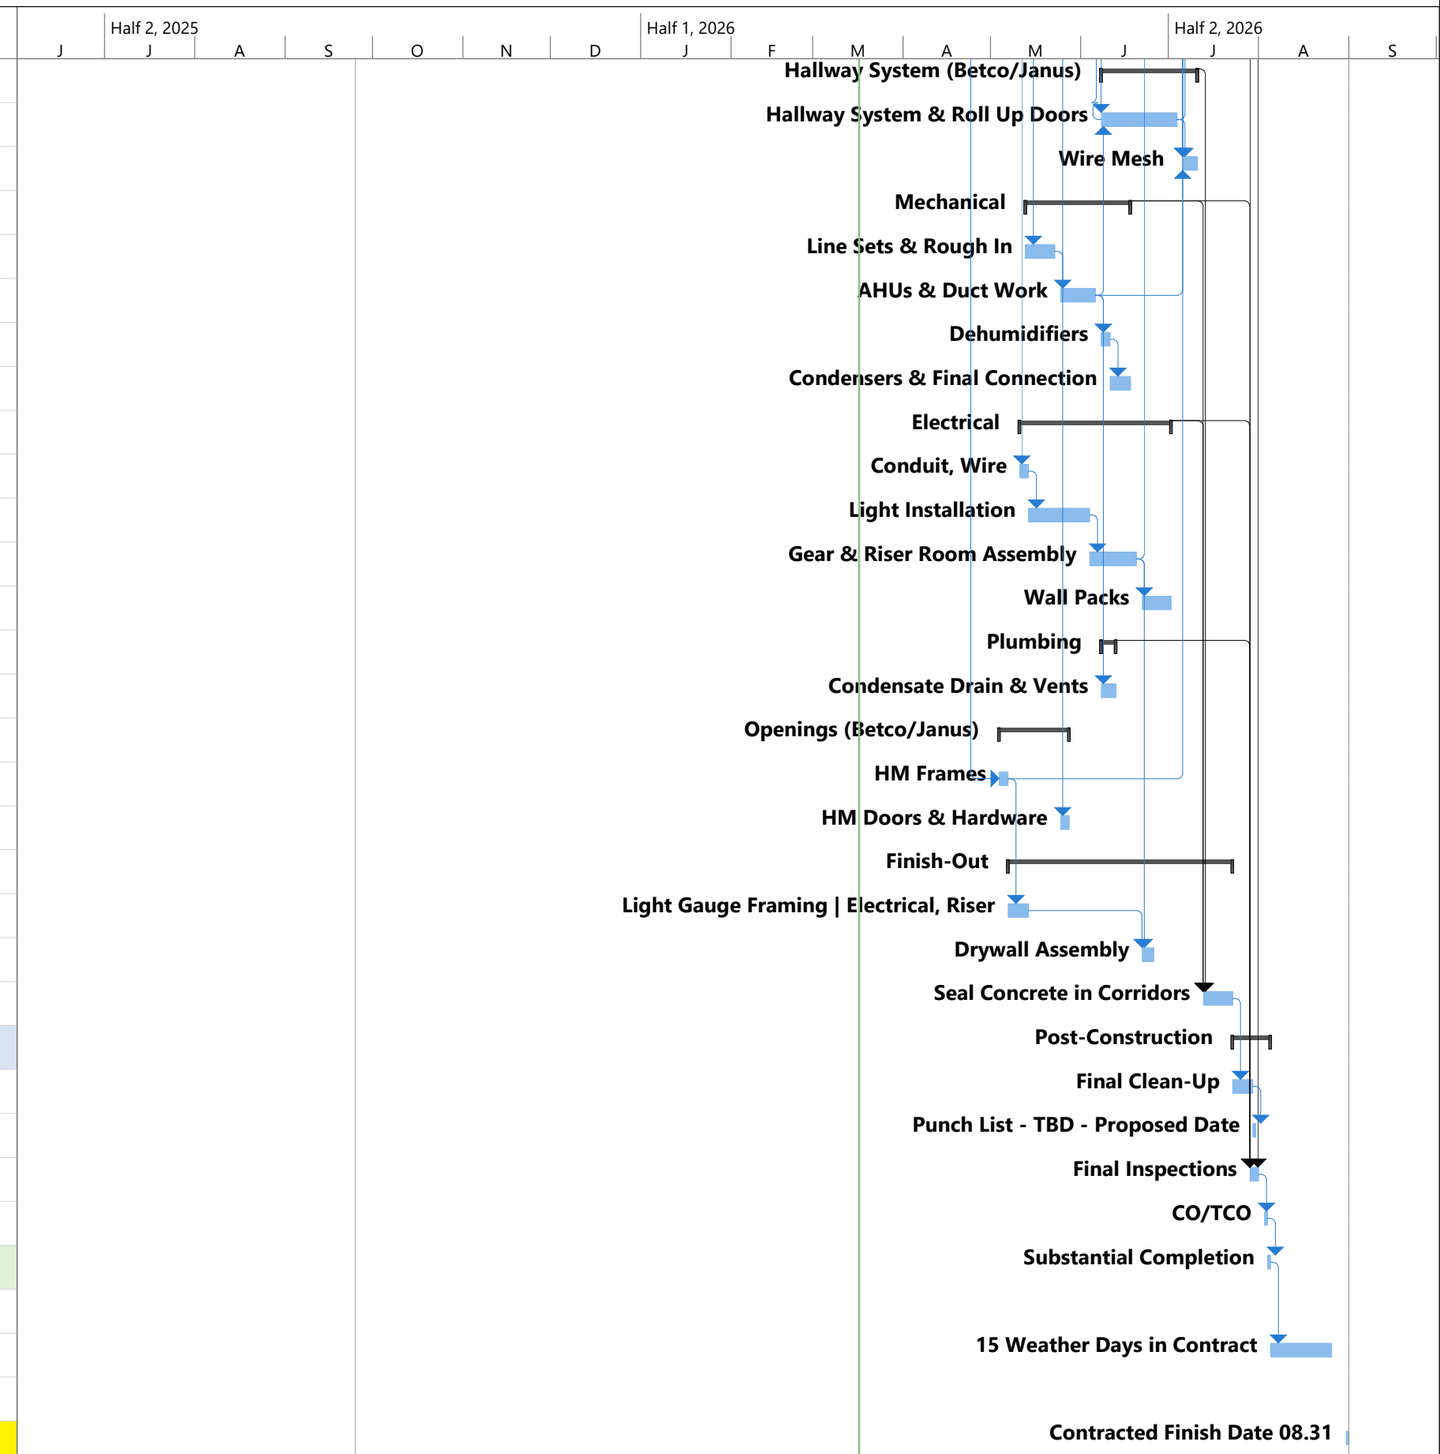
ID	Task Name	% Complete	Duration	Start	Finish
65	**Hallway System (Betco/Janus)**	**0%**	**25 days**	**Mon 6/8/26**	**Fri 7/10/26**
66	Hallway System & Roll Up Doors	0%	20 days	Mon 6/8/26	Fri 7/3/26
67	Wire Mesh	0%	5 days	Mon 7/6/26	Fri 7/10/26
68	**Mechanical**	**0%**	**26 days**	**Wed 5/13/26**	**Wed 6/17/26**
69	Line Sets & Rough In	0%	8 days	Wed 5/13/26	Fri 5/22/26
70	AHUs & Duct Work	0%	10 days	Mon 5/25/26	Fri 6/5/26
71	Dehumidifiers	0%	3 days	Mon 6/8/26	Wed 6/10/26
72	Condensers & Final Connection	0%	5 days	Thu 6/11/26	Wed 6/17/26
73	**Electrical**	**0%**	**38 days**	**Mon 5/11/26**	**Wed 7/1/26**
74	Conduit, Wire	0%	3 days	Mon 5/11/26	Wed 5/13/26
75	Light Installation	0%	15 days	Thu 5/14/26	Wed 6/3/26
76	Gear & Riser Room Assembly	0%	12 days	Thu 6/4/26	Fri 6/19/26
77	Wall Packs	0%	8 days	Mon 6/22/26	Wed 7/1/26
78	**Plumbing**	**0%**	**5 days**	**Mon 6/8/26**	**Fri 6/12/26**
79	Condensate Drain & Vents	0%	5 days	Mon 6/8/26	Fri 6/12/26
80	**Openings (Betco/Janus)**	**0%**	**18 days**	**Mon 5/4/26**	**Wed 5/27/26**
81	HM Frames	0%	3 days	Mon 5/4/26	Wed 5/6/26
82	HM Doors & Hardware	0%	3 days	Mon 5/25/26	Wed 5/27/26
83	**Finish-Out**	**0%**	**55 days**	**Thu 5/7/26**	**Wed 7/22/26**
84	Light Gauge Framing | Electrical, Riser	0%	5 days	Thu 5/7/26	Wed 5/13/26
85	Drywall Assembly	0%	4 days	Mon 6/22/26	Thu 6/25/26
86	Seal Concrete in Corridors	0%	8 days	Mon 7/13/26	Wed 7/22/26
87	**Post-Construction**	**0%**	**9 days**	**Thu 7/23/26**	**Tue 8/4/26**
88	Final Clean-Up	0%	5 days	Thu 7/23/26	Wed 7/29/26
89	Punch List - TBD - Proposed Date	0%	1 day	Thu 7/30/26	Thu 7/30/26
90	Final Inspections	0%	3 days	Wed 7/29/26	Fri 7/31/26
91	CO/TCO	0%	1 day	Mon 8/3/26	Mon 8/3/26
92	Substantial Completion	0%	1 day	Tue 8/4/26	Tue 8/4/26
93					
94	15 Weather Days in Contract	0%	15 days	Wed 8/5/26	Tue 8/25/26
95					
96	Contracted Finish Date 08.31	0%	1 day	Mon 8/31/26	Mon 8/31/26
