	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
1	**Public Storage Willis - TX 24198**	**224 days**	**223 days**	**1d**	**Thu 9/25/25**	**Thu 9/25/25**	**0d**	**Tue 8/4/26**	**Mon 8/3/26**	**1d**
2	**Pre-Construction**	**133 days**	**133 days**	**0d**	**Thu 9/25/25**	**Thu 9/25/25**	**0d**	**Mon 3/30/26**	**Mon 3/30/26**	**0d**
3	Contract Signed	1 day	1 day	0d	Thu 9/25/25	Thu 9/25/25	0d	Thu 9/25/25	Thu 9/25/25	0d
4	Building Permit	1 day	1 day	0d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/9/26	Fri 1/9/26	0d
5	Fire Tank Permit	1 day	1 day	0d	Mon 3/30/26	Mon 3/30/26	0d	Mon 3/30/26	Mon 3/30/26	0d
6	NTP - From PS	1 day	1 day	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 1/12/26	Mon 1/12/26	0d
7	Approval to go Vertical by AHJ	1 day	1 day	0d	Wed 3/25/26	Thu 3/26/26	-1d	Wed 3/25/26	Thu 3/26/26	-1d
8	**Procurament**	**44 days**	**67 days**	**-23d**	**Tue 3/31/26**	**Wed 3/11/26**	**14d**	**Mon 6/1/26**	**Fri 6/12/26**	**-9d**
9	Building Structure	2 days	2 days	0d	Tue 3/31/26	Wed 3/11/26	14d	Thu 4/2/26	Fri 3/13/26	14d
10	Hallway System	2 days	2 days	0d	Thu 5/28/26	Wed 6/10/26	-9d	Mon 6/1/26	Fri 6/12/26	-9d
11	Fire Tank Delivery	1 day	1 day	0d	Mon 5/25/26	Mon 5/25/26	0d	Mon 5/25/26	Mon 5/25/26	0d
12	**Site Work**	**116 days**	**102 days**	**14d**	**Mon 2/2/26**	**Mon 2/2/26**	**0d**	**Mon 7/13/26**	**Tue 6/23/26**	**14d**
13	**Earthwork**	**17 days**	**19 days**	**-2d**	**Mon 2/2/26**	**Mon 2/2/26**	**0d**	**Tue 2/24/26**	**Thu 2/26/26**	**-2d**
14	Erosion Control | BMPs	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	0d	Wed 2/4/26	Wed 2/4/26	0d
15	Demolition & Haul Off - For Bldg Pad	4 days	4 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Thu 2/12/26	Thu 2/12/26	0d
16	Grading | Cut & Fill	5 days	5 days	0d	Fri 2/13/26	Fri 2/13/26	0d	Thu 2/19/26	Thu 2/19/26	0d
17	Bulding Pad Preparation	3 days	5 days	-2d	Fri 2/20/26	Fri 2/20/26	0d	Tue 2/24/26	Thu 2/26/26	-2d
18	**Site Utilities**	**63 days**	**77 days**	**-14d**	**Thu 3/5/26**	**Fri 2/13/26**	**14d**	**Mon 6/1/26**	**Mon 6/1/26**	**0d**
19	Re-adjust existing storm		3 days			Fri 2/13/26			Tue 2/17/26	
20	Storm Sewer	4 days	5 days	-1d	Thu 3/5/26	Fri 2/27/26	4d	Tue 3/10/26	Thu 3/5/26	3d
21	Sanitary Sewer	4 days	6 days	-2d	Wed 3/11/26	Fri 3/6/26	3d	Mon 3/16/26	Fri 3/13/26	1d
22	Water Line	5 days	6 days	-1d	Tue 3/17/26	Mon 3/16/26	1d	Mon 3/23/26	Mon 3/23/26	0d
23	Utility Approval by AHJ	1 day	2 days	-1d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/24/26	Wed 3/25/26	-1d
24	**Fire Tank (By Others)**	**5 days**	**5 days**	**0d**	**Tue 5/26/26**	**Tue 5/26/26**	**0d**	**Mon 6/1/26**	**Mon 6/1/26**	**0d**
25	Fire Tank Installation	5 days	5 days	0d	Tue 5/26/26	Tue 5/26/26	0d	Mon 6/1/26	Mon 6/1/26	0d
26	**Exterior Improvements**	**93 days**	**66 days**	**27d**	**Thu 3/5/26**	**Tue 3/24/26**	**-13d**	**Mon 7/13/26**	**Tue 6/23/26**	**14d**
27	**Site Paving**	**12 days**	**22 days**	**-10d**	**Tue 3/24/26**	**Tue 3/24/26**	**0d**	**Wed 4/8/26**	**Wed 4/22/26**	**-10d**
28	Paving Subgrade Prep	6 days	8 days	-2d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/31/26	Thu 4/2/26	-2d
29	Fire Lane Concrete Paving	4 days	8 days	-4d	Wed 4/1/26	Fri 4/3/26	-2d	Mon 4/6/26	Tue 4/14/26	-6d
30	Light Duty Concrete Paving	2 days	6 days	-4d	Tue 4/7/26	Wed 4/15/26	-6d	Wed 4/8/26	Wed 4/22/26	-10d
31	**Detention Pond Work**	**14 days**	**9 days**	**5d**	**Thu 3/5/26**	**Fri 4/3/26**	**-21d**	**Tue 3/24/26**	**Wed 4/15/26**	**-16d**
32	Grading | Cut	10 days	5 days	5d	Thu 3/5/26	Fri 4/3/26	-21d	Wed 3/18/26	Thu 4/9/26	-16d
33	Storm Sewer	4 days	4 days	0d	Thu 3/19/26	Fri 4/10/26	-16d	Tue 3/24/26	Wed 4/15/26	-16d

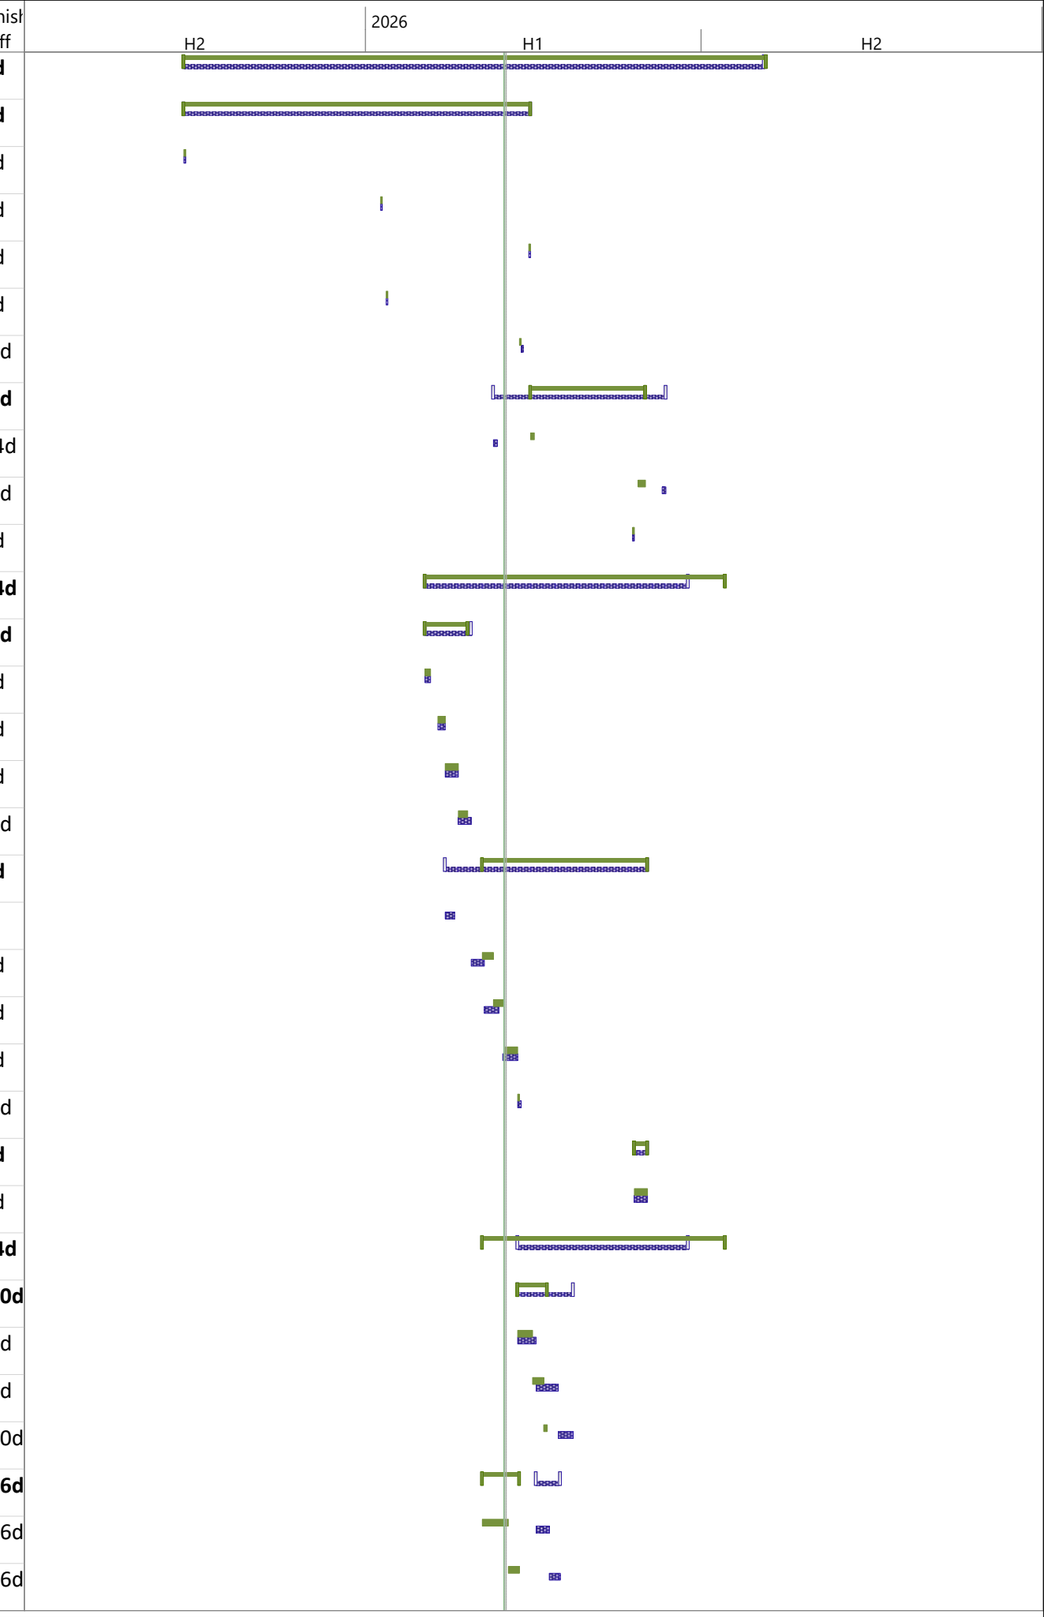

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
34	**Landscape & Irrigation**	**11 days**	**11 days**	**0d**	**Mon 6/22/26**	**Tue 6/2/26**	**14d**	**Mon 7/6/26**	**Tue 6/16/26**	**14d**
35	Irrigation Installation	6 days	6 days	0d	Mon 6/22/26	Tue 6/2/26	14d	Mon 6/29/26	Tue 6/9/26	14d
36	Landscape Installation	5 days	5 days	0d	Tue 6/30/26	Wed 6/10/26	14d	Mon 7/6/26	Tue 6/16/26	14d
37	**Gates & Fences**	**5 days**	**5 days**	**0d**	**Tue 7/7/26**	**Wed 6/17/26**	**14d**	**Mon 7/13/26**	**Tue 6/23/26**	**14d**
38	Chain Link Fence	3 days	3 days	0d	Tue 7/7/26	Wed 6/17/26	14d	Thu 7/9/26	Fri 6/19/26	14d
39	Double Swing Gate	2 days	2 days	0d	Fri 7/10/26	Mon 6/22/26	14d	Mon 7/13/26	Tue 6/23/26	14d
40	**Building Work**	**110 days**	**107 days**	**3d**	**Wed 2/25/26**	**Fri 2/27/26**	**-2d**	**Tue 7/28/26**	**Mon 7/27/26**	**1d**
41	**SOG | Foundation**	**6 days**	**12 days**	**-6d**	**Wed 2/25/26**	**Fri 2/27/26**	**-2d**	**Wed 3/4/26**	**Mon 3/16/26**	**-8d**
42	Form Board & Grade Beam Excavation	1 day	1 day	0d	Wed 2/25/26	Fri 2/27/26	-2d	Wed 2/25/26	Fri 2/27/26	-2d
43	Plumbing UG Rough-In		1 day			Mon 3/2/26			Mon 3/2/26	
44	Pest Control	1 day	1 day	0d	Thu 2/26/26	Tue 3/3/26	-3d	Thu 2/26/26	Tue 3/3/26	-3d
45	Set Up Poly & Rebar - Phase 1	2 days	3 days	-1d	Fri 2/27/26	Wed 3/4/26	-3d	Mon 3/2/26	Fri 3/6/26	-4d
46	Place and Finish Slab - Phase 1	1 day	1 day	0d	Tue 3/3/26	Mon 3/9/26	-4d	Tue 3/3/26	Mon 3/9/26	-4d
47	Undeground Plumbing Rough In	2 days	2 days	0d	Thu 2/26/26	Tue 3/10/26	-8d	Fri 2/27/26	Wed 3/11/26	-8d
48	Set Up Poly & Rebar - Phase 2	2 days	2 days	0d	Mon 3/2/26	Thu 3/12/26	-8d	Tue 3/3/26	Fri 3/13/26	-8d
49	Place and Finish Rebar - Phase 2	1 day	1 day	0d	Wed 3/4/26	Mon 3/16/26	-8d	Wed 3/4/26	Mon 3/16/26	-8d
50	**Steel Structure (Betco/Janus)**	**38 days**	**38 days**	**0d**	**Thu 4/9/26**	**Fri 3/20/26**	**14d**	**Mon 6/1/26**	**Tue 5/12/26**	**14d**
51	Framing & Interior Partitions	12 days	12 days	0d	Thu 4/9/26	Fri 3/20/26	14d	Fri 4/24/26	Mon 4/6/26	14d
52	Standing Seam Metal Roofing System	10 days	10 days	0d	Mon 4/27/26	Tue 4/7/26	14d	Fri 5/8/26	Mon 4/20/26	14d
53	Exterior Wall Assembly	10 days	10 days	0d	Mon 5/11/26	Tue 4/21/26	14d	Fri 5/22/26	Mon 5/4/26	14d
54	Gutter, Coping & Downpsouts	6 days	6 days	0d	Mon 5/25/26	Tue 5/5/26	14d	Mon 6/1/26	Tue 5/12/26	14d
55	**Masonry**	**4 days**	**4 days**	**0d**	**Mon 5/25/26**	**Tue 5/5/26**	**14d**	**Thu 5/28/26**	**Fri 5/8/26**	**14d**
56	Fire Pump Room	4 days	4 days	0d	Mon 5/25/26	Tue 5/5/26	14d	Thu 5/28/26	Fri 5/8/26	14d
57	**Fire Sprinkler System**	**30 days**	**29 days**	**1d**	**Mon 4/27/26**	**Tue 4/28/26**	**-1d**	**Fri 6/5/26**	**Fri 6/5/26**	**0d**
58	Sprinkler Installation	12 days	12 days	0d	Mon 4/27/26	Tue 4/28/26	-1d	Tue 5/12/26	Wed 5/13/26	-1d
59	Final Adjustment and Testing	4 days	4 days	0d	Tue 6/2/26	Tue 6/2/26	0d	Fri 6/5/26	Fri 6/5/26	0d
60	**Fire Alarm**	**19 days**	**19 days**	**0d**	**Wed 5/13/26**	**Thu 5/14/26**	**-1d**	**Mon 6/8/26**	**Tue 6/9/26**	**-1d**
61	Fire Alarm Installation	15 days	15 days	0d	Wed 5/13/26	Thu 5/14/26	-1d	Tue 6/2/26	Wed 6/3/26	-1d
62	Final Adjustment & Testing	4 days	4 days	0d	Wed 6/3/26	Thu 6/4/26	-1d	Mon 6/8/26	Tue 6/9/26	-1d
63	**ERCCS - TBD subject to AHJ Review**	**17 days**	**17 days**	**0d**	**Mon 7/6/26**	**Fri 7/3/26**	**1d**	**Tue 7/28/26**	**Mon 7/27/26**	**1d**
64	ERCCS Testing	2 days	2 days	0d	Mon 7/6/26	Fri 7/3/26	1d	Tue 7/7/26	Mon 7/6/26	1d
65	Submittal and Approval by AHJ	10 days	10 days	0d	Wed 7/8/26	Tue 7/7/26	1d	Tue 7/21/26	Mon 7/20/26	1d
66	ERCCS Installation	5 days	5 days	0d	Wed 7/22/26	Tue 7/21/26	1d	Tue 7/28/26	Mon 7/27/26	1d

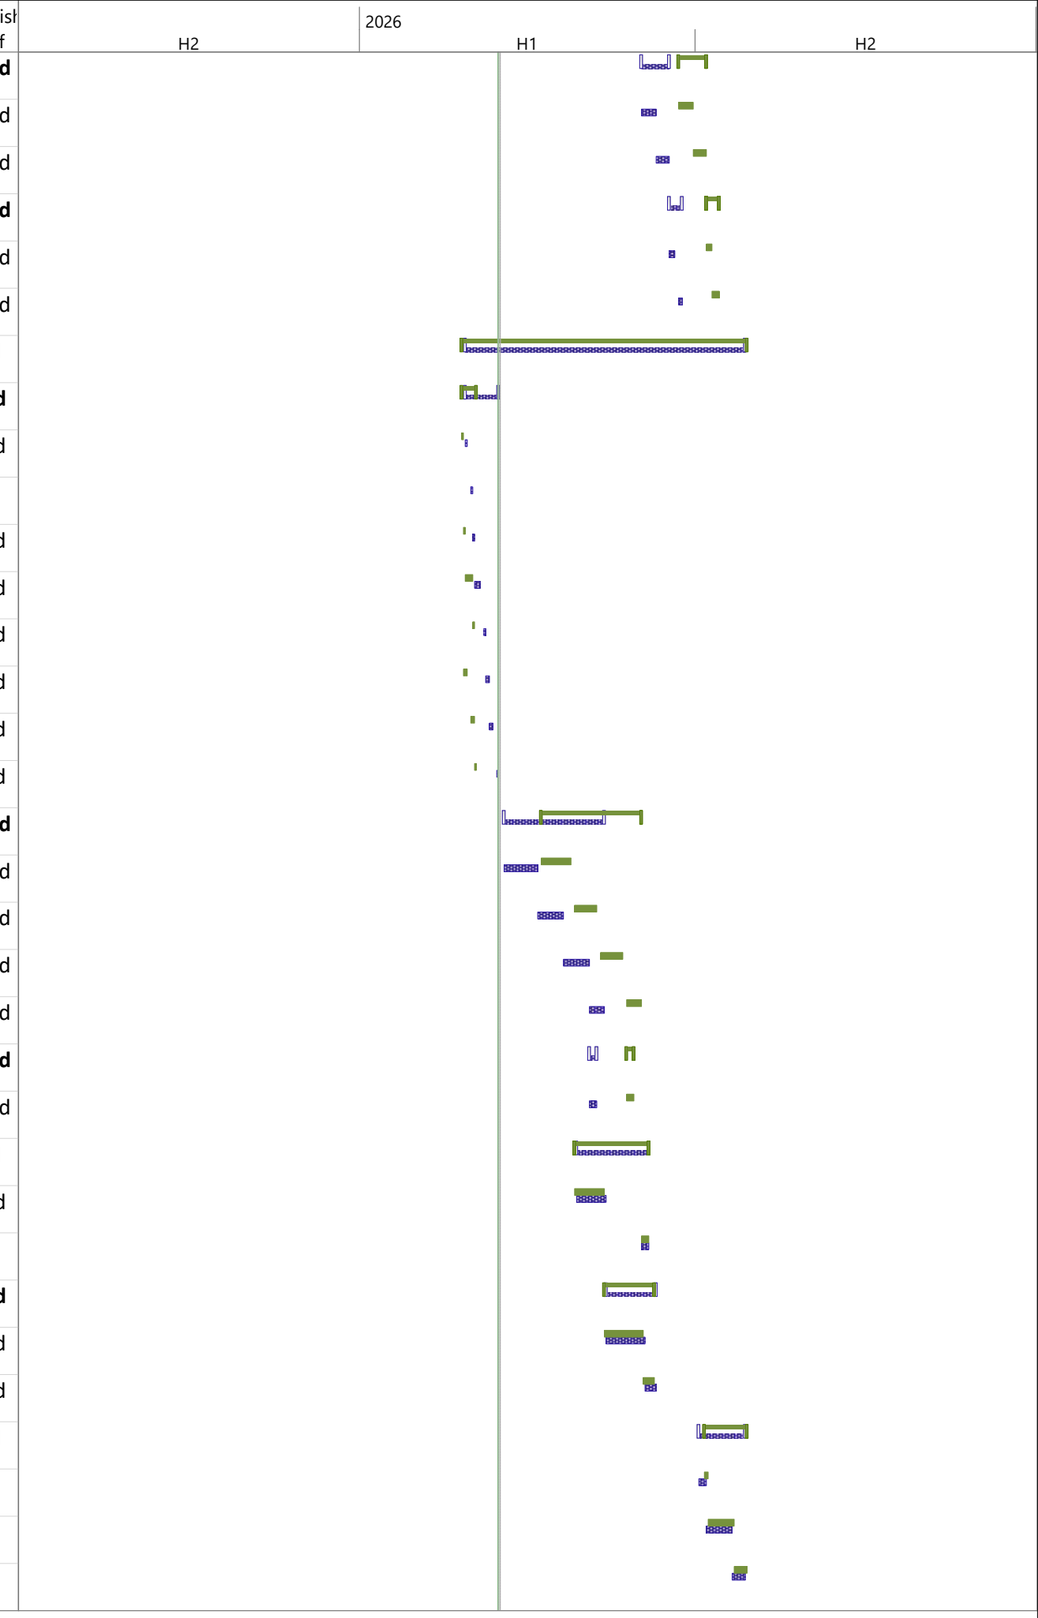
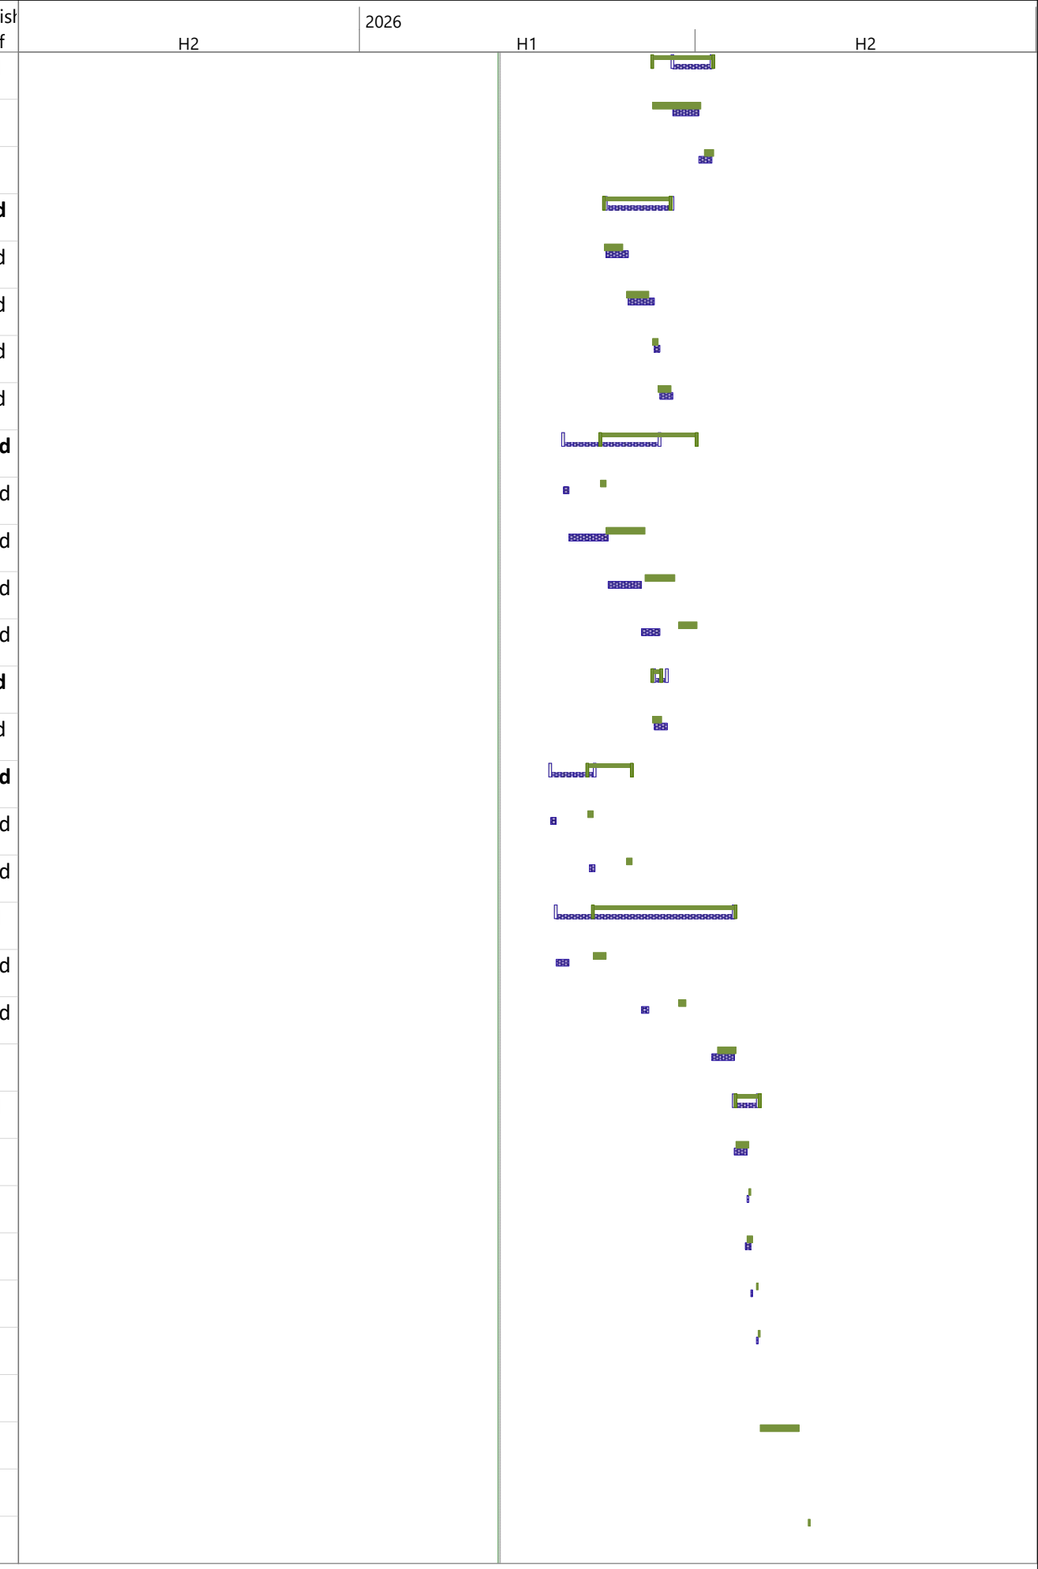
	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
67	**Hallway System (Betco/Janus)**	**25 days**	**15 days**	**10d**	**Mon 6/8/26**	**Fri 6/19/26**	**-9d**	**Fri 7/10/26**	**Thu 7/9/26**	**1d**
68	Hallway System & Roll Up Doors	20 days	10 days	10d	Mon 6/8/26	Fri 6/19/26	-9d	Fri 7/3/26	Thu 7/2/26	1d
69	Wire Mesh	5 days	5 days	0d	Mon 7/6/26	Fri 7/3/26	1d	Fri 7/10/26	Thu 7/9/26	1d
70	**Mechanical**	**26 days**	**26 days**	**0d**	**Wed 5/13/26**	**Thu 5/14/26**	**-1d**	**Wed 6/17/26**	**Thu 6/18/26**	**-1d**
71	Line Sets & Rough In	8 days	8 days	0d	Wed 5/13/26	Thu 5/14/26	-1d	Fri 5/22/26	Mon 5/25/26	-1d
72	AHUs & Duct Work	10 days	10 days	0d	Mon 5/25/26	Tue 5/26/26	-1d	Fri 6/5/26	Mon 6/8/26	-1d
73	Dehumidifiers	3 days	3 days	0d	Mon 6/8/26	Tue 6/9/26	-1d	Wed 6/10/26	Thu 6/11/26	-1d
74	Condensers & Final Connection	5 days	5 days	0d	Thu 6/11/26	Fri 6/12/26	-1d	Wed 6/17/26	Thu 6/18/26	-1d
75	**Electrical**	**38 days**	**38 days**	**0d**	**Mon 5/11/26**	**Tue 4/21/26**	**14d**	**Wed 7/1/26**	**Thu 6/11/26**	**14d**
76	Conduit, Wire	3 days	3 days	0d	Mon 5/11/26	Tue 4/21/26	14d	Wed 5/13/26	Thu 4/23/26	14d
77	Light Installation	15 days	15 days	0d	Thu 5/14/26	Fri 4/24/26	14d	Wed 6/3/26	Thu 5/14/26	14d
78	Gear & Riser Room Assembly	12 days	12 days	0d	Thu 6/4/26	Fri 5/15/26	14d	Fri 6/19/26	Mon 6/1/26	14d
79	Wall Packs	8 days	8 days	0d	Mon 6/22/26	Tue 6/2/26	14d	Wed 7/1/26	Thu 6/11/26	14d
80	**Plumbing**	**5 days**	**5 days**	**0d**	**Mon 6/8/26**	**Tue 6/9/26**	**-1d**	**Fri 6/12/26**	**Mon 6/15/26**	**-1d**
81	Condensate Drain & Vents	5 days	5 days	0d	Mon 6/8/26	Tue 6/9/26	-1d	Fri 6/12/26	Mon 6/15/26	-1d
82	**Openings (Betco/Janus)**	**18 days**	**18 days**	**0d**	**Mon 5/4/26**	**Tue 4/14/26**	**14d**	**Wed 5/27/26**	**Thu 5/7/26**	**14d**
83	HM Frames	3 days	3 days	0d	Mon 5/4/26	Tue 4/14/26	14d	Wed 5/6/26	Thu 4/16/26	14d
84	HM Doors & Hardware	3 days	3 days	0d	Mon 5/25/26	Tue 5/5/26	14d	Wed 5/27/26	Thu 5/7/26	14d
85	**Finish-Out**	**55 days**	**68 days**	**-13d**	**Thu 5/7/26**	**Fri 4/17/26**	**14d**	**Wed 7/22/26**	**Tue 7/21/26**	**1d**
86	Light Gauge Framing | Electrical, Riser	5 days	5 days	0d	Thu 5/7/26	Fri 4/17/26	14d	Wed 5/13/26	Thu 4/23/26	14d
87	Drywall Assembly	4 days	4 days	0d	Mon 6/22/26	Tue 6/2/26	14d	Thu 6/25/26	Fri 6/5/26	14d
88	Seal Concrete in Corridors	8 days	8 days	0d	Mon 7/13/26	Fri 7/10/26	1d	Wed 7/22/26	Tue 7/21/26	1d
89	**Post-Construction**	**9 days**	**9 days**	**0d**	**Thu 7/23/26**	**Wed 7/22/26**	**1d**	**Tue 8/4/26**	**Mon 8/3/26**	**1d**
90	Final Clean-Up	5 days	5 days	0d	Thu 7/23/26	Wed 7/22/26	1d	Wed 7/29/26	Tue 7/28/26	1d
91	Punch List - TBD - Proposed Date	1 day	1 day	0d	Thu 7/30/26	Wed 7/29/26	1d	Thu 7/30/26	Wed 7/29/26	1d
92	Final Inspections	3 days	3 days	0d	Wed 7/29/26	Tue 7/28/26	1d	Fri 7/31/26	Thu 7/30/26	1d
93	CO/TCO	1 day	1 day	0d	Mon 8/3/26	Fri 7/31/26	1d	Mon 8/3/26	Fri 7/31/26	1d
94	Substantial Completion	1 day	1 day	0d	Tue 8/4/26	Mon 8/3/26	1d	Tue 8/4/26	Mon 8/3/26	1d
95										
96	15 Weather Days in Contract	15 days			Wed 8/5/26			Tue 8/25/26		
97										
98	Contracted Finish Date 08.31	1 day			Mon 8/31/26			Mon 8/31/26
