Executive Landing Page

Public Storage Dashboard

Data Date: 1/16/2026

Type	Project	Region	Responsible
Construction	Aventura, FL	East Coast	Tracy Girard

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
5/21/2026	5/21/2026	0 Baseline (Blank) Previous	(Blank)

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	3/21/2025		3/21/2025	0		Mobilization	On Track – Gaining
Foundation Complete	6/10/2025		6/10/2025	0		Prep & Pour 2	On Track – Gaining
Structure Top Out	10/14/2025		10/14/2025	0		Pour 4Th, 5Th Floor Slab And Roof Deck	On Track – Gaining
Weather Tight	2/4/2026		2/4/2026	0		Install Roofing	On Track – Gaining
Conditioned Air	2/19/2026		2/19/2026	0		Mep Hookup Hvac Units	On Track – Gaining
Finishes Complete	2/23/2026		2/23/2026	0		Install Doors & Hardware	On Track – Gaining
Permanent Power	3/25/2026		3/25/2026	0		Install Electric Meter	On Track – Gaining
Elevator Complete	4/29/2026		4/29/2026	0		Install Elevators	On Track – Gaining
Contract Completion	5/21/2026		5/21/2026	0		Obtain Certificate Of Completion	On Track – Gaining
Hardscape/Landscape Complete	5/22/2026		5/22/2026	0		Jet Vac	On Track – Gaining

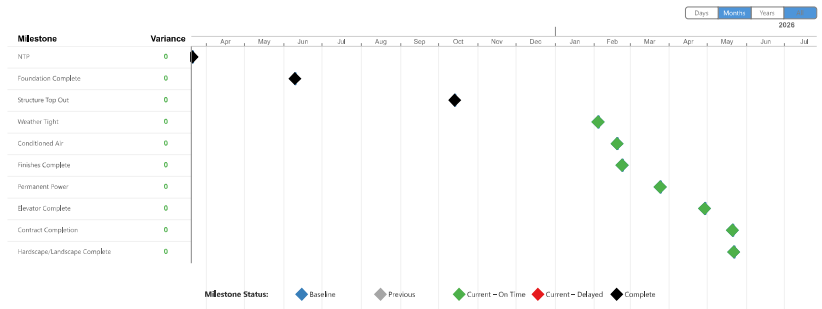

Baseline Variance

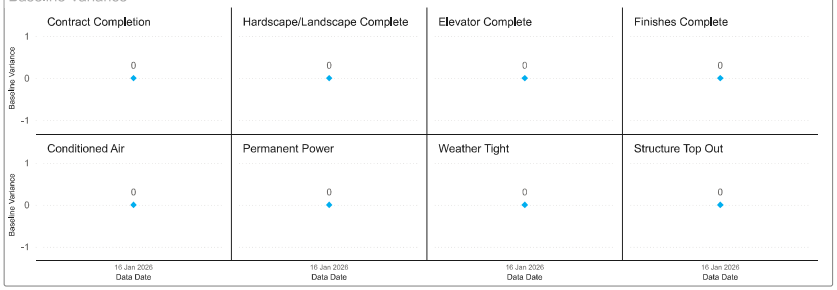

Schedule Performance Summary

Insufficient Schedule Data: Comparative analysis requires more schedules to produce figures

Powered By STELIC INSIGHT+ACTION=IMPACT
