RYCON Construction Inc.

Construction Schedule

Public Storage - Delray Beach, FL
Thu 2/12/26

Public Storage

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Comp.	Actual Start	Actual Finish
1	**Overall Project Duration - Public Storage - Delray Beach**	**414 days**	**Fri 11/29/24**	**Fri 7/3/26**	**Fri 11/29/24**	**Wed 7/1/26**	**69%**	**Fri 11/29/24**	**NA**
2	Contract Award	35 days	Fri 11/29/24	Thu 1/16/25	Fri 11/29/24	Thu 1/16/25	100%	Fri 11/29/24	Thu 1/16/25
3	Release Subcontractors	10 days	Fri 1/17/25	Thu 1/30/25	Fri 4/11/25	Thu 4/24/25	100%	Fri 4/11/25	Thu 4/24/25
4	**Obtain Vertical Building Pemit By Owner**	**1 day**	**Mon 4/28/25**	**Mon 4/28/25**	**Mon 4/28/25**	**Mon 4/28/25**	**100%**	Mon 4/28/25	Mon 4/28/25
5	**Obtain Water & Sewer Permit**	**1 day**	**Tue 5/6/25**	**Tue 5/6/25**	**Tue 5/6/25**	**Tue 5/6/25**	**100%**	Tue 5/6/25	Tue 5/6/25
6	**DELAY - Gopher Tortoise Relocation Permit - FWC**	**16 days**	**Fri 5/9/25**	**Fri 5/30/25**	**Fri 5/9/25**	**Fri 5/30/25**	**100%**	**Fri 5/9/25**	**Fri 5/30/25**
7	**DELAY - Gopher Tortoise Relocation**	**1 day**	**Thu 6/12/25**	**Thu 6/12/25**	**Thu 6/12/25**	**Thu 6/12/25**	**100%**	**Thu 6/12/25**	**Thu 6/12/25**
8	**City Precontruction Meeting**	**0 days**	**Tue 7/1/25**	**Tue 7/1/25**	**Mon 7/21/25**	**Mon 7/21/25**	**100%**	Mon 7/21/25	Mon 7/21/25
9	**SUBMITTALS**	**352 days**	**Fri 12/6/24**	**Thu 9/4/25**	**Fri 12/6/24**	**Mon 4/13/26**	**88%**	**Fri 12/6/24**	**NA**
10	**Site Submittals**	**125 days**	**Fri 1/24/25**	**Tue 7/1/25**	**Fri 1/24/25**	**Thu 7/17/25**	**100%**	**Fri 1/24/25**	**Thu 7/17/25**
11	Storm Drainage& Sewer System Submittals	5.4 wks	Fri 1/24/25	Mon 3/3/25	Fri 1/24/25	Mon 3/3/25	100%	Fri 1/24/25	Mon 3/3/25
12	Approval / EOR	40 days	Tue 3/4/25	Mon 4/28/25	Tue 3/4/25	Mon 4/28/25	100%	Tue 3/4/25	Mon 4/28/25
13	Revised Submittals	5 days	Tue 4/29/25	Mon 5/5/25	Tue 4/29/25	Mon 5/5/25	100%	Tue 4/29/25	Mon 5/5/25
14	Approval / EOR	8 days	Tue 5/6/25	Thu 5/15/25	Tue 5/6/25	Thu 5/15/25	100%	Tue 5/6/25	Thu 5/15/25
15	Fabricate and Deliver Structures	7.5 wks	Tue 5/27/25	Tue 7/1/25	Tue 5/27/25	Thu 7/17/25	100%	Tue 5/27/25	Thu 7/17/25
16	**Fire Sprinkler Shop Drawings**	**84 days**	**Fri 1/31/25**	**Wed 7/9/25**	**Fri 4/25/25**	**Wed 8/20/25**	**100%**	**Fri 4/25/25**	**Wed 8/20/25**
17	Request& Receive CAD Files	55 days	Fri 1/31/25	Tue 2/4/25	Fri 4/25/25	Thu 7/10/25	100%	Fri 4/25/25	Thu 7/10/25
18	Shop Drawing Submittal	12 days	Wed 2/5/25	Tue 2/25/25	Fri 7/11/25	Mon 7/28/25	100%	Fri 7/11/25	Mon 7/28/25
19	Approval / AOR	17 days	Wed 2/26/25	Tue 3/11/25	Tue 7/29/25	Wed 8/20/25	100%	Tue 7/29/25	Wed 8/20/25
20	City Submission& Approval Estimated	0 days	Tue 5/6/25	Mon 6/23/25	Mon 8/4/25	Mon 8/4/25	100%	Mon 8/4/25	Mon 8/4/25
21	Fire Sprinkler Permit	10 days	Thu 6/26/25	Wed 7/9/25	Wed 8/6/25	Tue 8/19/25	100%	Wed 8/6/25	Tue 8/19/25
22	**Structural Steel Shop Drawings**	**150 days**	**Fri 12/6/24**	**Thu 7/3/25**	**Fri 12/6/24**	**Thu 7/3/25**	**100%**	**Fri 12/6/24**	**Thu 7/3/25**
23	Release Structural Steel Pkg	88 days	Fri 12/6/24	Tue 4/8/25	Fri 12/6/24	Tue 4/8/25	100%	Fri 12/6/24	Tue 4/8/25
24	Structural Steel Shop Drawings Submittal	0 days	Fri 3/7/25	Fri 3/7/25	Fri 3/7/25	Fri 3/7/25	100%	Fri 3/7/25	Fri 3/7/25
25	Approval / AOR	49 days	Mon 3/10/25	Thu 5/15/25	Mon 3/10/25	Thu 5/15/25	100%	Mon 3/10/25	Thu 5/15/25
26	Fabricate Steel Pkg	6 wks	Fri 5/23/25	Thu 7/3/25	Fri 5/23/25	Thu 7/3/25	100%	Fri 5/23/25	Thu 7/3/25
27	**Cold Formed Framing**	**140 days**	**Fri 1/31/25**	**Thu 7/3/25**	**Fri 1/31/25**	**Thu 8/14/25**	**100%**	**Fri 1/31/25**	**Thu 8/14/25**
28	Release CFS Package	48 days	Fri 1/31/25	Tue 4/8/25	Fri 1/31/25	Tue 4/8/25	100%	Fri 1/31/25	Tue 4/8/25
29	Shop Drawings	0 days	Mon 4/7/25	Mon 4/7/25	Mon 4/7/25	Mon 4/7/25	100%	Mon 4/7/25	Mon 4/7/25
30	Approval / AOR	28 days	Tue 4/8/25	Thu 5/15/25	Tue 4/8/25	Thu 5/15/25	100%	Tue 4/8/25	Thu 5/15/25
31	Revised Submittals	4 days	Fri 5/16/25	Wed 5/21/25	Fri 5/16/25	Wed 5/21/25	100%	Fri 5/16/25	Wed 5/21/25
32	Approval / AOR	16 days	Mon 5/19/25	Mon 6/9/25	Mon 5/19/25	Mon 6/9/25	100%	Mon 5/19/25	Mon 6/9/25
33	Material Delivery	7 wks	Fri 5/16/25	Thu 7/3/25	Fri 6/27/25	Thu 8/14/25	100%	Fri 6/27/25	Thu 8/14/25
34	**Concrete / Masonry Submittals**	**138 days**	**Fri 1/31/25**	**Fri 6/27/25**	**Fri 1/31/25**	**Tue 8/12/25**	**100%**	**Fri 1/31/25**	**Tue 8/12/25**
35	Footing Rebar Submittal	23 days	Fri 1/31/25	Tue 3/4/25	Fri 1/31/25	Tue 3/4/25	100%	Fri 1/31/25	Tue 3/4/25
36	Approval AOR	53 days	Wed 3/5/25	Fri 5/16/25	Wed 3/5/25	Fri 5/16/25	100%	Wed 3/5/25	Fri 5/16/25
37	Concrete mix Submittals	68 days	Fri 1/31/25	Thu 2/13/25	Fri 4/25/25	Tue 7/29/25	100%	Fri 4/25/25	Tue 7/29/25
38	Approval AOR	10 days	Fri 2/14/25	Thu 2/27/25	Wed 7/30/25	Tue 8/12/25	100%	Wed 7/30/25	Tue 8/12/25
39	CMU Submittals	81 days	Fri 1/31/25	Fri 5/23/25	Fri 1/31/25	Fri 5/23/25	100%	Fri 1/31/25	Fri 5/23/25
40	Approval AOR	11 days	Mon 5/26/25	Mon 6/9/25	Mon 5/26/25	Mon 6/9/25	100%	Mon 5/26/25	Mon 6/9/25
41	Release Rebar	15 days	Mon 6/9/25	Fri 6/27/25	Mon 6/9/25	Fri 6/27/25	100%	Mon 6/9/25	Fri 6/27/25
42	**Roofing**	**85 days**	**Fri 1/17/25**	**Mon 5/12/25**	**Fri 10/31/25**	**Thu 2/26/26**	**68%**	**Fri 10/31/25**	**NA**
43	Roofing Submittal	30 days	Fri 1/17/25	Mon 3/3/25	Fri 10/31/25	Thu 12/11/25	100%	Fri 10/31/25	Thu 12/11/25
44	Approval / AOR	35 days	Tue 3/4/25	Mon 3/17/25	Fri 12/12/25	Thu 1/29/26	90%	Fri 12/12/25	NA
45	Release Roofing Material Production	5 days	Fri 1/17/25	Fri 1/17/25	Fri 1/30/26	Thu 2/5/26	0%	NA	NA
46	Fabricate & Deliver Roofing Material	4 wks	Tue 3/18/25	Mon 5/12/25	Fri 1/30/26	Thu 2/26/26	0%	NA	NA
47	**Storefront & Window Shop drawings**	**156 days**	**Fri 1/31/25**	**Tue 5/27/25**	**Mon 9/8/25**	**Mon 4/13/26**	**52%**	**Mon 9/8/25**	**NA**
48	Storefront& Window Submittal	18 days	Fri 1/31/25	Tue 2/11/25	Mon 9/8/25	Wed 10/1/25	100%	Mon 9/8/25	Wed 10/1/25
49	Approval / AOR	32 days	Wed 2/12/25	Tue 2/25/25	Wed 10/1/25	Thu 11/13/25	100%	Wed 10/1/25	Thu 11/13/25

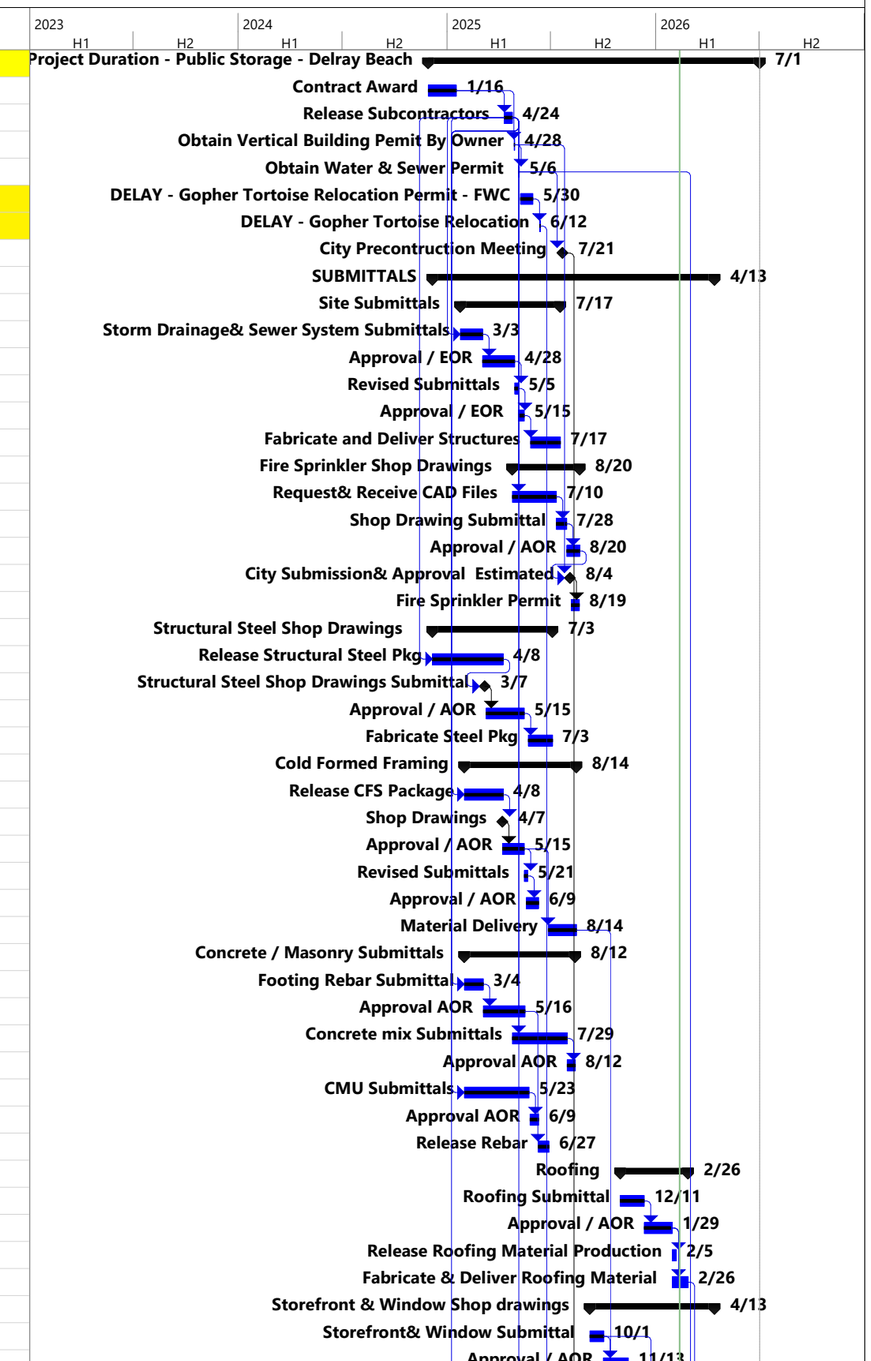

RYCON Construction Inc.

Construction Schedule

Public Storage - Delray Beach, FL

Thu 2/12/26

Public Storage

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Comp.	Actual Start	Actual Finish
50	Glazing Samples	9 days	NA	NA	Wed 12/24/25	Mon 1/5/26	100%	Wed 12/24/25	Mon 1/5/26
51	Approval / AOR	15 days	NA	NA	Tue 1/6/26	Mon 1/26/26	50%	Tue 1/6/26	NA
52	City Submission& Approval	15 days	Wed 2/26/25	Tue 3/25/25	Tue 1/27/26	Mon 2/16/26	0%	NA	NA
53	Fabricate and Deliver	40 days	Wed 3/26/25	Tue 5/27/25	Tue 2/17/26	Mon 4/13/26	0%	NA	NA
54	**HVAC Submittals**	**163 days**	**Fri 1/31/25**	**Thu 8/28/25**	**Tue 7/22/25**	**Thu 3/5/26**	**82%**	**Tue 7/22/25**	**NA**
55	Equipment, Air Distribution Submittals	10 days	Fri 1/31/25	Thu 2/20/25	Tue 7/22/25	Mon 8/4/25	100%	Tue 7/22/25	Mon 8/4/25
56	Approval / AOR & EOR	14 days	Fri 2/21/25	Thu 3/6/25	Mon 8/4/25	Thu 8/21/25	100%	Mon 8/4/25	Thu 8/21/25
57	Revised VRV Package - Rev 5	8 days	NA	NA	Fri 8/22/25	Tue 9/2/25	100%	Fri 8/22/25	Tue 9/2/25
58	Approval / AOR & EOR	10 days	NA	NA	Wed 9/3/25	Tue 9/16/25	100%	Wed 9/3/25	Tue 9/16/25
59	Additional Submittals Equipment Requested by EOR	55 days	NA	NA	Wed 9/17/25	Tue 12/2/25	100%	Wed 9/17/25	Tue 12/2/25
60	Approval / AOR & EOR	26 days	NA	NA	Wed 12/3/25	Wed 1/7/26	100%	Wed 12/3/25	Wed 1/7/26
61	3rd Revised Package Submitted - (Daikin Response)	1 day	NA	NA	Thu 1/8/26	Thu 1/8/26	100%	Thu 1/8/26	Thu 1/8/26
62	Approval AOR / EOR	10 days	NA	NA	Fri 1/9/26	Thu 1/22/26	100%	Fri 1/9/26	Thu 1/22/26
63	Fabricate and Delivery	6 wks	Fri 3/7/25	Thu 8/28/25	Fri 1/23/26	Thu 3/5/26	0%	NA	NA
64	**Electrical Submittals**	**197 days**	**Fri 1/31/25**	**Thu 9/4/25**	**Fri 4/25/25**	**Mon 1/26/26**	**92%**	**Fri 4/25/25**	**NA**
65	Gear and Lighting Submittals	20 days	Fri 1/31/25	Thu 2/27/25	Fri 4/25/25	Thu 5/22/25	100%	Fri 4/25/25	Thu 5/22/25
66	Approval / EOR	10 days	Fri 2/28/25	Thu 3/13/25	Tue 8/19/25	Mon 9/1/25	100%	Tue 8/19/25	Mon 9/1/25
67	Fabricate and Delivery	21 wks	Fri 3/14/25	Thu 9/4/25	Tue 9/2/25	Mon 1/26/26	90%	Tue 9/2/25	NA
68	**Elevator Submittals**	**300 days**	**Fri 1/31/25**	**Fri 8/8/25**	**Fri 1/31/25**	**Thu 3/26/26**	**78%**	**Fri 1/31/25**	**NA**
69	Submittals	13 days	Fri 1/31/25	Tue 2/18/25	Fri 1/31/25	Tue 2/18/25	100%	Fri 1/31/25	Tue 2/18/25
70	Approval / EOR	23 days	Wed 2/19/25	Fri 3/21/25	Wed 2/19/25	Fri 3/21/25	100%	Wed 2/19/25	Fri 3/21/25
71	Revised Submittals	77 days	Fri 1/31/25	Mon 5/19/25	Fri 1/31/25	Mon 5/19/25	100%	Fri 1/31/25	Mon 5/19/25
72	Approval / EOR	38 days	Tue 5/20/25	Mon 6/2/25	Tue 5/20/25	Thu 7/10/25	100%	Tue 5/20/25	Thu 7/10/25
73	Release Material form Sent to Schindler	1 day	NA	NA	Fri 11/21/25	Fri 11/21/25	100%	Fri 11/21/25	Fri 11/21/25
74	Fabricate and Delivery (Estimated)	18 wks	Mon 3/24/25	Fri 8/8/25	Fri 11/21/25	Thu 3/26/26	40%	Fri 11/21/25	NA
75	**Construction**	**268 days**	**Tue 6/24/25**	**Fri 7/3/26**	**Mon 6/23/25**	**Wed 7/1/26**	**42%**	**Mon 6/23/25**	**NA**
76	**Overall Site Construction**	**241 days**	**Tue 6/24/25**	**Mon 5/11/26**	**Mon 6/23/25**	**Mon 5/25/26**	**48%**	**Mon 6/23/25**	**NA**
77	Site Mobilization	4 days	Tue 6/24/25	Mon 7/7/25	Mon 6/23/25	Fri 6/27/25	100%	Mon 6/23/25	Fri 6/27/25
78	**Sitework**	**20 days**	**Tue 6/24/25**	**Mon 8/11/25**	**Mon 6/23/25**	**Fri 7/18/25**	**100%**	**Mon 6/23/25**	**Fri 7/18/25**
79	Build Construction Entrances	1 day	Tue 6/24/25	Wed 6/25/25	Mon 6/23/25	Mon 6/23/25	100%	Mon 6/23/25	Mon 6/23/25
80	Clear & Grub	7 days	Thu 6/26/25	Wed 7/9/25	Fri 6/27/25	Mon 7/7/25	100%	Fri 6/27/25	Mon 7/7/25
81	Erosion Control	1.3 days	NA	NA	Wed 7/2/25	Thu 7/3/25	100%	Wed 7/2/25	Thu 7/3/25
82	Site Survey& Layout (verify building pad)	3 days	Thu 7/10/25	Mon 7/14/25	Tue 7/8/25	Thu 7/10/25	100%	Tue 7/8/25	Thu 7/10/25
83	Construct Building Pad - Obtain Pad Certificate	6 days	Tue 7/15/25	Mon 7/28/25	Thu 7/10/25	Fri 7/18/25	100%	Thu 7/10/25	Fri 7/18/25
84	**Storm Drainage**	**148 days**	**Tue 10/7/25**	**Tue 11/11/25**	**Mon 7/28/25**	**Wed 2/18/26**	**89%**	**Mon 7/28/25**	**NA**
85	**PENDING RFI #08 - DRAINAGE CONFLICT**	**10 days**	**NA**	**NA**	**Wed 8/20/25**	**Tue 9/2/25**	**100%**	**Wed 8/20/25**	**Tue 9/2/25**
86	**Drainage Revision #01 (Estimated)**	**16 days**	**NA**	**NA**	**Wed 9/3/25**	**Wed 9/24/25**	**100%**	**Wed 9/3/25**	**Wed 9/24/25**
87	**Drainage Revision #02 (Pricing Approval)**	**32 days**	**NA**	**NA**	**Fri 10/17/25**	**Mon 12/1/25**	**100%**	**Fri 10/17/25**	**Mon 12/1/25**
88	**Drainage Revision #02 - County Approval**	**15 days**	**NA**	**NA**	**Thu 1/15/26**	**Wed 2/4/26**	**65%**	**Thu 1/15/26**	**NA**
89	Install Storm Structures	4 wks	Tue 10/7/25	Mon 10/27/25	Mon 7/28/25	Wed 2/18/26	85%	Mon 7/28/25	NA
90	Install storm pipe and exfiltration trenches	3 wks	Tue 10/21/25	Mon 11/10/25	Tue 7/29/25	Mon 2/9/26	85%	Tue 7/29/25	NA
91	Inspection	1 day	Tue 11/11/25	Tue 11/11/25	Mon 2/9/26	Tue 2/10/26	0%	NA	NA
92	**Sewer System**	**24 days**	**Tue 11/11/25**	**Mon 12/15/25**	**Mon 8/11/25**	**Thu 9/11/25**	**100%**	**Mon 8/11/25**	**Thu 9/11/25**
93	Tie into Existing Stub as required	1 day	Tue 11/11/25	Mon 11/17/25	Mon 8/11/25	Wed 8/13/25	100%	Mon 8/11/25	Wed 8/13/25
94	Install Sanitary Piping	21 days	Tue 11/18/25	Mon 12/15/25	Mon 8/11/25	Thu 9/11/25	100%	Mon 8/11/25	Thu 9/11/25
95	**Domestic Water Service**	**143 days**	**Tue 12/16/25**	**Mon 1/26/26**	**Tue 8/19/25**	**Thu 3/5/26**	**80%**	**Tue 8/19/25**	**NA**
96	Water Main installation	4 wks	Tue 12/16/25	Mon 12/29/25	Tue 8/19/25	Wed 10/8/25	100%	Tue 8/19/25	Wed 10/8/25
97	Tie-in to Existing Water Main	2 days	Fri 1/23/26	Mon 1/26/26	Thu 10/9/25	Fri 10/10/25	100%	Thu 10/9/25	Fri 10/10/25
98	**PBCWUD - Preliminary AB Review & Approval**	**16 days**	**NA**	**NA**	**Thu 10/16/25**	**Thu 11/6/25**	**100%**	**Thu 10/16/25**	**Thu 11/6/25**

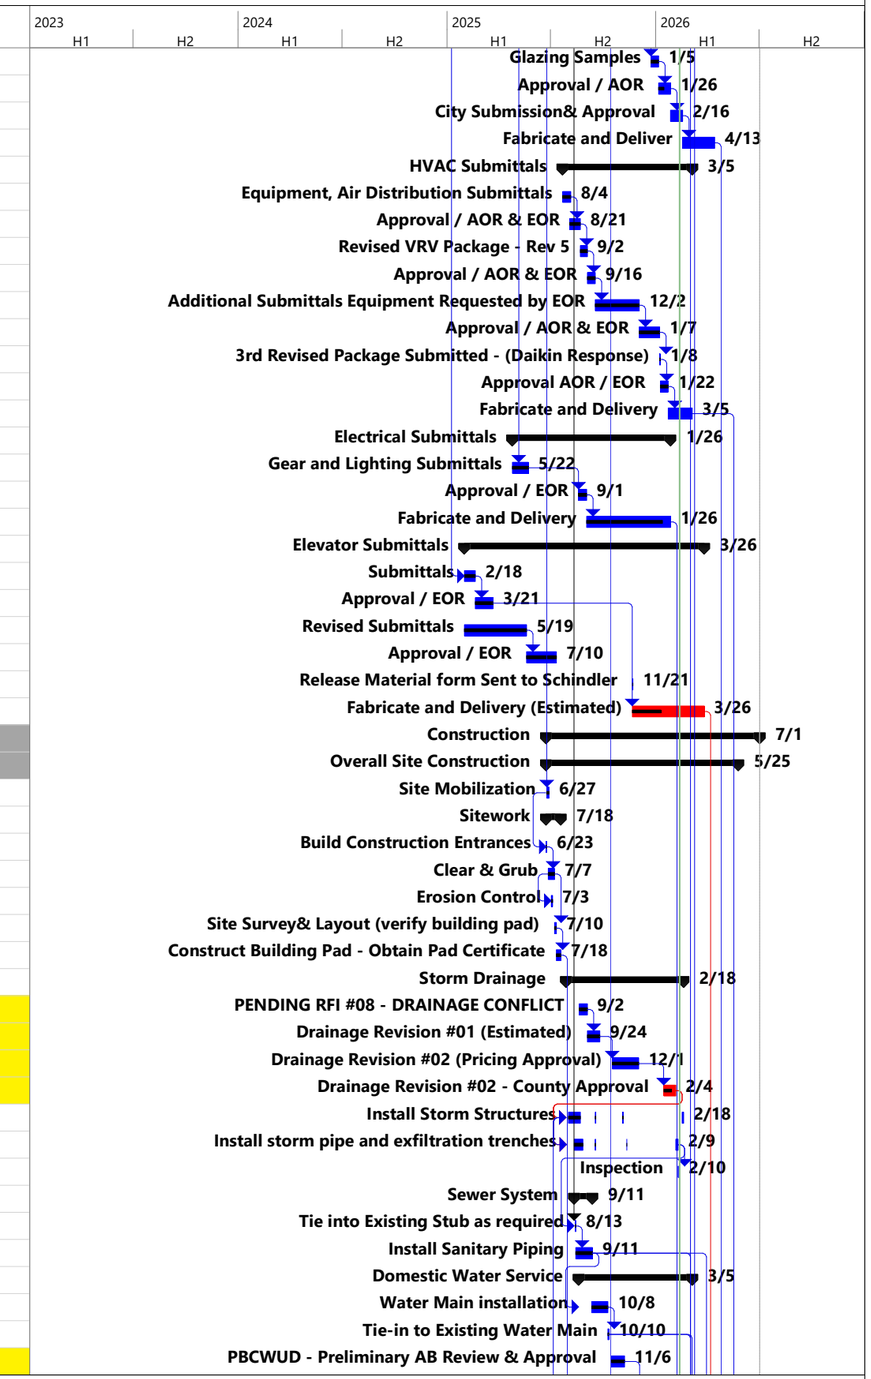

Construction Schedule

Public Storage - Delray Beach, FL

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Comp.	Actual Start	Actual Finish
99	PBCWUD - S/S AB Hard Copy Submitted Review & Approval	23 days	NA	NA	Thu 12/4/25	Mon 1/5/26	100%	Thu 12/4/25	Mon 1/5/26
100	PBCWUD - Revised AB (New comments provided)	20 days	NA	NA	Tue 1/6/26	Mon 2/2/26	70%	Tue 1/6/26	NA
101	Building Water Services	10 days	Tue 12/30/25	Mon 1/5/26	Tue 2/3/26	Mon 2/16/26	0%	NA	NA
102	Fire Line Underground w/ DDCV& FDC	3 days	Tue 1/20/26	Thu 1/22/26	Tue 3/3/26	Thu 3/5/26	0%	NA	NA
103	**Hardscape& Misc. Site Work**	**60 days**	**Tue 2/17/26**	**Mon 5/11/26**	**Tue 3/3/26**	**Mon 5/25/26**	**0%**	**NA**	**NA**
104	Fill balance of Site	15 days	Tue 2/17/26	Mon 3/9/26	Tue 3/3/26	Mon 3/23/26	0%	NA	NA
105	Primary Electrical Conduit	5 days	Tue 2/17/26	Mon 2/23/26	Tue 3/3/26	Mon 3/9/26	0%	NA	NA
106	Site Lighting, brooks boxes,& Fixture Installation	5 days	Tue 2/24/26	Mon 3/2/26	Tue 3/10/26	Mon 3/16/26	0%	NA	NA
107	Irrigation and ancillary conduit sleeves	5 days	Tue 2/24/26	Mon 3/2/26	Tue 3/10/26	Mon 3/16/26	0%	NA	NA
108	Sub-base	10 days	Tue 2/24/26	Mon 3/9/26	Tue 3/10/26	Mon 3/23/26	0%	NA	NA
109	Base	10 days	Tue 3/10/26	Mon 3/23/26	Tue 3/24/26	Mon 4/6/26	0%	NA	NA
110	Asphalt (first lift)	8 days	Thu 3/19/26	Mon 3/30/26	Thu 4/2/26	Mon 4/13/26	0%	NA	NA
111	Concrete Curbs	8 days	Tue 3/24/26	Thu 4/2/26	Tue 4/7/26	Thu 4/16/26	0%	NA	NA
112	Install Water Meter Boxes	5 days	Fri 3/27/26	Thu 4/2/26	Fri 4/10/26	Thu 4/16/26	0%	NA	NA
113	Sidewalks& Retaining Wall	20 days	Tue 3/31/26	Mon 4/27/26	Tue 4/14/26	Mon 5/11/26	0%	NA	NA
114	Landscape& Irrigation Installation	15 days	Fri 4/3/26	Thu 4/23/26	Fri 4/17/26	Thu 5/7/26	0%	NA	NA
115	Final Lift Asphalt	15 days	Fri 4/17/26	Thu 5/7/26	Fri 5/1/26	Thu 5/21/26	0%	NA	NA
116	Pavement Marking& Striping	5 days	Tue 5/5/26	Mon 5/11/26	Tue 5/19/26	Mon 5/25/26	0%	NA	NA
117	Jet Vac System	3 days	Thu 5/7/26	Mon 5/11/26	Thu 5/21/26	Mon 5/25/26	0%	NA	NA
118	CONVEYANCE PROCESS	54 days	Mon 12/29/25	Mon 4/27/26	Fri 3/6/26	Wed 5/20/26	0%	NA	NA
119	Water (Flush & Pressure Testing)	4 days	Tue 1/27/26	Fri 1/30/26	Fri 3/6/26	Wed 3/11/26	0%	NA	NA
120	Water Asbuilts (Partitial for HRS)	0 days	Tue 2/3/26	Tue 2/3/26	Fri 3/13/26	Fri 3/13/26	0%	NA	NA
121	Testing (Bacti Samples / Density Tests)	5 days	Mon 2/9/26	Fri 2/13/26	Thu 3/19/26	Wed 3/25/26	0%	NA	NA
122	Sewer Asbuilts	0 days	Mon 12/29/25	Mon 12/29/25	Fri 3/13/26	Fri 3/13/26	0%	NA	NA
123	Release of Lien	0 days	Fri 2/20/26	Fri 2/20/26	Wed 4/1/26	Wed 4/1/26	0%	NA	NA
124	HRS Certification (Submission)	6 wks	Mon 2/23/26	Fri 4/3/26	Thu 4/2/26	Wed 5/13/26	0%	NA	NA
125	Sewer (Leakage & Lamping)	3 days	Tue 3/17/26	Thu 3/19/26	Tue 3/31/26	Thu 4/2/26	0%	NA	NA
126	DERM Certification (Submission)	6 wks	Tue 3/17/26	Mon 4/27/26	Thu 4/2/26	Wed 5/13/26	0%	NA	NA
127	Water Meter Installation	5 days	Mon 4/6/26	Fri 4/10/26	Thu 5/14/26	Wed 5/20/26	0%	NA	NA
128	Final Asbuilts	1 day	Fri 4/17/26	Fri 4/17/26	Fri 5/1/26	Fri 5/1/26	0%	NA	NA
129	**Shell Construction**	**227 days**	**Tue 7/29/25**	**Wed 6/3/26**	**Wed 7/23/25**	**Thu 6/4/26**	**40%**	**Wed 7/23/25**	**NA**
130	Building Mobilize	3 days	Tue 7/29/25	Thu 7/31/25	Wed 7/23/25	Fri 7/25/25	100%	Wed 7/23/25	Fri 7/25/25
131	Prep and Reinforce Perimeter Footings	10 days	Fri 8/1/25	Mon 8/11/25	Mon 7/28/25	Fri 8/8/25	100%	Mon 7/28/25	Fri 8/8/25
132	Pour Perimeter Footings	4 days	NA	NA	Wed 8/6/25	Tue 8/12/25	100%	Wed 8/6/25	Tue 8/12/25
133	UG Plumbing	9 days	NA	NA	Mon 8/4/25	Thu 8/14/25	100%	Mon 8/4/25	Thu 8/14/25
134	UG Plumbing Inspection	1 day	NA	NA	Fri 8/15/25	Fri 8/15/25	100%	Fri 8/15/25	Fri 8/15/25
135	UG Electrical	9 days	NA	NA	Mon 8/4/25	Thu 8/14/25	100%	Mon 8/4/25	Thu 8/14/25
136	UG Electrical Inspection	1 day	NA	NA	Fri 8/15/25	Fri 8/15/25	100%	Fri 8/15/25	Fri 8/15/25
137	Elevator Pit Waterproofing	9 days	NA	NA	Fri 8/15/25	Wed 8/27/25	100%	Fri 8/15/25	Wed 8/27/25
138	WEATHER DELAY	1 day	NA	NA	Wed 9/3/25	Wed 9/3/25	100%	Wed 9/3/25	Wed 9/3/25
139	WEATHER DELAY	1 day	NA	NA	Fri 9/5/25	Fri 9/5/25	100%	Fri 9/5/25	Fri 9/5/25
140	Slab on Grade Prep and Pour with 1' of Footers	20 days	Fri 8/15/25	Thu 9/11/25	Fri 8/15/25	Fri 9/19/25	100%	Fri 8/15/25	Fri 9/19/25
141	WEATHER DELAY	1 day	NA	NA	Mon 9/22/25	Mon 9/22/25	100%	Mon 9/22/25	Mon 9/22/25
142	CMU	32 days	Fri 9/19/25	Thu 10/16/25	Wed 9/24/25	Fri 11/7/25	100%	Wed 9/24/25	Fri 11/7/25
143	CFS Framing & Decking	20 days	Fri 9/26/25	Thu 10/23/25	Tue 10/14/25	Mon 11/10/25	100%	Tue 10/14/25	Mon 11/10/25
144	Wall Rough Elec	30 days	Fri 10/24/25	Thu 11/20/25	Tue 11/11/25	Tue 12/23/25	100%	Tue 11/11/25	Tue 12/23/25
145	OH Elec	25 days	Fri 11/21/25	Thu 12/25/25	Wed 12/10/25	Tue 1/20/26	100%	Wed 12/10/25	Tue 1/20/26
146	Interior Build-Out	30 days	Fri 1/30/26	Thu 3/19/26	Thu 1/22/26	Thu 3/5/26	0%	Thu 1/22/26	NA

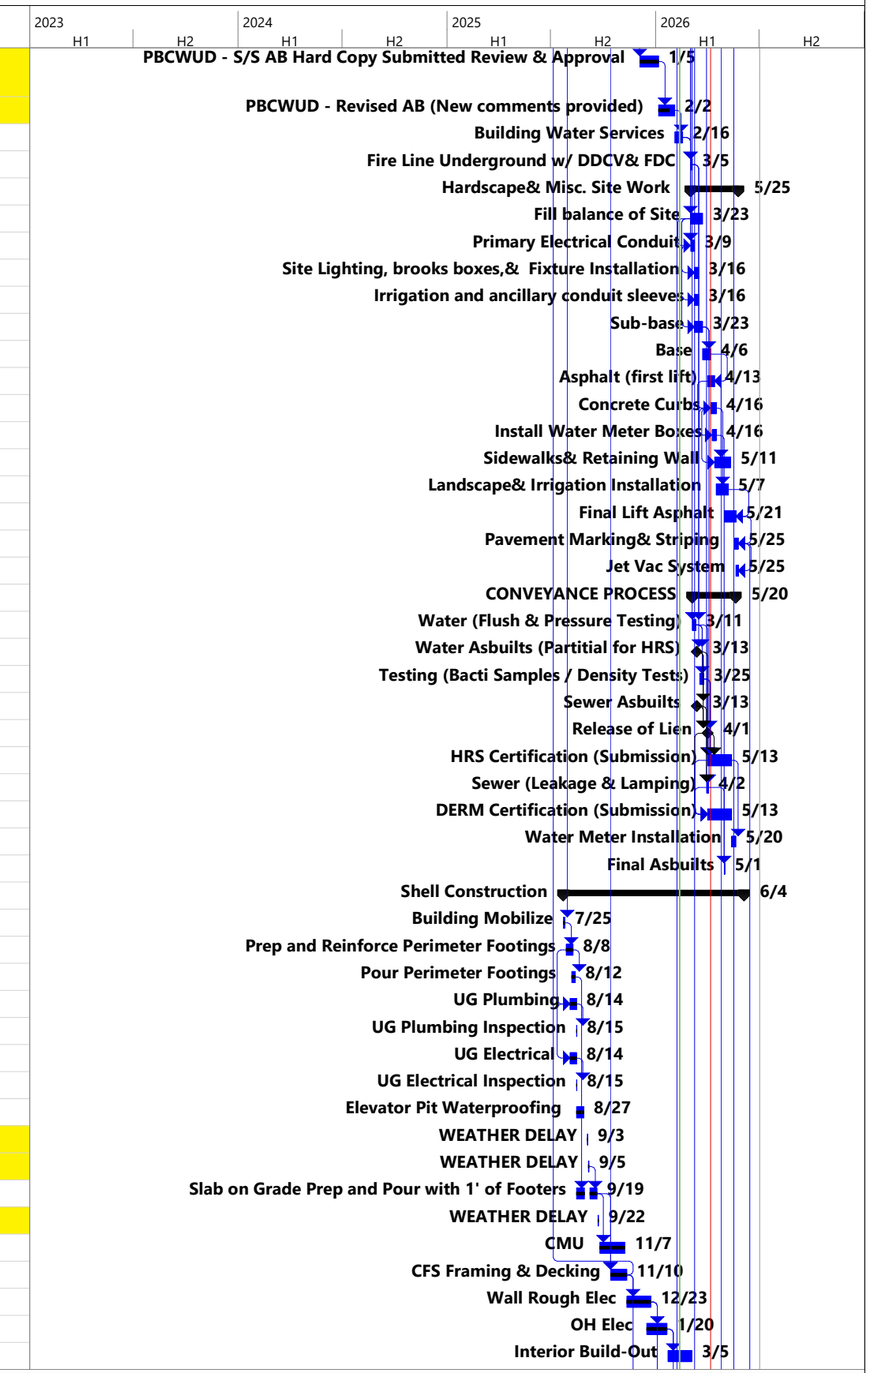

RYCON Construction Inc.

Construction Schedule

Public Storage - Delray Beach, FL

Thu 2/12/26

Public Storage
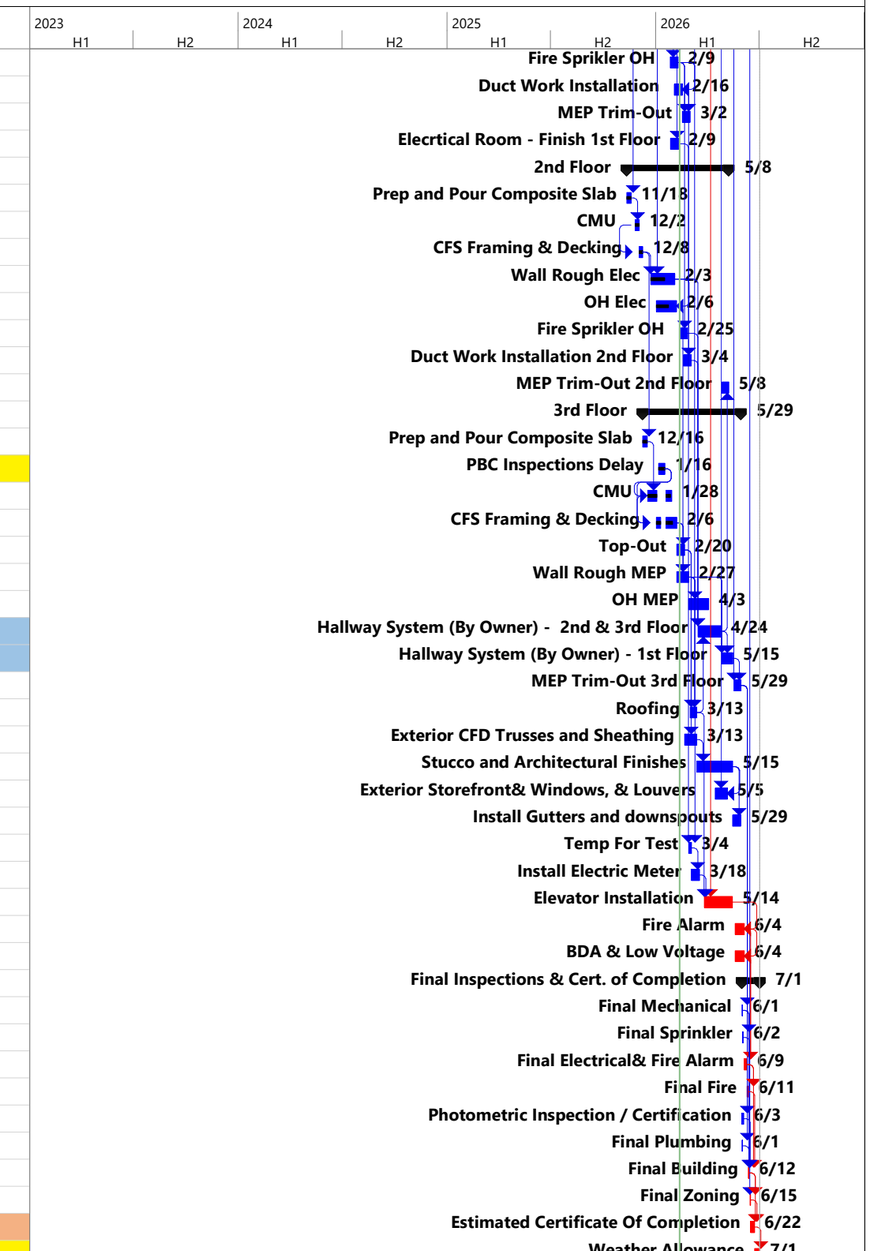
ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Comp.	Actual Start	Actual Finish
147	Fire Sprikler OH	10 days	NA	NA	Mon 1/26/26	Mon 2/9/26	0%	NA	NA
148	Duct Work Installation	10 days	NA	NA	Mon 2/2/26	Mon 2/16/26	0%	NA	NA
149	MEP Trim-Out	2 wks	Fri 1/30/26	Thu 2/12/26	Mon 2/16/26	Mon 3/2/26	0%	NA	NA
150	Elecrtical Room - Finish 1st Floor	10 days	Tue 2/10/26	Mon 3/2/26	Tue 1/27/26	Mon 2/9/26	0%	NA	NA
151	**2nd Floor**	**129 days**	**Fri 10/24/25**	**Thu 3/12/26**	**Tue 11/11/25**	**Fri 5/8/26**	**48%**	**Tue 11/11/25**	**NA**
152	Prep and Pour Composite Slab	6 days	Fri 10/24/25	Fri 11/7/25	Tue 11/11/25	Tue 11/18/25	100%	Tue 11/11/25	Tue 11/18/25
153	CMU	5 days	Mon 11/17/25	Fri 12/12/25	Wed 11/19/25	Tue 12/2/25	100%	Wed 11/19/25	Tue 12/2/25
154	CFS Framing & Decking	4 days	Mon 12/1/25	Fri 12/26/25	Fri 11/21/25	Mon 12/8/25	100%	Fri 11/21/25	Mon 12/8/25
155	Wall Rough Elec	30 days	Mon 12/29/25	Fri 1/16/26	Tue 12/23/25	Tue 2/3/26	60%	Tue 12/23/25	NA
156	OH Elec	25 days	Mon 1/19/26	Fri 2/20/26	Fri 1/2/26	Fri 2/6/26	60%	Fri 1/2/26	NA
157	Fire Sprikler OH	10 days	NA	NA	Wed 2/11/26	Wed 2/25/26	0%	NA	NA
158	Duct Work Installation 2nd Floor	10 days	NA	NA	Wed 2/18/26	Wed 3/4/26	0%	NA	NA
159	MEP Trim-Out 2nd Floor	2 wks	Fri 2/27/26	Thu 3/12/26	Mon 4/27/26	Fri 5/8/26	0%	NA	NA
160	**3rd Floor**	**124 days**	**Mon 12/29/25**	**Tue 5/5/26**	**Tue 12/9/25**	**Fri 5/29/26**	**30%**	**Tue 12/9/25**	**NA**
161	Prep and Pour Composite Slab	6 days	Mon 12/29/25	Fri 1/9/26	Tue 12/9/25	Tue 12/16/25	100%	Tue 12/9/25	Tue 12/16/25
162	**PBC Inspections Delay**	**9 days**	**NA**	**NA**	**Tue 1/6/26**	**Fri 1/16/26**	**100%**	**Tue 1/6/26**	**Fri 1/16/26**
163	CMU	20 days	Mon 1/19/26	Fri 2/13/26	Wed 12/17/25	Wed 1/28/26	90%	Wed 12/17/25	NA
164	CFS Framing & Decking	20 days	Wed 2/4/26	Tue 3/3/26	Mon 12/22/25	Fri 2/6/26	75%	Mon 12/22/25	NA
165	Top-Out	10 days	Wed 3/4/26	Tue 3/17/26	Fri 2/6/26	Fri 2/20/26	0%	NA	NA
166	Wall Rough MEP	15 days	Wed 3/4/26	Tue 3/24/26	Fri 2/6/26	Fri 2/27/26	0%	NA	NA
167	OH MEP	25 days	Wed 3/25/26	Tue 4/28/26	Fri 2/27/26	Fri 4/3/26	0%	NA	NA
168	Hallway System (By Owner) - 2nd & 3rd Floor	6 wks	Fri 1/30/26	Thu 2/26/26	Mon 3/16/26	Fri 4/24/26	0%	NA	NA
169	Hallway System (By Owner) - 1st Floor	3 wks	Wed 3/25/26	Tue 4/21/26	Mon 4/27/26	Fri 5/15/26	0%	NA	NA
170	MEP Trim-Out 3rd Floor	2 wks	Wed 4/22/26	Tue 5/5/26	Mon 5/18/26	Fri 5/29/26	0%	NA	NA
171	Roofing	10 days	Wed 3/18/26	Tue 3/31/26	Mon 3/2/26	Fri 3/13/26	0%	NA	NA
172	Exterior CFD Trusses and Sheathing	15 days	Wed 3/18/26	Tue 4/7/26	Fri 2/20/26	Fri 3/13/26	0%	NA	NA
173	Stucco and Architectural Finishes	45 days	Wed 3/4/26	Tue 5/5/26	Fri 3/13/26	Fri 5/15/26	0%	NA	NA
174	Exterior Storefront& Windows, & Louvers	15 days	Wed 3/18/26	Tue 4/14/26	Wed 4/15/26	Tue 5/5/26	0%	NA	NA
175	Install Gutters and downspouts	10 days	Wed 5/6/26	Tue 5/19/26	Fri 5/15/26	Fri 5/29/26	0%	NA	NA
176	**Temp For Test**	**3 days**	**Tue 3/3/26**	**Thu 3/5/26**	**Fri 2/27/26**	**Wed 3/4/26**	**0%**	**NA**	**NA**
177	**Install Electric Meter**	**10 days**	**Fri 3/6/26**	**Thu 3/19/26**	**Wed 3/4/26**	**Wed 3/18/26**	**0%**	**NA**	**NA**
178	Elevator Installation	35 days	Wed 4/1/26	Tue 5/19/26	Fri 3/27/26	Thu 5/14/26	0%	NA	NA
179	Fire Alarm	12 days	Wed 5/20/26	Tue 6/9/26	Wed 5/20/26	Thu 6/4/26	0%	NA	NA
180	BDA & Low Voltage	12 days	Wed 5/20/26	Tue 6/9/26	Wed 5/20/26	Thu 6/4/26	0%	NA	NA
181	**Final Inspections & Cert. of Completion**	**23 days**	**Wed 5/6/26**	**Tue 7/7/26**	**Mon 6/1/26**	**Wed 7/1/26**	**0%**	**NA**	**NA**
182	Final Mechanical	1 day	Tue 5/5/26	Wed 5/6/26	Mon 6/1/26	Mon 6/1/26	0%	NA	NA
183	Final Sprinkler	1 day	Wed 5/6/26	Thu 5/7/26	Tue 6/2/26	Tue 6/2/26	0%	NA	NA
184	Final Electrical& Fire Alarm	3 days	Fri 6/5/26	Wed 6/10/26	Fri 6/5/26	Tue 6/9/26	0%	NA	NA
185	Final Fire	2 days	Wed 6/10/26	Fri 6/12/26	Wed 6/10/26	Thu 6/11/26	0%	NA	NA
186	Photometric Inspection / Certification	3 days	Tue 5/5/26	Fri 5/8/26	Mon 6/1/26	Wed 6/3/26	0%	NA	NA
187	Final Plumbing	1 day	Tue 5/5/26	Wed 5/6/26	Mon 6/1/26	Mon 6/1/26	0%	NA	NA
188	Final Building	1 day	Fri 6/12/26	Mon 6/15/26	Fri 6/12/26	Fri 6/12/26	0%	NA	NA
189	Final Zoning	1 day	Mon 6/15/26	Tue 6/16/26	Mon 6/15/26	Mon 6/15/26	0%	NA	NA
190	Estimated Certificate Of Completion	5 days	Tue 6/16/26	Tue 6/23/26	Tue 6/16/26	Mon 6/22/26	0%	NA	NA
191	**Weather Allowance**	**7 days**	**Tue 6/23/26**	**Wed 7/1/26**	**Tue 6/23/26**	**Wed 7/1/26**	**0%**	**NA**	**NA**
