Executive Landing Page

Public Storage Dashboard — Data Date: **1/19/2026**

Type	Project	Region	Responsible
Construction	Delray, FL	East Coast	Tracy Girard

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
6/22/2026	6/22/2026	0 Baseline (Blank) Previous	(Blank)

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	6/27/2025		6/27/2025	0		Site Mobilization	On Track – Gaining
Foundation Complete	9/19/2025		9/19/2025	0		Slab On Grade Prep And Pour With 1' Of Footers	On Track – Gaining
1st Floor Finishes Complete	2/9/2026		2/9/2026	0		Electrical Room - Finish 1St Floor	On Track – Gaining
Structure Top Out	2/20/2026		2/20/2026	0		Top-Out	On Track – Gaining
Conditioned Air	3/4/2026		3/4/2026	0		Duct Work Installation 2Nd Floor	On Track – Gaining
Weather Tight	3/13/2026		3/13/2026	0		Roofing	On Track – Gaining
2nd Floor Finishes Complete	5/8/2026		5/8/2026	0		Mep Trim-Out 2Nd Floor	On Track – Gaining
Elevator Complete	5/14/2026		5/14/2026	0		Elevator Installation	On Track – Gaining
Hardscape/Landscape Complete	5/25/2026		5/25/2026	0		Jet Vac System	On Track – Gaining
3rd Floor Finishes Complete	5/29/2026		5/29/2026	0		Mep Trim-Out 3Rd Floor	On Track – Gaining
Permanent Power	6/4/2026		6/4/2026	0		Bda & Low Voltage	On Track – Gaining
Contract Completion	6/22/2026		6/22/2026	0		Estimated Certificate Of Completion	On Track – Gaining

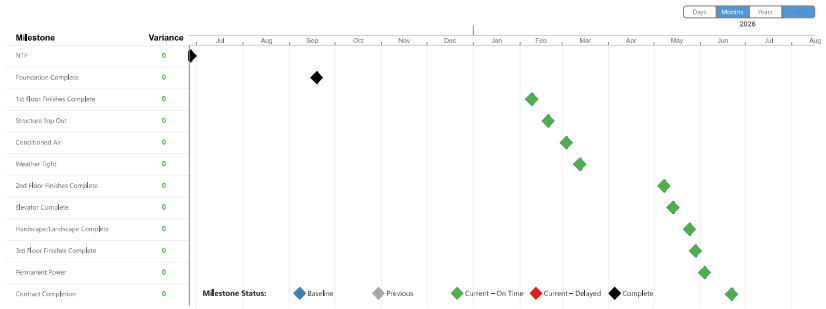

Baseline Variance

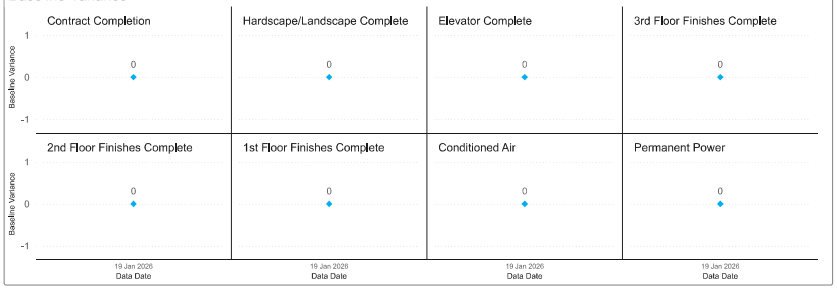

Schedule Performance Summary

Insufficient Schedule Data: Comparative analysis requires more schedules to produce figures

Powered By STELIC INSIGHT+ACTION=IMPACT
