Construction Schedule

Public Storage - Delray Beach, FL

Wed 3/25/26

ID	Task Name	% Comp.	Duration	Contract Start	Contract Finish
1	**Overall Project Duration - Public Storage - Delray Beach**	**84%**	**414 days**	**Fri 11/29/24**	**Fri 7/3/26**
9	**SUBMITTALS**	**99%**	**345 days**	**Fri 12/6/24**	**Thu 9/4/25**
68	**Elevator Submittals**	**94%**	**305 days**	**Fri 1/31/25**	**Fri 8/8/25**
74	Fabricate and Delivery (Estimated)	85%	19 wks	Mon 3/24/25	Fri 8/8/25
75	**Construction**	**64%**	**268 days**	**Tue 6/24/25**	**Fri 7/3/26**
76	**Overall Site Construction**	**68%**	**249 days**	**Tue 6/24/25**	**Mon 5/11/26**
95	**Domestic Water Service**	**94%**	**154 days**	**Tue 12/16/25**	**Mon 1/26/26**
104	**PBCWUD Review - W&S AB After 1st Lift**	**0%**	**5 days**	**NA**	**NA**
105	**Hardscape& Misc. Site Work**	**50%**	**54 days**	**Tue 2/17/26**	**Mon 5/11/26**
115	Sidewalks	25%	20 days	Tue 3/31/26	Mon 4/27/26
116	Irrigation Installation	25%	15 days	Fri 4/3/26	Thu 4/23/26
117	Final Lift Asphalt	0%	15 days	Fri 4/17/26	Thu 5/7/26
118	Pavement Marking& Striping	0%	5 days	Tue 5/5/26	Mon 5/11/26
119	Jet Vac System	0%	3 days	Thu 5/7/26	Mon 5/11/26
120	**CONVEYANCE PROCESS**	**0%**	**54 days**	**Mon 12/29/25**	**Mon 4/27/26**
121	Water (Flush & Pressure Testing)	0%	4 days	Tue 1/27/26	Fri 1/30/26
122	Water Asbuilts (Partitial for HRS)	0%	0 days	Tue 2/3/26	Tue 2/3/26
123	Testing (Bacti Samples / Density Tests)	0%	5 days	Mon 2/9/26	Fri 2/13/26
124	Sewer Asbuilts	0%	0 days	Mon 12/29/25	Mon 12/29/25
125	Release of Lien	0%	0 days	Fri 2/20/26	Fri 2/20/26

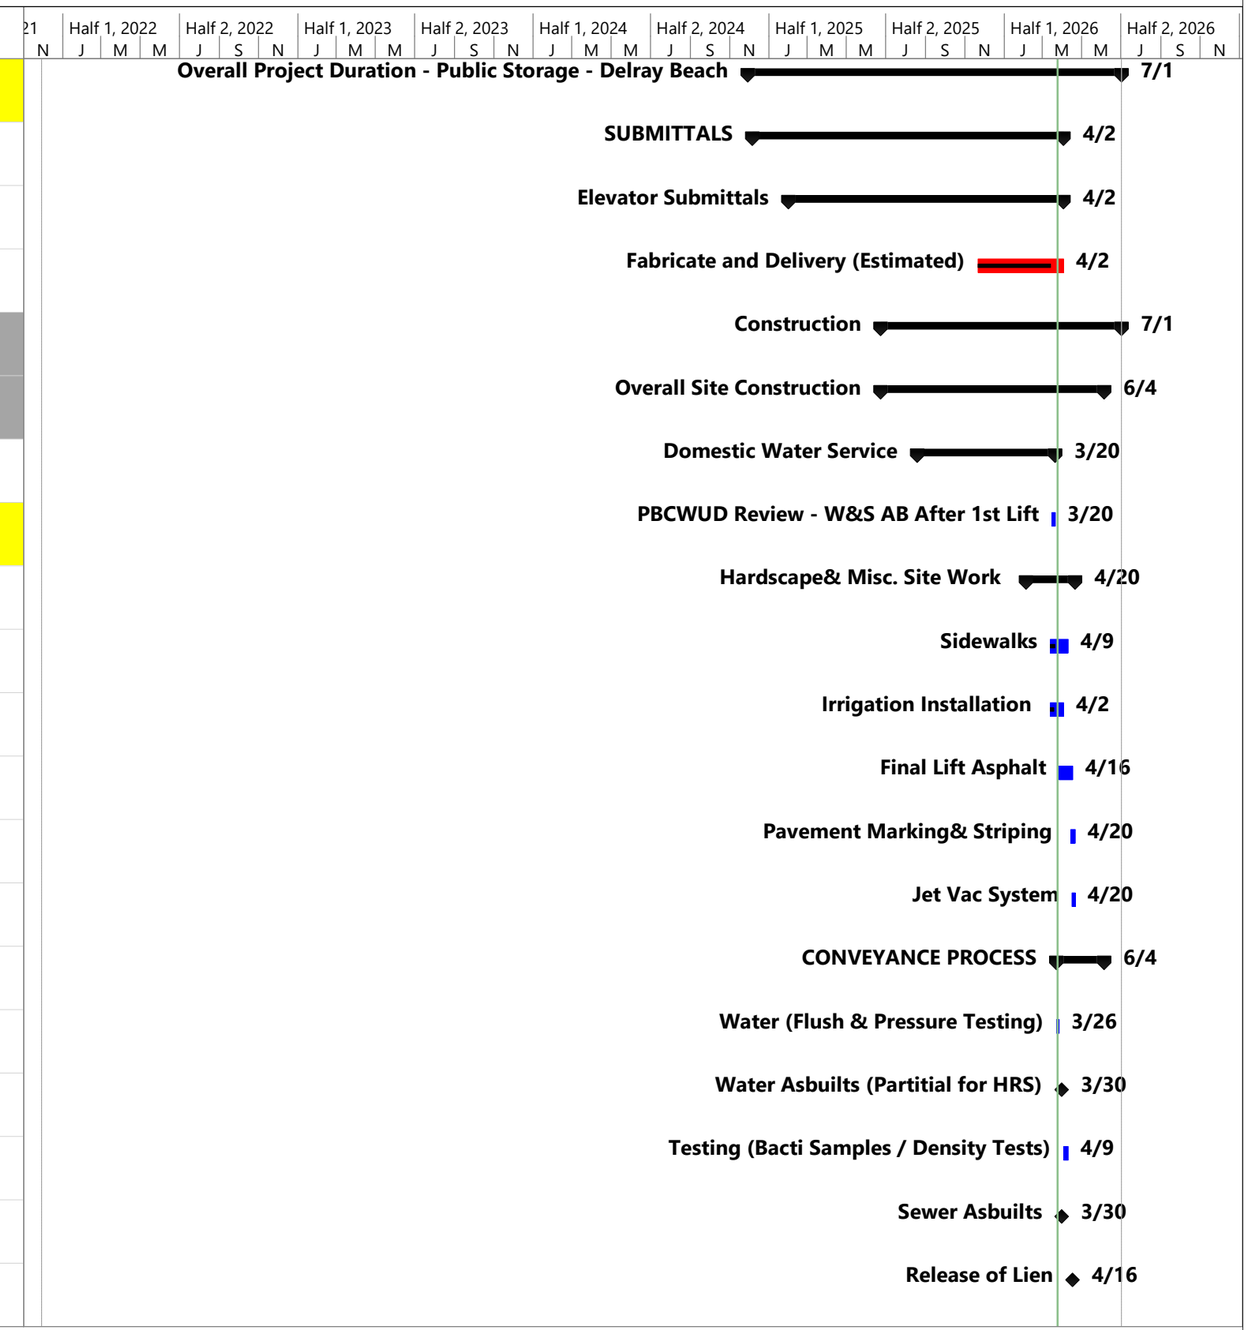

Construction Schedule

Public Storage - Delray Beach, FL

Wed 3/25/26

ID	Task Name	% Comp.	Duration	Contract Start	Contract Finish
126	**HRS Certification (Submission)**	**0%**	**6 wks**	**Mon 2/23/26**	**Fri 4/3/26**
127	Sewer (Leakage & Lamping)	0%	3 days	Tue 3/17/26	Thu 3/19/26
128	DERM Certification (Submission)	0%	6 wks	Tue 3/17/26	Mon 4/27/26
129	Water Meter Installation	0%	5 days	Mon 4/6/26	Fri 4/10/26
130	**Final Asbuilts**	**0%**	**1 day**	**Fri 4/17/26**	**Fri 4/17/26**
131	**Shell Construction**	**63%**	**227 days**	**Tue 7/29/25**	**Wed 6/3/26**
148	Interior Build-Out	40%	45 days	Fri 1/30/26	Thu 3/19/26
150	Electrical Room - Finish	70%	20 days	Tue 2/10/26	Mon 3/2/26
152	MEP Trim-Out	45%	2 wks	Fri 1/30/26	Thu 2/12/26
153	**2nd Floor**	**88%**	**130 days**	**Fri 10/24/25**	**Thu 3/12/26**
160	Duct Work Installation	75%	10 days	NA	NA
161	MEP Trim-Out	0%	2 wks	Fri 2/27/26	Thu 3/12/26
162	**3rd Floor**	**80%**	**126 days**	**Mon 12/29/25**	**Tue 5/5/26**
171	OH Elec	85%	25 days	Wed 3/25/26	Tue 4/28/26
172	Fire Sprikler OH	0%	10 days	NA	NA
173	Duct Work Install	0%	8 days	NA	NA
174	MEP Trim-Out	0%	2 wks	Wed 4/22/26	Tue 5/5/26
175	Roofing	15%	10 days	Wed 3/18/26	Tue 3/31/26
176	Hallway System (By Owner) - 2nd & 3rd Floor	0%	5 wks	Fri 1/30/26	Thu 2/26/26
177	Hallway System (By Owner) - 1st Floor	0%	2 wks	Wed 3/25/26	Tue 4/21/26

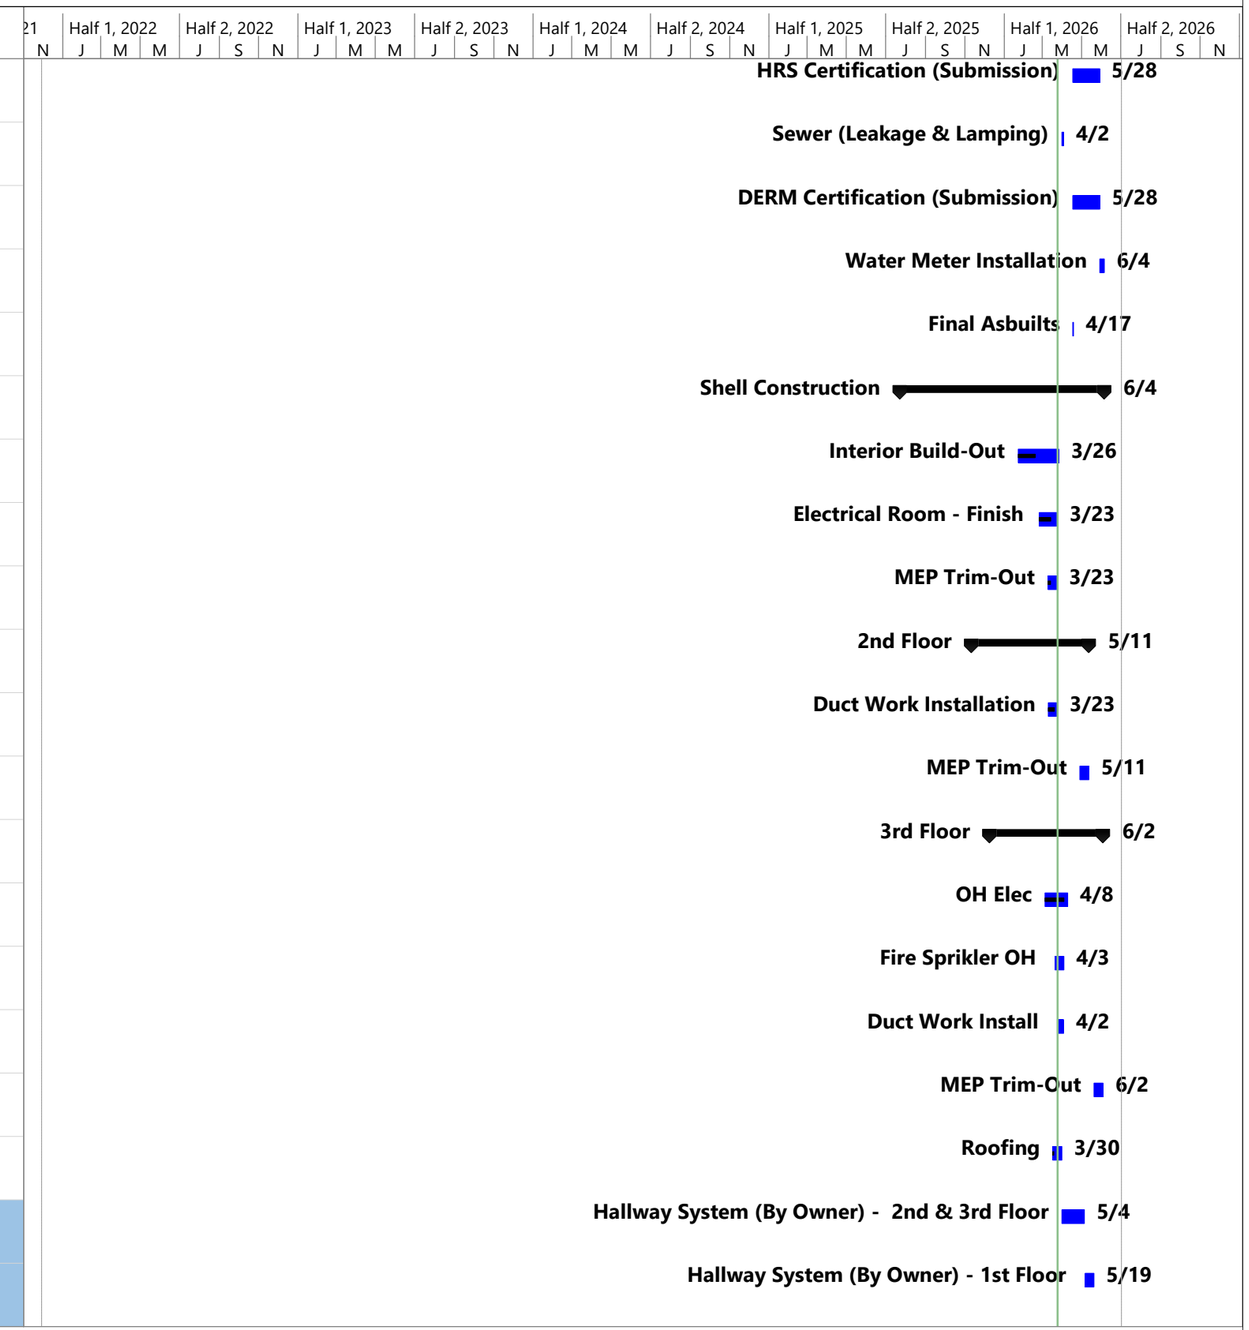

Construction Schedule

Public Storage - Delray Beach, FL

Wed 3/25/26
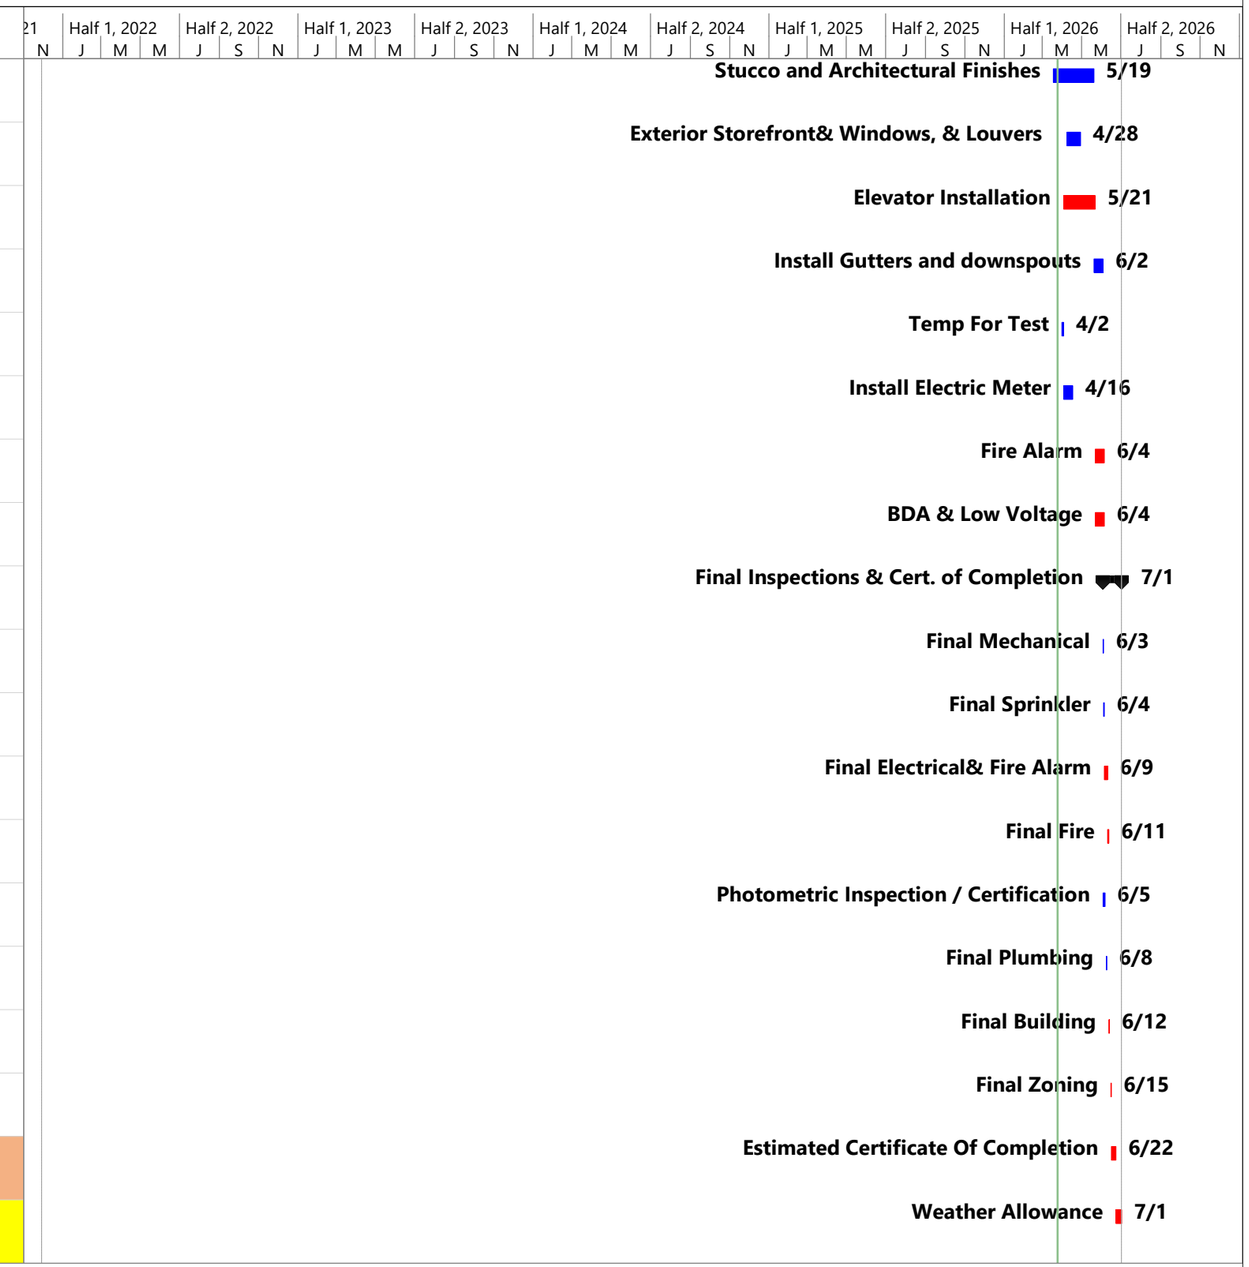
ID	Task Name	% Comp.	Duration	Contract Start	Contract Finish
178	Stucco and Architectural Finishes	0%	45 days	Wed 3/4/26	Tue 5/5/26
179	Exterior Storefront& Windows, & Louvers	0%	15 days	Wed 3/18/26	Tue 4/14/26
180	Elevator Installation	0%	35 days	Wed 4/1/26	Tue 5/19/26
181	Install Gutters and downspouts	0%	10 days	Wed 5/6/26	Tue 5/19/26
182	**Temp For Test**	**0%**	**3 days**	**Tue 3/3/26**	**Thu 3/5/26**
183	**Install Electric Meter**	**0%**	**10 days**	**Fri 3/6/26**	**Thu 3/19/26**
184	Fire Alarm	0%	10 days	Wed 5/20/26	Tue 6/9/26
185	BDA & Low Voltage	0%	10 days	Wed 5/20/26	Tue 6/9/26
186	**Final Inspections & Cert. of Completion**	**0%**	**21 days**	**Wed 5/6/26**	**Tue 7/7/26**
187	Final Mechanical	0%	1 day	Tue 5/5/26	Wed 5/6/26
188	Final Sprinkler	0%	1 day	Wed 5/6/26	Thu 5/7/26
189	Final Electrical& Fire Alarm	0%	3 days	Fri 6/5/26	Wed 6/10/26
190	Final Fire	0%	2 days	Wed 6/10/26	Fri 6/12/26
191	Photometric Inspection / Certification	0%	3 days	Tue 5/5/26	Fri 5/8/26
192	Final Plumbing	0%	1 day	Tue 5/5/26	Wed 5/6/26
193	Final Building	0%	1 day	Fri 6/12/26	Mon 6/15/26
194	Final Zoning	0%	1 day	Mon 6/15/26	Tue 6/16/26
195	Estimated Certificate Of Completion	0%	5 days	Tue 6/16/26	Tue 6/23/26
196	**Weather Allowance**	**0%**	**7 days**	**Tue 6/23/26**	**Wed 7/1/26**
