Executive Landing Page | Landing Page

Public Storage Dashboard

Data Date: 3/17/2026

Type	Project	Region	Responsible
Construction	Delray, FL	East Coast	Tracy Girard

Baseline Completion Date	Current Completion Date	Schedule Variance	Work Compression
6/22/2026	6/22/2026	0 days Prev: 0 days | Trend: 0 days → No Change	

Critical Path Status & Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	6/27/2025	6/27/2025	6/27/2025	0	0	Site Mobilization	On Track – Gaining
Foundation Complete	9/19/2025	9/19/2025	9/19/2025	0	0	Slab On Grade Prep And Pour With 1' Of Footers	On Track – Gaining
Structure Top Out	2/20/2026	2/20/2026	2/24/2026	-4	-4	Top-Out	Delayed – Slipping
Conditioned Air	3/4/2026	3/4/2026	3/23/2026	-19	-19	Duct Work Installation 2Nd Floor	Delayed – Slipping
1st Floor Finishes Complete	2/9/2026	2/9/2026	3/23/2026	-42	-42	Elecrtical Room - Finish 1St Floor	Delayed – Slipping
Weather Tight	3/13/2026	3/13/2026	3/30/2026	-17	-17	Roofing	Delayed – Slipping
Hardscape/Landscape Complete	5/25/2026	5/25/2026	4/20/2026	35	35	Jet Vac System	On Track – Gaining
2nd Floor Finishes Complete	5/8/2026	5/8/2026	5/11/2026	-3	-3	Mep Trim-Out 2Nd Floor	Delayed – Slipping
Elevator Complete	5/14/2026	5/14/2026	5/21/2026	-7	-7	Elevator Installation	Delayed – Slipping
3rd Floor Finishes Complete	5/29/2026	5/29/2026	6/2/2026	-4	-4	Mep Trim-Out 3Rd Floor	Delayed – Slipping
Permanent Power	6/4/2026	6/4/2026	6/4/2026	0	0	Bda & Low Voltage	On Track – Gaining
Contract Completion	6/22/2026	6/22/2026	6/22/2026	0	0	Estimated Certificate Of Completion	On Track – Gaining

Baseline Variance Trends — Critical Milestones

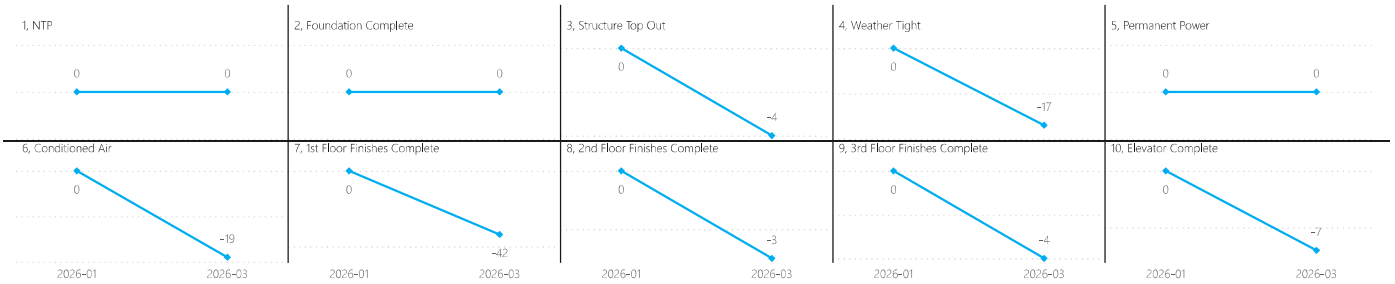

Schedule Performance Summary

Summary: Several core metrics reflect significant concerns regarding schedule logic, stability, and execution risk. The compounded effect of low schedule quality, sustained critical path compression, and ongoing logic changes h… the probability of downstream schedule slippage or resource conflicts. Management attention should focus on validating and repairing the schedule network, controlling further changes, and reassessing the feasibility of forecasted milestones.

Schedule Validation Score: 55.00 — ALERT

The SV Score is critically low, indicating significant schedule quality issues such as poor logic, excessive constraints, or technical noncompliance with best practices. Immediate review and correction of logic flaws are strongly recommended to restore schedule reliability.

Critical Path Compression: 10.00% — ALERT

There has been substantial compression on the critical path, which risks overloading resources and compromising execution quality. Continued compression at this level suggests an urgent need for rescheduling or recovery strategy reassessment.

Critical Path Variance: 10.00% — WARNING

The critical path duration has increased notably compared to baseline, suggesting slippage on key project deliverables. Close monitoring and mitigation planning are advised to prevent further delays.

Schedule Change Index: 8.00% — WARNING

The percentage of activities changed this period exceeds stability thresholds, highlighting risk of excessive schedule volatility. Improved change control discipline and validation of major changes are needed.

Compare Remaining Compression: -5%

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Powered By STELIC
