ID	Task Name	Duration	Start	Finish
1	**Public Storage Selma, NC**	**263 days**	**Mon 25/10/06**	**Fri 26/10/09**
2	Award Contract	0 days	Mon 25/10/06	Mon 25/10/06
3	**Mobilization**	**6 days**	**Mon 25/12/01**	**Mon 25/12/08**
4	Mobilization (Site Fence, Layout, Barricades, Etc.)	1 day	Mon 26/01/05	Mon 26/01/05
5	SWPPP	5 days	Mon 25/12/15	Fri 25/12/19
6	**Demo/Site Work**	**84 days**	**Mon 26/01/05**	**Thu 26/04/30**
7	Clearing and Grubbing	10 days	Mon 26/01/05	Fri 26/01/16
8	Dewatering	5 days	Mon 26/01/19	Fri 26/01/23
9	Rough Grading	18 days	Mon 26/01/19	Wed 26/02/11
10	Storm System	21 days	Thu 26/02/12	Thu 26/03/12
11	Sanitary Sewer	5 days	Fri 26/03/13	Thu 26/03/19
12	Water	10 days	Fri 26/03/20	Thu 26/04/02
13	Site Electrical	10 days	Fri 26/04/03	Thu 26/04/16
14	Building Tie In	10 days	Fri 26/04/17	Thu 26/04/30
15	**Building A**	**139 days**	**Thu 26/02/05**	**Tue 26/08/18**
16	**Structure**	**109 days**	**Thu 26/02/05**	**Tue 26/07/07**
17	**First Floor**	**59 days**	**Thu 26/02/05**	**Tue 26/04/28**
18	Building Pad Delivery (Bldg A)	5 days	Thu 26/02/05	Wed 26/02/11
19	Elevator Pit - Excavate	5 days	Thu 26/02/12	Wed 26/02/18
20	Elevator Pit - Form and Pour	10 days	Thu 26/02/19	Wed 26/03/04
21	FRP Foundations / Foundation CMU - Area 1	7 days	Thu 26/02/12	Fri 26/02/20
22	Concrete Retaining Walls	10 days	Mon 26/02/23	Fri 26/03/06
23	FRP Foundations/Foundation Area 2	7 days	Mon 26/03/09	Tue 26/03/17
24	Under Slab MEP	10 days	Wed 26/03/04	Tue 26/03/17
25	Slab #1 Prep / Pour (North Half)	10 days	Wed 26/03/11	Tue 26/03/24
26	CMU shafts	15 days	Wed 26/03/25	Tue 26/04/14
27	Slab #2 Prep / Pour (South Half)	10 days	Wed 26/03/25	Tue 26/04/07
28	Janus Framing System (North Half)	15 days	Wed 26/03/25	Tue 26/04/14
29	Janus Framing System (South Half)	10 days	Wed 26/04/15	Tue 26/04/28
30	**Second Floor**	**40 days**	**Wed 26/04/15**	**Tue 26/06/09**
31	Elevated Slab #1 (North Half) Prep/Pour	5 days	Wed 26/04/15	Tue 26/04/21
32	Elevated Slab #2 (South Half) Prep/Pour	5 days	Wed 26/04/29	Tue 26/05/05
33	Janus Framing System (North Half)	15 days	Wed 26/04/29	Tue 26/05/19
34	Janus Framing System (South Half)	10 days	Wed 26/05/20	Tue 26/06/02
35	Roof Decking	5 days	Wed 26/06/03	Tue 26/06/09
36	**Stairs**	**20 days**	**Wed 26/06/10**	**Tue 26/07/07**
37	Stair #1	10 days	Wed 26/06/10	Tue 26/06/23
38	Stair #2	10 days	Wed 26/06/24	Tue 26/07/07
39	**Roof**	**10 days**	**Wed 26/06/10**	**Tue 26/06/23**
40	Metal Roofing	10 days	Wed 26/06/10	Tue 26/06/23
41	**Framing and MEP**	**80 days**	**Wed 26/04/29**	**Tue 26/08/18**
42	**First Floor**	**65 days**	**Wed 26/04/29**	**Tue 26/07/28**
43	Interior Framing	5 days	Wed 26/04/29	Tue 26/05/05
44	1st Floor MEP Rough-In Area 1	20 days	Wed 26/05/06	Tue 26/06/02
45	1st Floor MEP Rough-In Area 2	15 days	Wed 26/06/03	Tue 26/06/23
46	1st Floor MEP Trim Out Area 1	10 days	Wed 26/07/08	Tue 26/07/21
47	1st Floor MEP Trim Out Area 2	5 days	Wed 26/07/22	Tue 26/07/28
48	**Second Floor**	**50 days**	**Wed 26/06/10**	**Tue 26/08/18**
49	Interior Framing	5 days	Wed 26/06/10	Tue 26/06/16
50	2nd Floor MEP Rough-In Area 2	15 days	Wed 26/06/24	Tue 26/07/14
51	2nd Floor MEP Rough-In Area 2	15 days	Wed 26/07/15	Tue 26/08/04
52	2nd Floor MEP Trim Out Area 1	10 days	Wed 26/07/29	Tue 26/08/11
53	2nd Floor MEP Trim Out Area 2	5 days	Wed 26/08/12	Tue 26/08/18
54	**Elevator**	**30 days**	**Tue 26/06/23**	**Tue 26/08/04**
55	Delivery	0 days	Tue 26/06/23	Tue 26/06/23
56	Elevator 1 - First Floor	5 days	Wed 26/06/24	Tue 26/06/30
57	Elevator 1 - Second Floor	5 days	Wed 26/07/01	Tue 26/07/07

ID	Task Name	Duration	Start	Finish
58	Elevator 2 - First Floor	5 days	Wed 26/07/08	Tue 26/07/14
59	Elevator 2 - Second Floor	5 days	Wed 26/07/15	Tue 26/07/21
60	Infill Doors	5 days	Wed 26/07/15	Tue 26/07/21
61	Test / Adjust	5 days	Wed 26/07/22	Tue 26/07/28
62	State Inspection	5 days	Wed 26/07/29	Tue 26/08/04
63	**Exterior Finishes**	**50 days**	**Wed 26/05/06**	**Tue 26/07/14**
64	Masonry Veneer	15 days	Wed 26/05/06	Tue 26/05/26
65	Metal Panels Completion	15 days	Wed 26/05/27	Tue 26/06/16
66	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	Wed 26/06/17	Tue 26/06/30
67	Automatic Entrance Door	5 days	Wed 26/05/27	Tue 26/06/02
68	Exterior Paint	10 days	Wed 26/06/17	Tue 26/06/30
69	Exterior Signage Install	10 days	Wed 26/07/01	Tue 26/07/14
70	Canopy	10 days	Wed 26/07/01	Tue 26/07/14
71	**Building B**	**85 days**	**Thu 26/02/12**	**Wed 26/06/10**
72	**Structure**	**55 days**	**Thu 26/02/12**	**Wed 26/04/29**
73	**First Floor**	**50 days**	**Thu 26/02/12**	**Wed 26/04/22**
74	Building Pad Delivery (Bldg B)	5 days	Thu 26/02/12	Wed 26/02/18
75	FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/02/19	Wed 26/02/25
76	FRP Foundations/Foundation Area 2	5 days	Thu 26/02/26	Wed 26/03/04
77	Under Slab MEP	5 days	Thu 26/03/05	Wed 26/03/11
78	Slab Prep / Pour	5 days	Thu 26/03/12	Wed 26/03/18
79	CMU Walls	10 days	Thu 26/03/19	Wed 26/04/01
80	Janus Framing System	10 days	Thu 26/04/02	Wed 26/04/15
81	Roof Decking	5 days	Thu 26/04/16	Wed 26/04/22
82	**Roof**	**5 days**	**Thu 26/04/23**	**Wed 26/04/29**
83	Metal Roofing	5 days	Thu 26/04/23	Wed 26/04/29
84	**Framing and MEP**	**30 days**	**Thu 26/04/16**	**Wed 26/05/27**
85	**First Floor**	**30 days**	**Thu 26/04/16**	**Wed 26/05/27**
86	Interior Framing	5 days	Thu 26/04/16	Wed 26/04/22
87	1st Floor MEP Rough-In Area 1	10 days	Thu 26/04/23	Wed 26/05/06
88	Finishes	10 days	Thu 26/04/30	Wed 26/05/13
89	1st Floor MEP Trim Out Area 1	10 days	Thu 26/05/14	Wed 26/05/27
90	**Exterior Finishes**	**35 days**	**Thu 26/04/23**	**Wed 26/06/10**
91	Metal Panels Completion	15 days	Thu 26/04/23	Wed 26/05/13
92	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	Thu 26/05/14	Wed 26/05/27
93	Automatic Entrance Door	5 days	Thu 26/05/14	Wed 26/05/20
94	Exterior Paint	10 days	Thu 26/05/14	Wed 26/05/27
95	Exterior Signage Install	10 days	Thu 26/05/28	Wed 26/06/10
96	Canopy	10 days	Thu 26/05/28	Wed 26/06/10
97	**Building C**	**85 days**	**Thu 26/02/19**	**Wed 26/06/17**
98	**Structure**	**55 days**	**Thu 26/02/19**	**Wed 26/05/06**
99	**First Floor**	**50 days**	**Thu 26/02/19**	**Wed 26/04/29**
100	Building Pad Delivery (Bldg C)	5 days	Thu 26/02/19	Wed 26/02/25
101	FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/02/26	Wed 26/03/04
102	FRP Foundations/Foundation Area 2	5 days	Thu 26/03/05	Wed 26/03/11
103	Under Slab MEP	5 days	Thu 26/03/12	Wed 26/03/18
104	Slab Prep / Pour	5 days	Thu 26/03/19	Wed 26/03/25
105	CMU Walls	10 days	Thu 26/04/02	Wed 26/04/15
106	Janus Framing System	5 days	Thu 26/04/16	Wed 26/04/22
107	Roof Decking	5 days	Thu 26/04/23	Wed 26/04/29
108	**Roof**	**5 days**	**Thu 26/04/30**	**Wed 26/05/06**
109	Metal Roofing	5 days	Thu 26/04/30	Wed 26/05/06
110	**Framing and MEP**	**20 days**	**Thu 26/05/07**	**Wed 26/06/03**
111	**First Floor**	**20 days**	**Thu 26/05/07**	**Wed 26/06/03**
112	1st Floor MEP Rough-In Area 1	10 days	Thu 26/05/07	Wed 26/05/20
113	1st Floor MEP Trim Out Area 1	10 days	Thu 26/05/21	Wed 26/06/03
114	**Exterior Finishes**	**25 days**	**Thu 26/05/14**	**Wed 26/06/17**

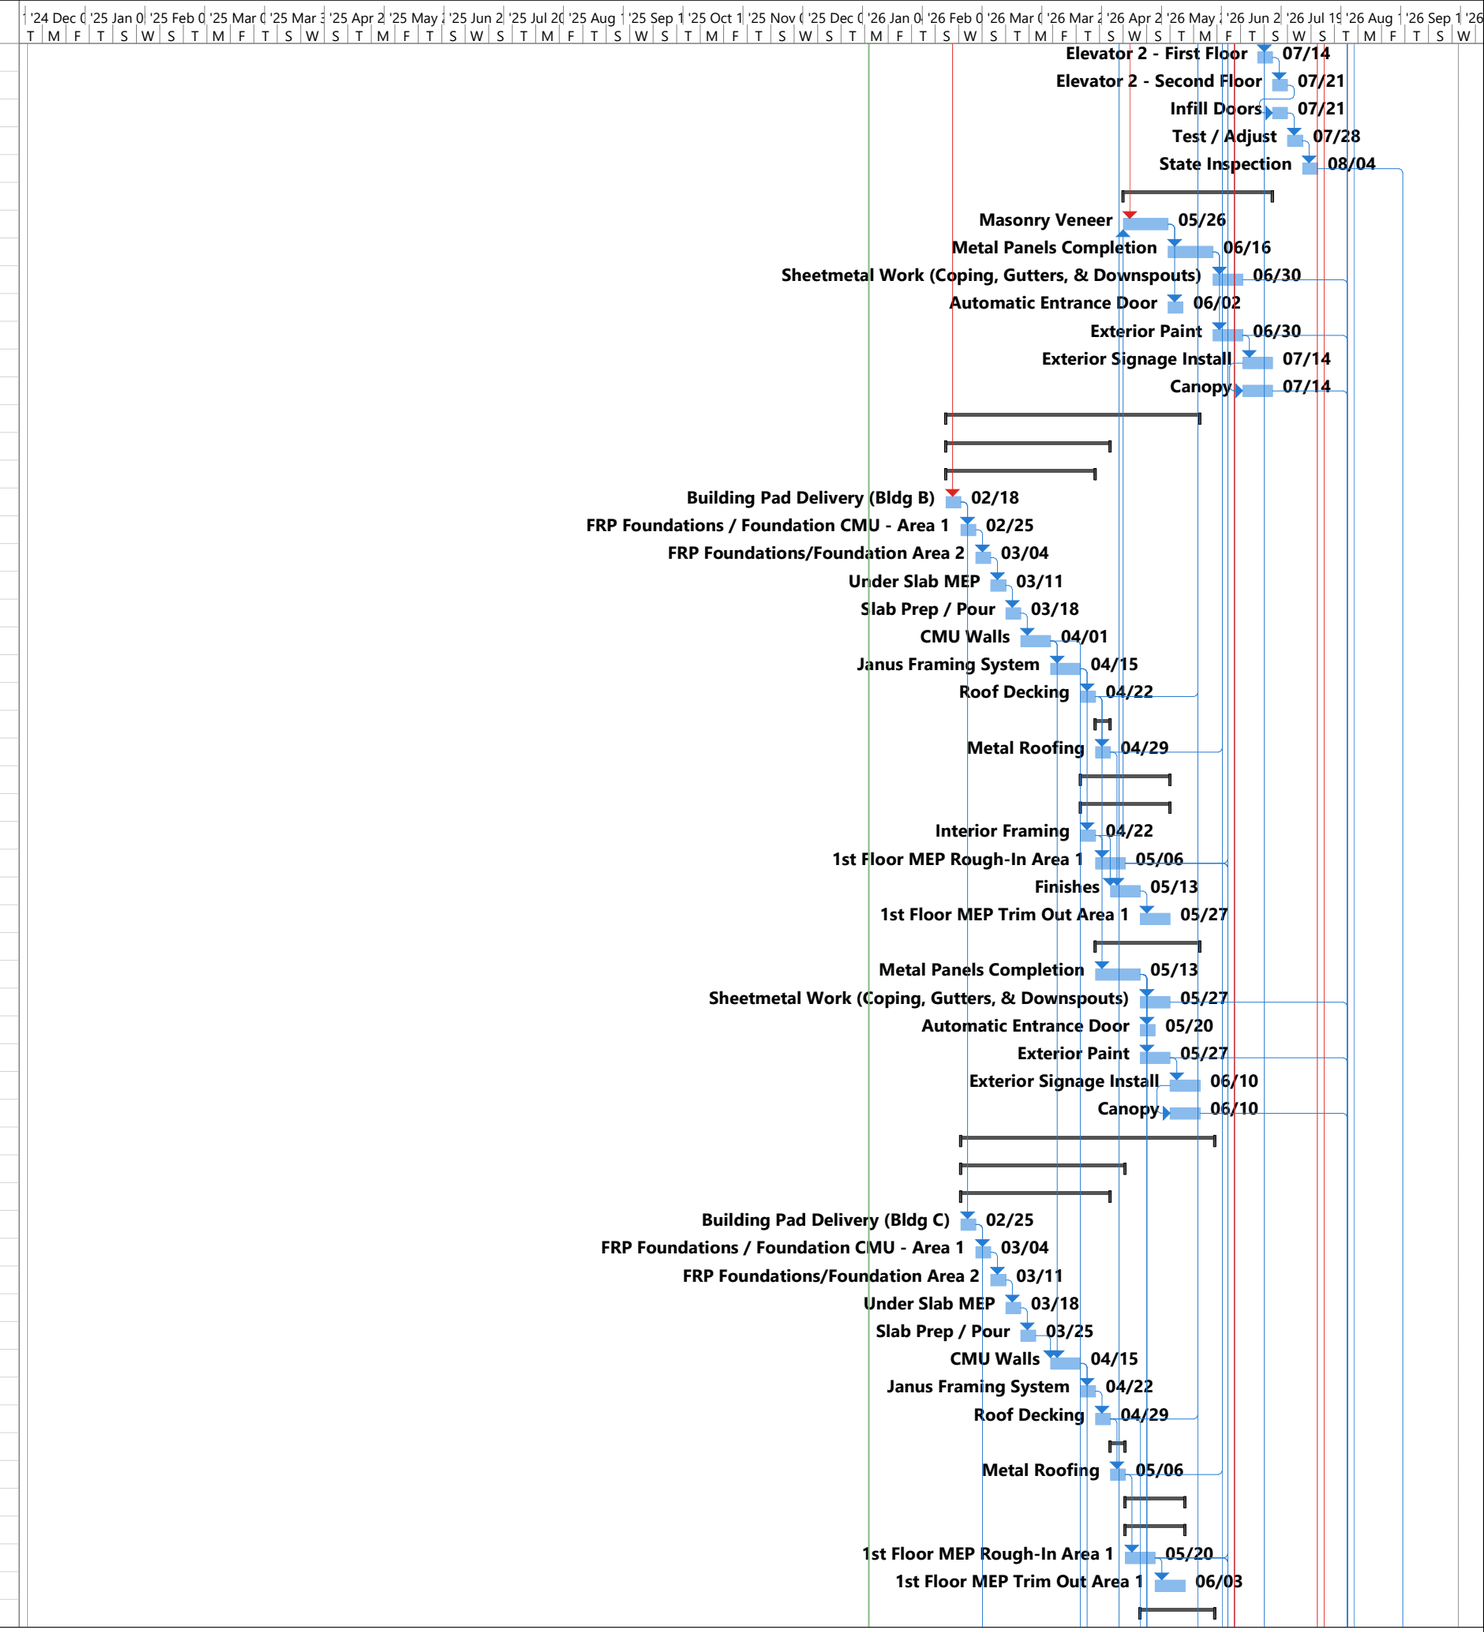
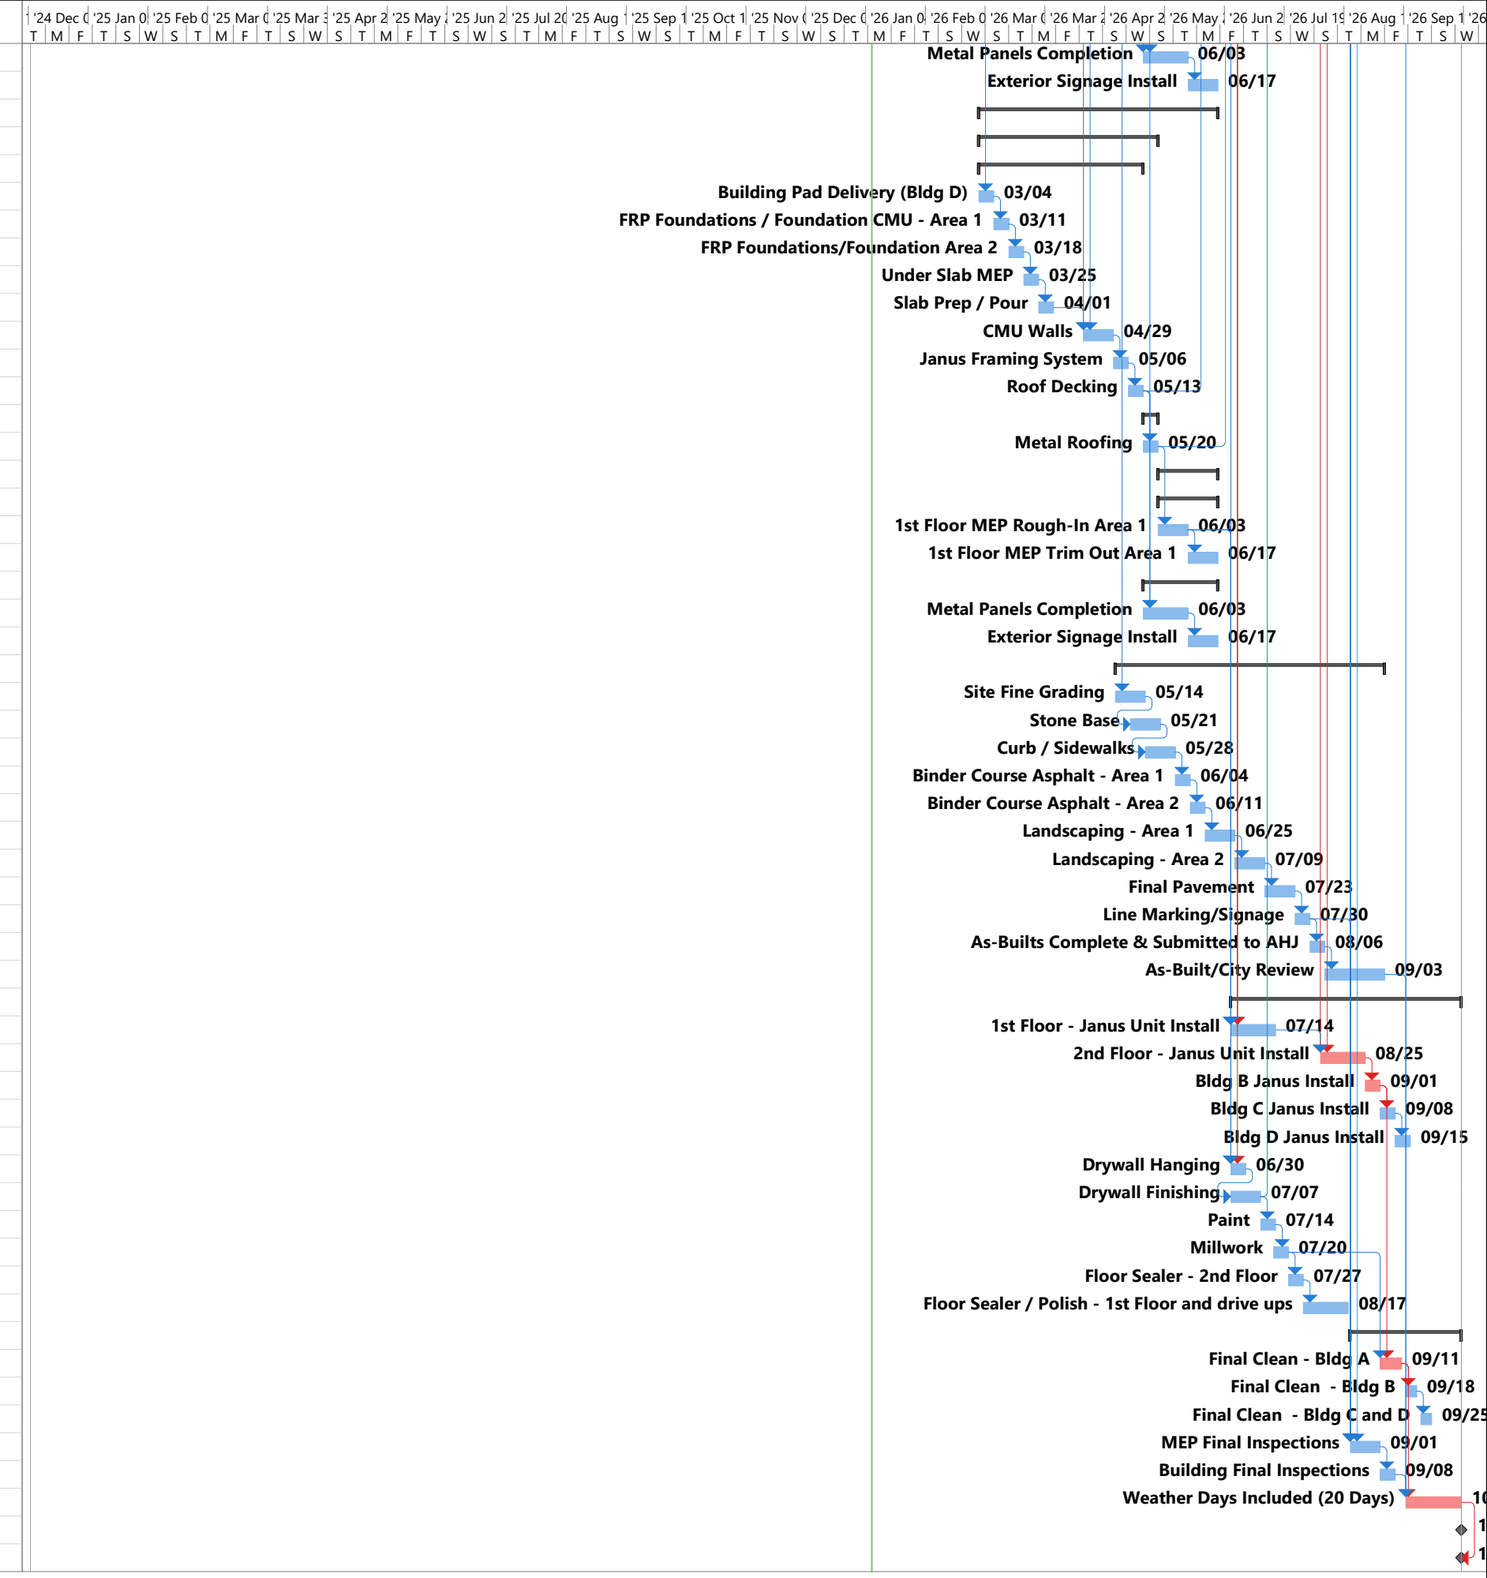
ID	Task Name	Duration	Start	Finish
115	Metal Panels Completion	15 days	Thu 26/05/14	Wed 26/06/03
116	Exterior Signage Install	10 days	Thu 26/06/04	Wed 26/06/17
117	**Building D**	**80 days**	**Thu 26/02/26**	**Wed 26/06/17**
118	**Structure**	**60 days**	**Thu 26/02/26**	**Wed 26/05/20**
119	**First Floor**	**55 days**	**Thu 26/02/26**	**Wed 26/05/13**
120	Building Pad Delivery (Bldg D)	5 days	Thu 26/02/26	Wed 26/03/04
121	FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/03/05	Wed 26/03/11
122	FRP Foundations/Foundation Area 2	5 days	Thu 26/03/12	Wed 26/03/18
123	Under Slab MEP	5 days	Thu 26/03/19	Wed 26/03/25
124	Slab Prep / Pour	5 days	Thu 26/03/26	Wed 26/04/01
125	CMU Walls	10 days	Thu 26/04/16	Wed 26/04/29
126	Janus Framing System	5 days	Thu 26/04/30	Wed 26/05/06
127	Roof Decking	5 days	Thu 26/05/07	Wed 26/05/13
128	**Roof**	**5 days**	**Thu 26/05/14**	**Wed 26/05/20**
129	Metal Roofing	5 days	Thu 26/05/14	Wed 26/05/20
130	**Framing and MEP**	**20 days**	**Thu 26/05/21**	**Wed 26/06/17**
131	**First Floor**	**20 days**	**Thu 26/05/21**	**Wed 26/06/17**
132	1st Floor MEP Rough-In Area 1	10 days	Thu 26/05/21	Wed 26/06/03
133	1st Floor MEP Trim Out Area 1	10 days	Thu 26/06/04	Wed 26/06/17
134	**Exterior Finishes**	**25 days**	**Thu 26/05/14**	**Wed 26/06/17**
135	Metal Panels Completion	15 days	Thu 26/05/14	Wed 26/06/03
136	Exterior Signage Install	10 days	Thu 26/06/04	Wed 26/06/17
137	**Site Finishes**	**90 days**	**Fri 26/05/01**	**Thu 26/09/03**
138	Site Fine Grading	10 days	Fri 26/05/01	Thu 26/05/14
139	Stone Base	10 days	Fri 26/05/08	Thu 26/05/21
140	Curb / Sidewalks	10 days	Fri 26/05/15	Thu 26/05/28
141	Binder Course Asphalt - Area 1	5 days	Fri 26/05/29	Thu 26/06/04
142	Binder Course Asphalt - Area 2	5 days	Fri 26/06/05	Thu 26/06/11
143	Landscaping - Area 1	10 days	Fri 26/06/12	Thu 26/06/25
144	Landscaping - Area 2	10 days	Fri 26/06/26	Thu 26/07/09
145	Final Pavement	10 days	Fri 26/07/10	Thu 26/07/23
146	Line Marking/Signage	5 days	Fri 26/07/24	Thu 26/07/30
147	As-Builts Complete & Submitted to AHJ	5 days	Fri 26/07/31	Thu 26/08/06
148	As-Built/City Review	20 days	Fri 26/08/07	Thu 26/09/03
149	**Interior Upfit**	**78 days**	**Wed 26/06/24**	**Fri 26/10/09**
150	1st Floor - Janus Unit Install	15 days	Wed 26/06/24	Tue 26/07/14
151	2nd Floor - Janus Unit Install	15 days	Wed 26/08/05	Tue 26/08/25
152	Bldg B Janus Install	5 days	Wed 26/08/26	Tue 26/09/01
153	Bldg C Janus Install	5 days	Wed 26/09/02	Tue 26/09/08
154	Bldg D Janus Install	5 days	Wed 26/09/09	Tue 26/09/15
155	Drywall Hanging	5 days	Wed 26/06/24	Tue 26/06/30
156	Drywall Finishing	10 days	Wed 26/06/24	Tue 26/07/07
157	Paint	5 days	Wed 26/07/08	Tue 26/07/14
158	Millwork	5 days	Tue 26/07/14	Mon 26/07/20
159	Floor Sealer - 2nd Floor	5 days	Tue 26/07/21	Mon 26/07/27
160	Floor Sealer / Polish - 1st Floor and drive ups	15 days	Tue 26/07/28	Mon 26/08/17
161	**Closeout**	**38 days**	**Wed 26/08/19**	**Fri 26/10/09**
162	Final Clean - Bldg A	8 days	Wed 26/09/02	Fri 26/09/11
163	Final Clean - Bldg B	5 days	Mon 26/09/14	Fri 26/09/18
164	Final Clean - Bldg C and D	5 days	Mon 26/09/21	Fri 26/09/25
165	MEP Final Inspections	10 days	Wed 26/08/19	Tue 26/09/01
166	Building Final Inspections	5 days	Wed 26/09/02	Tue 26/09/08
167	Weather Days Included (20 Days)	20 days	Mon 26/09/14	Fri 26/10/09
168	**Substantial Completion**	**0 days**	**Fri 26/10/09**	**Fri 26/10/09**
169	Substantial Completion	0 days	Fri 26/10/09	Fri 26/10/09
