ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
1			**Public Storage Selma, NC**	**263 days**	**Mon 25/10/06**	**Fri 26/10/09**		**4%**
2	✓		Award Contract	0 days	Mon 25/10/06	Mon 25/10/06		100%
3	✓		**Mobilization**	**6 days**	**Mon 25/12/01**	**Mon 25/12/08**		**100%**
4	✓		Mobilization (Site Fence, Layout, Barricades, Etc.)	1 day	Mon 26/01/05	Mon 26/01/05	2SS+63 days	100%
5	✓		SWPPP	5 days	Mon 25/12/15	Fri 25/12/19	4FS-16 days	100%
6			**Demo/Site Work**	**84 days**	**Mon 26/01/05**	**Thu 26/04/30**	**5FS+10 days**	**26%**
7			Clearing and Grubbing	10 days	Mon 26/01/05	Fri 26/01/16	5FS-6 days	90%
8	✓		Dewatering	5 days	Mon 26/01/19	Fri 26/01/23	7	100%
9			Rough Grading	18 days	Mon 26/01/19	Wed 26/02/11	8SS	50%
10			Storm System	21 days	Thu 26/02/12	Thu 26/03/12	9	0%
11			Sanitary Sewer	5 days	Fri 26/03/13	Thu 26/03/19	10	0%
12			Water	10 days	Fri 26/03/20	Thu 26/04/02	11	0%
13			Site Electrical	10 days	Fri 26/04/03	Thu 26/04/16	12	0%
14			Building Tie In	10 days	Fri 26/04/17	Thu 26/04/30	12;13	0%
15			**Building A**	**144 days**	**Thu 26/02/05**	**Tue 26/08/25**		**2%**
16			**Structure**	**104 days**	**Thu 26/02/05**	**Tue 26/06/30**		**4%**
17			**First Floor**	**64 days**	**Thu 26/02/05**	**Tue 26/05/05**		**6%**
18	✓		Weather Delay(Snow & Ice)	5 days	Thu 26/02/05	Wed 26/02/11	9FS-5 days	100%
19			Building Pad Delivery (Bldg A)	5 days	Thu 26/02/12	Wed 26/02/18	9FS-5 days;18	40%
20			Elevator Pit - Excavate	5 days	Thu 26/02/19	Wed 26/02/25	19	0%
21			Elevator Pit - Form and Pour	10 days	Thu 26/02/26	Wed 26/03/11	20	0%
22			FRP Foundations / Foundation CMU - Area 1	7 days	Thu 26/02/19	Fri 26/02/27	19	0%
23			Concrete Retaining Walls	10 days	Mon 26/03/02	Fri 26/03/13	22	0%
24			FRP Foundations/Foundation Area 2	7 days	Mon 26/03/16	Tue 26/03/24	23	0%
25			Under Slab MEP	10 days	Wed 26/03/11	Tue 26/03/24	24FS-10 days	0%
26			Slab #1 Prep / Pour (North Half)	10 days	Wed 26/03/18	Tue 26/03/31	25FS-5 days;2	0%
27			CMU shafts	15 days	Wed 26/04/01	Tue 26/04/21	26	0%
28			Slab #2 Prep / Pour (South Half)	10 days	Wed 26/04/01	Tue 26/04/14	26	0%
29			Janus Framing System (North Half)	15 days	Wed 26/04/01	Tue 26/04/21	26	0%
30			Janus Framing System (South Half)	10 days	Wed 26/04/22	Tue 26/05/05	29	0%
31			**Second Floor**	**40 days**	**Wed 26/04/22**	**Tue 26/06/16**		**0%**
32			Elevated Slab #1 (North Half) Prep/Pour	5 days	Wed 26/04/22	Tue 26/04/28	30FS-10 days	0%
33			Elevated Slab #2 (South Half) Prep/Pour	5 days	Wed 26/05/06	Tue 26/05/12	30;32	0%
34			Janus Framing System (North Half)	15 days	Wed 26/05/06	Tue 26/05/26	32;30	0%

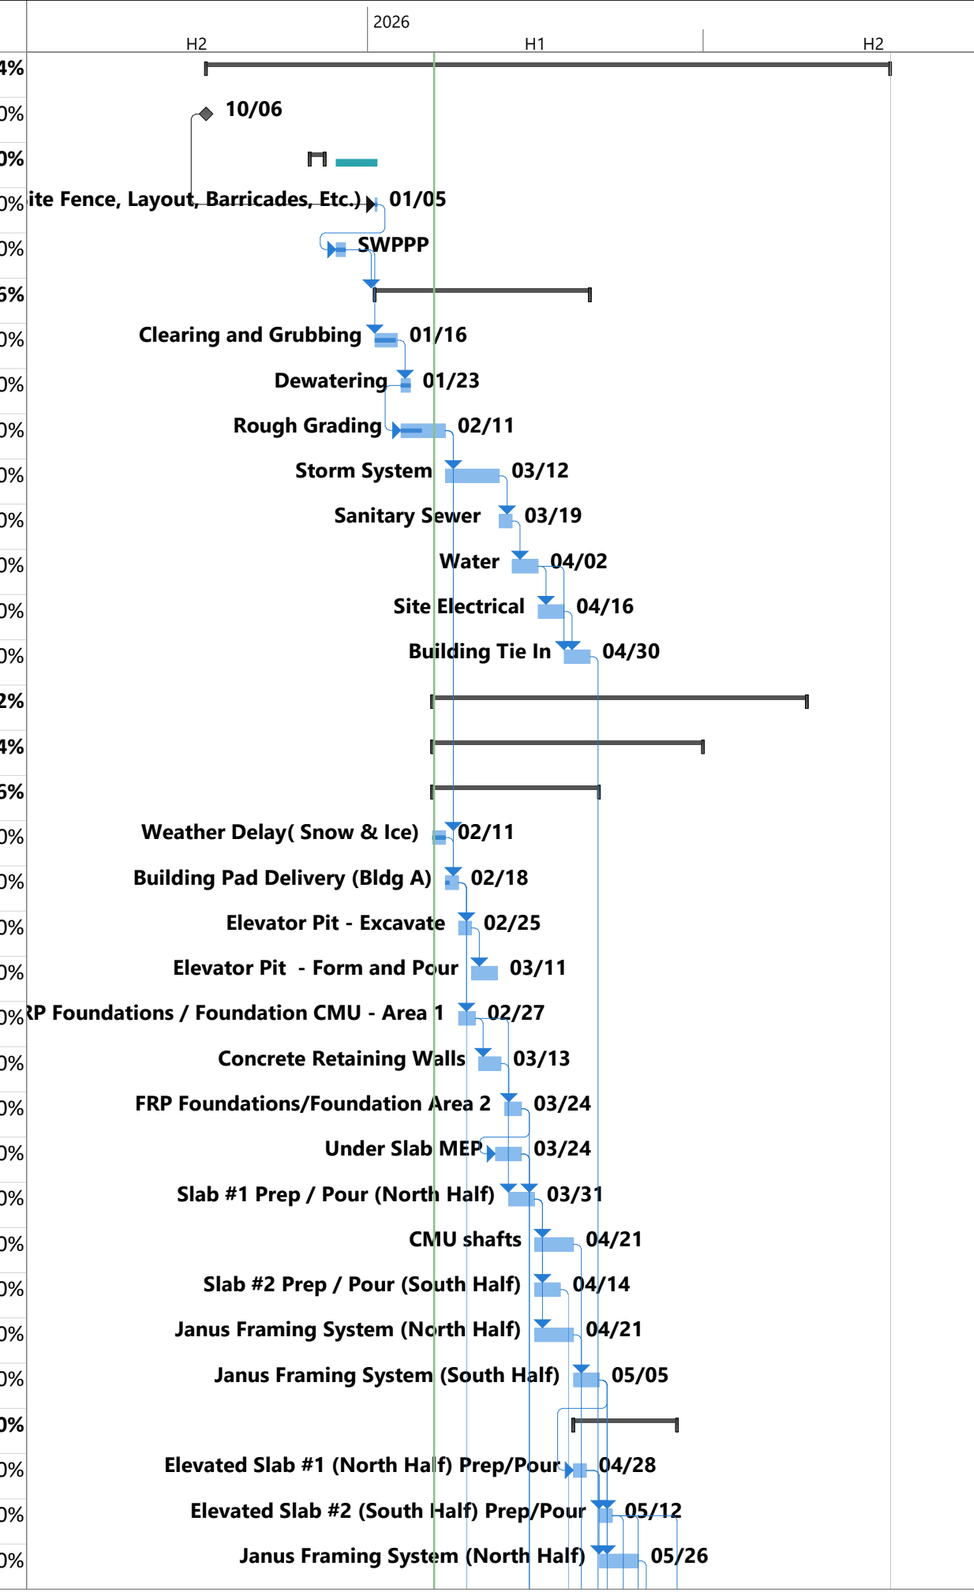

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
35		Janus Framing System (South Half)	10 days	Wed 26/05/27	Tue 26/06/09	34;33	0%
36		Roof Decking	5 days	Wed 26/06/10	Tue 26/06/16	35	0%
37		**Stairs**	**20 days**	**Tue 26/05/19**	**Mon 26/06/15**		**0%**
38		Stair #1	10 days	Tue 26/05/19	Mon 26/06/01	33FS+4 days	0%
39		Stair #2	10 days	Tue 26/06/02	Mon 26/06/15	38	0%
40		**Roof**	**10 days**	**Wed 26/06/17**	**Tue 26/06/30**		**0%**
41		Metal Roofing	10 days	Wed 26/06/17	Tue 26/06/30	36	0%
42		**Framing and MEP**	**80 days**	**Wed 26/05/06**	**Tue 26/08/25**		**0%**
43		**First Floor**	**65 days**	**Wed 26/05/06**	**Tue 26/08/04**		**0%**
44		Interior Framing	5 days	Wed 26/05/06	Tue 26/05/12	30	0%
45		1st Floor MEP Rough-In Area 1	20 days	Wed 26/05/13	Tue 26/06/09	44	0%
46		1st Floor MEP Rough-In Area 2	15 days	Wed 26/06/10	Tue 26/06/30	45	0%
47		1st Floor MEP Trim Out Area 1	10 days	Wed 26/07/15	Tue 26/07/28	157;45	0%
48		1st Floor MEP Trim Out Area 2	5 days	Wed 26/07/29	Tue 26/08/04	47	0%
49		**Second Floor**	**50 days**	**Wed 26/06/17**	**Tue 26/08/25**		**0%**
50		Interior Framing	5 days	Wed 26/06/17	Tue 26/06/23	33;36;82;108	0%
51		2nd Floor MEP Rough-In Area 2	15 days	Wed 26/07/01	Tue 26/07/21	45;50;46;88;1	0%
52		2nd Floor MEP Rough-In Area 2	15 days	Wed 26/07/22	Tue 26/08/11	51	0%
53		2nd Floor MEP Trim Out Area 1	10 days	Wed 26/08/05	Tue 26/08/18	48	0%
54		2nd Floor MEP Trim Out Area 2	5 days	Wed 26/08/19	Tue 26/08/25	53	0%
55		**Elevator**	**30 days**	**Mon 26/07/13**	**Mon 26/08/24**		**0%**
56		Delivery	0 days	Mon 26/07/13	Mon 26/07/13	41FS+9 days;	0%
57		Elevator 1 - First Floor	5 days	Tue 26/07/14	Mon 26/07/20	56SS	0%
58		Elevator 1 - Second Floor	5 days	Tue 26/07/21	Mon 26/07/27	57	0%
59		Elevator 2 - First Floor	5 days	Tue 26/07/28	Mon 26/08/03	58	0%
60		Elevator 2 - Second Floor	5 days	Tue 26/08/04	Mon 26/08/10	59	0%
61		Infill Doors	5 days	Tue 26/08/04	Mon 26/08/10	60FS-5 days	0%
62		Test / Adjust	5 days	Tue 26/08/11	Mon 26/08/17	61	0%
63		State Inspection	5 days	Tue 26/08/18	Mon 26/08/24	62	0%
64		**Exterior Finishes**	**50 days**	**Wed 26/05/27**	**Tue 26/08/04**		**0%**
65		Masonry Veneer	15 days	Wed 26/05/27	Tue 26/06/16	44;87	0%
66		Metal Panels Completion	15 days	Wed 26/06/17	Tue 26/07/07	65	0%
67		Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	Wed 26/07/01	Tue 26/07/14	41	0%
68		Automatic Entrance Door	5 days	Wed 26/06/17	Tue 26/06/23	65	0%

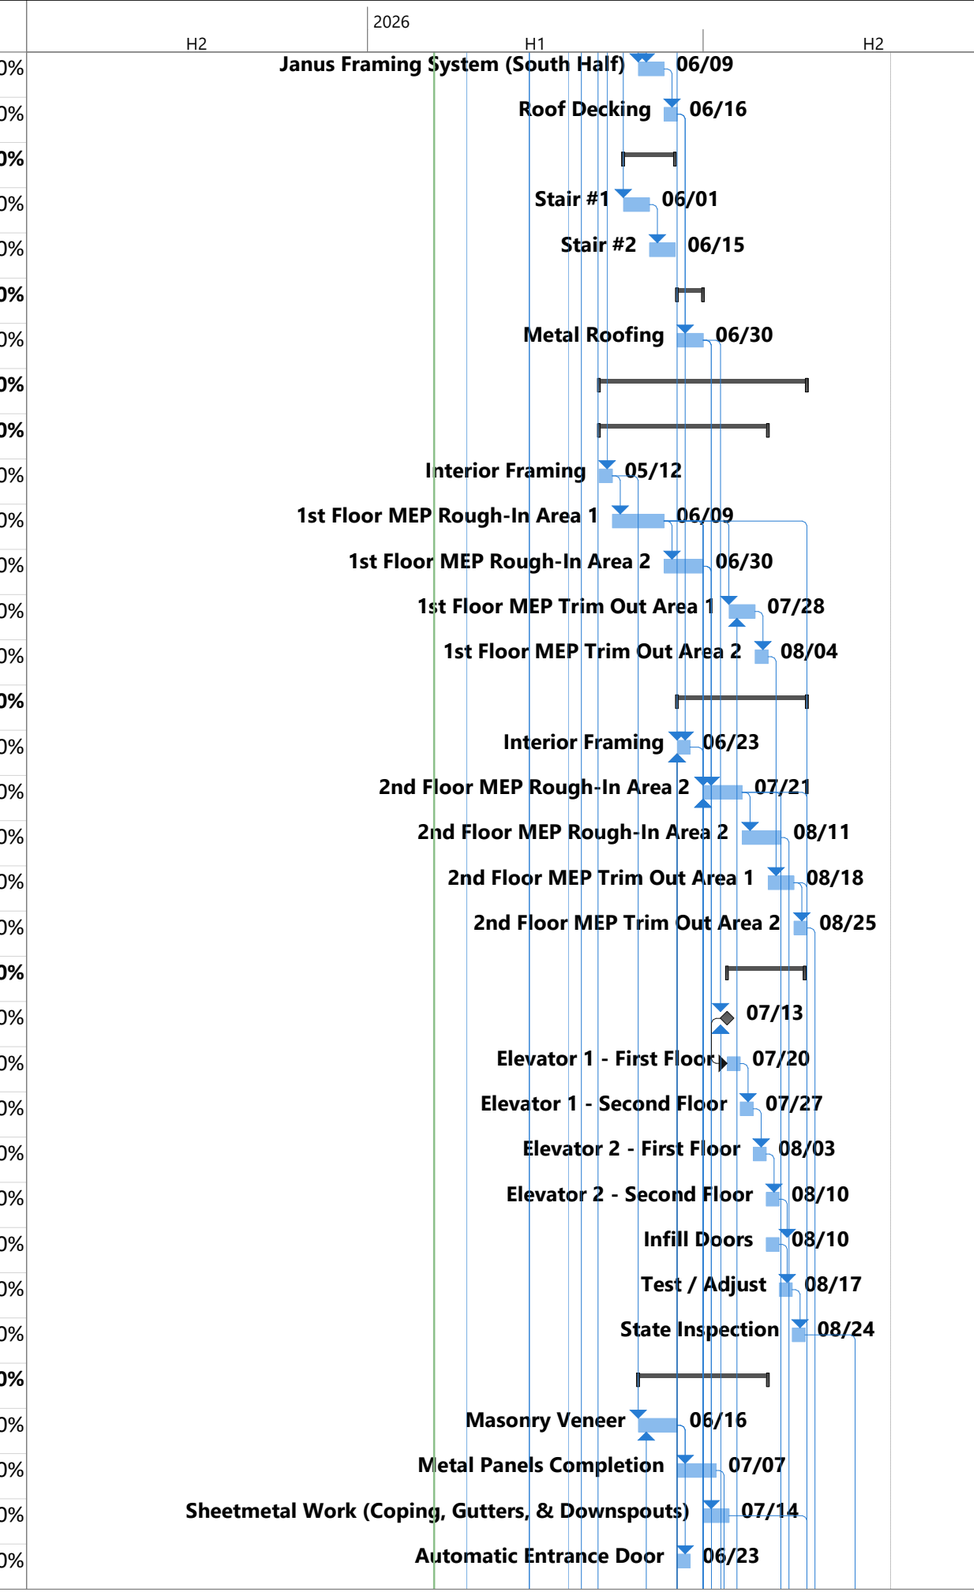

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
69		Exterior Paint	10 days	Wed 26/07/08	Tue 26/07/21	66	0%
70		Exterior Signage Install	10 days	Wed 26/07/22	Tue 26/08/04	69	0%
71		Canopy	10 days	Wed 26/07/22	Tue 26/08/04	70SS	0%
72		**Building B**	**99 days**	**Thu 26/02/19**	**Tue 26/07/07**		**0%**
73		**Structure**	**69 days**	**Thu 26/02/19**	**Tue 26/05/26**		**0%**
74		**First Floor**	**64 days**	**Thu 26/02/19**	**Tue 26/05/19**		**0%**
75		Building Pad Delivery (Bldg B)	5 days	Thu 26/02/19	Wed 26/02/25	19	0%
76		FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/02/26	Wed 26/03/04	75	0%
77		FRP Foundations/Foundation Area 2	5 days	Wed 26/03/25	Tue 26/03/31	24	0%
78		Under Slab MEP	5 days	Wed 26/03/25	Tue 26/03/31	25	0%
79		Slab Prep / Pour	5 days	Wed 26/04/15	Tue 26/04/21	28	0%
80		CMU Walls	10 days	Wed 26/04/22	Tue 26/05/05	27	0%
81		Janus Framing System	10 days	Wed 26/05/06	Tue 26/05/19	80	0%
82		Roof Decking	0 days	Tue 26/05/19	Tue 26/05/19	81	0%
83		**Roof**	**5 days**	**Wed 26/05/20**	**Tue 26/05/26**		**0%**
84		Metal Roofing	5 days	Wed 26/05/20	Tue 26/05/26	82	0%
85		**Framing and MEP**	**25 days**	**Wed 26/05/20**	**Tue 26/06/23**		**0%**
86		**First Floor**	**25 days**	**Wed 26/05/20**	**Tue 26/06/23**		**0%**
87		Interior Framing	5 days	Wed 26/05/20	Tue 26/05/26	81	0%
88		1st Floor MEP Rough-In Area 1	10 days	Wed 26/05/27	Tue 26/06/09	87	0%
89		Finishes	10 days	Wed 26/05/27	Tue 26/06/09	84;87	0%
90		1st Floor MEP Trim Out Area 1	10 days	Wed 26/06/10	Tue 26/06/23	89	0%
91		**Exterior Finishes**	**35 days**	**Wed 26/05/20**	**Tue 26/07/07**		**0%**
92		Metal Panels Completion	15 days	Wed 26/05/20	Tue 26/06/09	82	0%
93		Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	Wed 26/06/10	Tue 26/06/23	92	0%
94		Automatic Entrance Door	5 days	Wed 26/06/10	Tue 26/06/16	92	0%
95		Exterior Paint	10 days	Wed 26/06/10	Tue 26/06/23	92	0%
96		Exterior Signage Install	10 days	Wed 26/06/24	Tue 26/07/07	95	0%
97		Canopy	10 days	Wed 26/06/24	Tue 26/07/07	96SS	0%
98		**Building C**	**99 days**	**Thu 26/02/26**	**Tue 26/07/14**		**0%**
99		**Structure**	**74 days**	**Thu 26/02/26**	**Tue 26/06/09**		**0%**
100		**First Floor**	**69 days**	**Thu 26/02/26**	**Tue 26/06/02**		**0%**
101		Building Pad Delivery (Bldg C)	5 days	Thu 26/02/26	Wed 26/03/04	75	0%
102		FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/03/05	Wed 26/03/11	101	0%

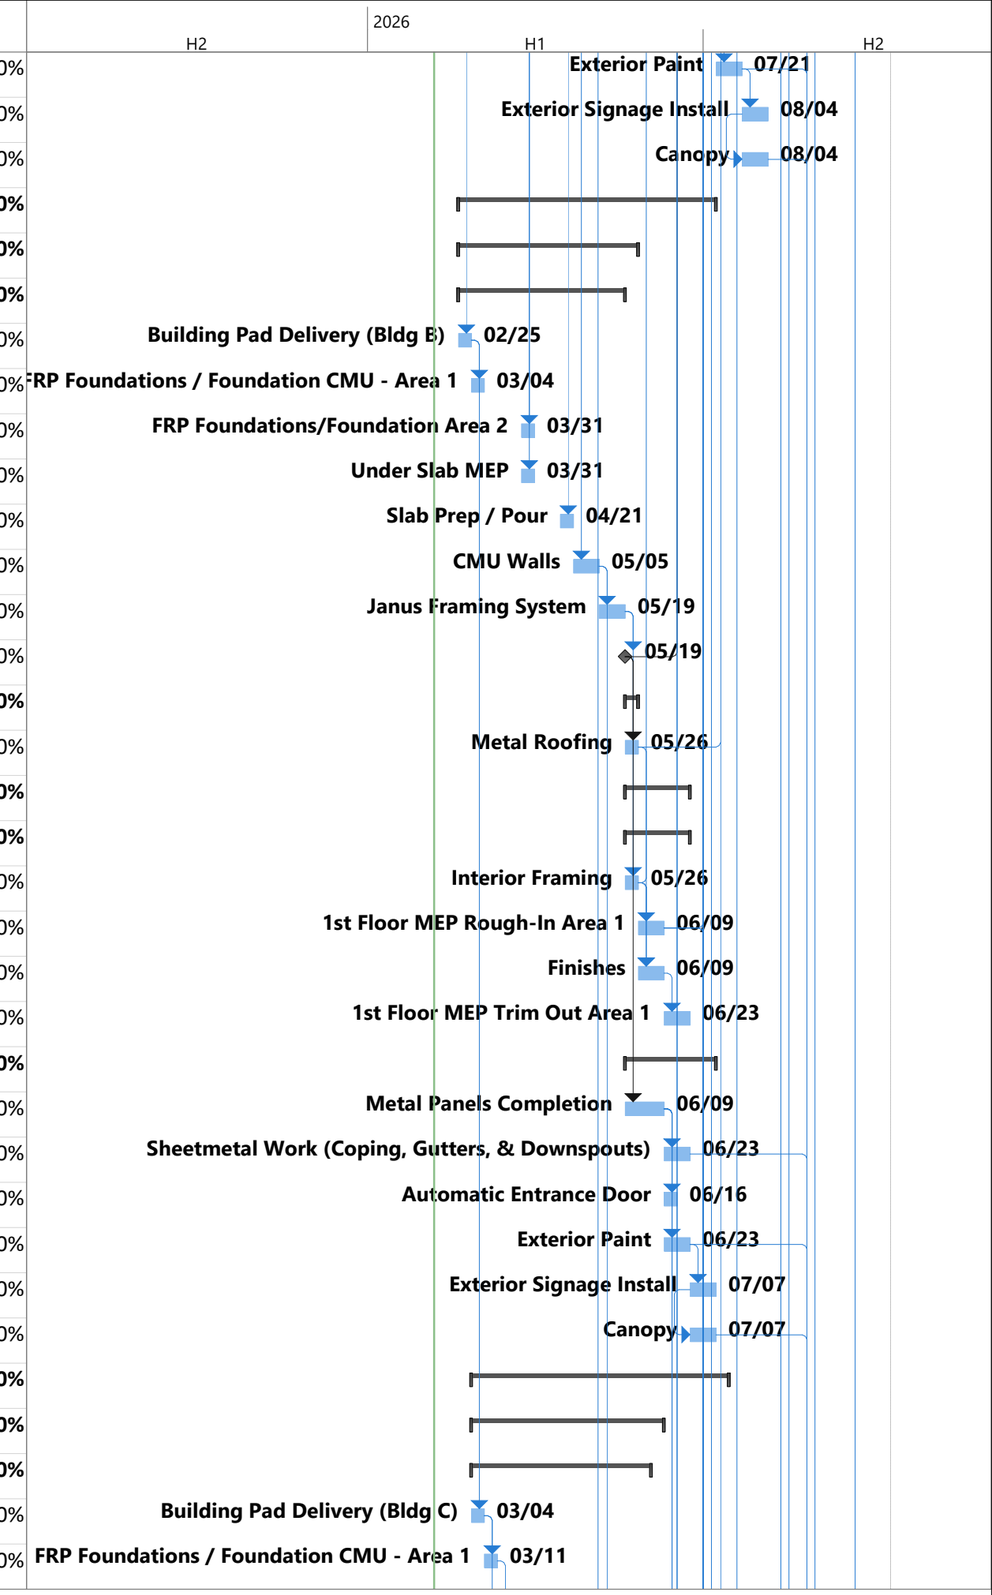

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
103		FRP Foundations/Foundation Area 2	5 days	Thu 26/03/12	Wed 26/03/18	102	0%
104		Under Slab MEP	5 days	Thu 26/03/19	Wed 26/03/25	103	0%
105		Slab Prep / Pour	5 days	Thu 26/03/26	Wed 26/04/01	104	0%
106		CMU Walls	10 days	Wed 26/05/06	Tue 26/05/19	105;80	0%
107		Janus Framing System	5 days	Wed 26/05/20	Tue 26/05/26	106	0%
108		Roof Decking	5 days	Wed 26/05/27	Tue 26/06/02	107	0%
109		**Roof**	**5 days**	**Wed 26/06/03**	**Tue 26/06/09**		**0%**
110		Metal Roofing	5 days	Wed 26/06/03	Tue 26/06/09	108	0%
111		**Framing and MEP**	**20 days**	**Wed 26/06/10**	**Tue 26/07/07**		**0%**
112		**First Floor**	**20 days**	**Wed 26/06/10**	**Tue 26/07/07**		**0%**
113		1st Floor MEP Rough-In Area 1	10 days	Wed 26/06/10	Tue 26/06/23	110	0%
114		1st Floor MEP Trim Out Area 1	10 days	Wed 26/06/24	Tue 26/07/07	113	0%
115		**Exterior Finishes**	**25 days**	**Wed 26/06/10**	**Tue 26/07/14**		**0%**
116		Metal Panels Completion	15 days	Wed 26/06/10	Tue 26/06/30	108;92	0%
117		Exterior Signage Install	10 days	Wed 26/07/01	Tue 26/07/14	116	0%
118		**Building D**	**94 days**	**Thu 26/03/05**	**Tue 26/07/14**		**0%**
119		**Structure**	**57 days**	**Thu 26/03/05**	**Fri 26/05/22**		**0%**
120		**First Floor**	**52 days**	**Thu 26/03/05**	**Fri 26/05/15**		**0%**
121		Building Pad Delivery (Bldg D)	5 days	Thu 26/03/05	Wed 26/03/11	101	0%
122		FRP Foundations / Foundation CMU - Area 1	5 days	Thu 26/03/19	Wed 26/03/25	121FS+5 days	0%
123		FRP Foundations/Foundation Area 2	5 days	Thu 26/03/26	Wed 26/04/01	122	0%
124		Under Slab MEP	5 days	Thu 26/04/02	Wed 26/04/08	123	0%
125		Slab Prep / Pour	5 days	Thu 26/04/09	Wed 26/04/15	124	0%
126		CMU Walls	10 days	Mon 26/04/20	Fri 26/05/01	124FS+7 days	0%
127		Janus Framing System	5 days	Mon 26/05/04	Fri 26/05/08	126	0%
128		Roof Decking	5 days	Mon 26/05/11	Fri 26/05/15	127	0%
129		**Roof**	**5 days**	**Mon 26/05/18**	**Fri 26/05/22**		**0%**
130		Metal Roofing	5 days	Mon 26/05/18	Fri 26/05/22	128	0%
131		**Framing and MEP**	**20 days**	**Mon 26/05/25**	**Fri 26/06/19**		**0%**
132		**First Floor**	**20 days**	**Mon 26/05/25**	**Fri 26/06/19**		**0%**
133		1st Floor MEP Rough-In Area 1	10 days	Mon 26/05/25	Fri 26/06/05	130	0%
134		1st Floor MEP Trim Out Area 1	10 days	Mon 26/06/08	Fri 26/06/19	133	0%
135		**Exterior Finishes**	**25 days**	**Wed 26/06/10**	**Tue 26/07/14**		**0%**
136		Metal Panels Completion	15 days	Wed 26/06/10	Tue 26/06/30	128;92	0%

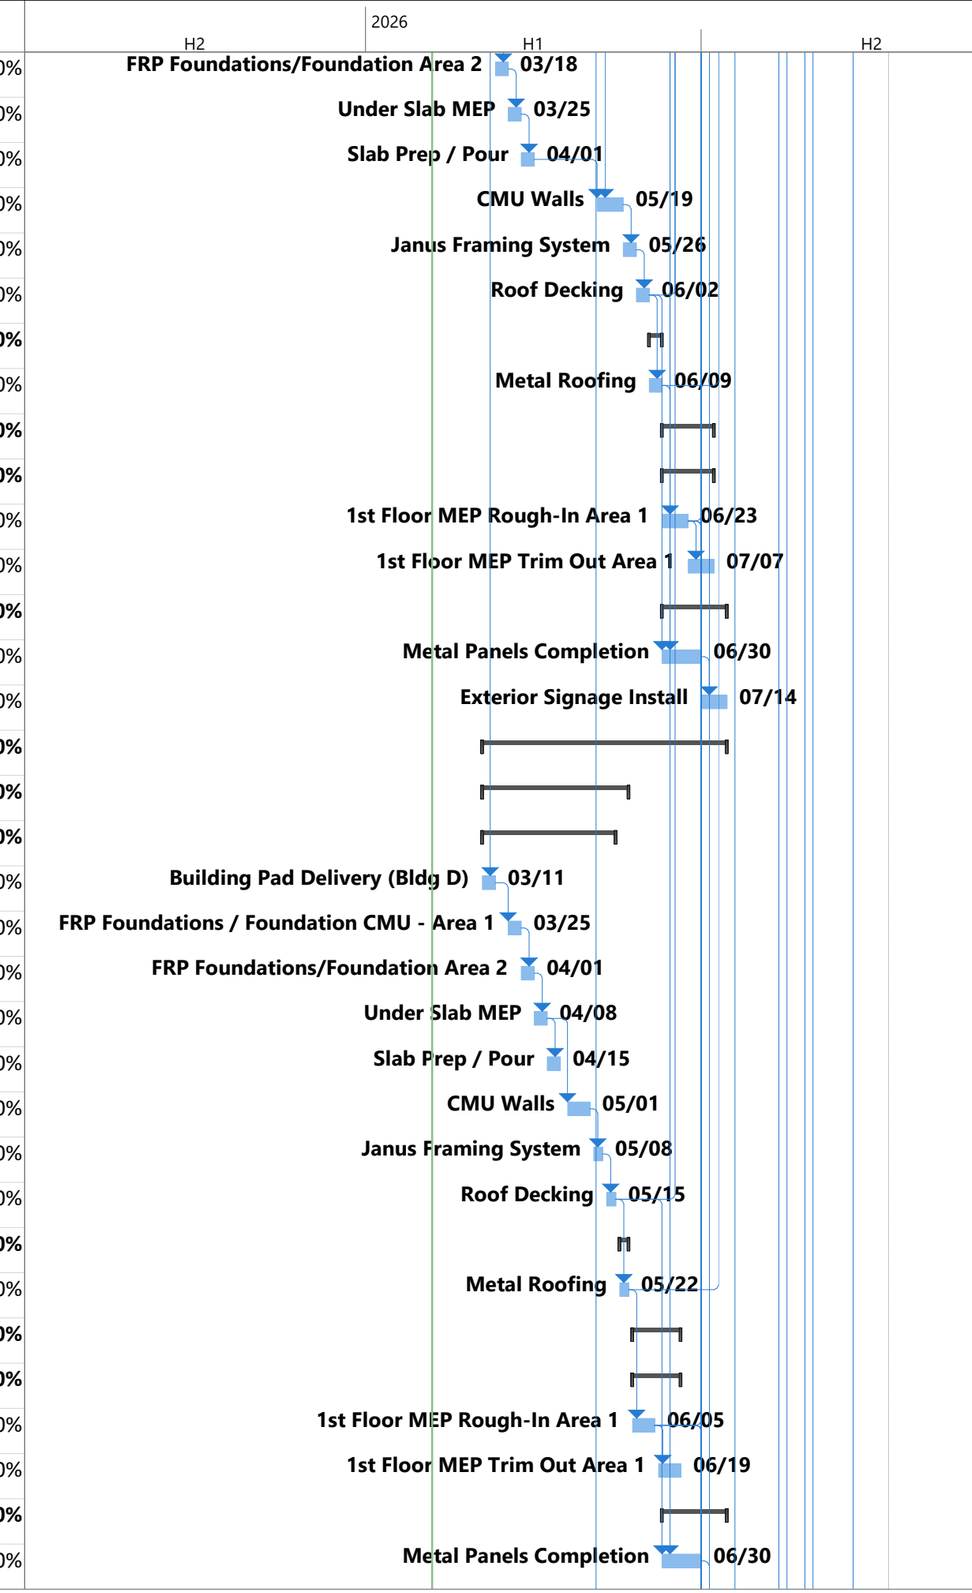

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
137		Exterior Signage Install	10 days	Wed 26/07/01	Tue 26/07/14	136	0%
138		**Site Finishes**	**90 days**	**Fri 26/05/01**	**Thu 26/09/03**		**0%**
139		Site Fine Grading	10 days	Fri 26/05/01	Thu 26/05/14	14	0%
140		Stone Base	10 days	Fri 26/05/08	Thu 26/05/21	139FS-5 days	0%
141		Curb / Sidewalks	10 days	Fri 26/05/15	Thu 26/05/28	140FS-5 days	0%
142		Binder Course Asphalt - Area 1	5 days	Fri 26/05/29	Thu 26/06/04	141	0%
143		Binder Course Asphalt - Area 2	5 days	Fri 26/06/05	Thu 26/06/11	142	0%
144		Landscaping - Area 1	10 days	Fri 26/06/12	Thu 26/06/25	143	0%
145		Landscaping - Area 2	10 days	Fri 26/06/26	Thu 26/07/09	144	0%
146		Final Pavement	10 days	Fri 26/07/10	Thu 26/07/23	145	0%
147		Line Marking/Signage	5 days	Fri 26/07/24	Thu 26/07/30	146	0%
148		As-Builts Complete & Submitted to AHJ	5 days	Fri 26/07/31	Thu 26/08/06	147	0%
149		As-Built/City Review	20 days	Fri 26/08/07	Thu 26/09/03	148	0%
150		**Interior Upfit**	**73 days**	**Wed 26/07/01**	**Fri 26/10/09**		**3%**
151		1st Floor - Janus Unit Install	15 days	Wed 26/07/01	Tue 26/07/21	45;46;88;113	0%
152		2nd Floor - Janus Unit Install	15 days	Wed 26/08/12	Tue 26/09/01	51;52;151	0%
153		Bldg B Janus Install	5 days	Wed 26/09/02	Tue 26/09/08	152	0%
154		Bldg C Janus Install	5 days	Wed 26/09/09	Tue 26/09/15	153	0%
155		Bldg D Janus Install	5 days	Wed 26/09/16	Tue 26/09/22	154	0%
156		Drywall Hanging	5 days	Wed 26/07/01	Tue 26/07/07	45;46;88;113	0%
157		Drywall Finishing	10 days	Wed 26/07/01	Tue 26/07/14	156FS-5 days	0%
158		Paint	5 days	Wed 26/07/15	Tue 26/07/21	157	0%
159		Millwork	5 days	Tue 26/07/21	Mon 26/07/27	158FS-1 day	0%
160		Floor Sealer - 2nd Floor	5 days	Tue 26/07/28	Mon 26/08/03	159	0%
161		Floor Sealer / Polish - 1st Floor and drive ups	15 days	Tue 26/08/04	Mon 26/08/24	160	0%
162		**Closeout**	**33 days**	**Wed 26/08/26**	**Fri 26/10/09**		**8%**
163		Final Clean - Bldg A	8 days	Wed 26/09/09	Fri 26/09/18	159;153	0%
164		Final Clean - Bldg B	5 days	Mon 26/09/21	Fri 26/09/25	163	0%
165		Final Clean - Bldg C and D	5 days	Mon 26/09/28	Fri 26/10/02	164	0%
166		MEP Final Inspections	10 days	Wed 26/08/26	Tue 26/09/08	67;71;69;147	0%
167		Building Final Inspections	5 days	Wed 26/09/09	Tue 26/09/15	166	0%
168		Weather Days Included (20 Days)	15 days	Mon 26/09/21	Fri 26/10/09	149;63;163;1	25%
169		**Substantial Completion**	**0 days**	**Fri 26/10/09**	**Fri 26/10/09**		**0%**
170		Substantial Completion	0 days	Fri 26/10/09	Fri 26/10/09	168FF	0%

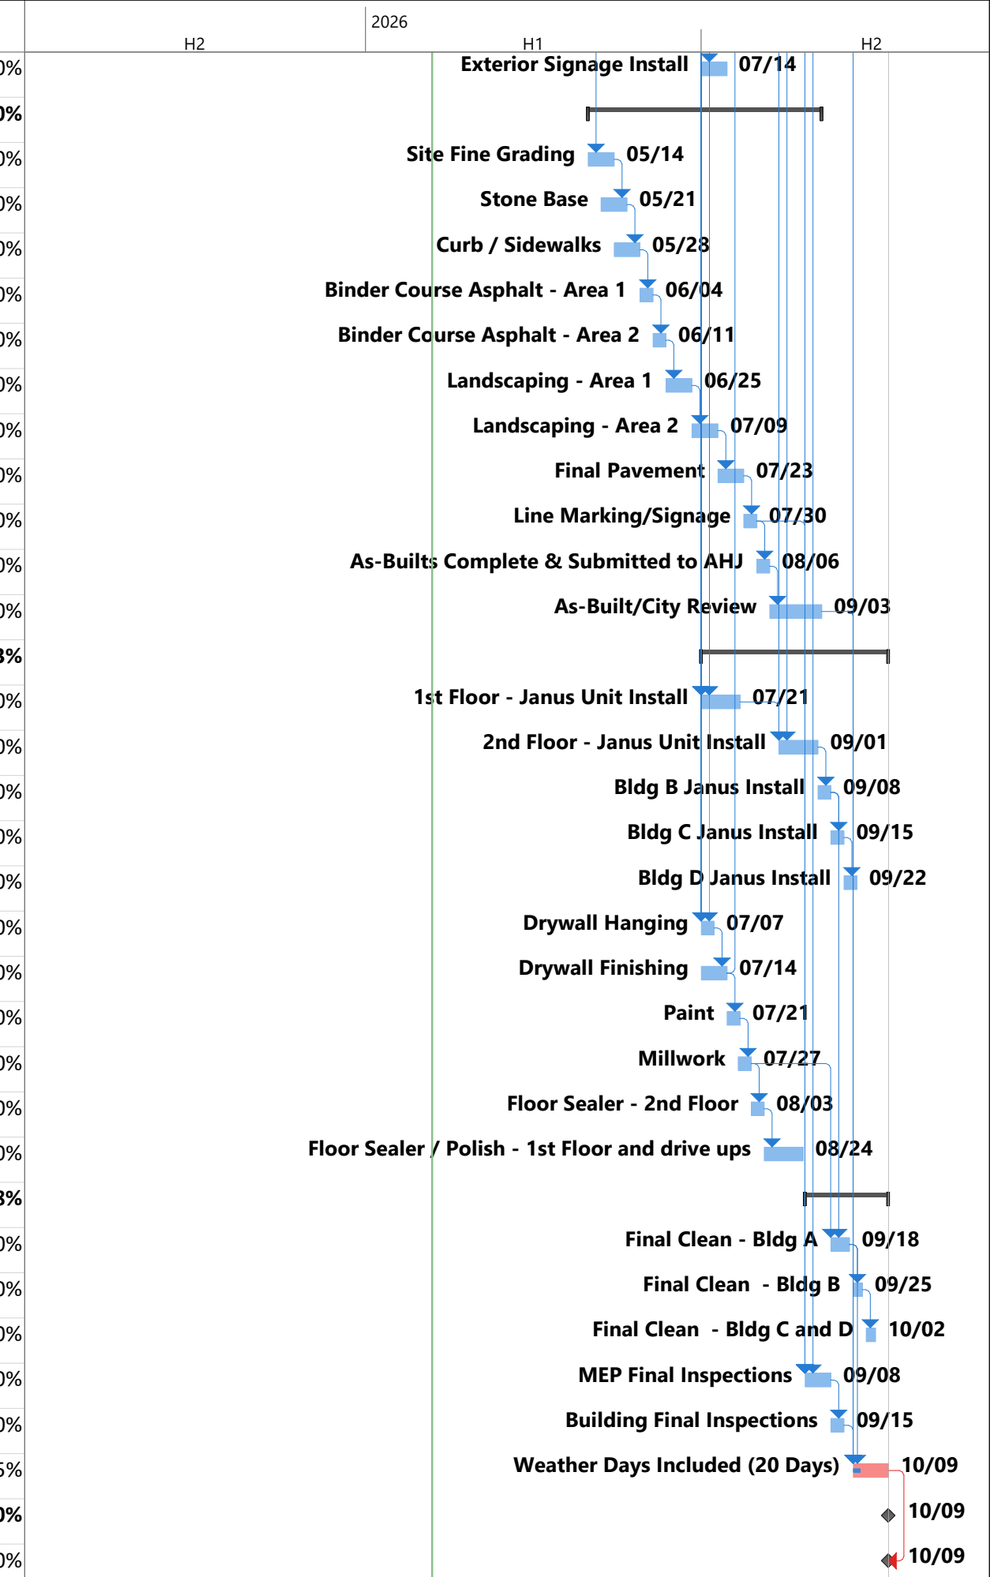

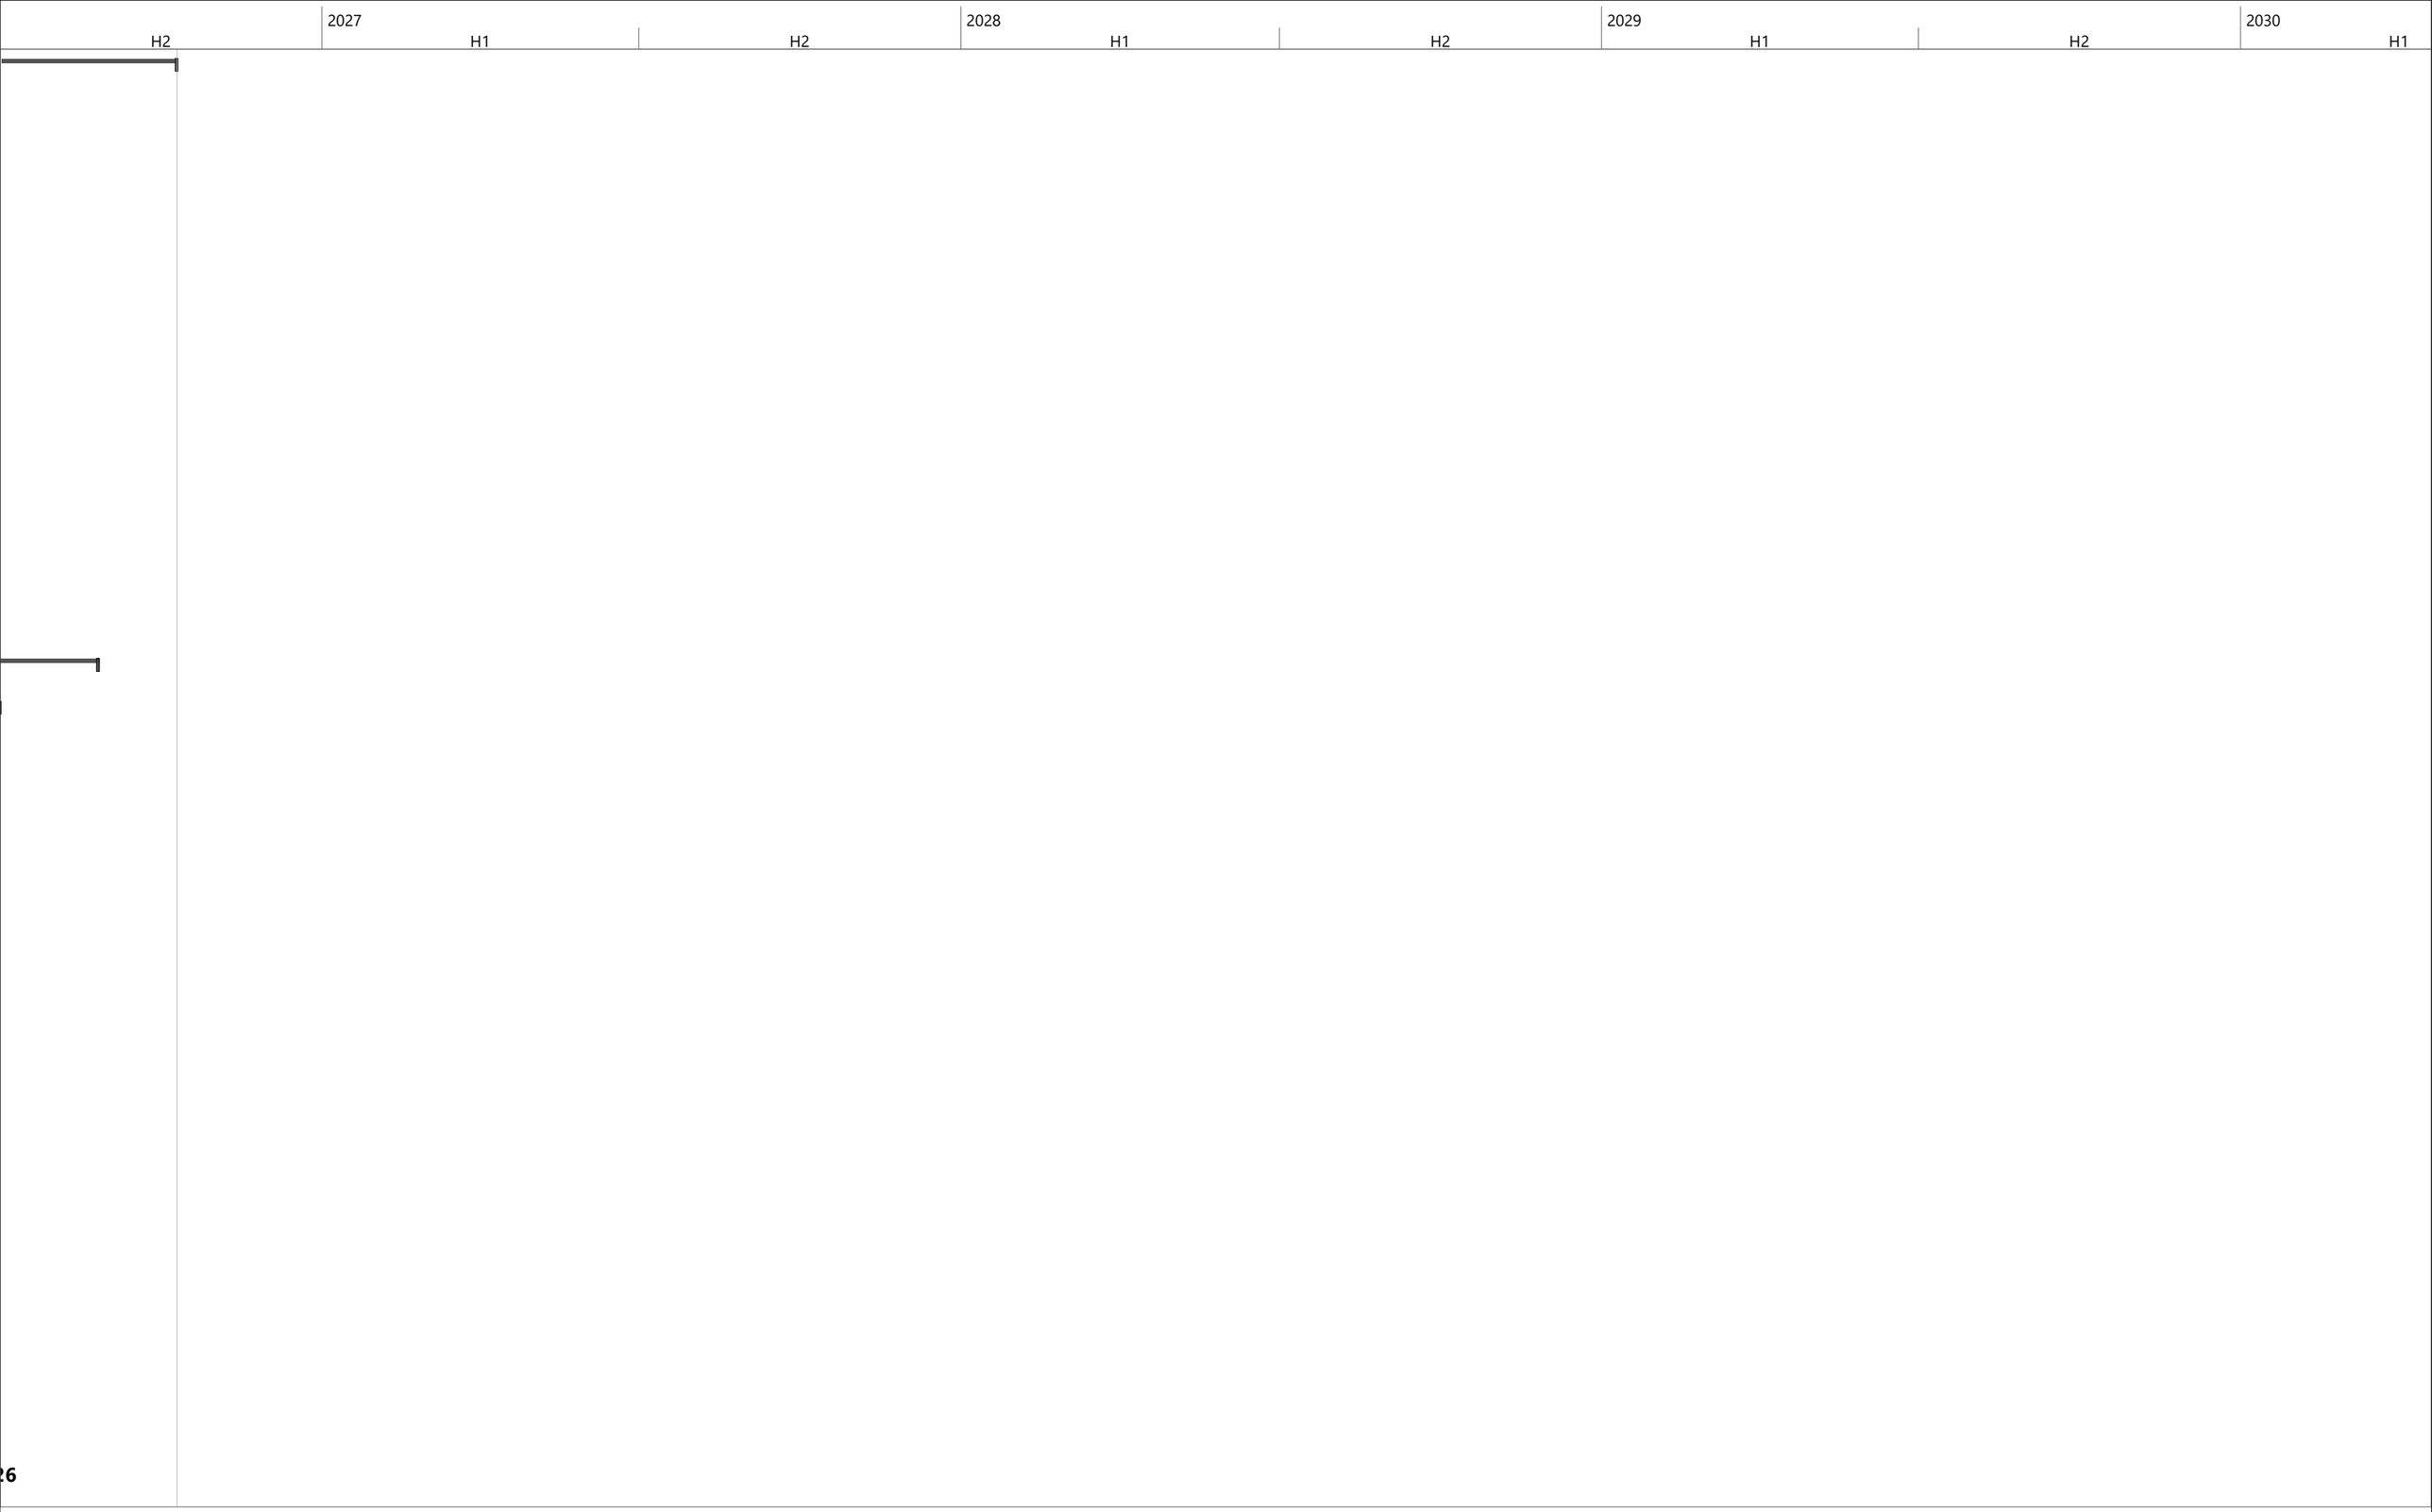
2027
2028
2029
2030
H2
H1
H2
H1
H2
H1
H2
H1
26

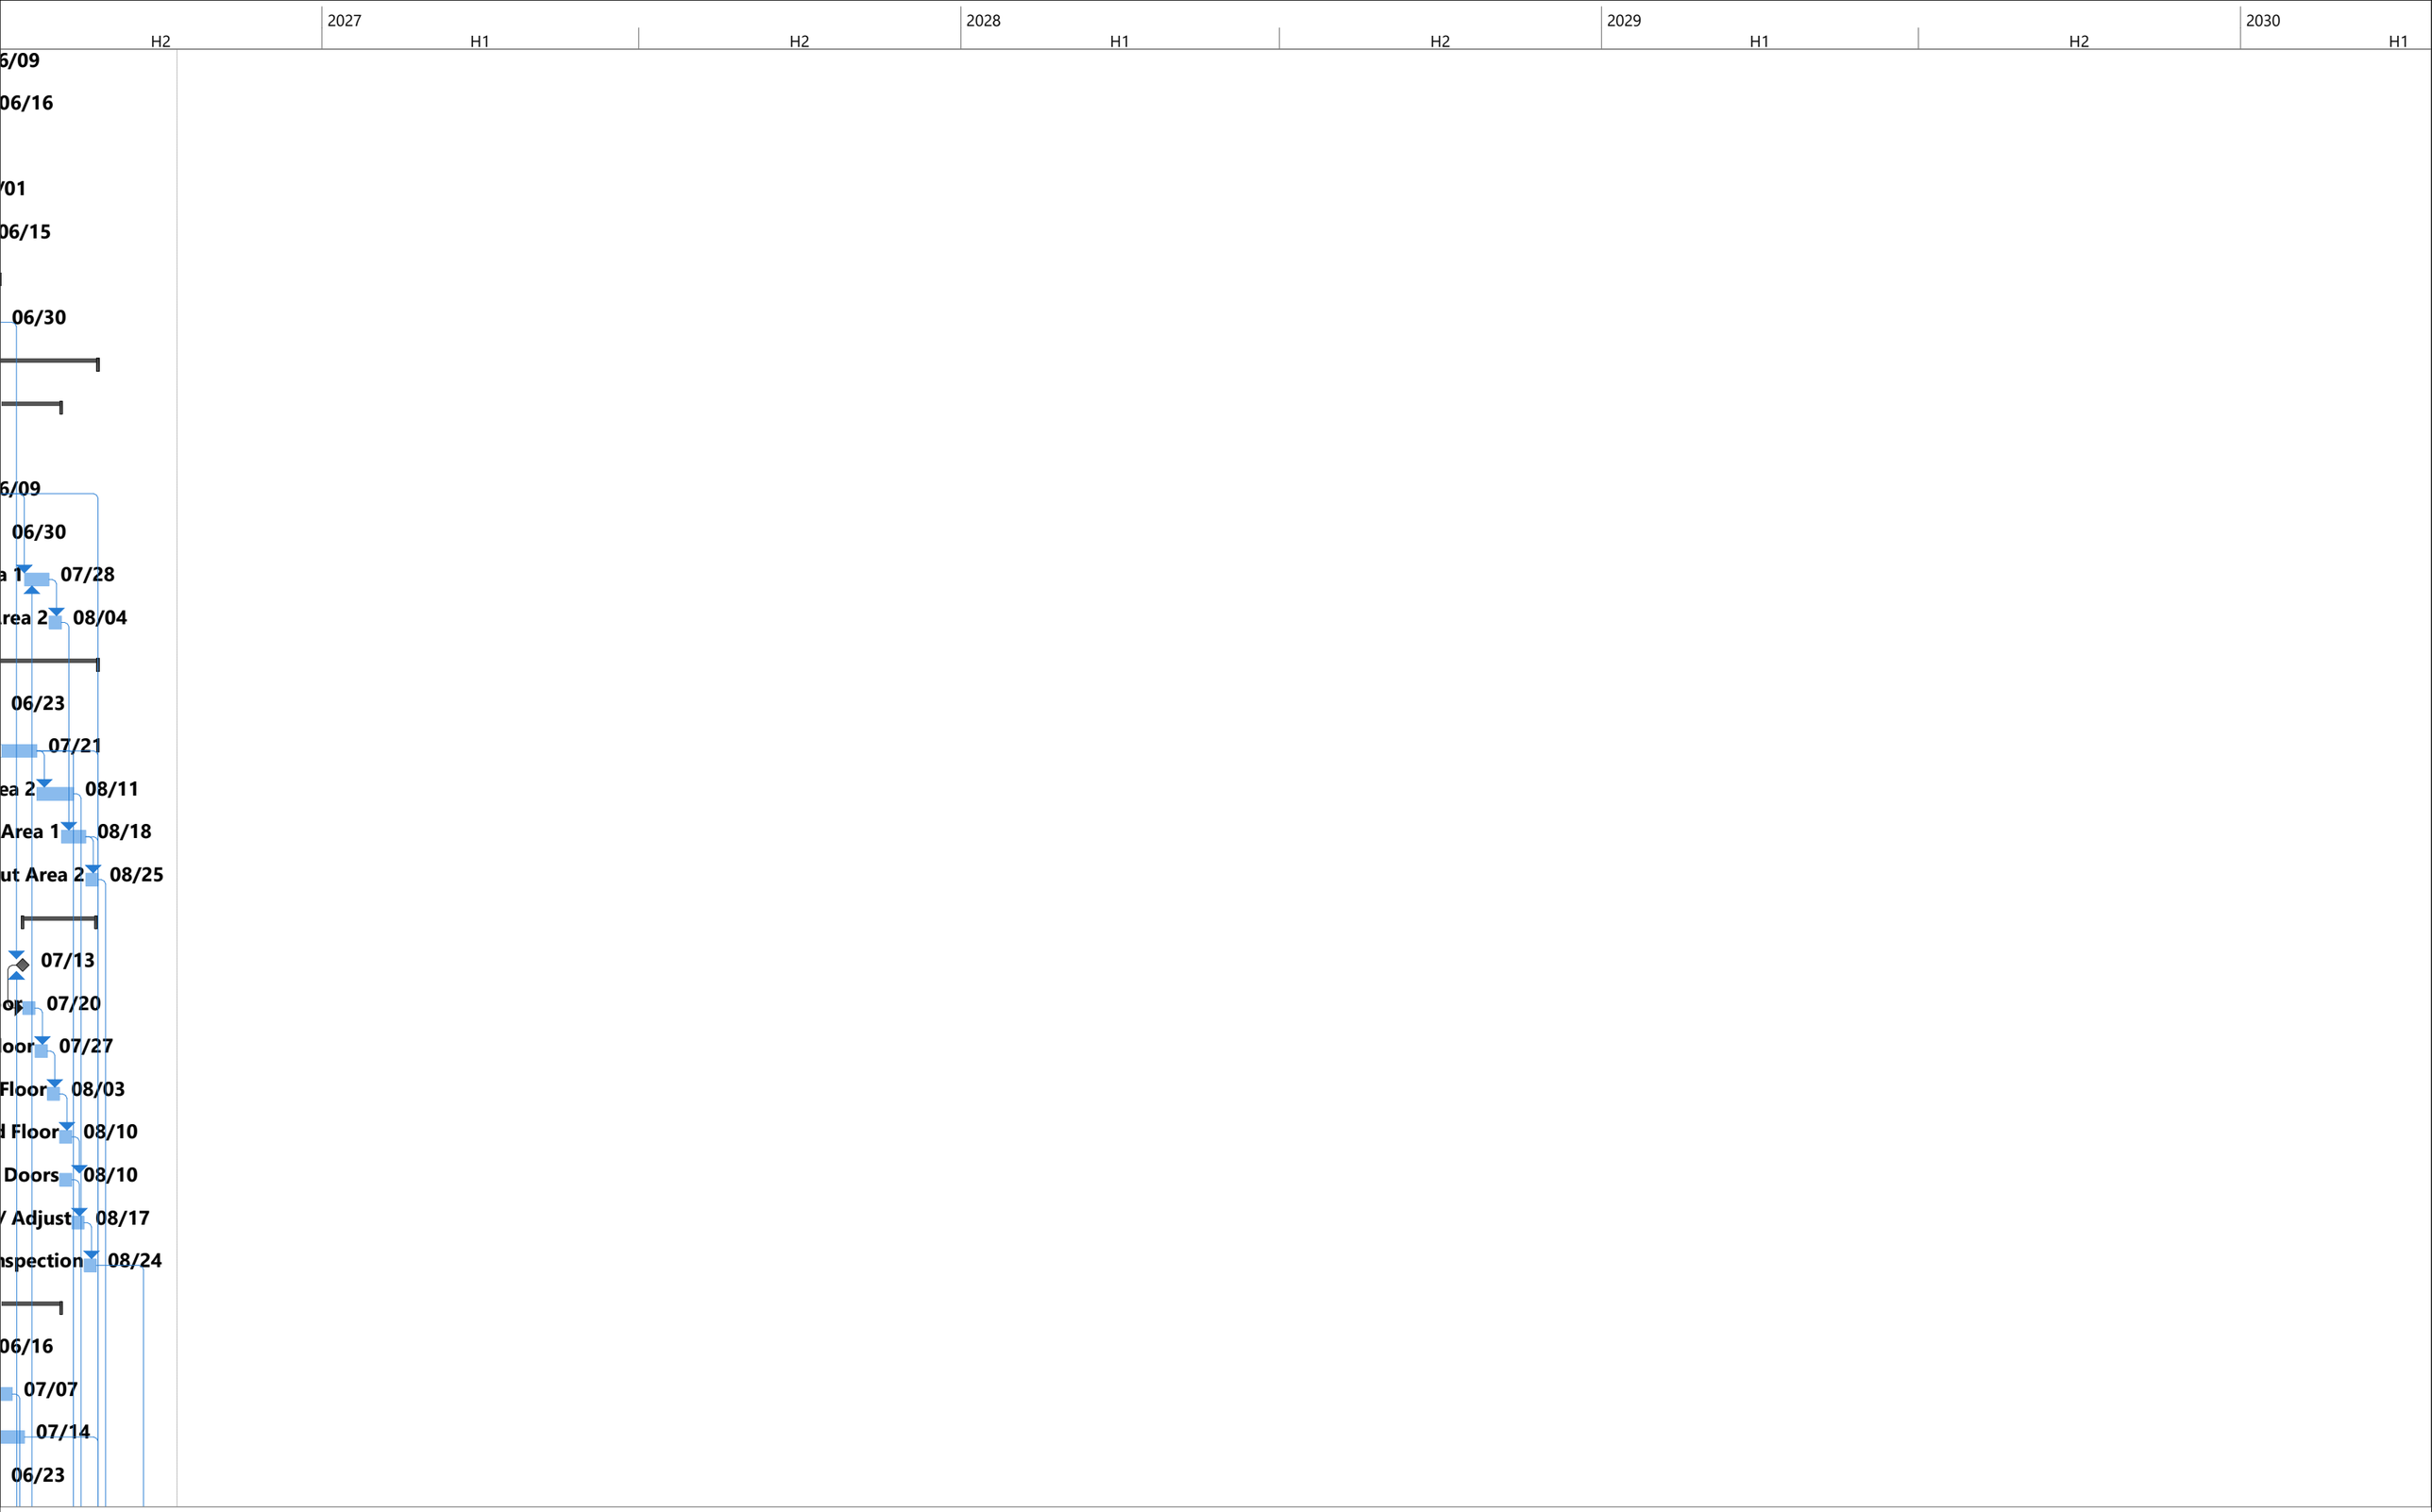
2027
2028
2029
2030
H2
H1
H2
H1
H2
H1
H2
H1
6/09
06/16
/01
06/15
06/30
6/09
06/30
a 1
07/28
rea 2
08/04
06/23
07/21
ea 2
08/11
Area 1
08/18
ut Area 2
08/25
07/13
or
07/20
oor
07/27
Floor
08/03
d Floor
08/10
Doors
08/10
/ Adjust
08/17
nspection
08/24
06/16
07/07
07/14
06/23

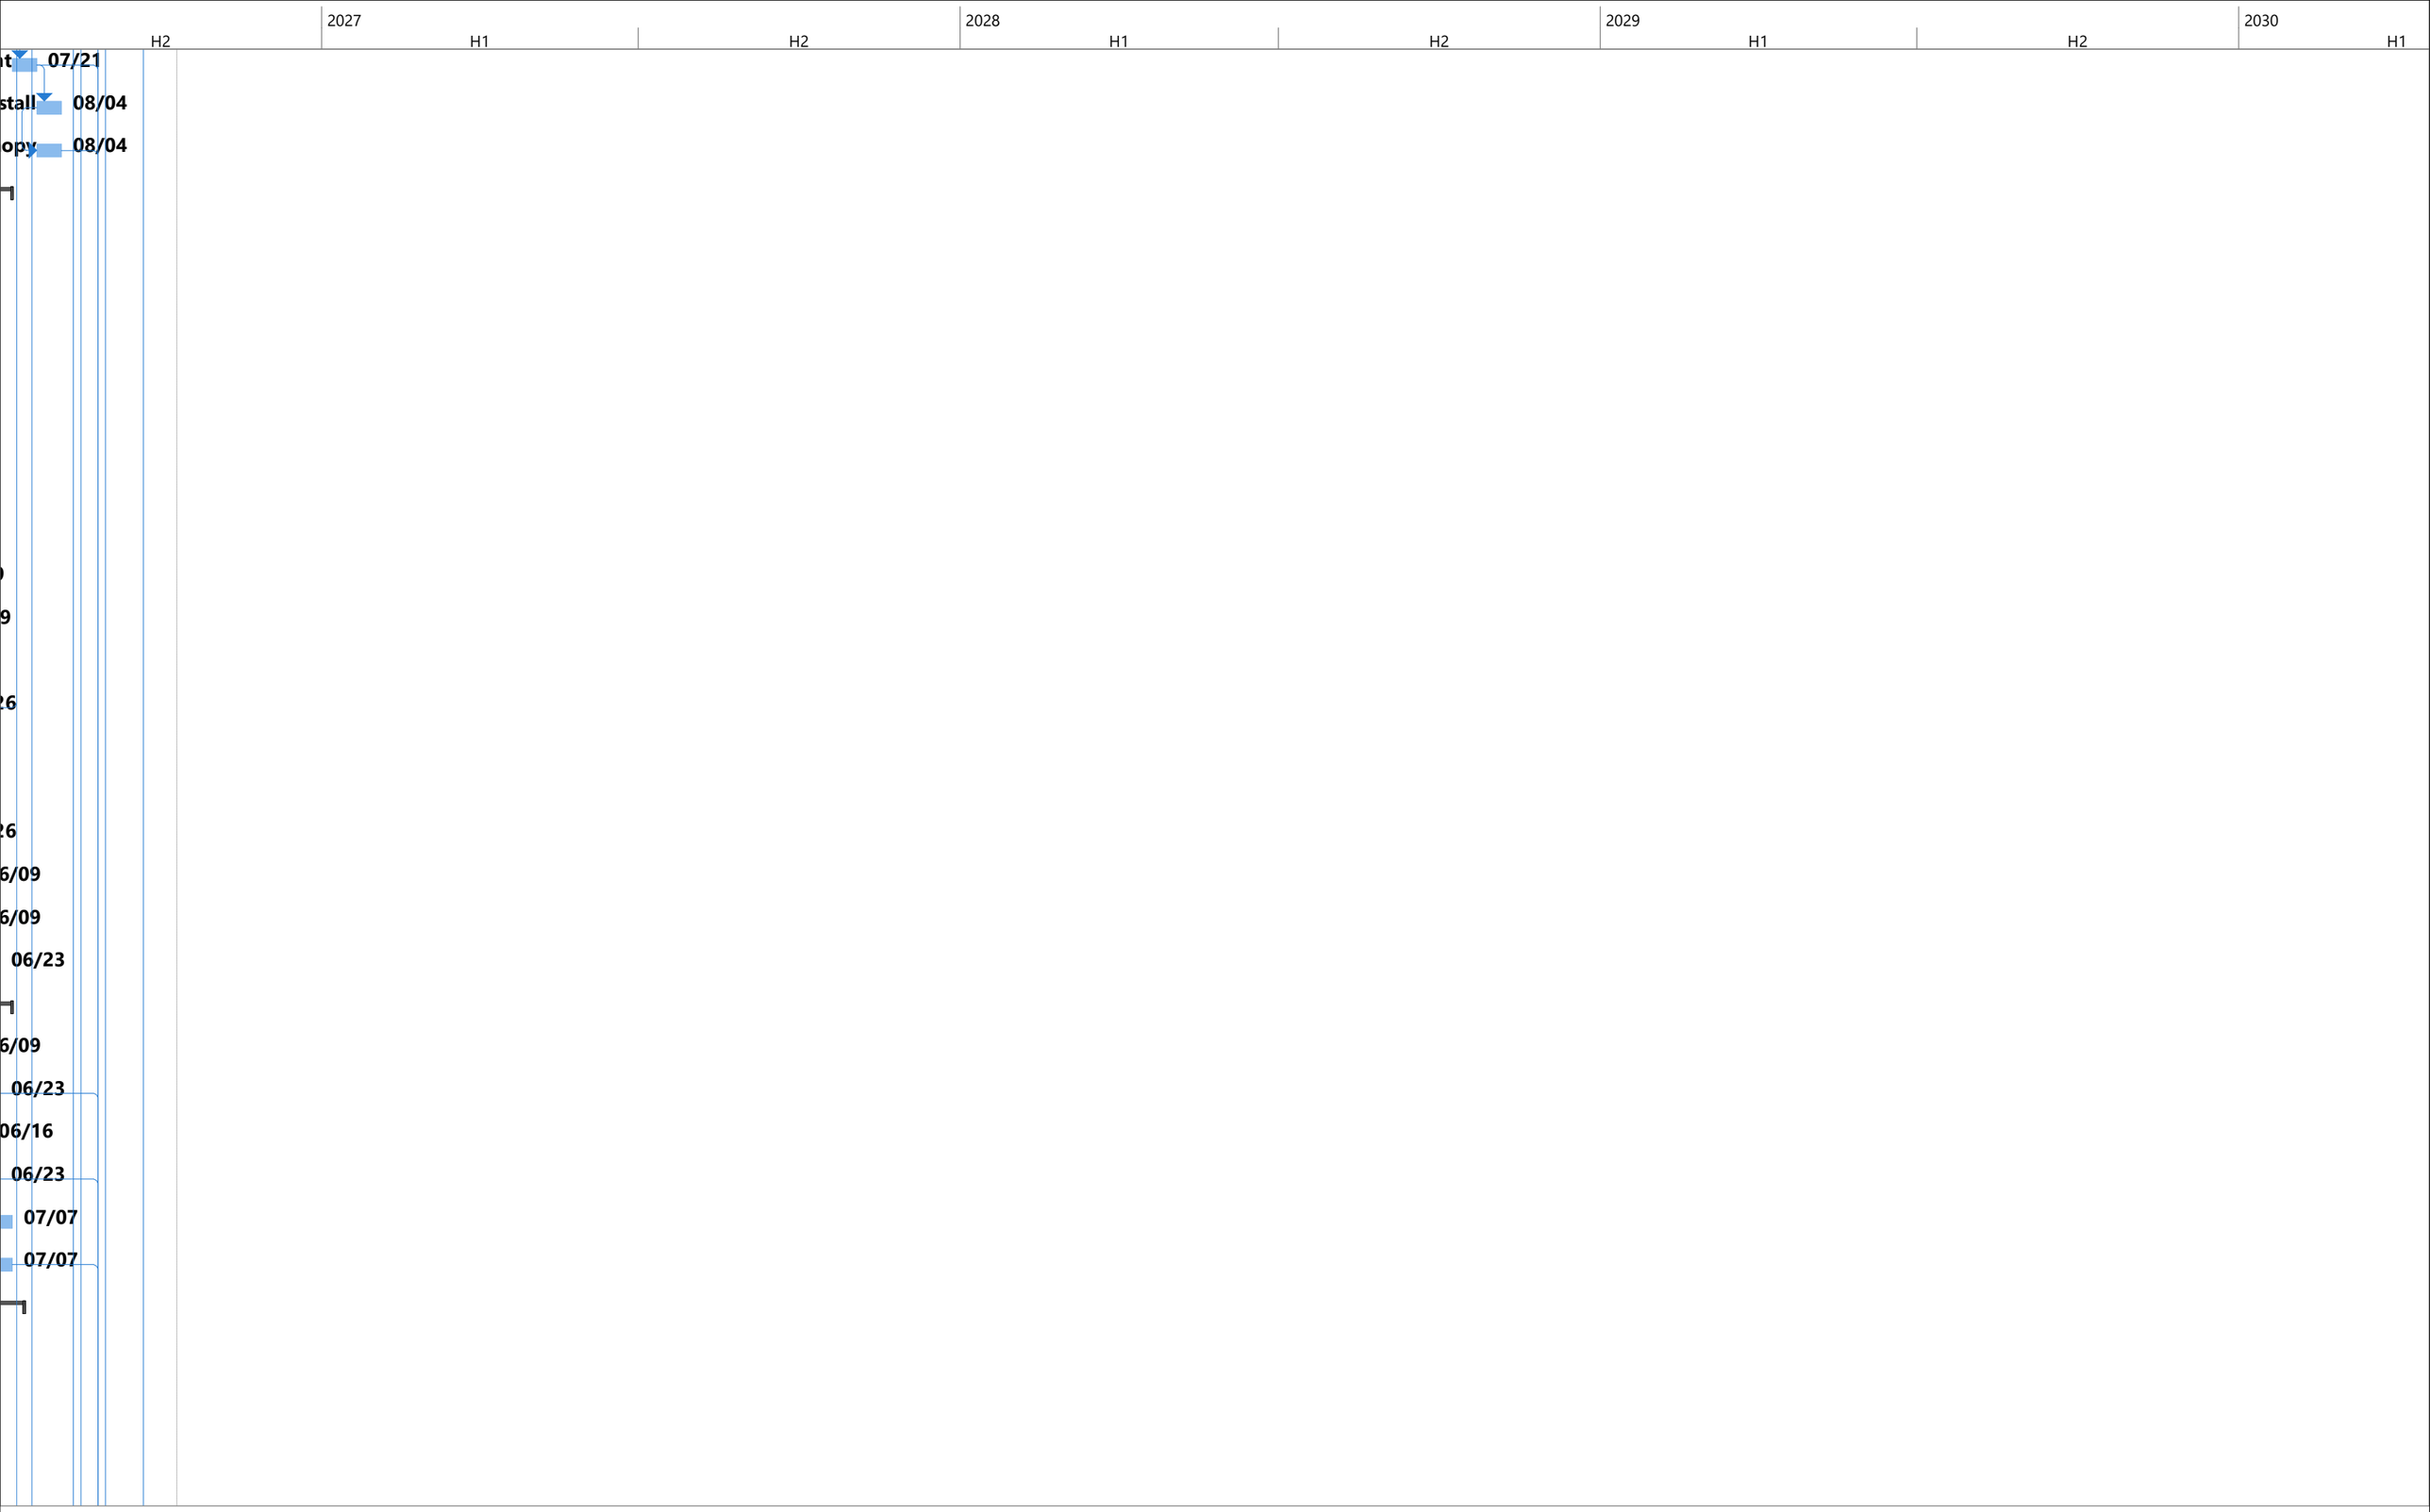
2027
2028
2029
2030
H2
H1
H2
H1
H2
H1
H2
H1
07/21
08/04
08/04
06/23
06/23
06/16
06/23
07/07
07/07

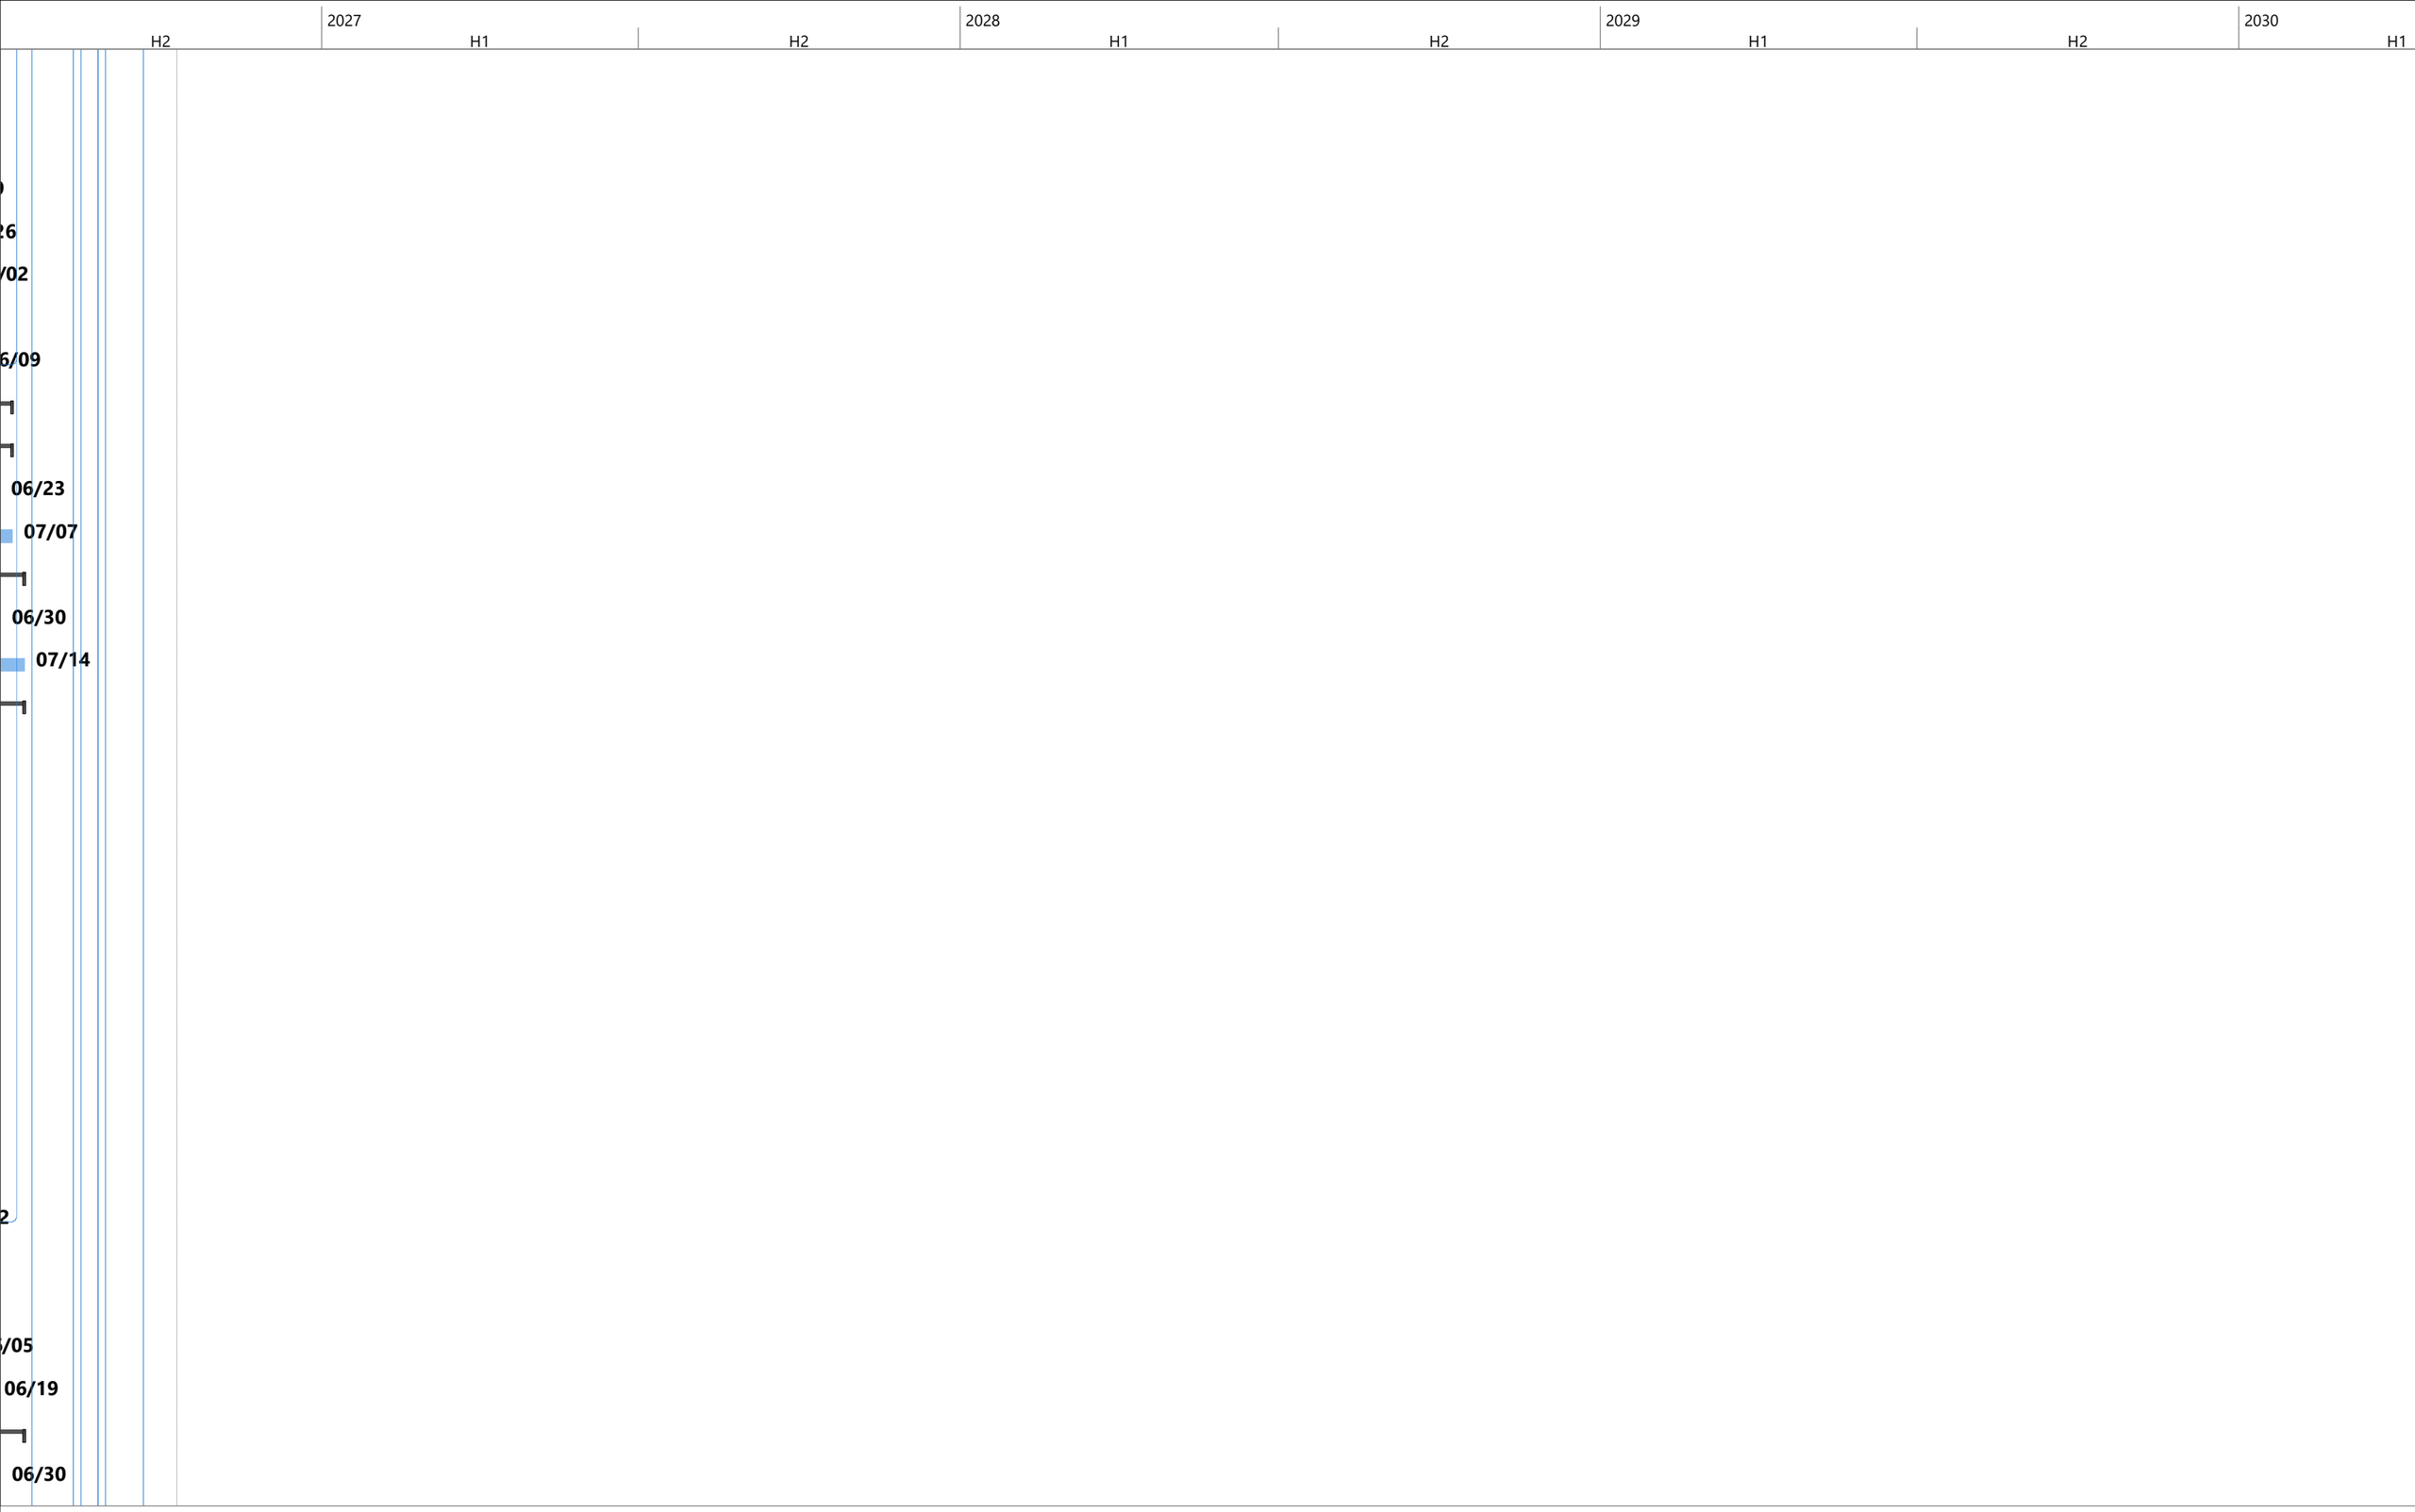
2027
2028
2029
2030
H2
H1
H2
H1
H2
H1
H2
H1
9
26
/02
6/09
06/23
07/07
06/30
07/14
2
/05
06/19
06/30

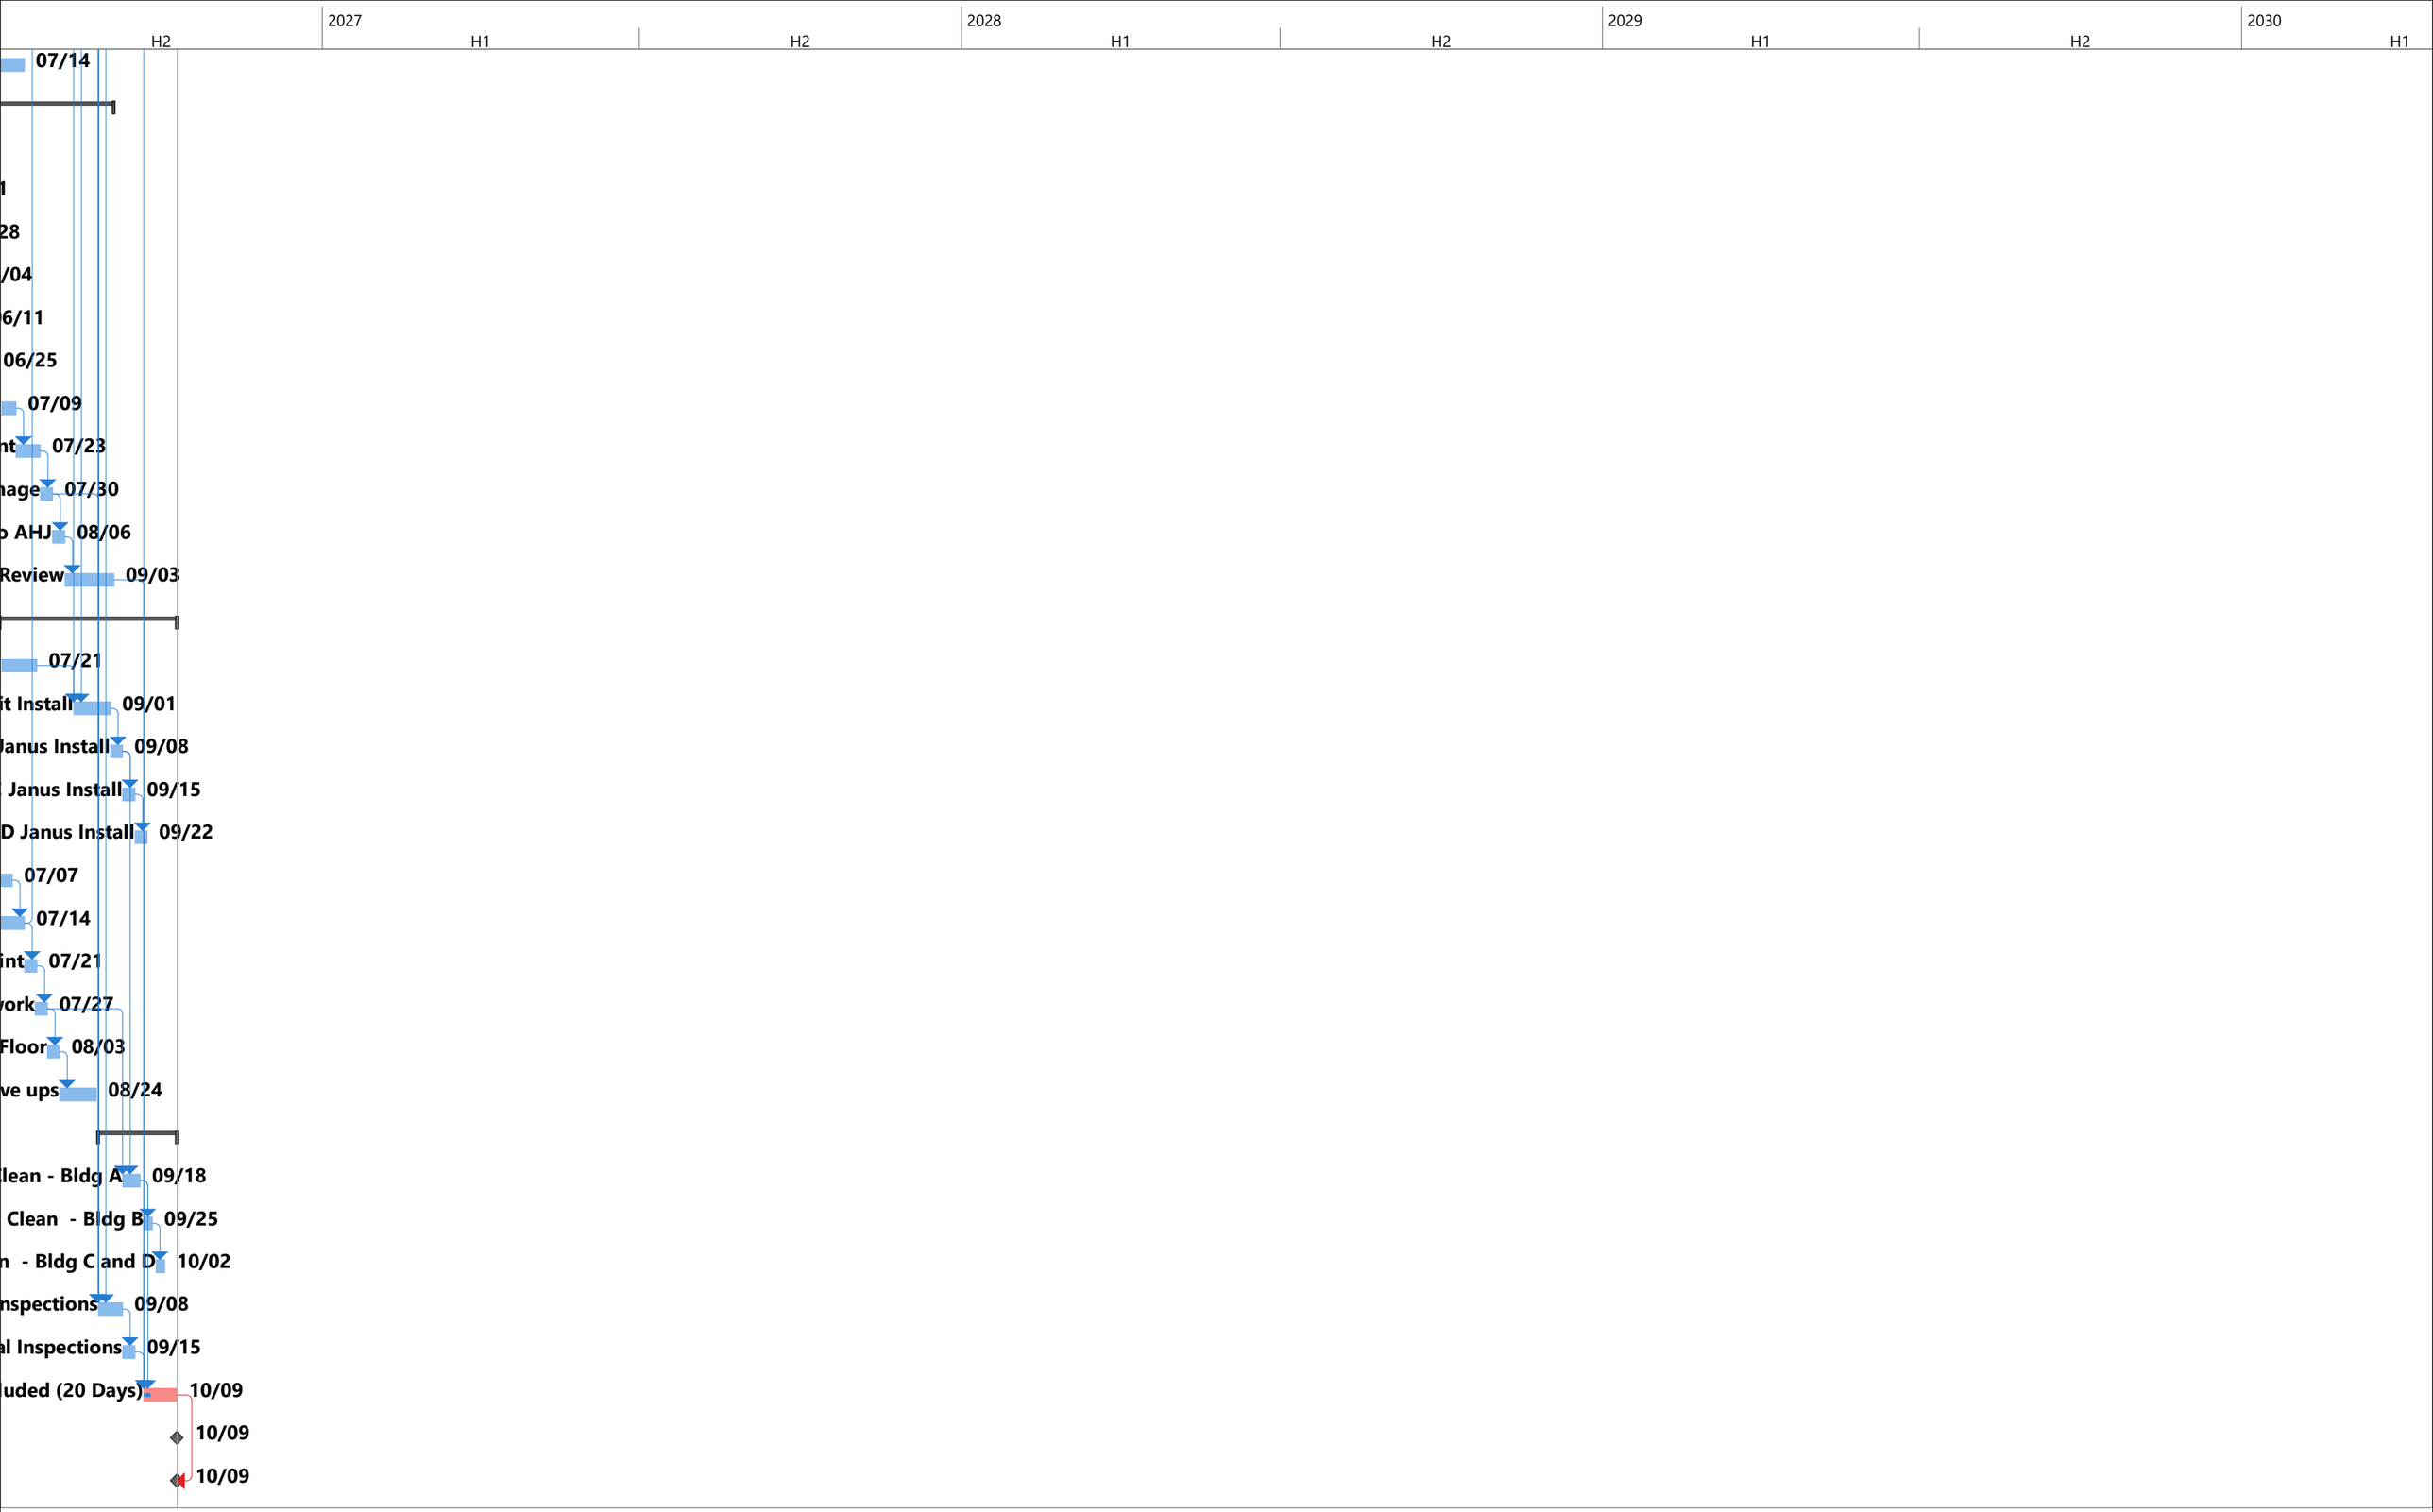
2027
2028
2029
2030
H2
H1
H2
H1
H2
H1
H2
H1
07/14
28
/04
6/11
06/25
07/09
nt
07/23
nage
07/30
o AHJ
08/06
Review
09/03
07/21
it Install
09/01
Janus Install
09/08
Janus Install
09/15
D Janus Install
09/22
07/07
07/14
int
07/21
ork
07/27
Floor
08/03
ve ups
08/24
lean - Bldg A
09/18
Clean - Bldg B
09/25
n - Bldg C and D
10/02
nspections
09/08
al Inspections
09/15
luded (20 Days)
10/09
10/09
10/09
