Executive Landing Page

Public Storage Dashboard

Data Date: 12/8/2025

Type	Project	Region	Responsible
Construction	Selma, NC	East Coast	Ross Kremers

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
10/9/2026	10/9/2026	0 Baseline 0 Previous	Remaining Work Compression : -1%

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	10/6/2025	10/6/2025	10/6/2025	0	0	Award Contract	On Track – Gaining
Foundation Complete	3/24/2026	3/24/2026	3/31/2026	-7	-7	Slab #1 Prep / Pour (North Half)	Delayed – Slipping
Permanent Power	4/30/2026	4/30/2026	4/30/2026	0	0	Building Tie In	On Track – Gaining
Structure Top Out	6/9/2026	6/9/2026	6/16/2026	-7	-7	Roof Decking - Building A	Delayed – Slipping
Weather Tight	6/23/2026	6/23/2026	6/30/2026	-7	-7	Metal Roofing - Building A	Delayed – Slipping
1st Floor Finishes Complete	8/11/2026	8/11/2026	8/18/2026	-7	-7	2Nd Floor Mep Trim Out Area 1 - Building A	Delayed – Slipping
Hardscape/Landscape Complete	9/3/2026	9/3/2026	9/3/2026	0	0	As-Built/City Review	On Track – Gaining
Contract Completion	10/9/2026	10/9/2026	10/9/2026	0	0	Substantial Completion	On Track – Gaining

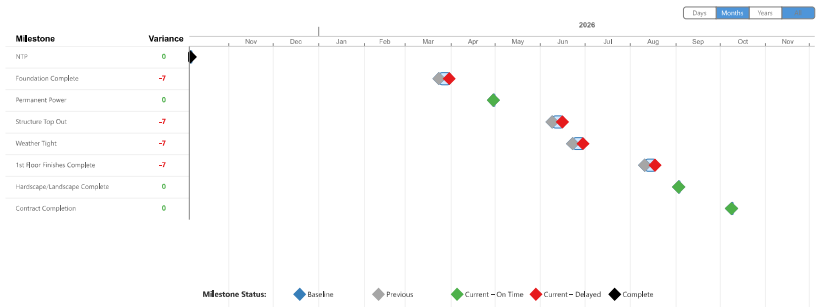

Baseline Variance

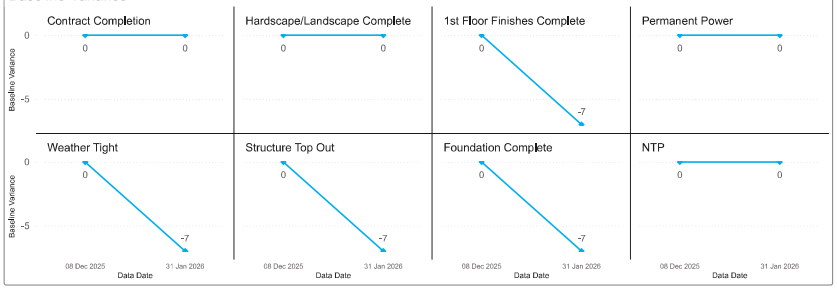

Schedule Performance Summary

Summary

The low Schedule Validation Score presents a substantial risk to project delivery, as the quality and reliability of the schedule network are compromised. Elevated schedule changes add to this risk, stressing the need for immediate schedule quality reviews, corrective validation efforts, and stricter change management to regain forecast integrity and control.

Remaining Work Compression : -1%

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea… by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased – more work per period is required.

Schedule Change Index: 10,00% — WARNING

The percentage of logic or date changes since the last update is at the upper end of the warning range, signaling increased schedule volatility. Efforts should be made to stabilize plan changes and reinforce planning discipline.

Schedule Validation Score: 61,00% — ALERT

The Schedule Validator Score is critically low, indicating significant deficiencies in baseline logic, technical integrity, or best practice compliance. Immediate review and remediation of schedule quality issues are required to ensure reliability of forecasting and progress tracking

Powered By STELIC INSIGHT+ACTION=IMPACT
