	Name	Duration: Current	Duration: Previous	Dura Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Public Storage Selma, NC**	**263 days**	**263 days**	**0d**	**Mon 25/10/06**	**Mon 25/10/06**	**0d**	**Fri 26/10/09**	**Fri 26/10/09**	**0d**
2	Award Contract	0 days	0 days	0d	Mon 25/10/06	Mon 25/10/06	0d	Mon 25/10/06	Mon 25/10/06	0d
3	**Mobilization**	**6 days**	**6 days**	**0d**	**Mon 25/12/01**	**Mon 25/12/01**	**0d**	**Mon 25/12/08**	**Mon 25/12/08**	**0d**
4	Mobilization (Site Fence, Layout, Barricades, Etc.)	1 day	1 day	0d	Mon 26/01/05	Mon 26/01/05	0d	Mon 26/01/05	Mon 26/01/05	0d
5	SWPPP	5 days	5 days	0d	Mon 25/12/15	Mon 25/12/15	0d	Fri 25/12/19	Fri 25/12/19	0d
6	**Demo/Site Work**	**84 days**	**84 days**	**0d**	**Mon 26/01/05**	**Mon 26/01/05**	**0d**	**Thu 26/04/30**	**Thu 26/04/30**	**0d**
7	Clearing and Grubbing	10 days	10 days	0d	Mon 26/01/05	Mon 26/01/05	0d	Fri 26/01/16	Fri 26/01/16	0d
8	Dewatering	5 days	5 days	0d	Mon 26/01/19	Mon 26/01/19	0d	Fri 26/01/23	Fri 26/01/23	0d
9	Rough Grading	18 days	18 days	0d	Mon 26/01/19	Mon 26/01/19	0d	Wed 26/02/11	Wed 26/02/11	0d
10	Storm System	21 days	21 days	0d	Thu 26/02/12	Thu 26/02/12	0d	Thu 26/03/12	Thu 26/03/12	0d
11	Sanitary Sewer	5 days	5 days	0d	Fri 26/03/13	Fri 26/03/13	0d	Thu 26/03/19	Thu 26/03/19	0d
12	Water	10 days	10 days	0d	Fri 26/03/20	Fri 26/03/20	0d	Thu 26/04/02	Thu 26/04/02	0d
13	Site Electrical	10 days	10 days	0d	Fri 26/04/03	Fri 26/04/03	0d	Thu 26/04/16	Thu 26/04/16	0d
14	Building Tie In	10 days	10 days	0d	Fri 26/04/17	Fri 26/04/17	0d	Thu 26/04/30	Thu 26/04/30	0d
15	**Building A**	**144 days**	**139 days**	**5d**	**Thu 26/02/05**	**Thu 26/02/05**	**0d**	**Tue 26/08/25**	**Tue 26/08/18**	**5d**
16	**Structure**	**104 days**	**109 days**	**-5d**	**Thu 26/02/05**	**Thu 26/02/05**	**0d**	**Tue 26/06/30**	**Tue 26/07/07**	**-5d**
17	**First Floor**	**64 days**	**59 days**	**5d**	**Thu 26/02/05**	**Thu 26/02/05**	**0d**	**Tue 26/05/05**	**Tue 26/04/28**	**5d**
18	Weather Delay(Snow & Ice)	5 days			Thu 26/02/05			Wed 26/02/11		
19	Building Pad Delivery (Bldg A)	5 days	5 days	0d	Thu 26/02/12	Thu 26/02/05	5d	Wed 26/02/18	Wed 26/02/11	5d
20	Elevator Pit - Excavate	5 days	5 days	0d	Thu 26/02/19	Thu 26/02/12	5d	Wed 26/02/25	Wed 26/02/18	5d
21	Elevator Pit - Form and Pour	10 days	10 days	0d	Thu 26/02/26	Thu 26/02/19	5d	Wed 26/03/11	Wed 26/03/04	5d
22	FRP Foundations / Foundation CMU - Area 1	7 days	7 days	0d	Thu 26/02/19	Thu 26/02/12	5d	Fri 26/02/27	Fri 26/02/20	5d
23	Concrete Retaining Walls	10 days	10 days	0d	Mon 26/03/02	Mon 26/02/23	5d	Fri 26/03/13	Fri 26/03/06	5d
24	FRP Foundations/Foundation Area 2	7 days	7 days	0d	Mon 26/03/16	Mon 26/03/09	5d	Tue 26/03/24	Tue 26/03/17	5d
25	Under Slab MEP	10 days	10 days	0d	Wed 26/03/11	Wed 26/03/04	5d	Tue 26/03/24	Tue 26/03/17	5d
26	Slab #1 Prep / Pour (North Half)	10 days	10 days	0d	Wed 26/03/18	Wed 26/03/11	5d	Tue 26/03/31	Tue 26/03/24	5d
27	CMU shafts	15 days	15 days	0d	Wed 26/04/01	Wed 26/03/25	5d	Tue 26/04/21	Tue 26/04/14	5d
28	Slab #2 Prep / Pour (South Half)	10 days	10 days	0d	Wed 26/04/01	Wed 26/03/25	5d	Tue 26/04/14	Tue 26/04/07	5d
29	Janus Framing System (North Half)	15 days	15 days	0d	Wed 26/04/01	Wed 26/03/25	5d	Tue 26/04/21	Tue 26/04/14	5d
30	Janus Framing System (South Half)	10 days	10 days	0d	Wed 26/04/22	Wed 26/04/15	5d	Tue 26/05/05	Tue 26/04/28	5d
31	**Second Floor**	**40 days**	**40 days**	**0d**	**Wed 26/04/22**	**Wed 26/04/15**	**5d**	**Tue 26/06/16**	**Tue 26/06/09**	**5d**
32	Elevated Slab #1 (North Half) Prep/Pour	5 days	5 days	0d	Wed 26/04/22	Wed 26/04/15	5d	Tue 26/04/28	Tue 26/04/21	5d
33	Elevated Slab #2 (South Half) Prep/Pour	5 days	5 days	0d	Wed 26/05/06	Wed 26/04/29	5d	Tue 26/05/12	Tue 26/05/05	5d
34	Janus Framing System (North Half)	15 days	15 days	0d	Wed 26/05/06	Wed 26/04/29	5d	Tue 26/05/26	Tue 26/05/19	5d

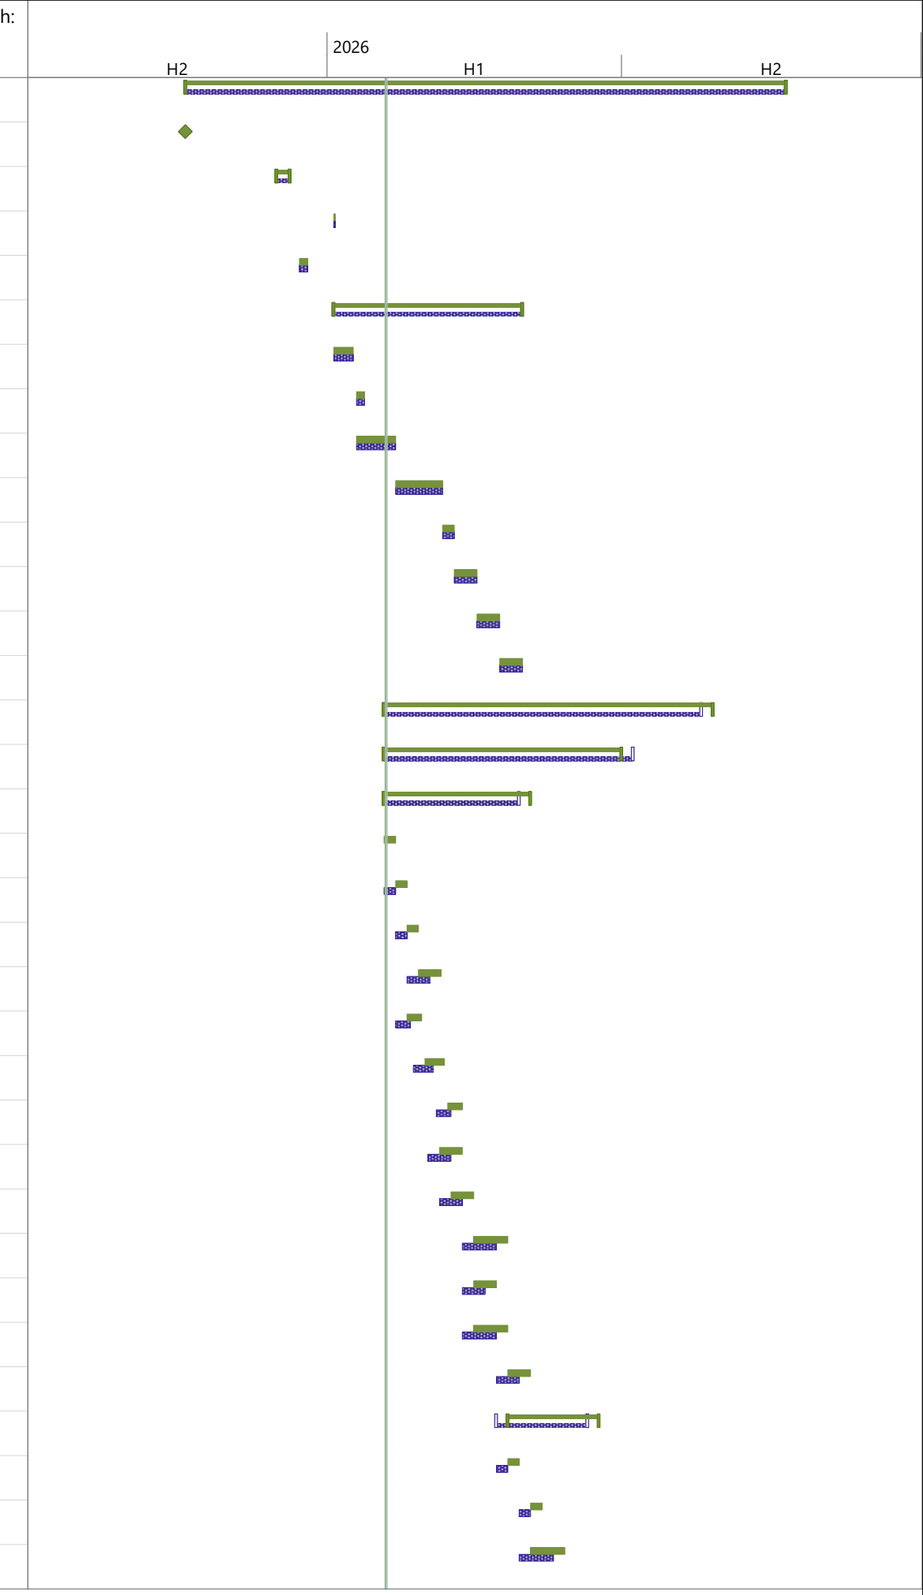

	Name	Duration: Current	Duration: Previous	Dura Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
35	Janus Framing System (South Half)	10 days	10 days	0d	Wed 26/05/27	Wed 26/05/20	5d	Tue 26/06/09	Tue 26/06/02	5d
36	Roof Decking	5 days	5 days	0d	Wed 26/06/10	Wed 26/06/03	5d	Tue 26/06/16	Tue 26/06/09	5d
37	**Stairs**	**20 days**	**20 days**	**0d**	**Tue 26/05/19**	**Wed 26/06/10**	**-16d**	**Mon 26/06/15**	**Tue 26/07/07**	**-16d**
38	Stair #1	10 days	10 days	0d	Tue 26/05/19	Wed 26/06/10	-16d	Mon 26/06/01	Tue 26/06/23	-16d
39	Stair #2	10 days	10 days	0d	Tue 26/06/02	Wed 26/06/24	-16d	Mon 26/06/15	Tue 26/07/07	-16d
40	**Roof**	**10 days**	**10 days**	**0d**	**Wed 26/06/17**	**Wed 26/06/10**	**5d**	**Tue 26/06/30**	**Tue 26/06/23**	**5d**
41	Metal Roofing	10 days	10 days	0d	Wed 26/06/17	Wed 26/06/10	5d	Tue 26/06/30	Tue 26/06/23	5d
42	**Framing and MEP**	**80 days**	**80 days**	**0d**	**Wed 26/05/06**	**Wed 26/04/29**	**5d**	**Tue 26/08/25**	**Tue 26/08/18**	**5d**
43	**First Floor**	**65 days**	**65 days**	**0d**	**Wed 26/05/06**	**Wed 26/04/29**	**5d**	**Tue 26/08/04**	**Tue 26/07/28**	**5d**
44	Interior Framing	5 days	5 days	0d	Wed 26/05/06	Wed 26/04/29	5d	Tue 26/05/12	Tue 26/05/05	5d
45	1st Floor MEP Rough-In Area 1	20 days	20 days	0d	Wed 26/05/13	Wed 26/05/06	5d	Tue 26/06/09	Tue 26/06/02	5d
46	1st Floor MEP Rough-In Area 2	15 days	15 days	0d	Wed 26/06/10	Wed 26/06/03	5d	Tue 26/06/30	Tue 26/06/23	5d
47	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Wed 26/07/15	Wed 26/07/08	5d	Tue 26/07/28	Tue 26/07/21	5d
48	1st Floor MEP Trim Out Area 2	5 days	5 days	0d	Wed 26/07/29	Wed 26/07/22	5d	Tue 26/08/04	Tue 26/07/28	5d
49	**Second Floor**	**50 days**	**50 days**	**0d**	**Wed 26/06/17**	**Wed 26/06/10**	**5d**	**Tue 26/08/25**	**Tue 26/08/18**	**5d**
50	Interior Framing	5 days	5 days	0d	Wed 26/06/17	Wed 26/06/10	5d	Tue 26/06/23	Tue 26/06/16	5d
51	2nd Floor MEP Rough-In Area 2	15 days	15 days	0d	Wed 26/07/01	Wed 26/06/24	5d	Tue 26/07/21	Tue 26/07/14	5d
52	2nd Floor MEP Rough-In Area 2	15 days	15 days	0d	Wed 26/07/22	Wed 26/07/15	5d	Tue 26/08/11	Tue 26/08/04	5d
53	2nd Floor MEP Trim Out Area 1	10 days	10 days	0d	Wed 26/08/05	Wed 26/07/29	5d	Tue 26/08/18	Tue 26/08/11	5d
54	2nd Floor MEP Trim Out Area 2	5 days	5 days	0d	Wed 26/08/19	Wed 26/08/12	5d	Tue 26/08/25	Tue 26/08/18	5d
55	**Elevator**	**30 days**	**30 days**	**0d**	**Mon 26/07/13**	**Tue 26/06/23**	**14d**	**Mon 26/08/24**	**Tue 26/08/04**	**14d**
56	Delivery	0 days	0 days	0d	Mon 26/07/13	Tue 26/06/23	14d	Mon 26/07/13	Tue 26/06/23	14d
57	Elevator 1 - First Floor	5 days	5 days	0d	Tue 26/07/14	Wed 26/06/24	14d	Mon 26/07/20	Tue 26/06/30	14d
58	Elevator 1 - Second Floor	5 days	5 days	0d	Tue 26/07/21	Wed 26/07/01	14d	Mon 26/07/27	Tue 26/07/07	14d
59	Elevator 2 - First Floor	5 days	5 days	0d	Tue 26/07/28	Wed 26/07/08	14d	Mon 26/08/03	Tue 26/07/14	14d
60	Elevator 2 - Second Floor	5 days	5 days	0d	Tue 26/08/04	Wed 26/07/15	14d	Mon 26/08/10	Tue 26/07/21	14d
61	Infill Doors	5 days	5 days	0d	Tue 26/08/04	Wed 26/07/15	14d	Mon 26/08/10	Tue 26/07/21	14d
62	Test / Adjust	5 days	5 days	0d	Tue 26/08/11	Wed 26/07/22	14d	Mon 26/08/17	Tue 26/07/28	14d
63	State Inspection	5 days	5 days	0d	Tue 26/08/18	Wed 26/07/29	14d	Mon 26/08/24	Tue 26/08/04	14d
64	**Exterior Finishes**	**50 days**	**50 days**	**0d**	**Wed 26/05/27**	**Wed 26/05/06**	**15d**	**Tue 26/08/04**	**Tue 26/07/14**	**15d**
65	Masonry Veneer	15 days	15 days	0d	Wed 26/05/27	Wed 26/05/06	15d	Tue 26/06/16	Tue 26/05/26	15d
66	Metal Panels Completion	15 days	15 days	0d	Wed 26/06/17	Wed 26/05/27	15d	Tue 26/07/07	Tue 26/06/16	15d
67	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	10 days	0d	Wed 26/07/01	Wed 26/06/17	10d	Tue 26/07/14	Tue 26/06/30	10d
68	Automatic Entrance Door	5 days	5 days	0d	Wed 26/06/17	Wed 26/05/27	15d	Tue 26/06/23	Tue 26/06/02	15d

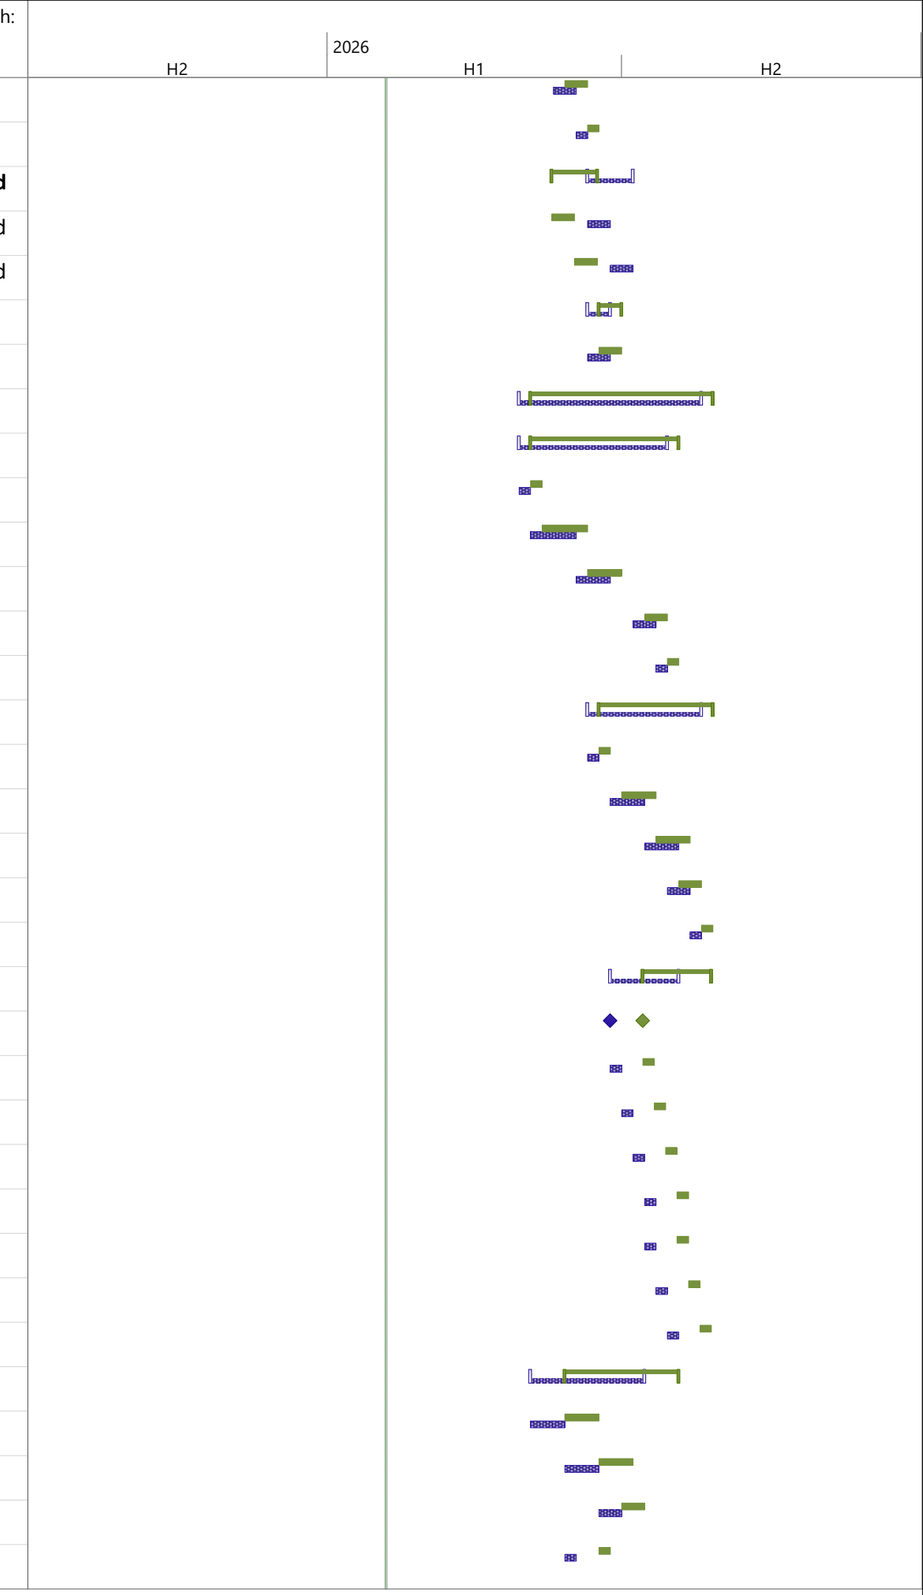

	Name	Duration: Current	Duration: Previous	Dura Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
69	Exterior Paint	10 days	10 days	0d	Wed 26/07/08	Wed 26/06/17	15d	Tue 26/07/21	Tue 26/06/30	15d
70	Exterior Signage Install	10 days	10 days	0d	Wed 26/07/22	Wed 26/07/01	15d	Tue 26/08/04	Tue 26/07/14	15d
71	Canopy	10 days	10 days	0d	Wed 26/07/22	Wed 26/07/01	15d	Tue 26/08/04	Tue 26/07/14	15d
72	**Building B**	**99 days**	**85 days**	**14d**	**Thu 26/02/19**	**Thu 26/02/12**	**5d**	**Tue 26/07/07**	**Wed 26/06/10**	**19d**
73	**Structure**	**69 days**	**55 days**	**14d**	**Thu 26/02/19**	**Thu 26/02/12**	**5d**	**Tue 26/05/26**	**Wed 26/04/29**	**19d**
74	**First Floor**	**64 days**	**50 days**	**14d**	**Thu 26/02/19**	**Thu 26/02/12**	**5d**	**Tue 26/05/19**	**Wed 26/04/22**	**19d**
75	Building Pad Delivery (Bldg B)	5 days	5 days	0d	Thu 26/02/19	Thu 26/02/12	5d	Wed 26/02/25	Wed 26/02/18	5d
76	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Thu 26/02/26	Thu 26/02/19	5d	Wed 26/03/04	Wed 26/02/25	5d
77	FRP Foundations/Foundation Area 2	5 days	5 days	0d	Wed 26/03/25	Thu 26/02/26	19d	Tue 26/03/31	Wed 26/03/04	19d
78	Under Slab MEP	5 days	5 days	0d	Wed 26/03/25	Thu 26/03/05	14d	Tue 26/03/31	Wed 26/03/11	14d
79	Slab Prep / Pour	5 days	5 days	0d	Wed 26/04/15	Thu 26/03/12	24d	Tue 26/04/21	Wed 26/03/18	24d
80	CMU Walls	10 days	10 days	0d	Wed 26/04/22	Thu 26/03/19	24d	Tue 26/05/05	Wed 26/04/01	24d
81	Janus Framing System	10 days	10 days	0d	Wed 26/05/06	Thu 26/04/02	24d	Tue 26/05/19	Wed 26/04/15	24d
82	Roof Decking	0 days	5 days	-5d	Tue 26/05/19	Thu 26/04/16	24d	Tue 26/05/19	Wed 26/04/22	19d
83	**Roof**	**5 days**	**5 days**	**0d**	**Wed 26/05/20**	**Thu 26/04/23**	**19d**	**Tue 26/05/26**	**Wed 26/04/29**	**19d**
84	Metal Roofing	5 days	5 days	0d	Wed 26/05/20	Thu 26/04/23	19d	Tue 26/05/26	Wed 26/04/29	19d
85	**Framing and MEP**	**25 days**	**30 days**	**-5d**	**Wed 26/05/20**	**Thu 26/04/16**	**24d**	**Tue 26/06/23**	**Wed 26/05/27**	**19d**
86	**First Floor**	**25 days**	**30 days**	**-5d**	**Wed 26/05/20**	**Thu 26/04/16**	**24d**	**Tue 26/06/23**	**Wed 26/05/27**	**19d**
87	Interior Framing	5 days	5 days	0d	Wed 26/05/20	Thu 26/04/16	24d	Tue 26/05/26	Wed 26/04/22	24d
88	1st Floor MEP Rough-In Area 1	10 days	10 days	0d	Wed 26/05/27	Thu 26/04/23	24d	Tue 26/06/09	Wed 26/05/06	24d
89	Finishes	10 days	10 days	0d	Wed 26/05/27	Thu 26/04/30	19d	Tue 26/06/09	Wed 26/05/13	19d
90	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/23	Wed 26/05/27	19d
91	**Exterior Finishes**	**35 days**	**35 days**	**0d**	**Wed 26/05/20**	**Thu 26/04/23**	**19d**	**Tue 26/07/07**	**Wed 26/06/10**	**19d**
92	Metal Panels Completion	15 days	15 days	0d	Wed 26/05/20	Thu 26/04/23	19d	Tue 26/06/09	Wed 26/05/13	19d
93	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	10 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/23	Wed 26/05/27	19d
94	Automatic Entrance Door	5 days	5 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/16	Wed 26/05/20	19d
95	Exterior Paint	10 days	10 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/23	Wed 26/05/27	19d
96	Exterior Signage Install	10 days	10 days	0d	Wed 26/06/24	Thu 26/05/28	19d	Tue 26/07/07	Wed 26/06/10	19d
97	Canopy	10 days	10 days	0d	Wed 26/06/24	Thu 26/05/28	19d	Tue 26/07/07	Wed 26/06/10	19d
98	**Building C**	**99 days**	**85 days**	**14d**	**Thu 26/02/26**	**Thu 26/02/19**	**5d**	**Tue 26/07/14**	**Wed 26/06/17**	**19d**
99	**Structure**	**74 days**	**55 days**	**19d**	**Thu 26/02/26**	**Thu 26/02/19**	**5d**	**Tue 26/06/09**	**Wed 26/05/06**	**24d**
100	**First Floor**	**69 days**	**50 days**	**19d**	**Thu 26/02/26**	**Thu 26/02/19**	**5d**	**Tue 26/06/02**	**Wed 26/04/29**	**24d**
101	Building Pad Delivery (Bldg C)	5 days	5 days	0d	Thu 26/02/26	Thu 26/02/19	5d	Wed 26/03/04	Wed 26/02/25	5d
102	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Thu 26/03/05	Thu 26/02/26	5d	Wed 26/03/11	Wed 26/03/04	5d

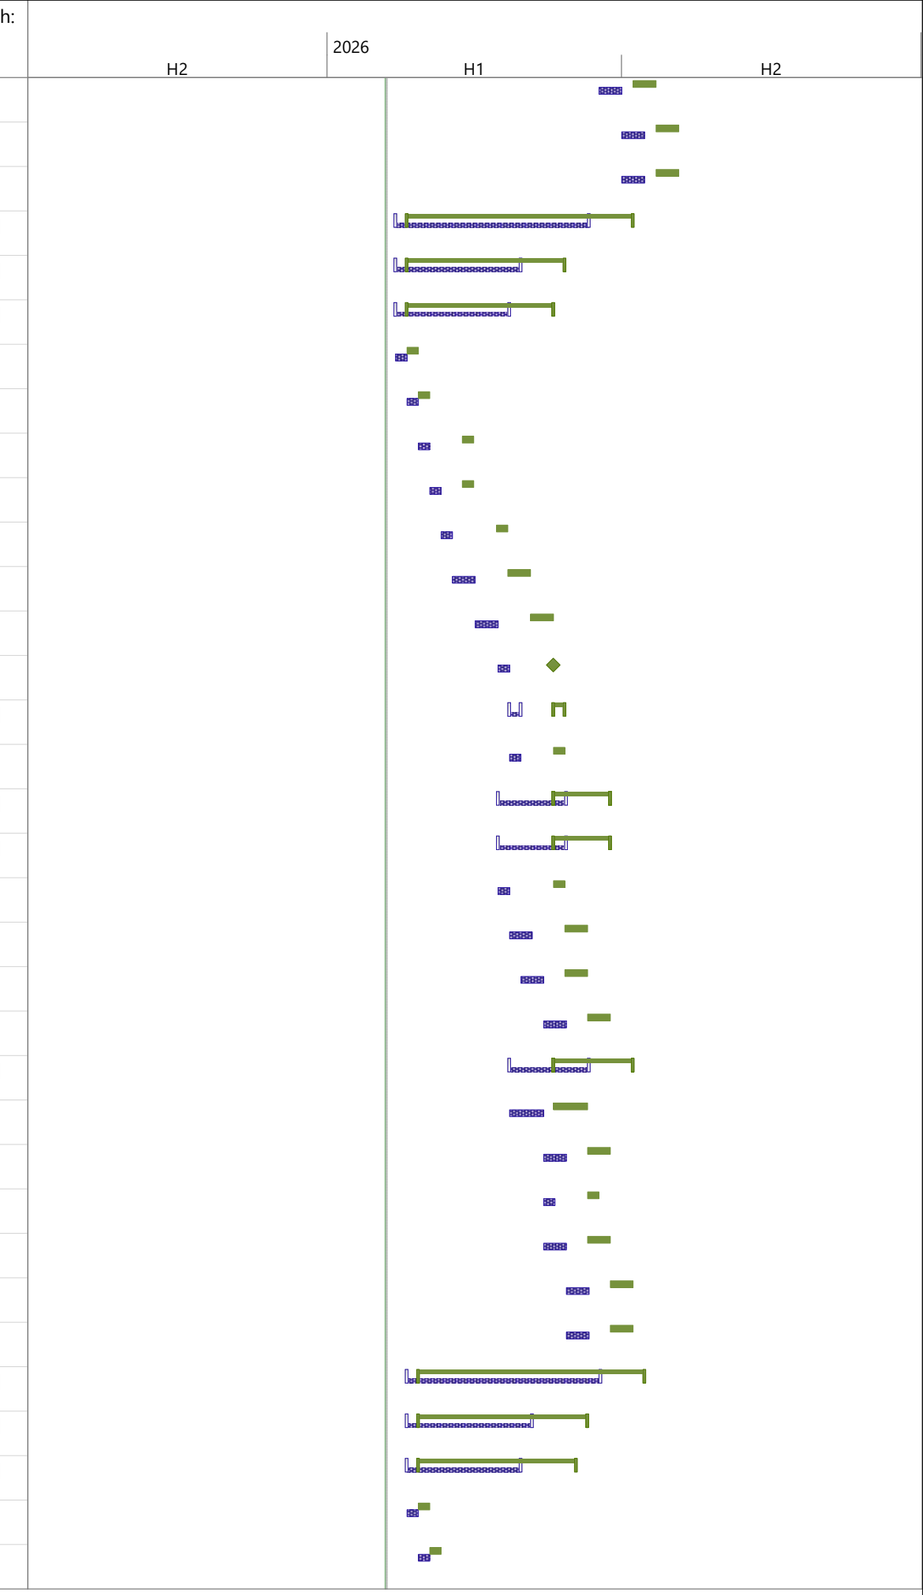

	Name	Duration: Current	Duration: Previous	Dura Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
103	FRP Foundations/Foundation Area 2	5 days	5 days	0d	Thu 26/03/12	Thu 26/03/05	5d	Wed 26/03/18	Wed 26/03/11	5d
104	Under Slab MEP	5 days	5 days	0d	Thu 26/03/19	Thu 26/03/12	5d	Wed 26/03/25	Wed 26/03/18	5d
105	Slab Prep / Pour	5 days	5 days	0d	Thu 26/03/26	Thu 26/03/19	5d	Wed 26/04/01	Wed 26/03/25	5d
106	CMU Walls	10 days	10 days	0d	Wed 26/05/06	Thu 26/04/02	24d	Tue 26/05/19	Wed 26/04/15	24d
107	Janus Framing System	5 days	5 days	0d	Wed 26/05/20	Thu 26/04/16	24d	Tue 26/05/26	Wed 26/04/22	24d
108	Roof Decking	5 days	5 days	0d	Wed 26/05/27	Thu 26/04/23	24d	Tue 26/06/02	Wed 26/04/29	24d
109	**Roof**	**5 days**	**5 days**	**0d**	**Wed 26/06/03**	**Thu 26/04/30**	**24d**	**Tue 26/06/09**	**Wed 26/05/06**	**24d**
110	Metal Roofing	5 days	5 days	0d	Wed 26/06/03	Thu 26/04/30	24d	Tue 26/06/09	Wed 26/05/06	24d
111	**Framing and MEP**	**20 days**	**20 days**	**0d**	**Wed 26/06/10**	**Thu 26/05/07**	**24d**	**Tue 26/07/07**	**Wed 26/06/03**	**24d**
112	**First Floor**	**20 days**	**20 days**	**0d**	**Wed 26/06/10**	**Thu 26/05/07**	**24d**	**Tue 26/07/07**	**Wed 26/06/03**	**24d**
113	1st Floor MEP Rough-In Area 1	10 days	10 days	0d	Wed 26/06/10	Thu 26/05/07	24d	Tue 26/06/23	Wed 26/05/20	24d
114	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Wed 26/06/24	Thu 26/05/21	24d	Tue 26/07/07	Wed 26/06/03	24d
115	**Exterior Finishes**	**25 days**	**25 days**	**0d**	**Wed 26/06/10**	**Thu 26/05/14**	**19d**	**Tue 26/07/14**	**Wed 26/06/17**	**19d**
116	Metal Panels Completion	15 days	15 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/30	Wed 26/06/03	19d
117	Exterior Signage Install	10 days	10 days	0d	Wed 26/07/01	Thu 26/06/04	19d	Tue 26/07/14	Wed 26/06/17	19d
118	**Building D**	**94 days**	**80 days**	**14d**	**Thu 26/03/05**	**Thu 26/02/26**	**5d**	**Tue 26/07/14**	**Wed 26/06/17**	**19d**
119	**Structure**	**57 days**	**60 days**	**-3d**	**Thu 26/03/05**	**Thu 26/02/26**	**5d**	**Fri 26/05/22**	**Wed 26/05/20**	**2d**
120	**First Floor**	**52 days**	**55 days**	**-3d**	**Thu 26/03/05**	**Thu 26/02/26**	**5d**	**Fri 26/05/15**	**Wed 26/05/13**	**2d**
121	Building Pad Delivery (Bldg D)	5 days	5 days	0d	Thu 26/03/05	Thu 26/02/26	5d	Wed 26/03/11	Wed 26/03/04	5d
122	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Thu 26/03/19	Thu 26/03/05	10d	Wed 26/03/25	Wed 26/03/11	10d
123	FRP Foundations/Foundation Area 2	5 days	5 days	0d	Thu 26/03/26	Thu 26/03/12	10d	Wed 26/04/01	Wed 26/03/18	10d
124	Under Slab MEP	5 days	5 days	0d	Thu 26/04/02	Thu 26/03/19	10d	Wed 26/04/08	Wed 26/03/25	10d
125	Slab Prep / Pour	5 days	5 days	0d	Thu 26/04/09	Thu 26/03/26	10d	Wed 26/04/15	Wed 26/04/01	10d
126	CMU Walls	10 days	10 days	0d	Mon 26/04/20	Thu 26/04/16	2d	Fri 26/05/01	Wed 26/04/29	2d
127	Janus Framing System	5 days	5 days	0d	Mon 26/05/04	Thu 26/04/30	2d	Fri 26/05/08	Wed 26/05/06	2d
128	Roof Decking	5 days	5 days	0d	Mon 26/05/11	Thu 26/05/07	2d	Fri 26/05/15	Wed 26/05/13	2d
129	**Roof**	**5 days**	**5 days**	**0d**	**Mon 26/05/18**	**Thu 26/05/14**	**2d**	**Fri 26/05/22**	**Wed 26/05/20**	**2d**
130	Metal Roofing	5 days	5 days	0d	Mon 26/05/18	Thu 26/05/14	2d	Fri 26/05/22	Wed 26/05/20	2d
131	**Framing and MEP**	**20 days**	**20 days**	**0d**	**Mon 26/05/25**	**Thu 26/05/21**	**2d**	**Fri 26/06/19**	**Wed 26/06/17**	**2d**
132	**First Floor**	**20 days**	**20 days**	**0d**	**Mon 26/05/25**	**Thu 26/05/21**	**2d**	**Fri 26/06/19**	**Wed 26/06/17**	**2d**
133	1st Floor MEP Rough-In Area 1	10 days	10 days	0d	Mon 26/05/25	Thu 26/05/21	2d	Fri 26/06/05	Wed 26/06/03	2d
134	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Mon 26/06/08	Thu 26/06/04	2d	Fri 26/06/19	Wed 26/06/17	2d
135	**Exterior Finishes**	**25 days**	**25 days**	**0d**	**Wed 26/06/10**	**Thu 26/05/14**	**19d**	**Tue 26/07/14**	**Wed 26/06/17**	**19d**
136	Metal Panels Completion	15 days	15 days	0d	Wed 26/06/10	Thu 26/05/14	19d	Tue 26/06/30	Wed 26/06/03	19d

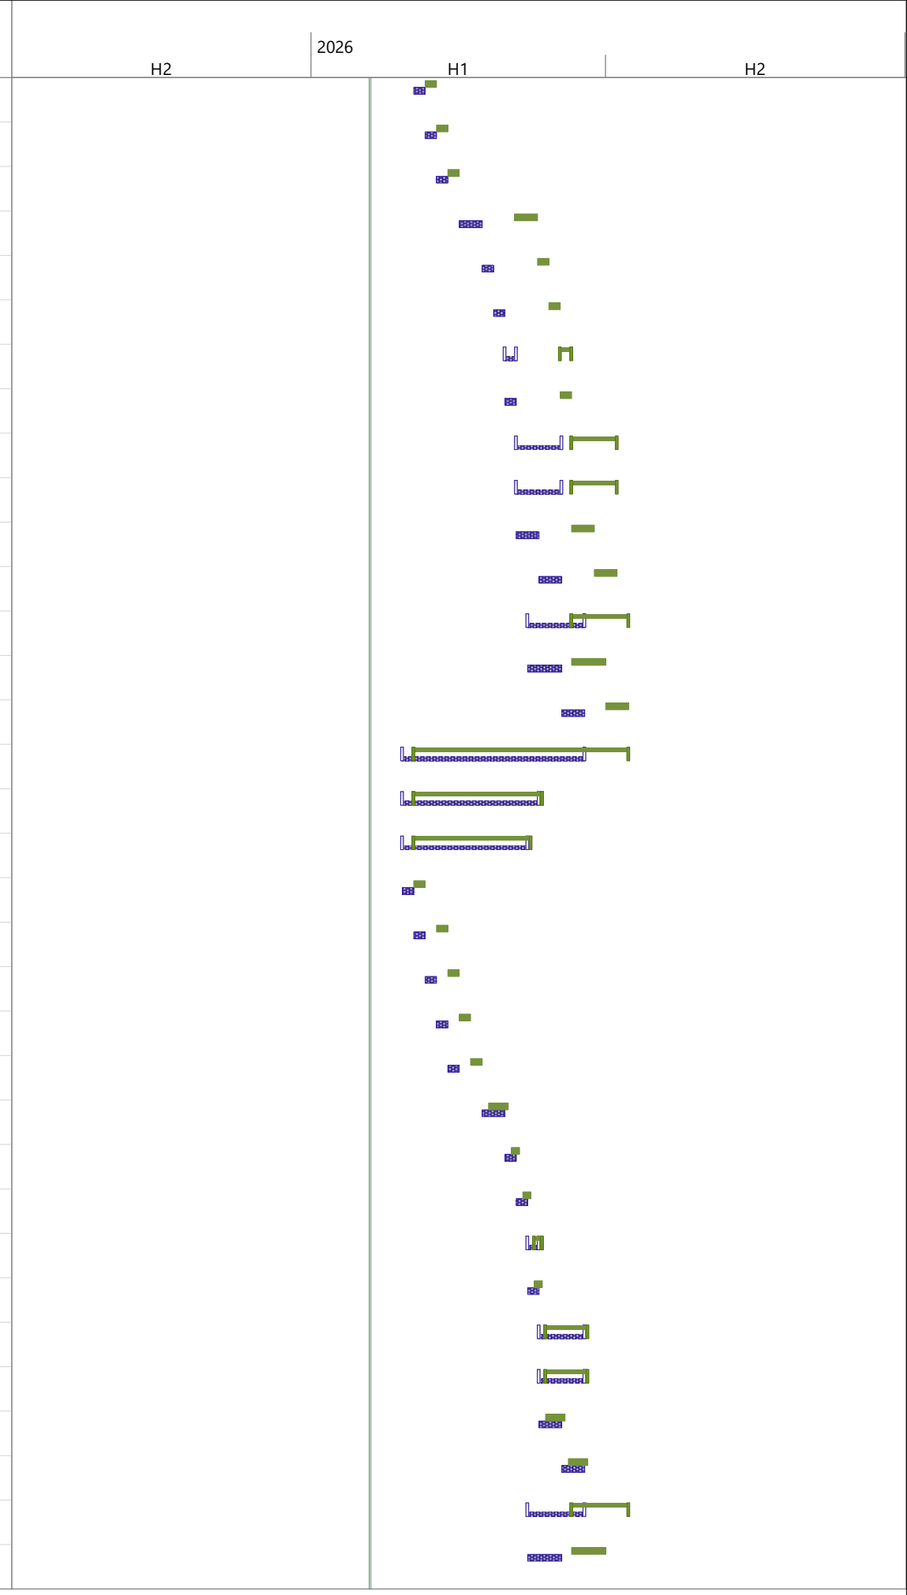
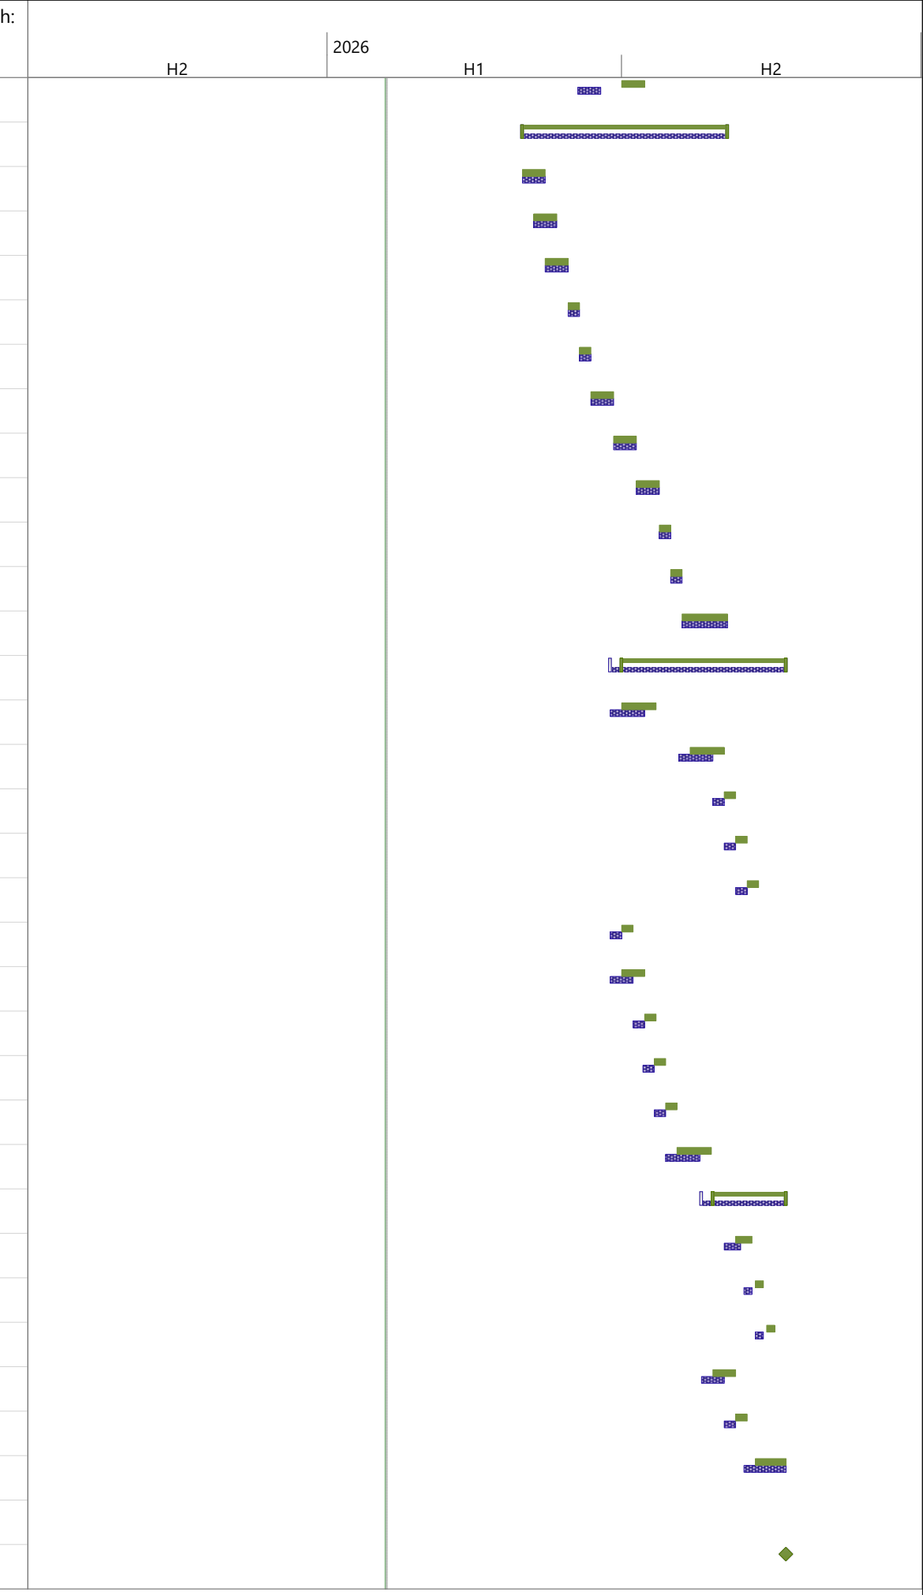
	Name	Duration: Current	Duration: Previous	Dura Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
137	Exterior Signage Install	10 days	10 days	0d	Wed 26/07/01	Thu 26/06/04	19d	Tue 26/07/14	Wed 26/06/17	19d
138	**Site Finishes**	**90 days**	**90 days**	**0d**	**Fri 26/05/01**	**Fri 26/05/01**	**0d**	**Thu 26/09/03**	**Thu 26/09/03**	**0d**
139	Site Fine Grading	10 days	10 days	0d	Fri 26/05/01	Fri 26/05/01	0d	Thu 26/05/14	Thu 26/05/14	0d
140	Stone Base	10 days	10 days	0d	Fri 26/05/08	Fri 26/05/08	0d	Thu 26/05/21	Thu 26/05/21	0d
141	Curb / Sidewalks	10 days	10 days	0d	Fri 26/05/15	Fri 26/05/15	0d	Thu 26/05/28	Thu 26/05/28	0d
142	Binder Course Asphalt - Area 1	5 days	5 days	0d	Fri 26/05/29	Fri 26/05/29	0d	Thu 26/06/04	Thu 26/06/04	0d
143	Binder Course Asphalt - Area 2	5 days	5 days	0d	Fri 26/06/05	Fri 26/06/05	0d	Thu 26/06/11	Thu 26/06/11	0d
144	Landscaping - Area 1	10 days	10 days	0d	Fri 26/06/12	Fri 26/06/12	0d	Thu 26/06/25	Thu 26/06/25	0d
145	Landscaping - Area 2	10 days	10 days	0d	Fri 26/06/26	Fri 26/06/26	0d	Thu 26/07/09	Thu 26/07/09	0d
146	Final Pavement	10 days	10 days	0d	Fri 26/07/10	Fri 26/07/10	0d	Thu 26/07/23	Thu 26/07/23	0d
147	Line Marking/Signage	5 days	5 days	0d	Fri 26/07/24	Fri 26/07/24	0d	Thu 26/07/30	Thu 26/07/30	0d
148	As-Builts Complete & Submitted to AHJ	5 days	5 days	0d	Fri 26/07/31	Fri 26/07/31	0d	Thu 26/08/06	Thu 26/08/06	0d
149	As-Built/City Review	20 days	20 days	0d	Fri 26/08/07	Fri 26/08/07	0d	Thu 26/09/03	Thu 26/09/03	0d
150	**Interior Upfit**	**73 days**	**78 days**	**-5d**	**Wed 26/07/01**	**Wed 26/06/24**	**5d**	**Fri 26/10/09**	**Fri 26/10/09**	**0d**
151	1st Floor - Janus Unit Install	15 days	15 days	0d	Wed 26/07/01	Wed 26/06/24	5d	Tue 26/07/21	Tue 26/07/14	5d
152	2nd Floor - Janus Unit Install	15 days	15 days	0d	Wed 26/08/12	Wed 26/08/05	5d	Tue 26/09/01	Tue 26/08/25	5d
153	Bldg B Janus Install	5 days	5 days	0d	Wed 26/09/02	Wed 26/08/26	5d	Tue 26/09/08	Tue 26/09/01	5d
154	Bldg C Janus Install	5 days	5 days	0d	Wed 26/09/09	Wed 26/09/02	5d	Tue 26/09/15	Tue 26/09/08	5d
155	Bldg D Janus Install	5 days	5 days	0d	Wed 26/09/16	Wed 26/09/09	5d	Tue 26/09/22	Tue 26/09/15	5d
156	Drywall Hanging	5 days	5 days	0d	Wed 26/07/01	Wed 26/06/24	5d	Tue 26/07/07	Tue 26/06/30	5d
157	Drywall Finishing	10 days	10 days	0d	Wed 26/07/01	Wed 26/06/24	5d	Tue 26/07/14	Tue 26/07/07	5d
158	Paint	5 days	5 days	0d	Wed 26/07/15	Wed 26/07/08	5d	Tue 26/07/21	Tue 26/07/14	5d
159	Millwork	5 days	5 days	0d	Tue 26/07/21	Tue 26/07/14	5d	Mon 26/07/27	Mon 26/07/20	5d
160	Floor Sealer - 2nd Floor	5 days	5 days	0d	Tue 26/07/28	Tue 26/07/21	5d	Mon 26/08/03	Mon 26/07/27	5d
161	Floor Sealer / Polish - 1st Floor and drive ups	15 days	15 days	0d	Tue 26/08/04	Tue 26/07/28	5d	Mon 26/08/24	Mon 26/08/17	5d
162	**Closeout**	**33 days**	**38 days**	**-5d**	**Wed 26/08/26**	**Wed 26/08/19**	**5d**	**Fri 26/10/09**	**Fri 26/10/09**	**0d**
163	Final Clean - Bldg A	8 days	8 days	0d	Wed 26/09/09	Wed 26/09/02	5d	Fri 26/09/18	Fri 26/09/11	5d
164	Final Clean - Bldg B	5 days	5 days	0d	Mon 26/09/21	Mon 26/09/14	5d	Fri 26/09/25	Fri 26/09/18	5d
165	Final Clean - Bldg C and D	5 days	5 days	0d	Mon 26/09/28	Mon 26/09/21	5d	Fri 26/10/02	Fri 26/09/25	5d
166	MEP Final Inspections	10 days	10 days	0d	Wed 26/08/26	Wed 26/08/19	5d	Tue 26/09/08	Tue 26/09/01	5d
167	Building Final Inspections	5 days	5 days	0d	Wed 26/09/09	Wed 26/09/02	5d	Tue 26/09/15	Tue 26/09/08	5d
168	Weather Days Included (20 Days)	15 days	20 days	-5d	Mon 26/09/21	Mon 26/09/14	5d	Fri 26/10/09	Fri 26/10/09	0d
169	**Substantial Completion**	**0 days**	**0 days**	**0d**	**Fri 26/10/09**	**Fri 26/10/09**	**0d**	**Fri 26/10/09**	**Fri 26/10/09**	**0d**
170	Substantial Completion	0 days	0 days	0d	Fri 26/10/09	Fri 26/10/09	0d	Fri 26/10/09	Fri 26/10/09	0d
