ID	Task Name	Duration	Start	Finish
1	**Public Storage Selma, NC**	**263 days**	**Mon 10/6/25**	**Fri 10/9/26**
2	Award Contract	0 days	Mon 10/6/25	Mon 10/6/25
3	**Mobilization**	**6 days**	**Mon 12/1/25**	**Mon 12/8/25**
4	Mobilization (Site Fence, Layout, Barricades, Etc.)	1 day	Mon 1/5/26	Mon 1/5/26
5	SWPPP	5 days	Mon 12/15/25	Fri 12/19/25
6	**Demo/Site Work**	**87 days**	**Mon 1/5/26**	**Tue 5/5/26**
7	Clearing and Grubbing	10 days	Mon 1/5/26	Fri 1/16/26
8	Dewatering	5 days	Mon 1/19/26	Fri 1/23/26
9	Rough Grading	18 days	Mon 1/19/26	Wed 2/11/26
10	Storm System	21 days	Mon 3/2/26	Mon 3/30/26
11	Sanitary Sewer	5 days	Tue 3/31/26	Mon 4/6/26
12	Water	10 days	Fri 3/20/26	Thu 4/2/26
13	Site Electrical	10 days	Wed 4/8/26	Tue 4/21/26
14	Building Tie In	10 days	Wed 4/22/26	Tue 5/5/26
15	**Building A**	**149 days**	**Tue 1/27/26**	**Fri 8/21/26**
16	**Structure**	**133 days**	**Tue 1/27/26**	**Thu 7/30/26**
17	**First Floor**	**93 days**	**Tue 1/27/26**	**Thu 6/4/26**
18	Weather Delay(Snow & Ice)	12 days	Tue 1/27/26	Wed 2/11/26
19	Building Pad Delivery (Bldg A)	5 days	Mon 3/9/26	Fri 3/13/26
20	Elevator Pit - Excavate	2 days	Mon 3/9/26	Tue 3/10/26
21	Elevator Pit - Form and Pour	10 days	Tue 3/10/26	Mon 3/23/26
22	FRP Foundations / Foundation CMU - Area 1	7 days	Mon 3/16/26	Tue 3/24/26
23	Concrete Retaining Walls	10 days	Wed 3/25/26	Tue 4/7/26
24	FRP Foundations/Foundation Area 2	7 days	Wed 4/8/26	Thu 4/16/26
25	Under Slab MEP	10 days	Fri 4/3/26	Thu 4/16/26
26	Slab #1 Prep / Pour (North Half)	10 days	Fri 4/10/26	Thu 4/23/26
27	CMU shafts	15 days	Fri 4/24/26	Thu 5/14/26
28	Slab #2 Prep / Pour (South Half)	10 days	Fri 4/24/26	Thu 5/7/26
29	Janus Framing System (North Half)	15 days	Fri 4/24/26	Thu 5/14/26
30	Janus Framing System (South Half)	15 days	Fri 5/15/26	Thu 6/4/26
31	**Second Floor**	**40 days**	**Fri 5/22/26**	**Thu 7/16/26**
32	Elevated Slab #1 (North Half) Prep/Pour	5 days	Fri 5/22/26	Thu 5/28/26
33	Elevated Slab #2 (South Half) Prep/Pour	5 days	Fri 5/29/26	Thu 6/4/26
34	Janus Framing System (North Half)	15 days	Fri 6/5/26	Thu 6/25/26
35	Janus Framing System (South Half)	15 days	Fri 6/26/26	Thu 7/16/26
36	**Stairs**	**20 days**	**Fri 5/15/26**	**Thu 6/11/26**
37	Stair #1	10 days	Fri 5/15/26	Thu 5/28/26
38	Stair #2	10 days	Fri 5/29/26	Thu 6/11/26
39	**Roof**	**10 days**	**Fri 7/17/26**	**Thu 7/30/26**
40	Metal Roofing	10 days	Fri 7/17/26	Thu 7/30/26
41	**Framing and MEP**	**50 days**	**Fri 5/29/26**	**Thu 8/6/26**
42	**First Floor**	**35 days**	**Fri 5/29/26**	**Thu 7/16/26**
43	Interior Framing	5 days	Fri 6/5/26	Thu 6/11/26
44	1st Floor MEP Rough-In Area 1	20 days	Fri 5/29/26	Thu 6/25/26
45	1st Floor MEP Rough-In Area 2	15 days	Fri 6/5/26	Thu 6/25/26
46	1st Floor MEP Trim Out Area 1	10 days	Fri 6/26/26	Thu 7/9/26
47	1st Floor MEP Trim Out Area 2	5 days	Fri 7/10/26	Thu 7/16/26
48	**Second Floor**	**45 days**	**Fri 6/5/26**	**Thu 8/6/26**
49	Interior Framing	5 days	Fri 6/5/26	Thu 6/11/26
50	2nd Floor MEP Rough-In Area 2	15 days	Fri 6/26/26	Thu 7/16/26
51	2nd Floor MEP Rough-In Area 2	15 days	Fri 7/17/26	Thu 8/6/26
52	2nd Floor MEP Trim Out Area 1	10 days	Fri 7/17/26	Thu 7/30/26
53	2nd Floor MEP Trim Out Area 2	5 days	Fri 7/31/26	Thu 8/6/26
54	**Elevator**	**30 days**	**Mon 7/13/26**	**Fri 8/21/26**
55	Delivery	0 days	Mon 7/13/26	Mon 7/13/26

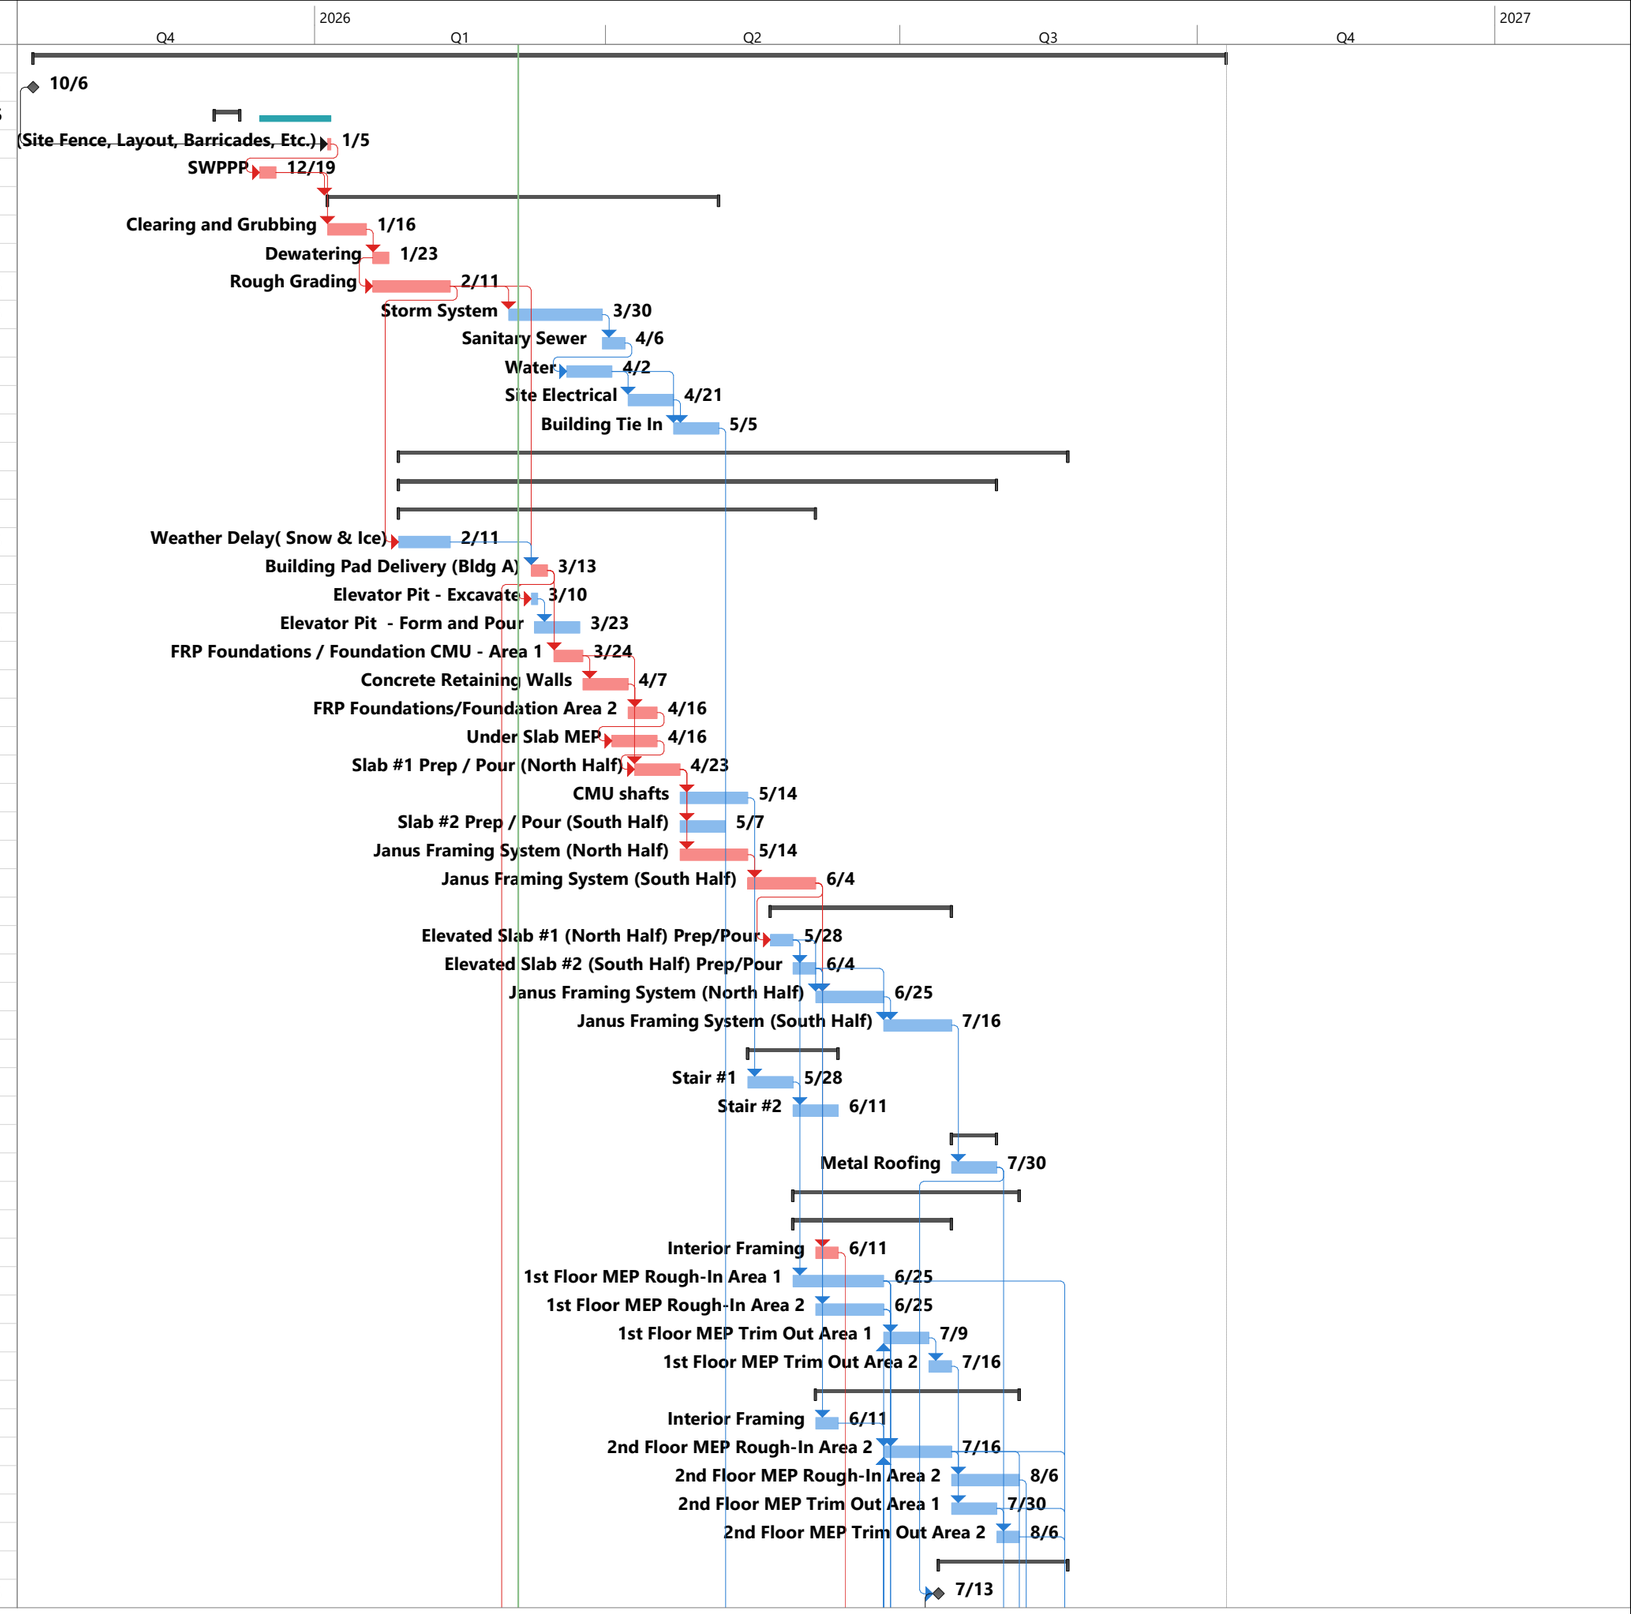

ID	Task Name	Duration	Start	Finish
56	Elevator 1 - First Floor	5 days	Mon 7/13/26	Fri 7/17/26
57	Elevator 1 - Second Floor	5 days	Mon 7/20/26	Fri 7/24/26
58	Elevator 2 - First Floor	5 days	Mon 7/27/26	Fri 7/31/26
59	Elevator 2 - Second Floor	5 days	Mon 8/3/26	Fri 8/7/26
60	Infill Doors	5 days	Mon 8/3/26	Fri 8/7/26
61	Test / Adjust	5 days	Mon 8/10/26	Fri 8/14/26
62	State Inspection	5 days	Mon 8/17/26	Fri 8/21/26
63	**Exterior Finishes**	**50 days**	**Fri 6/12/26**	**Thu 8/20/26**
64	Masonry Veneer	15 days	Fri 6/12/26	Thu 7/2/26
65	Metal Panels Completion	15 days	Fri 7/3/26	Thu 7/23/26
66	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	Fri 7/31/26	Thu 8/13/26
67	Automatic Entrance Door	5 days	Fri 7/3/26	Thu 7/9/26
68	Exterior Paint	10 days	Fri 7/24/26	Thu 8/6/26
69	Exterior Signage Install	10 days	Fri 8/7/26	Thu 8/20/26
70	Canopy	10 days	Fri 8/7/26	Thu 8/20/26
71	**Building B**	**75 days**	**Wed 3/4/26**	**Tue 6/16/26**
72	**Structure**	**35 days**	**Wed 3/4/26**	**Tue 4/21/26**
73	**First Floor**	**30 days**	**Wed 3/4/26**	**Tue 4/14/26**
74	Building Pad Delivery (Bldg B)	3 days	Wed 3/4/26	Fri 3/6/26
75	FRP Foundations / Foundation CMU - Area 1	5 days	Mon 3/9/26	Fri 3/13/26
76	Under Slab MEP	5 days	Mon 3/9/26	Fri 3/13/26
77	Slab Prep / Pour	5 days	Thu 3/12/26	Wed 3/18/26
78	CMU Walls	10 days	Wed 3/25/26	Tue 4/7/26
79	Janus Framing System	5 days	Wed 4/8/26	Tue 4/14/26
80	**Roof**	**5 days**	**Mon 4/6/26**	**Fri 4/10/26**
81	Metal Roofing	5 days	Wed 4/15/26	Tue 4/21/26
82	**Framing and MEP**	**25 days**	**Wed 4/15/26**	**Tue 5/19/26**
83	**First Floor**	**25 days**	**Wed 4/15/26**	**Tue 5/19/26**
84	Interior Framing	5 days	Wed 4/15/26	Tue 4/21/26
85	1st Floor MEP Rough-In Area 1	10 days	Wed 4/22/26	Tue 5/5/26
86	Finishes	10 days	Wed 4/22/26	Tue 5/5/26
87	1st Floor MEP Trim Out Area 1	10 days	Wed 5/6/26	Tue 5/19/26
88	**Exterior Finishes**	**25 days**	**Wed 5/13/26**	**Tue 6/16/26**
89	Metal Panels Completion	5 days	Wed 5/13/26	Tue 5/19/26
90	Sheetmetal Work (Coping, Gutters, & Downspouts)	3 days	Wed 5/20/26	Fri 5/22/26
91	Automatic Entrance Door	5 days	Wed 5/20/26	Tue 5/26/26
92	Exterior Paint	10 days	Wed 5/20/26	Tue 6/2/26
93	Exterior Signage Install	10 days	Wed 6/3/26	Tue 6/16/26
94	Canopy	10 days	Wed 6/3/26	Tue 6/16/26
95	**Building C**	**48 days**	**Mon 3/2/26**	**Wed 5/6/26**
96	**Structure**	**35 days**	**Mon 3/2/26**	**Fri 4/17/26**
97	**First Floor**	**30 days**	**Mon 3/2/26**	**Fri 4/10/26**
98	Building Pad Delivery (Bldg C)	5 days	Mon 3/2/26	Fri 3/6/26
99	FRP Foundations / Foundation CMU - Area 1	5 days	Wed 3/4/26	Tue 3/10/26
100	FRP Foundations/Foundation Area 2	5 days	Wed 3/11/26	Tue 3/17/26
101	Under Slab MEP	5 days	Wed 3/11/26	Tue 3/17/26
102	Slab Prep / Pour	5 days	Wed 3/11/26	Tue 3/17/26
103	CMU Walls	10 days	Mon 3/23/26	Fri 4/3/26
104	Janus Framing System	5 days	Mon 4/6/26	Fri 4/10/26
105	**Roof**	**5 days**	**Mon 4/13/26**	**Fri 4/17/26**
106	Metal Roofing	5 days	Mon 4/13/26	Fri 4/17/26
107	**Framing and MEP**	**4 days**	**Mon 4/20/26**	**Thu 4/23/26**
108	**First Floor**	**4 days**	**Mon 4/20/26**	**Thu 4/23/26**
109	1st Floor MEP Rough-In Area 1	2 days	Mon 4/20/26	Tue 4/21/26
110	1st Floor MEP Trim Out Area 1	2 days	Wed 4/22/26	Thu 4/23/26

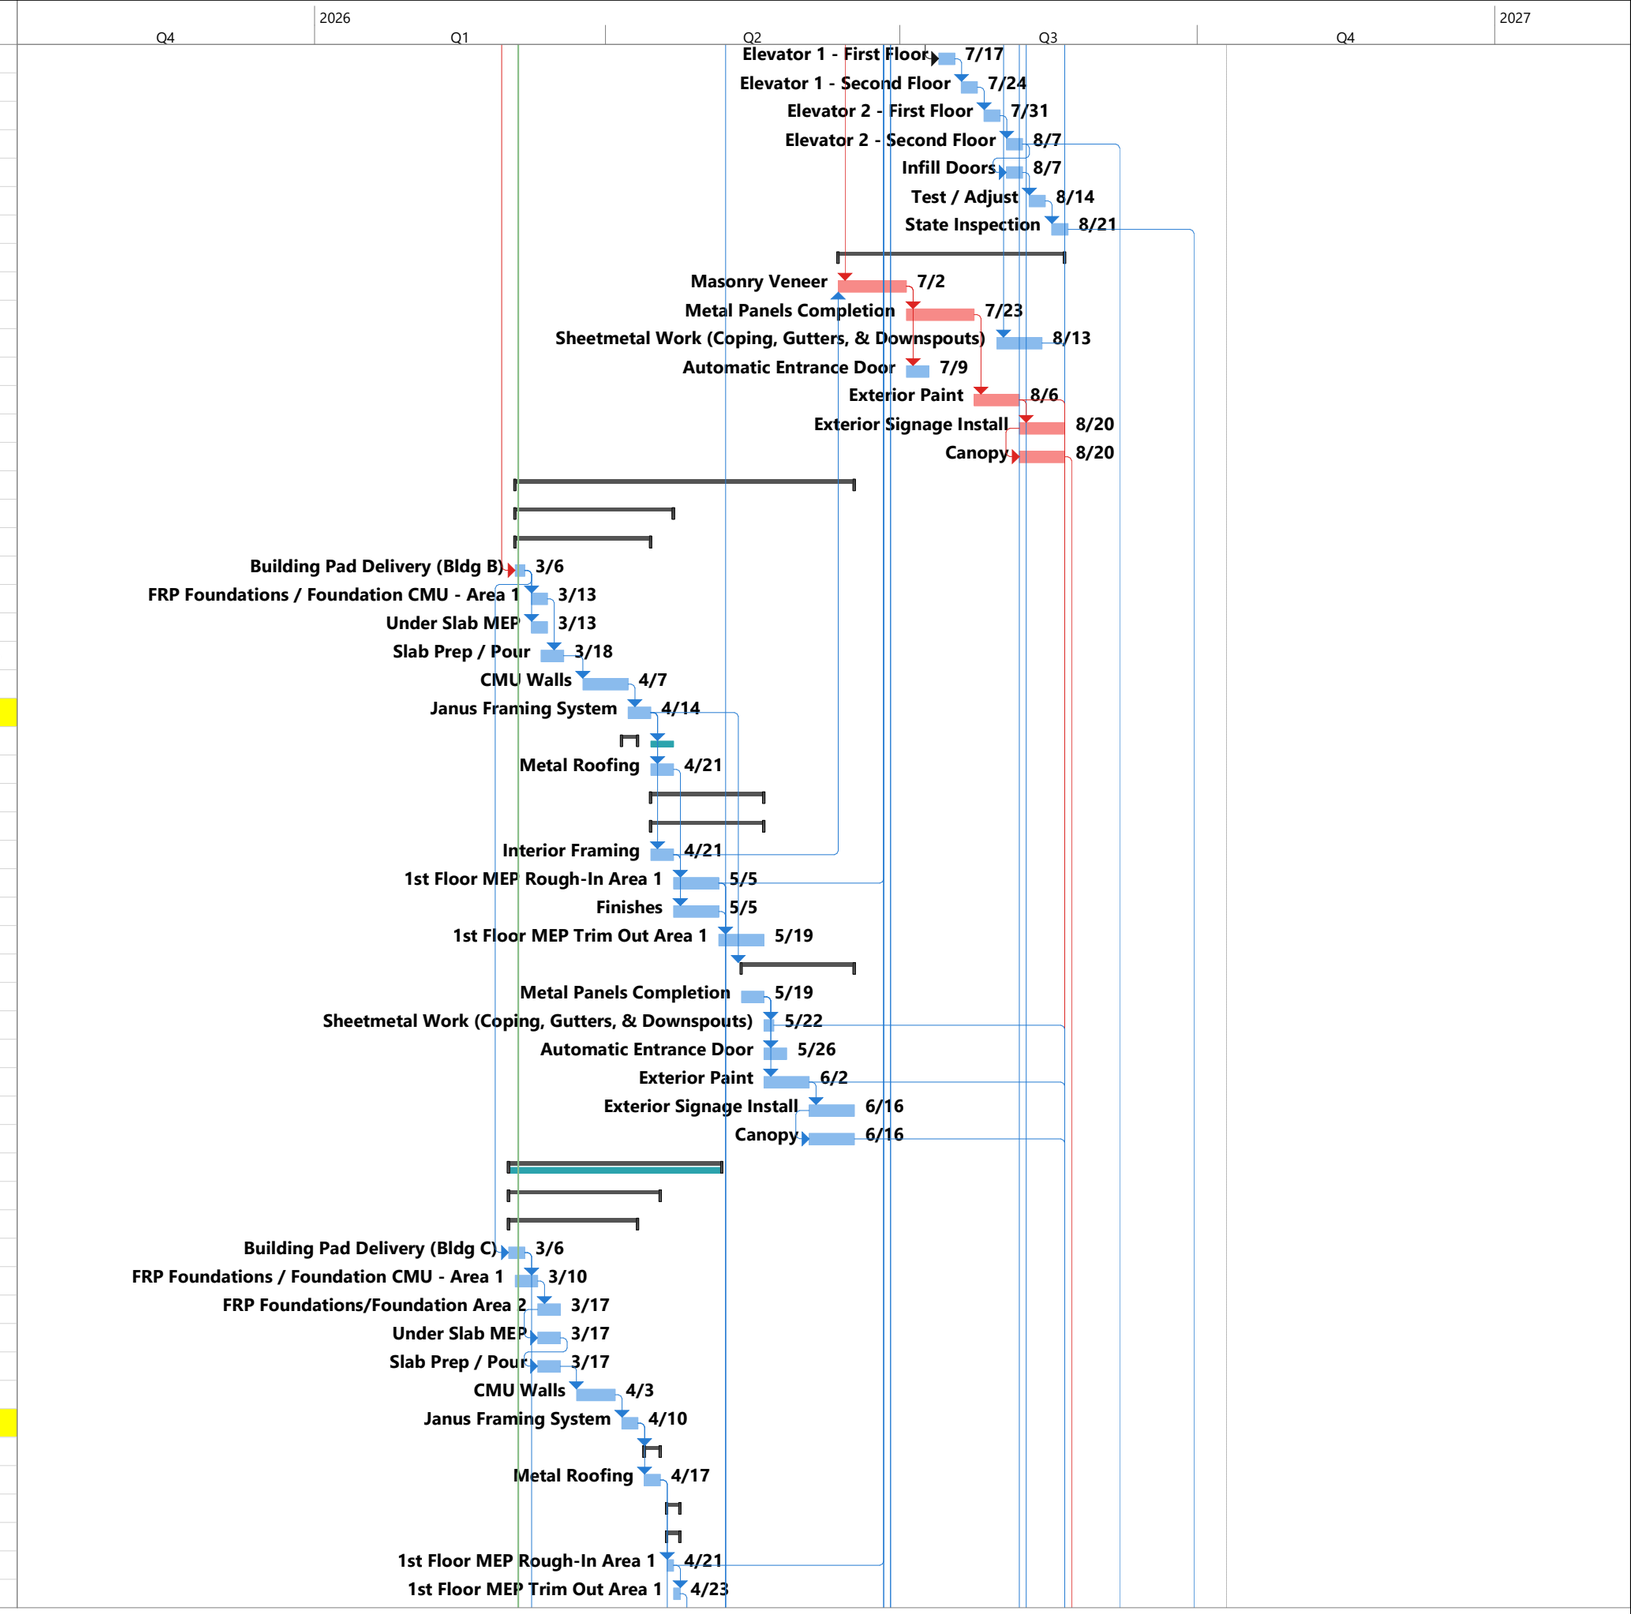
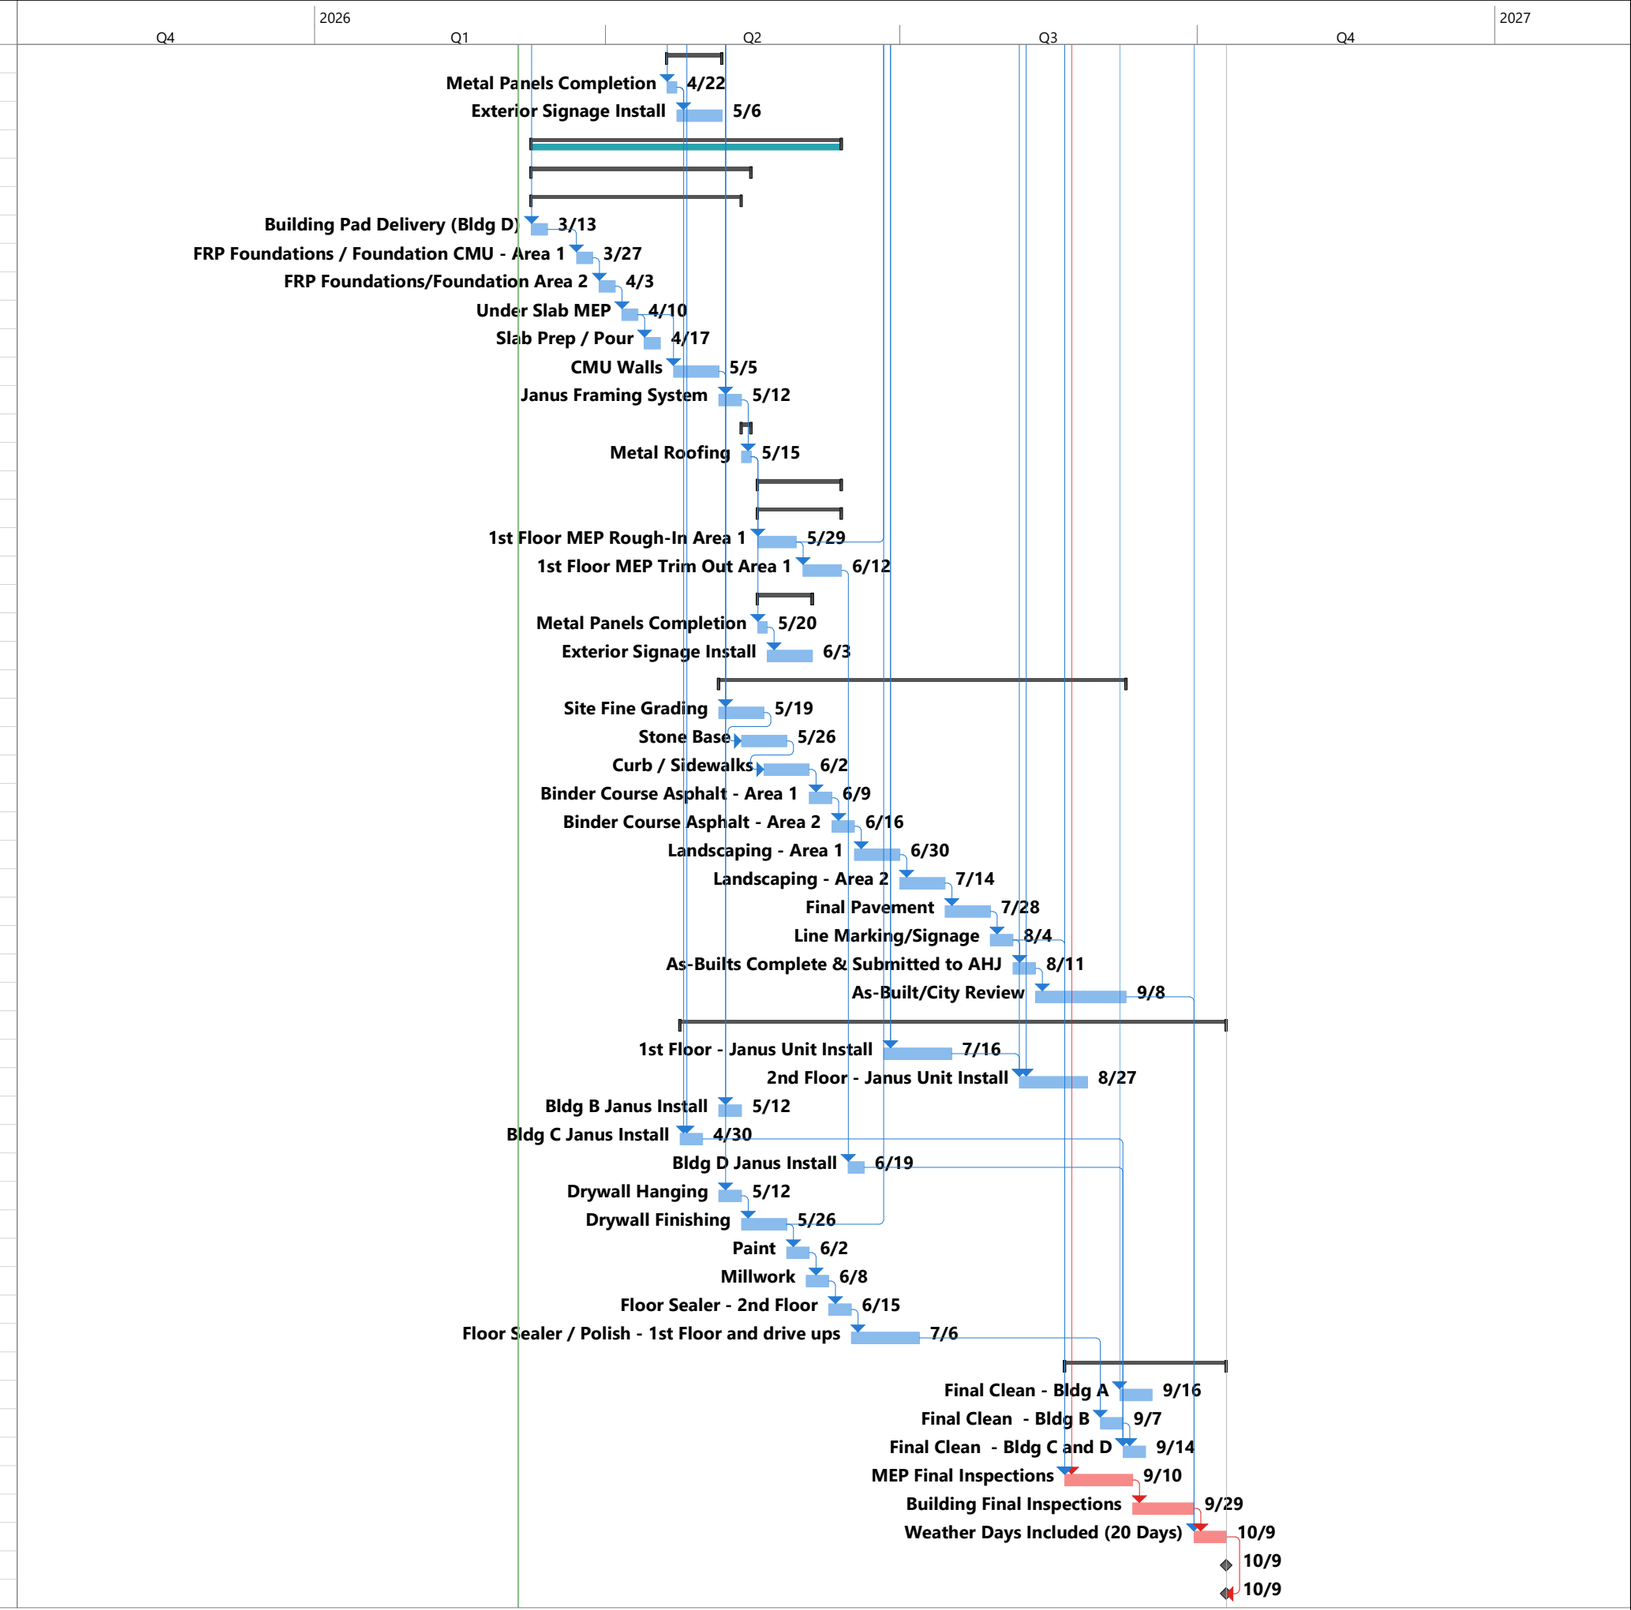
ID	Task Name	Duration	Start	Finish
111	**Exterior Finishes**	**13 days**	**Mon 4/20/26**	**Wed 5/6/26**
112	Metal Panels Completion	3 days	Mon 4/20/26	Wed 4/22/26
113	Exterior Signage Install	10 days	Thu 4/23/26	Wed 5/6/26
114	**Building D**	**70 days**	**Mon 3/9/26**	**Fri 6/12/26**
115	**Structure**	**50 days**	**Mon 3/9/26**	**Fri 5/15/26**
116	**First Floor**	**47 days**	**Mon 3/9/26**	**Tue 5/12/26**
117	Building Pad Delivery (Bldg D)	5 days	Mon 3/9/26	Fri 3/13/26
118	FRP Foundations / Foundation CMU - Area 1	5 days	Mon 3/23/26	Fri 3/27/26
119	FRP Foundations/Foundation Area 2	5 days	Mon 3/30/26	Fri 4/3/26
120	Under Slab MEP	5 days	Mon 4/6/26	Fri 4/10/26
121	Slab Prep / Pour	5 days	Mon 4/13/26	Fri 4/17/26
122	CMU Walls	10 days	Wed 4/22/26	Tue 5/5/26
123	Janus Framing System	5 days	Wed 5/6/26	Tue 5/12/26
124	**Roof**	**3 days**	**Wed 5/13/26**	**Fri 5/15/26**
125	Metal Roofing	3 days	Wed 5/13/26	Fri 5/15/26
126	**Framing and MEP**	**20 days**	**Mon 5/18/26**	**Fri 6/12/26**
127	**First Floor**	**20 days**	**Mon 5/18/26**	**Fri 6/12/26**
128	1st Floor MEP Rough-In Area 1	10 days	Mon 5/18/26	Fri 5/29/26
129	1st Floor MEP Trim Out Area 1	10 days	Mon 6/1/26	Fri 6/12/26
130	**Exterior Finishes**	**13 days**	**Mon 5/18/26**	**Wed 6/3/26**
131	Metal Panels Completion	3 days	Mon 5/18/26	Wed 5/20/26
132	Exterior Signage Install	10 days	Thu 5/21/26	Wed 6/3/26
133	**Site Finishes**	**90 days**	**Wed 5/6/26**	**Tue 9/8/26**
134	Site Fine Grading	10 days	Wed 5/6/26	Tue 5/19/26
135	Stone Base	10 days	Wed 5/13/26	Tue 5/26/26
136	Curb / Sidewalks	10 days	Wed 5/20/26	Tue 6/2/26
137	Binder Course Asphalt - Area 1	5 days	Wed 6/3/26	Tue 6/9/26
138	Binder Course Asphalt - Area 2	5 days	Wed 6/10/26	Tue 6/16/26
139	Landscaping - Area 1	10 days	Wed 6/17/26	Tue 6/30/26
140	Landscaping - Area 2	10 days	Wed 7/1/26	Tue 7/14/26
141	Final Pavement	10 days	Wed 7/15/26	Tue 7/28/26
142	Line Marking/Signage	5 days	Wed 7/29/26	Tue 8/4/26
143	As-Builts Complete & Submitted to AHJ	5 days	Wed 8/5/26	Tue 8/11/26
144	As-Built/City Review	20 days	Wed 8/12/26	Tue 9/8/26
145	**Interior Upfit**	**121 days**	**Fri 4/24/26**	**Fri 10/9/26**
146	1st Floor - Janus Unit Install	15 days	Fri 6/26/26	Thu 7/16/26
147	2nd Floor - Janus Unit Install	15 days	Fri 8/7/26	Thu 8/27/26
148	Bldg B Janus Install	5 days	Wed 5/6/26	Tue 5/12/26
149	Bldg C Janus Install	5 days	Fri 4/24/26	Thu 4/30/26
150	Bldg D Janus Install	5 days	Mon 6/15/26	Fri 6/19/26
151	Drywall Hanging	5 days	Wed 5/6/26	Tue 5/12/26
152	Drywall Finishing	10 days	Wed 5/13/26	Tue 5/26/26
153	Paint	5 days	Wed 5/27/26	Tue 6/2/26
154	Millwork	5 days	Tue 6/2/26	Mon 6/8/26
155	Floor Sealer - 2nd Floor	5 days	Tue 6/9/26	Mon 6/15/26
156	Floor Sealer / Polish - 1st Floor and drive ups	15 days	Tue 6/16/26	Mon 7/6/26
157	**Closeout**	**36 days**	**Fri 8/21/26**	**Fri 10/9/26**
158	Final Clean - Bldg A	8 days	Mon 9/7/26	Wed 9/16/26
159	Final Clean - Bldg B	5 days	Tue 9/1/26	Mon 9/7/26
160	Final Clean - Bldg C and D	5 days	Tue 9/8/26	Mon 9/14/26
161	MEP Final Inspections	15 days	Fri 8/21/26	Thu 9/10/26
162	Building Final Inspections	13 days	Fri 9/11/26	Tue 9/29/26
163	Weather Days Included (20 Days)	8 days	Wed 9/30/26	Fri 10/9/26
164	**Substantial Completion**	**0 days**	**Fri 10/9/26**	**Fri 10/9/26**
165	Substantial Completion	0 days	Fri 10/9/26	Fri 10/9/26
