Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 3/4/2026

Type	Project	Region	Responsible
Construction	Selma, NC	East Coast	Ross Kremers

Baseline Completion Date	Current Completion Date	Schedule Variance	Work Compression
10/9/2026	10/9/2026	0 days Prev: 0 days | Trend: 0 days → No Change	

Critical Path Status & Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	10/6/2025	10/6/2025	10/6/2025	0	0	Award Contract	On Track – Gaining
Foundation Complete	3/24/2026	3/31/2026	4/23/2026	-30	-23	Slab #1 Prep / Pour (North Half)	Delayed – Slipping
Weather Tight	6/16/2026	7/7/2026	7/23/2026	-37	-16	Metal Panels Completion - Building A	Delayed – Slipping
Permanent Power	4/30/2026	4/30/2026	5/5/2026	-5	-5	Building Tie In	Delayed – Slipping
1st Floor Finishes Complete	8/11/2026	8/18/2026	7/30/2026	12	19	2Nd Floor Mep Trim Out Area 1 - Building A	On Track – Gaining
2nd Floor Finishes Complete			8/6/2026			2Nd Floor Mep Trim Out Area 2 - Building A	On Track – Gaining
Hardscape/Landscape Complete	9/3/2026	9/3/2026	9/8/2026	-5	-5	As-Built/City Review	Delayed – Slipping
Contract Completion	10/9/2026	10/9/2026	10/9/2026	0	0	Substantial Completion	On Track – Gaining

Baseline Variance Trends — Critical Milestones

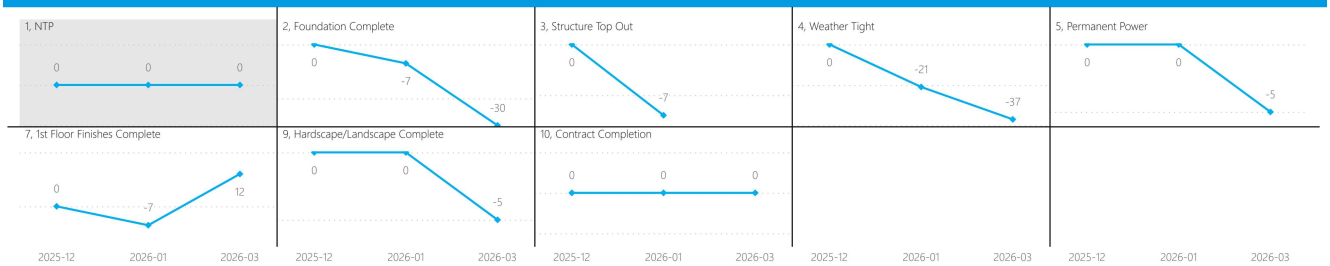

Schedule Performance Summary

Powered By STELIC INSIGHT • ACTION • IMPACT
