Public Storage Ten Mile Rd

Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
1		**GENERAL REQUIREMENTS AND CONDITIONS**	**241 days**	**Mon 25/09/08**	**Tue 26/08/18**
2		**Notice to Proceed**	**1 day**	**Mon 25/09/08**	**Mon 25/09/08**
3		DELAY - PERMIT DELAY	32 days	Tue 25/09/09	Wed 25/10/22
4		**Obtain Building Permit**	**0 days**	**Wed 25/10/22**	**Wed 25/10/22**
5		**ACHD ROW Permit**	**0 days**	**Wed 25/10/29**	**Wed 25/10/29**
6		**Obtain LDIR Approval to Proceed**	**0 days**	**Mon 25/10/27**	**Mon 25/10/27**
7		Receive CAD Base Files from Public Storage	10 days	Tue 25/09/09	Mon 25/09/22
8		Procure Early Work Subcontractors	5 days	Tue 25/09/09	Mon 25/09/15
9		Procure Remaining Subcontractors	20 days	Tue 25/09/16	Mon 25/10/13
10		Submittals (SWPPP/NOI)	10 days	Tue 25/09/16	Mon 25/09/29
11		Submittals (SES /Switchgear)	10 days	Tue 25/09/16	Mon 25/09/29
12		Submittals (numerous)	70 days	Tue 25/10/14	Fri 26/01/23
13		PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	40 days	Tue 25/09/09	Mon 25/11/03
14		PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	40 days	Tue 25/09/23	Mon 25/11/17
15		Procure SES's/Switchgears (6 mos ~ 130 WD)	130 days	Tue 25/09/30	Fri 26/04/03
16		Fire Sprinkler Design and Approval	55 days	Tue 25/10/14	Fri 26/01/02
17		Fire Alarm System Design and Approval	40 days	Tue 25/10/14	Wed 25/12/10
18		**ASPHALT BATCH PLANT SHUTDOWN**	70 days	Mon 25/11/17	Thu 26/02/26
19		**TWENTY WORKING DAYS OF WEATHER DELAY**	17 days	Mon 26/07/27	Tue 26/08/18
20		**Substantial Completion**	**0 days**	**Tue 26/08/18**	**Tue 26/08/18**
21		Clean Up and Project Close Out	5 days	Wed 26/07/15	Tue 26/07/21
22		Demobilize	3 days	Wed 26/07/22	Fri 26/07/24
23		**SITEWORK**	**196 days**	**Mon 25/09/08**	**Mon 26/06/15**
24		Mobilization	5 days	Mon 25/09/08	Mon 25/09/15
25		Construction Staking & Surveying	70 days	Mon 25/09/08	Wed 25/12/17
26		Inspections and Testing	100 days	Fri 25/09/12	Fri 26/02/13
27		Erosion Control & SWPP	5 days	Tue 25/09/16	Mon 25/09/22

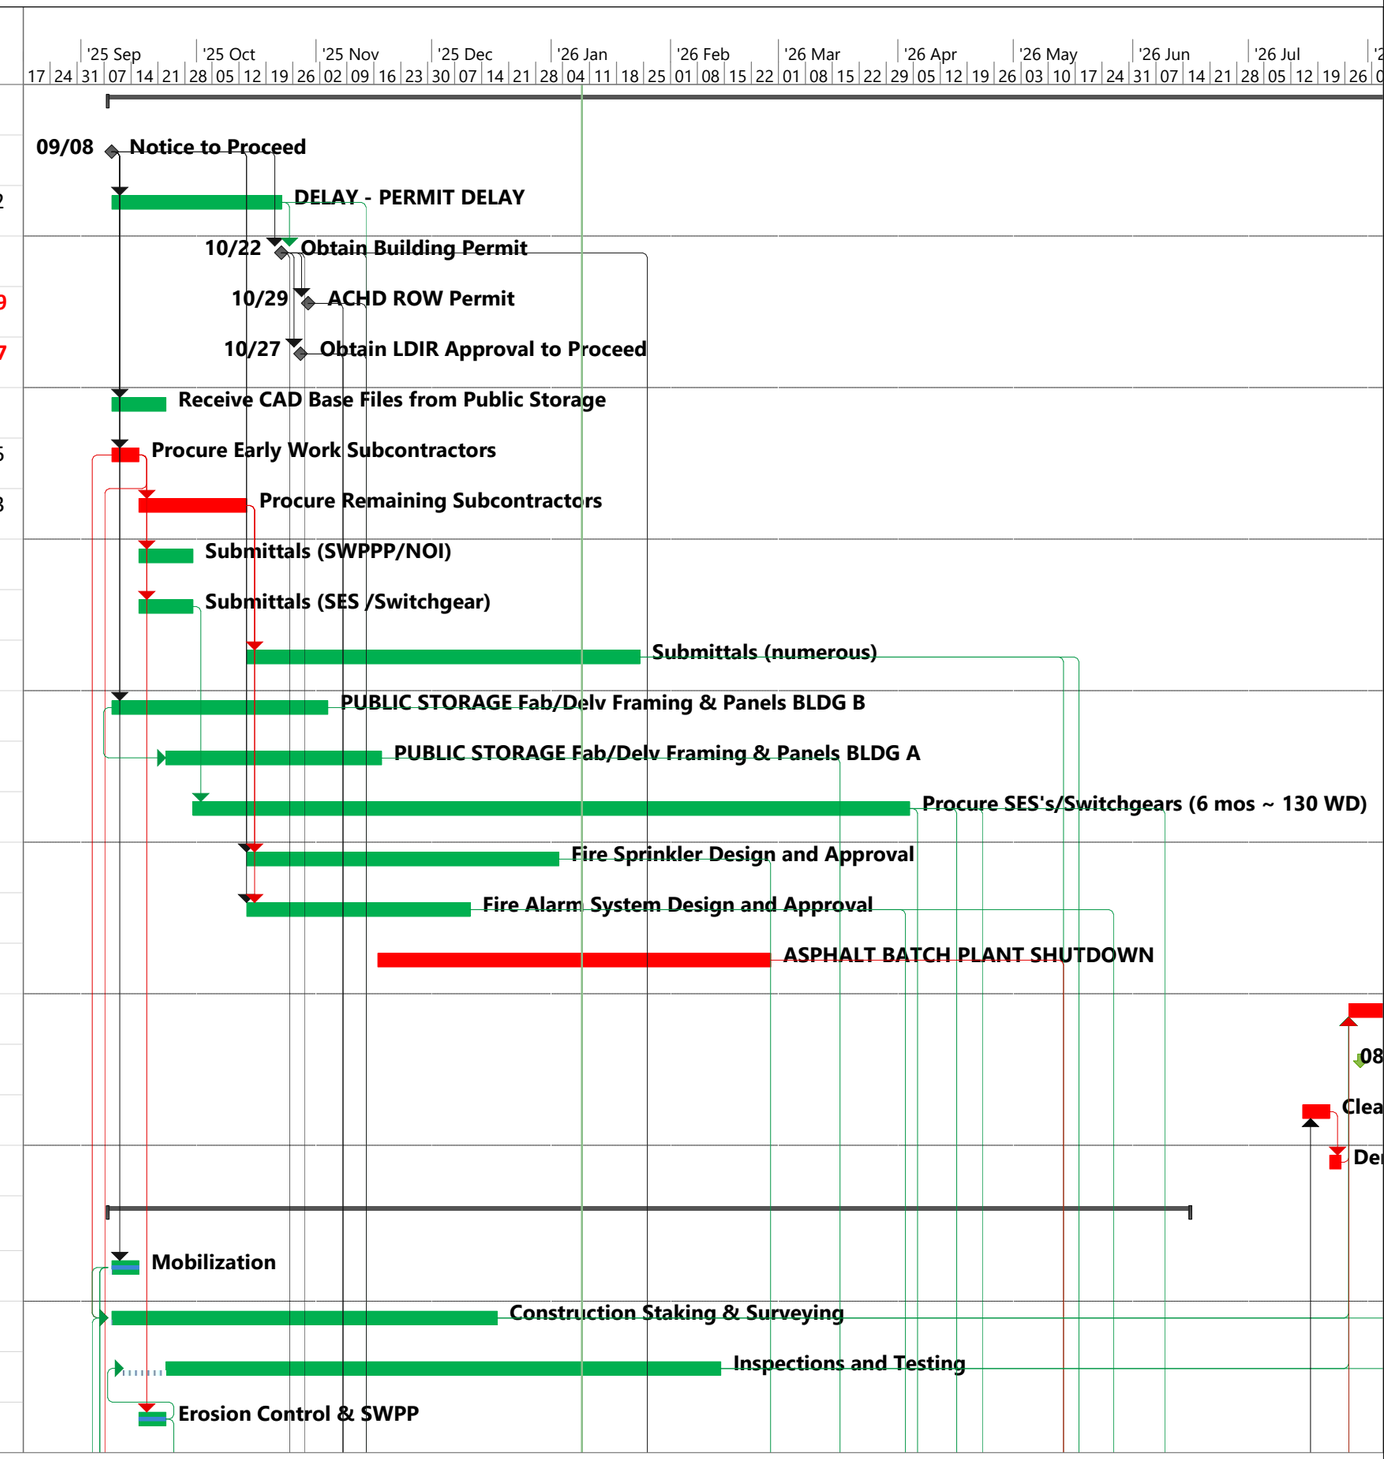

Printed: Fri 26/01/09 08:48

Public Storage Ten Mile Rd
Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
28		Maintain Erosion Control	100 days	Tue 25/09/23	Fri 26/02/13
29		Structure Demo (Partial Building & RV Storage)	5 days	Mon 25/11/03	Fri 25/11/07
30		**Site Demolition (Trees,Sawcut, Asphalt, Base)**	**0 days**	**Mon 25/09/08**	**Fri 25/09/12**
31		Re-Mobilization	4 days	Thu 25/10/23	Tue 25/10/28
32		Clear/Grub & Overlot Grading	12 days	Mon 25/09/08	Tue 25/09/23
33		FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	Wed 25/10/29	Thu 25/11/06
34		Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	Fri 25/11/14	Thu 25/12/04
35		Storm Drain Lines and Devices	15 days	Thu 26/03/26	Wed 26/04/15
36		Storm Drain Lines South	6 days	Mon 25/12/22	Tue 25/12/30
37		DELAY - GIRR License Agreement Approval to Proceed	6 days	Fri 25/12/05	Fri 25/12/12
38		DELAY - RFI #14 - GIRR Separation	4 days	Mon 25/12/15	Thu 25/12/18
39		Site - GIRR Piping & Devices	10 days	Wed 25/12/31	Wed 26/01/14
40		Site - Water Line Ten Mile Tie-In	2 days	Sat 25/11/08	Tue 25/11/11
41		Site - Water Line & Fire Lines/Hydrants and Devices Remaining	12 days	Thu 26/01/08	Fri 26/01/23
42		Complete Utility Lines Tie-ins to Building A	5 days	Thu 26/04/16	Wed 26/04/22
43		Gravel Road	5 days	Mon 26/01/26	Fri 26/01/30
44		BLDG A Foundation Excavation	5 days	Mon 26/01/26	Fri 26/01/30
45		DELAY - BUILDING B FOOTING OVER-EX	4 days	Fri 25/10/31	Wed 25/11/05
46		BLDG B Foundation Excavation	6 days	Wed 25/10/29	Wed 25/11/05
47		BLDG A - Interoir Backfill Foundations	3 days	Mon 26/02/16	Wed 26/02/18
48		BLDG A - Exterior Backfill Foundations	3 days	Mon 26/02/23	Wed 26/02/25
49		BLDG B Backfill Foundations	18 days	Mon 25/12/15	Fri 26/01/09
50		BLDG A SOG Prep	5 days	Thu 26/02/26	Wed 26/03/04
51		**BLDG B SOG Prep**	**0 days**	**Mon 25/12/01**	**Mon 25/12/01**
52		FRAGNET - Bldg B Soft Spot Repair	8 days	Thu 25/12/04	Mon 25/12/15
53		Site Flatwork and Curb & Gutter	15 days	Thu 26/04/23	Wed 26/05/13
54		Landscaping and Irrigation	15 days	Mon 26/05/18	Mon 26/06/08

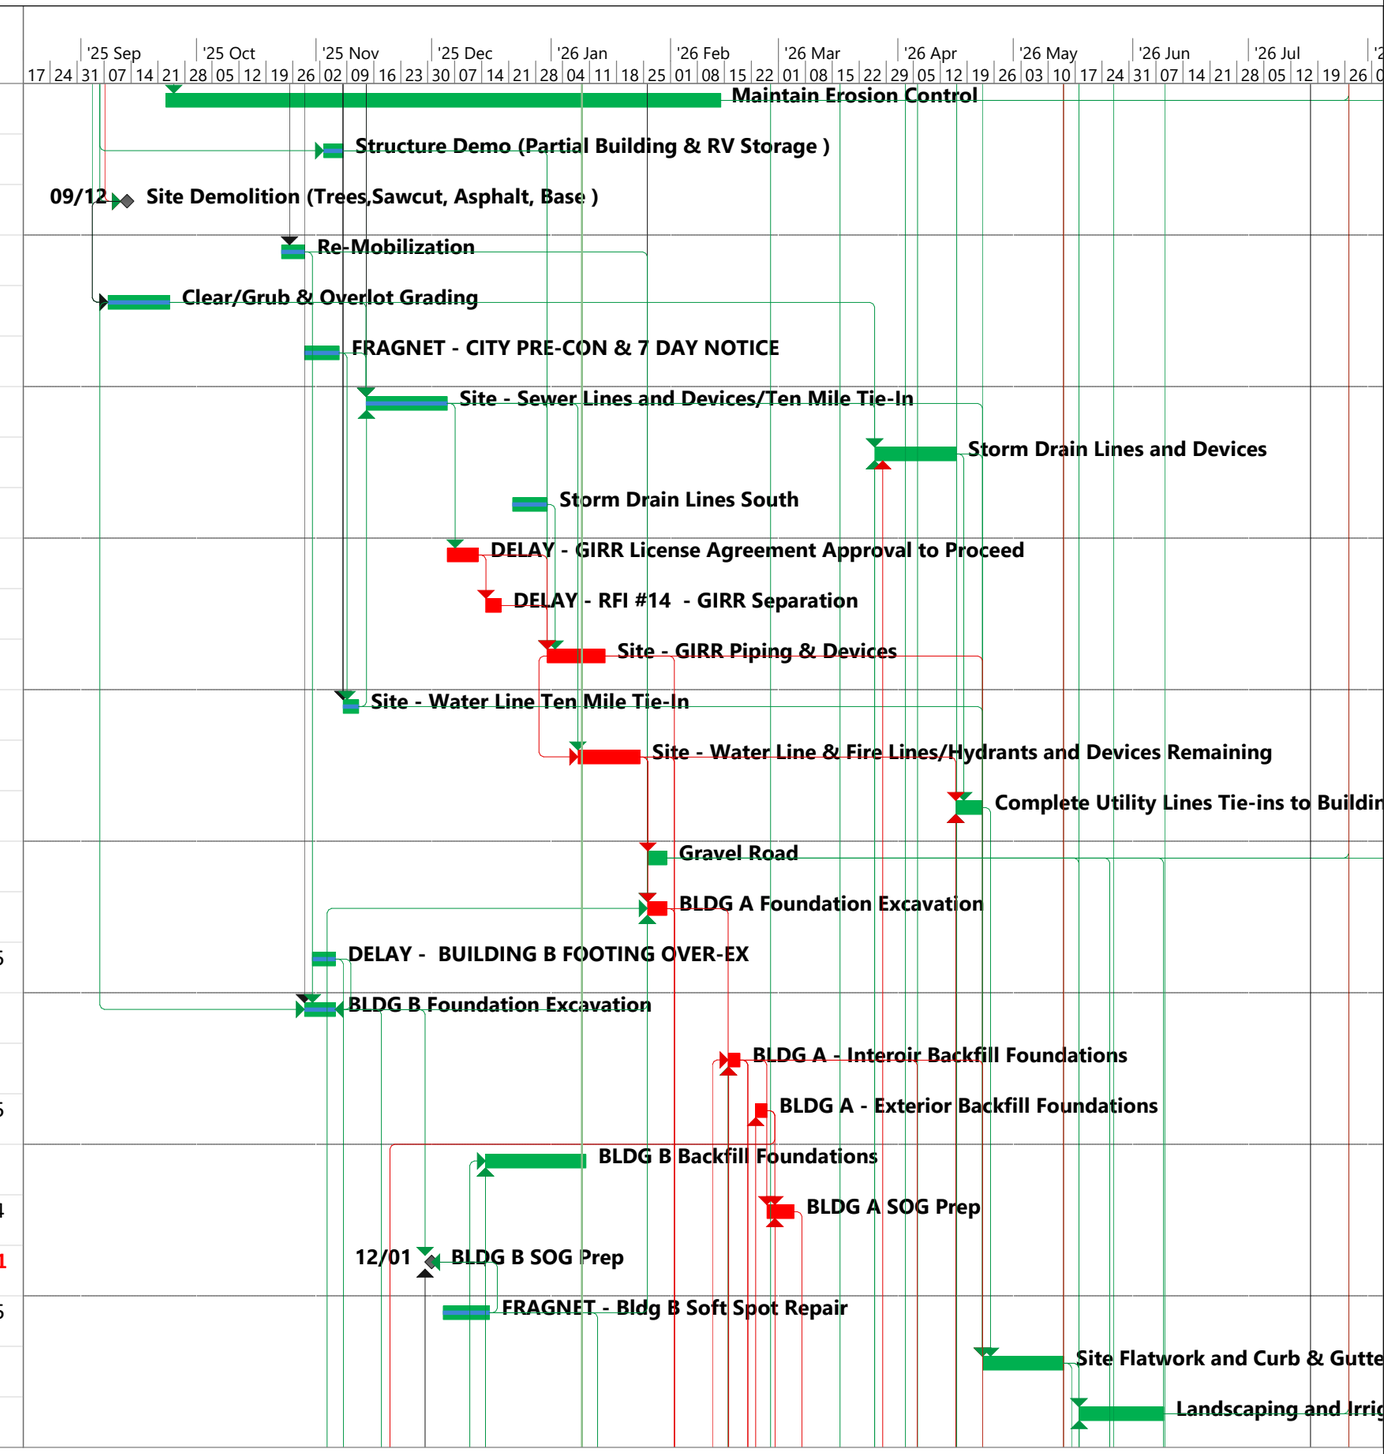

Printed: Fri 26/01/09 08:48

Public Storage Ten Mile Rd
Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
55		Asphalt Paving	2 days	Thu 26/05/14	Fri 26/05/15
56		Pavement Markings, Signage & Bumpers	2 days	Mon 26/05/18	Tue 26/05/19
57		Site Fencing Chainlink	5 days	Mon 26/05/18	Fri 26/05/22
58		Site Fencing Vinyl	10 days	Tue 26/05/26	Mon 26/06/08
59		Site Fencing Rod Iron and Gates	5 days	Tue 26/06/09	Mon 26/06/15
60		WEATHER DELAY - Rain and High Winds	2 days	Wed 25/12/17	Thu 25/12/18
61		WEATHER DELAY - Rain	1 day	Mon 25/12/22	Mon 25/12/22
62		**BUILDING B**	**157 days**	**Thu 25/11/06**	**Fri 26/06/19**
63		**CONCRETE WORK**	**42 days**	**Thu 25/11/06**	**Thu 26/01/08**
64		BLDG B Foundation	14 days	Thu 25/11/06	Tue 25/11/25
65		BLDG B Dampproofing	1 day	Tue 25/11/18	Wed 25/11/26
66		BLDG B Slab On Grade	17 days	Mon 25/12/15	Thu 26/01/08
67		**BLDG B Slab On Grade Complete**	**0 days**	**Thu 26/01/08**	**Thu 26/01/08**
68		**STEEL AND METALS**	**80 days**	**Fri 26/01/09**	**Thu 26/04/30**
69		Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	Fri 26/01/09	Thu 26/02/12
70		Frame & Panel Partition & Corridor Walls (JANUS)	20 days	Fri 26/04/03	Thu 26/04/30
71		**WOOD & FRP**	**5 days**	**Fri 26/03/13**	**Thu 26/03/19**
72		Misc Finish Carpentry	5 days	Fri 26/03/13	Thu 26/03/19
73		**ROOF & SIDING**	**30 days**	**Fri 26/02/13**	**Thu 26/03/26**
74		Exterior Sheathing, Weather Barrier & Rigid Insulation	10 days	Fri 26/02/27	Thu 26/03/12
75		CMU Veneer	15 days	Fri 26/02/27	Thu 26/03/19
76		Exterior Metal Panels (JANUS)	10 days	Fri 26/03/13	Thu 26/03/26
77		Install Roof & Roof Insulation (JANUS)	10 days	Fri 26/02/13	Thu 26/02/26
78		**BLDG B Roofing Complete**	**0 days**	**Thu 26/02/26**	**Thu 26/02/26**
79		**DOORS & WINDOWS**	**20 days**	**Fri 26/05/22**	**Fri 26/06/19**
80		F&I Storage Unit Doors (JANUS)	20 days	Fri 26/05/22	Fri 26/06/19
81		F&I HM Doors and Hardware (JANUS)	15 days	Fri 26/05/22	Fri 26/06/12

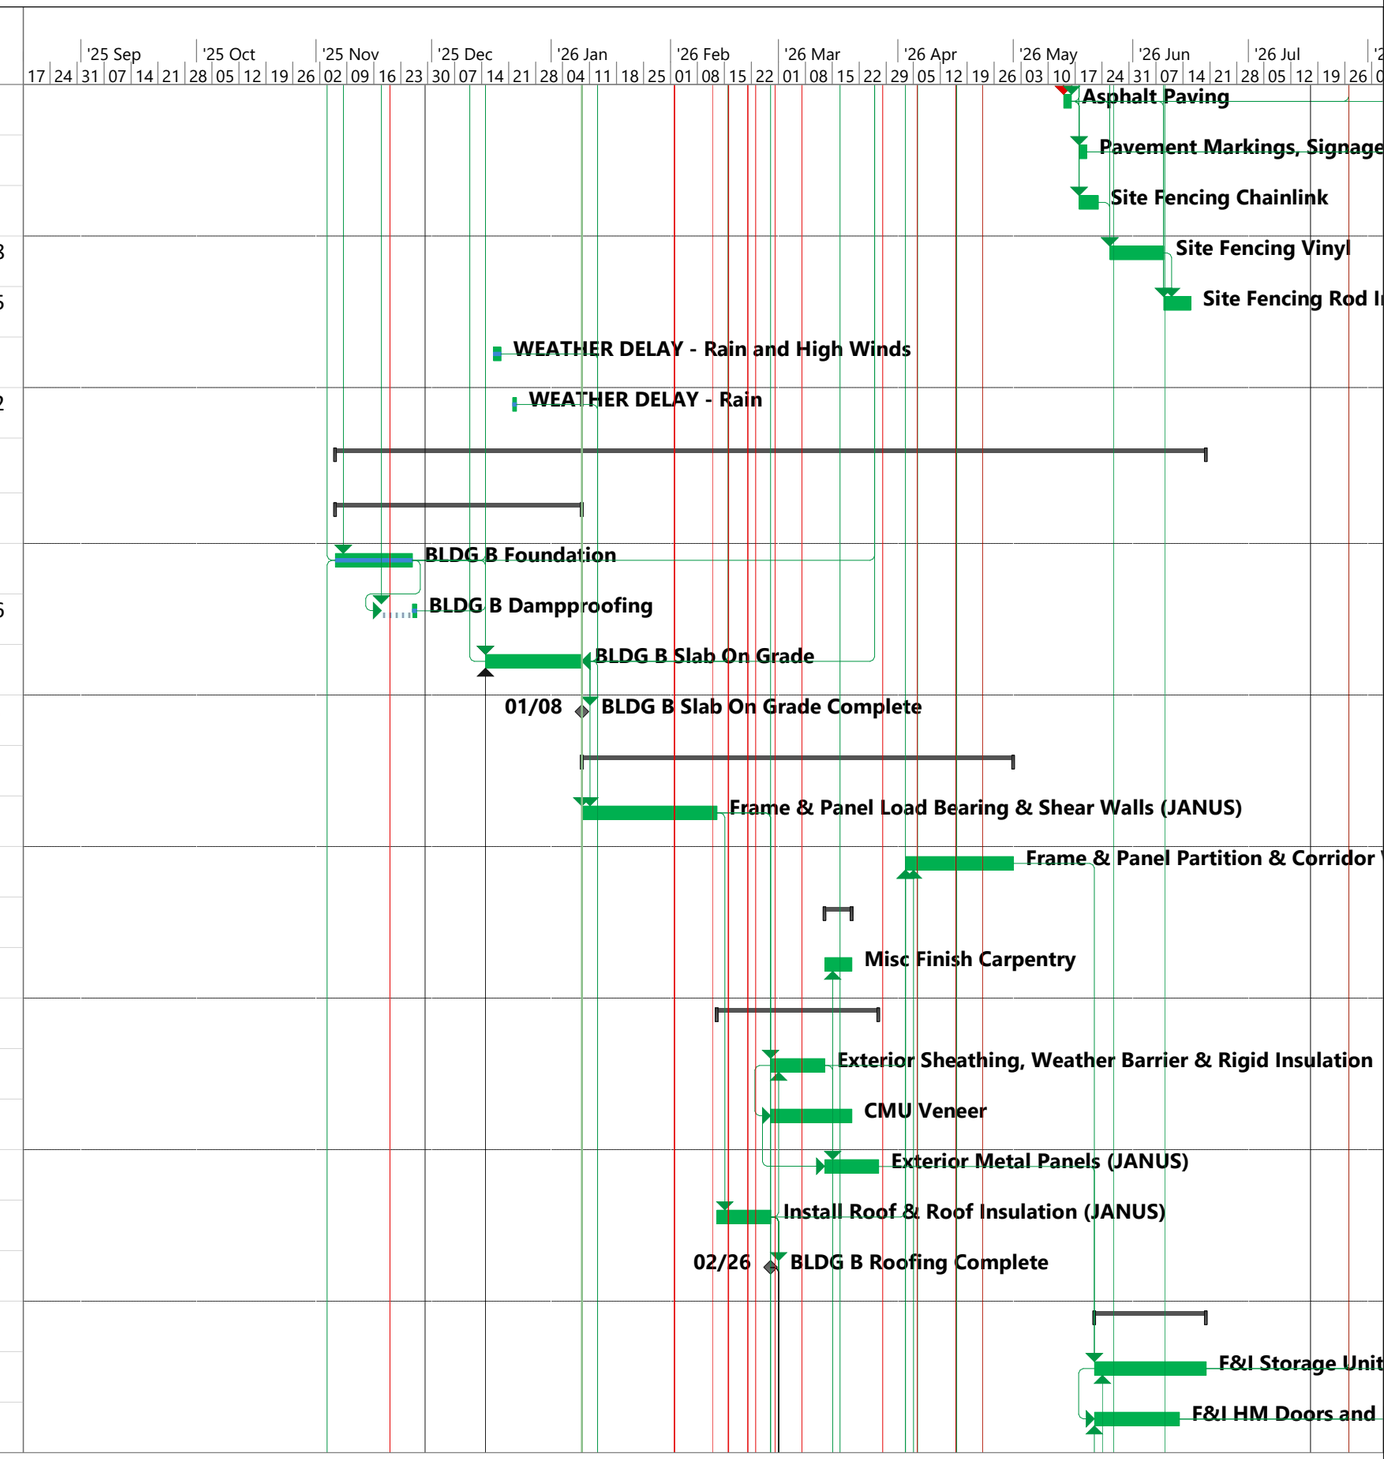

Printed: Fri 26/01/09 08:48

Public Storage Ten Mile Rd
Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
82		**FINISHES**	**30 days**	**Fri 26/02/27**	**Thu 26/04/09**
83		Install Gypsum Board	10 days	Fri 26/02/27	Thu 26/03/12
84		Bathroom Tile	5 days	Fri 26/03/13	Thu 26/03/19
85		Flooring	5 days	Fri 26/03/20	Thu 26/03/26
86		Painting	10 days	Fri 26/03/27	Thu 26/04/09
87		**SPECIALTIES**	**23 days**	**Fri 26/03/13**	**Tue 26/04/14**
88		Install Misc Equipment & Lockers	20 days	Fri 26/03/13	Thu 26/04/09
89		Bathroom Accessories	2 days	Fri 26/03/20	Mon 26/03/23
90		Building Interior Signage	3 days	Fri 26/04/10	Tue 26/04/14
91		**FIRE SPRINKLERS**	**30 days**	**Fri 26/02/27**	**Thu 26/04/09**
92		Fire Sprinkler System Rough In	15 days	Fri 26/02/27	Thu 26/03/19
93		Fire Sprinkler System Trim Out	15 days	Fri 26/03/20	Thu 26/04/09
94		**PLUMBING**	**107 days**	**Thu 25/11/13**	**Thu 26/04/16**
95		Plumbing Rough-in Underground	5 days	Thu 25/11/13	Wed 25/11/19
96		Gas, Water, Sewer Lines	15 days	Fri 26/02/27	Thu 26/03/19
97		Bathroom Fixtures	10 days	Fri 26/03/20	Thu 26/04/02
98		Other Plumbing Fixtures	10 days	Fri 26/04/03	Thu 26/04/16
99		**HVAC**	**30 days**	**Fri 26/02/27**	**Thu 26/04/09**
100		HVAC Installation	25 days	Fri 26/02/27	Thu 26/04/02
101		HVAC Commisioning	5 days	Fri 26/04/03	Thu 26/04/09
102		**ELECTRICAL**	**137 days**	**Thu 25/11/20**	**Fri 26/06/05**
103		**Building Rough-in Underground**	**0 days**	**Thu 25/11/20**	**Tue 25/11/25**
104		Elect Rough-In	25 days	Fri 26/02/27	Thu 26/04/02
105		New Service Equipment Install, Wire & Inspect	10 days	Mon 26/04/06	Fri 26/04/17
106		Install and Wire Panels	15 days	Fri 26/03/13	Thu 26/04/02
107		**Permanent Power On**	**0 days**	**Fri 26/04/17**	**Fri 26/04/17**
108		Electric Lights, Devices and Trim	55 days	Fri 26/03/13	Fri 26/05/29

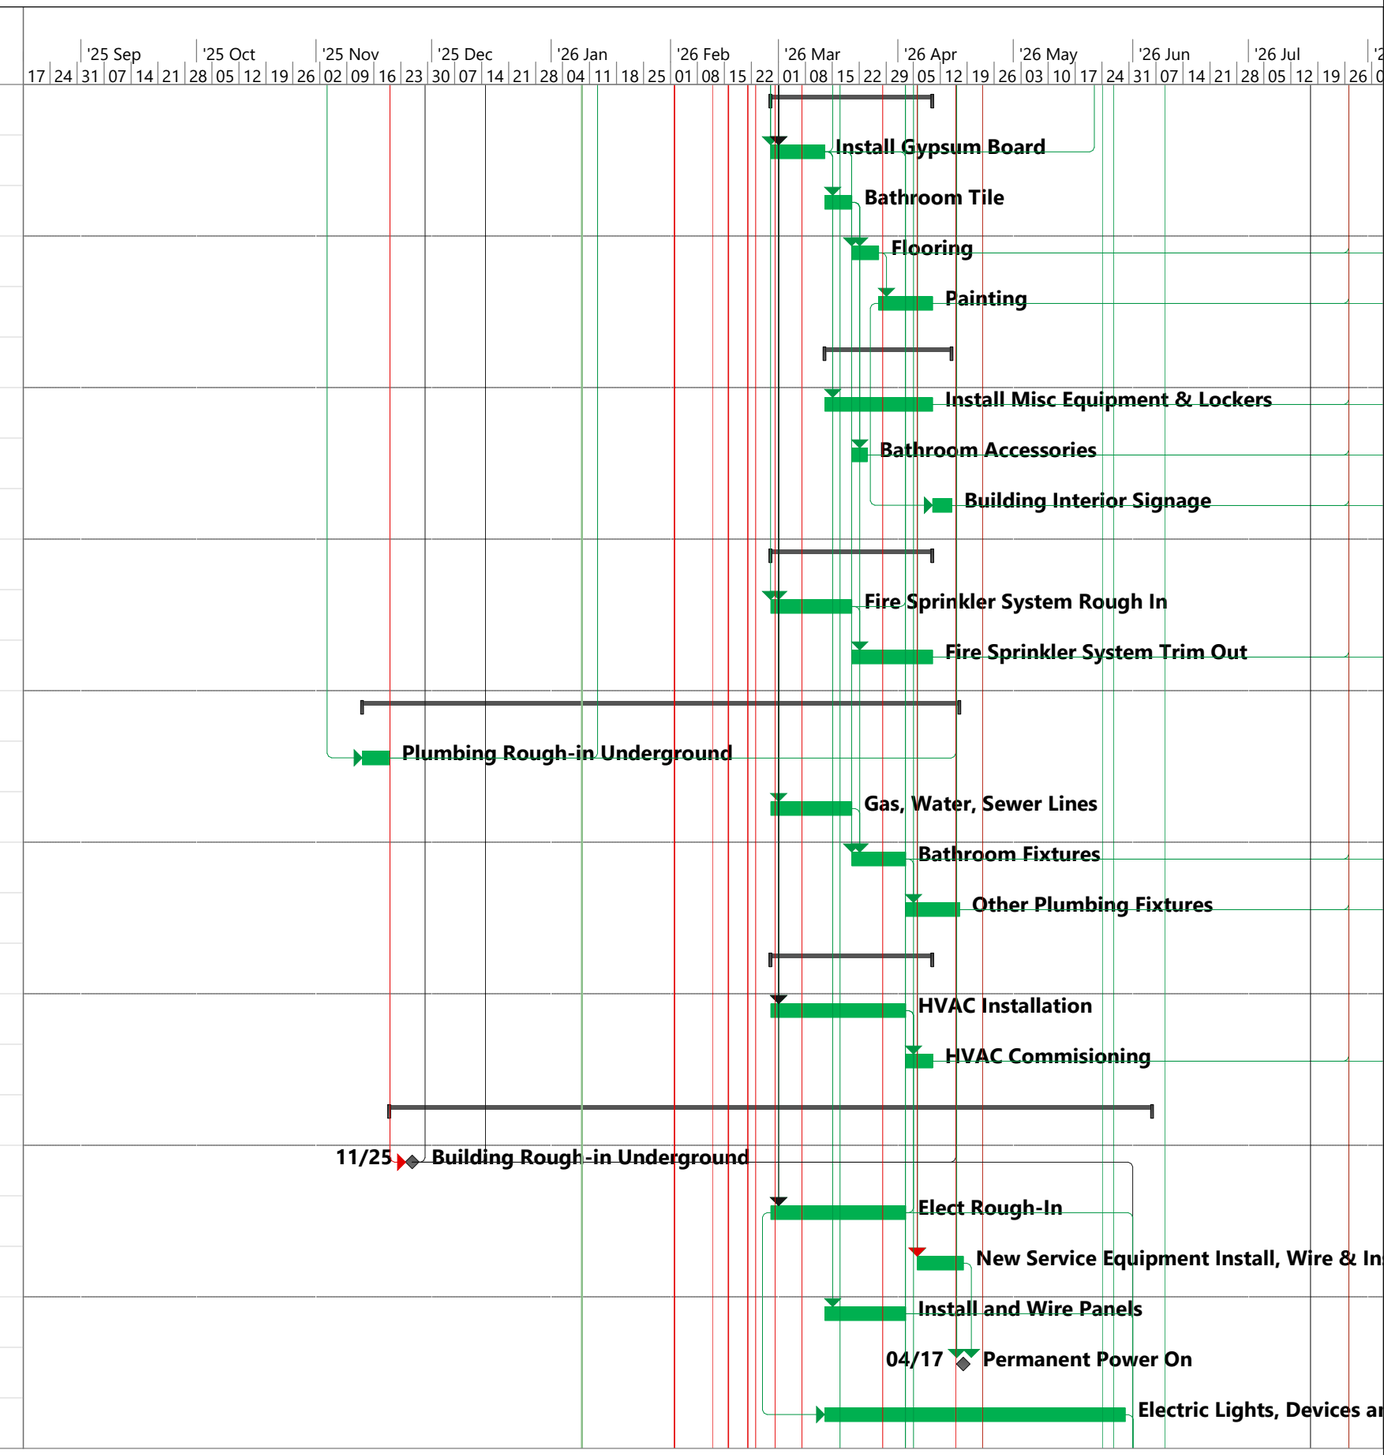

Printed: Fri 26/01/09 08:48

Public Storage Ten Mile Rd
Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
109		Fire Alarm System	5 days	Fri 26/04/03	Thu 26/04/09
110		Electrical Commissioning	5 days	Mon 26/06/01	Fri 26/06/05
111		**BUILDING A**	**115 days**	**Mon 26/02/02**	**Tue 26/07/14**
112		**CONCRETE WORK**	**38 days**	**Mon 26/02/02**	**Wed 26/03/25**
113		BLDG A Foundation	10 days	Mon 26/02/02	Fri 26/02/13
114		BLDG A Dampproofing	2 days	Mon 26/02/16	Tue 26/02/17
115		BLDG A Exterior Footing Insulation	3 days	Wed 26/02/18	Fri 26/02/20
116		BLDG A Slab On Grade	15 days	Thu 26/03/05	Wed 26/03/25
117		**BLDG A Slab On Grade Complete**	**0 days**	**Wed 26/03/25**	**Wed 26/03/25**
118		**STEEL AND METALS**	**44 days**	**Tue 26/03/17**	**Fri 26/05/15**
119		Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	Tue 26/03/17	Mon 26/04/20
120		Frame & Panel Partition & Corridor Walls (JANUS)	15 days	Tue 26/04/21	Mon 26/05/11
121		Canopy Install	8 days	Wed 26/05/06	Fri 26/05/15
122		**WOOD & FRP**	**5 days**	**Wed 26/05/20**	**Wed 26/05/27**
123		Misc Finish Carpentry	5 days	Wed 26/05/20	Wed 26/05/27
124		**ROOF & SIDING**	**26 days**	**Tue 26/04/21**	**Wed 26/05/27**
125		Exterior Sheathing, Weather Barrier & Rigid Insulation	10 days	Wed 26/04/22	Tue 26/05/05
126		CMU Veneer	15 days	Wed 26/05/06	Wed 26/05/27
127		Exterior Metal Panels (JANUS)	10 days	Fri 26/05/08	Thu 26/05/21
128		Install Roof & Roof Insulation (JANUS)	5 days	Tue 26/04/21	Mon 26/04/27
129		**BLDG A Roofing Complete**	**0 days**	**Mon 26/04/27**	**Mon 26/04/27**
130		**DOORS & WINDOWS**	**11 days**	**Tue 26/05/12**	**Wed 26/05/27**
131		F&I Storage Unit Doors (JANUS)	5 days	Tue 26/05/12	Mon 26/05/18
132		F&I HM Doors and Hardware (JANUS)	5 days	Wed 26/05/20	Wed 26/05/27
133		**FINISHES**	**30 days**	**Wed 26/05/06**	**Wed 26/06/17**
134		Install Gypsum Board	10 days	Wed 26/05/06	Tue 26/05/19
135		Painting	10 days	Wed 26/05/20	Wed 26/06/03

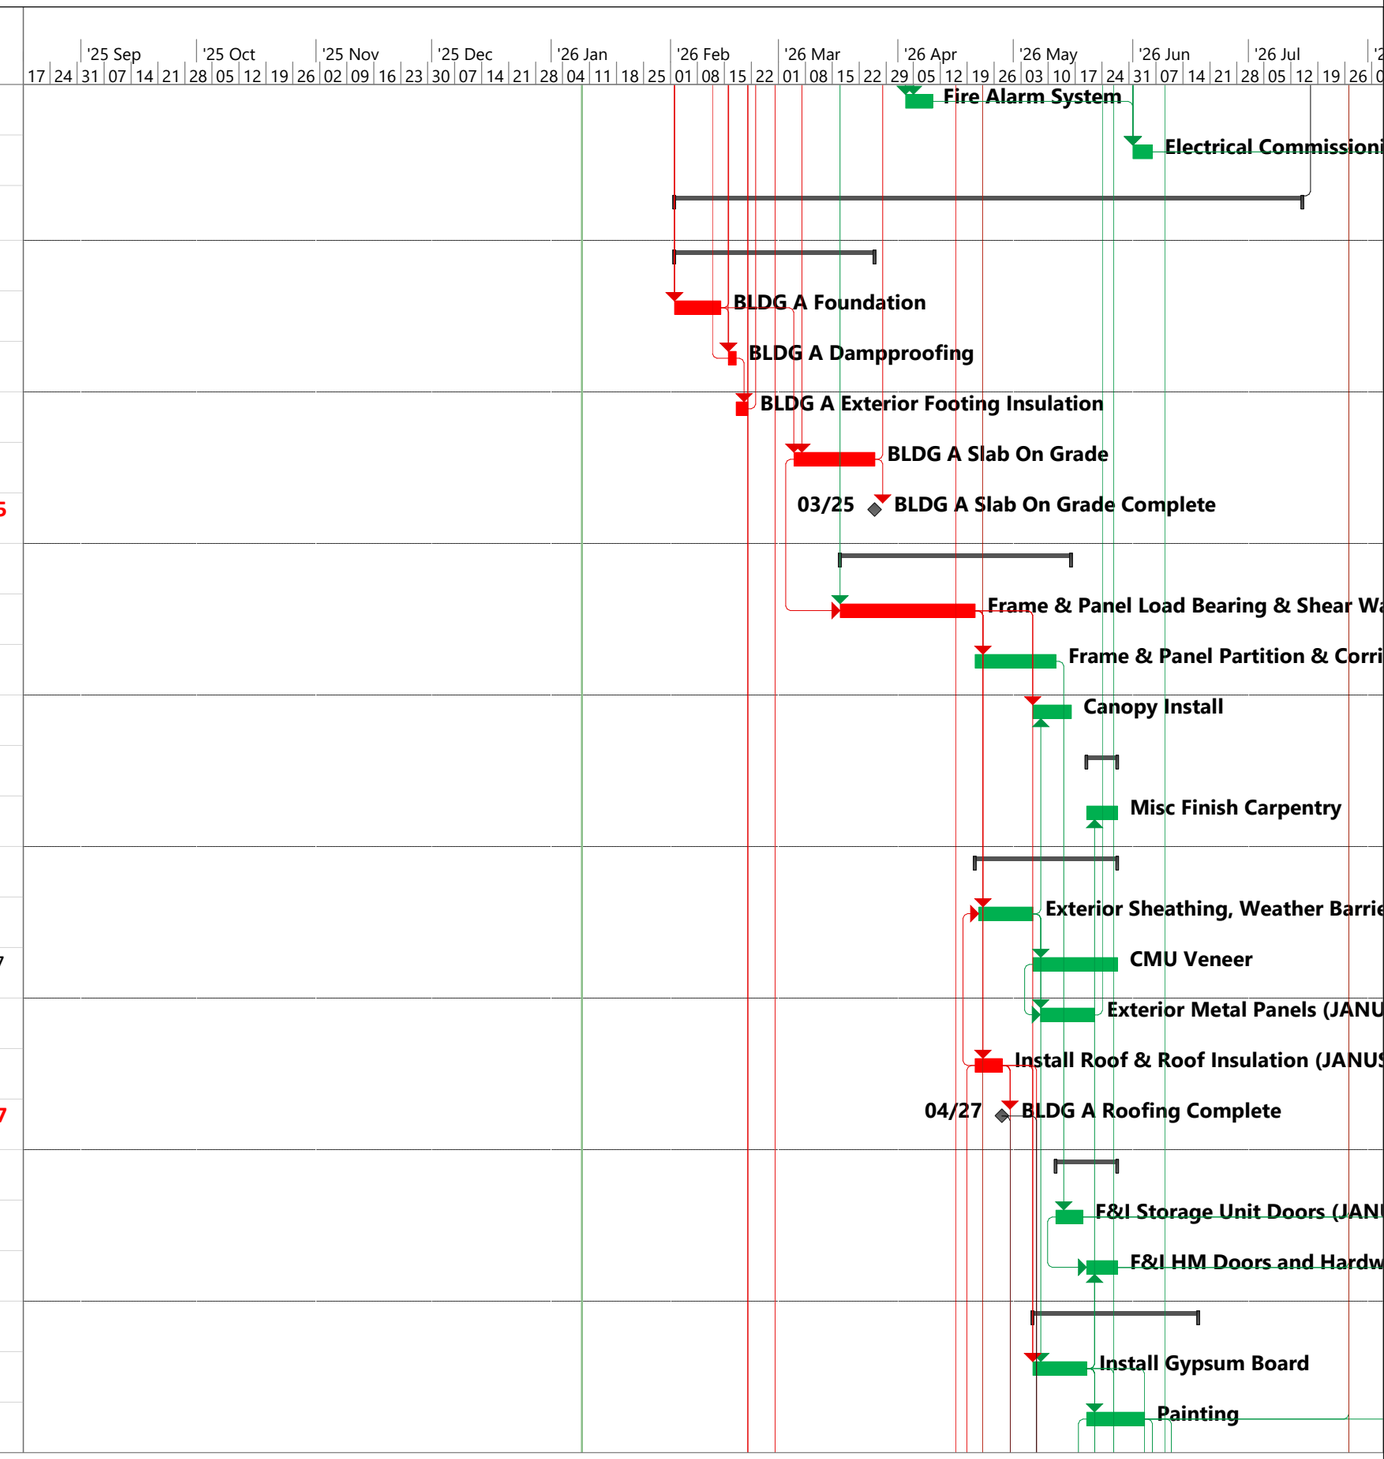

Printed: Fri 26/01/09 08:48

Public Storage Ten Mile Rd
Contract Schedule (10/29/2025 Update)

ID	Task Mod	Task Name	Duration	Start	Finish
136		Flooring Polished Conc.	5 days	Thu 26/06/04	Wed 26/06/10
137		FRP & Vinyl Base	5 days	Thu 26/06/11	Wed 26/06/17
138		**SPECIALTIES**	**22 days**	**Wed 26/05/20**	**Fri 26/06/19**
139		Install Misc Equipment & Lockers	20 days	Wed 26/05/20	Wed 26/06/17
140		Bathroom Accessories	2 days	Thu 26/06/18	Fri 26/06/19
141		Building Interior Signage	3 days	Thu 26/06/04	Mon 26/06/08
142		**FIRE SPRINKLERS**	**30 days**	**Tue 26/04/28**	**Tue 26/06/09**
143		Fire Sprinkler System Rough In	15 days	Tue 26/04/28	Mon 26/05/18
144		Fire Sprinkler System Trim Out	15 days	Tue 26/05/19	Tue 26/06/09
145		**PLUMBING**	**84 days**	**Thu 26/02/19**	**Wed 26/06/17**
146		Plumbing Rough-in Underground	5 days	Thu 26/02/19	Wed 26/02/25
147		Gas, Water, Sewer Lines	15 days	Tue 26/04/28	Mon 26/05/18
148		Bathroom Fixtures	10 days	Wed 26/05/20	Wed 26/06/03
149		Other Plumbing Fixtures	10 days	Thu 26/06/04	Wed 26/06/17
150		**HVAC**	**30 days**	**Tue 26/04/28**	**Tue 26/06/09**
151		HVAC Installation	20 days	Tue 26/04/28	Tue 26/05/26
152		HVAC Commisioning	10 days	Wed 26/05/27	Tue 26/06/09
153		**ELECTRICAL**	**102 days**	**Thu 26/02/19**	**Tue 26/07/14**
154		Building Rough-in Underground	5 days	Thu 26/02/19	Wed 26/02/25
155		Elect Rough-In	25 days	Thu 26/04/23	Thu 26/05/28
156		New Service Equipment Install, Wire & Inspect	10 days	Thu 26/04/23	Wed 26/05/06
157		Install and Wire Panels	15 days	Wed 26/05/20	Wed 26/06/10
158		**Permanent Power On**	**0 days**	**Wed 26/06/10**	**Wed 26/06/10**
159		Electric Lights, Devices and Trim	42 days	Thu 26/05/07	Tue 26/07/07
160		Fire Alarm System	5 days	Wed 26/05/27	Tue 26/06/02
161		Electrical Commissioning	5 days	Wed 26/07/08	Tue 26/07/14

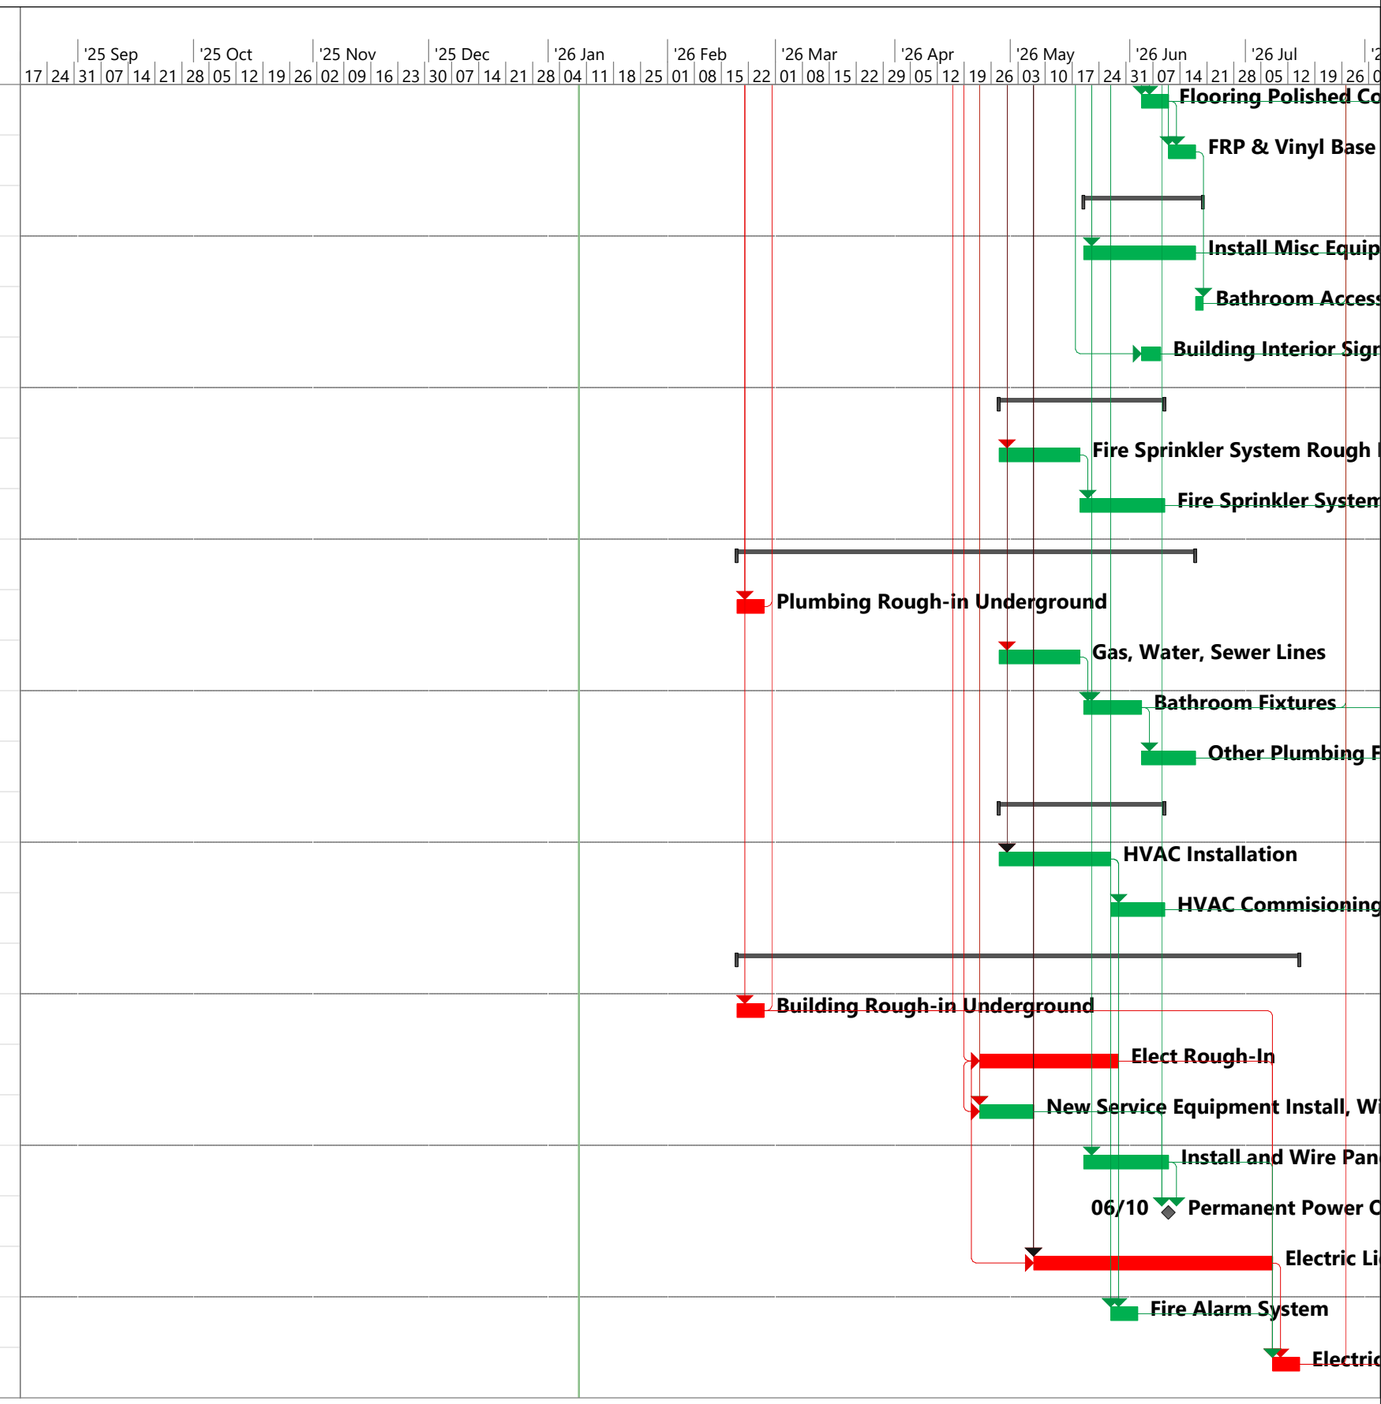

Printed: Fri 26/01/09 08:48
