Executive Landing Page | Landing Page

Public Storage Dashboard

Data Date: 3/20/2026

Type	Project	Region	Responsible
Construction	Meridian, ID	Central	Josh Pait

Baseline Completion Date	Current Completion Date	Schedule Variance	Work Compression
7/22/2026	9/21/2026	-61 days Prev: -27 days | Trend: -34 days ▼ Worsening	Remaining Work Compression: 19.00% — WARNING

Critical Path Status & Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	9/8/2025	9/8/2025	9/8/2025	0	0	Notice To Proceed	On Track – Gaining
Foundation Complete	1/28/2026	3/23/2026	4/22/2026	-84	-30	Bldg A Slab On Grade Complete	Delayed – Slipping
Weather Tight	3/18/2026	4/30/2026	6/3/2026	-77	-34	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	Delayed – Slipping
Structure Top Out	3/25/2026	4/30/2026	6/10/2026	-77	-41	Bldg A Roofing Complete	Delayed – Slipping
Weather Tight	3/18/2026	4/30/2026	6/10/2026	-84	-41	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	Delayed – Slipping
Permanent Power		6/5/2026	7/16/2026		-41	Permanent Power On- Building A	On Track – Gaining
Hardscape/Landscape Complete	4/17/2026	6/16/2026	7/17/2026	-91	-31	Site Fencing Rod Iron And Gates	Delayed – Slipping
Conditioned Air	5/6/2026	6/12/2026	7/23/2026	-78	-41	Hvac Commisioning - Building A	Delayed – Slipping
1st Floor Finishes Complete	5/1/2026	6/16/2026	7/27/2026	-87	-41	Bathroom Accessories- Building A	Delayed – Slipping
Contract Completion	7/22/2026	8/18/2026	9/21/2026	-61	-34	Substantial Completion	Delayed – Slipping

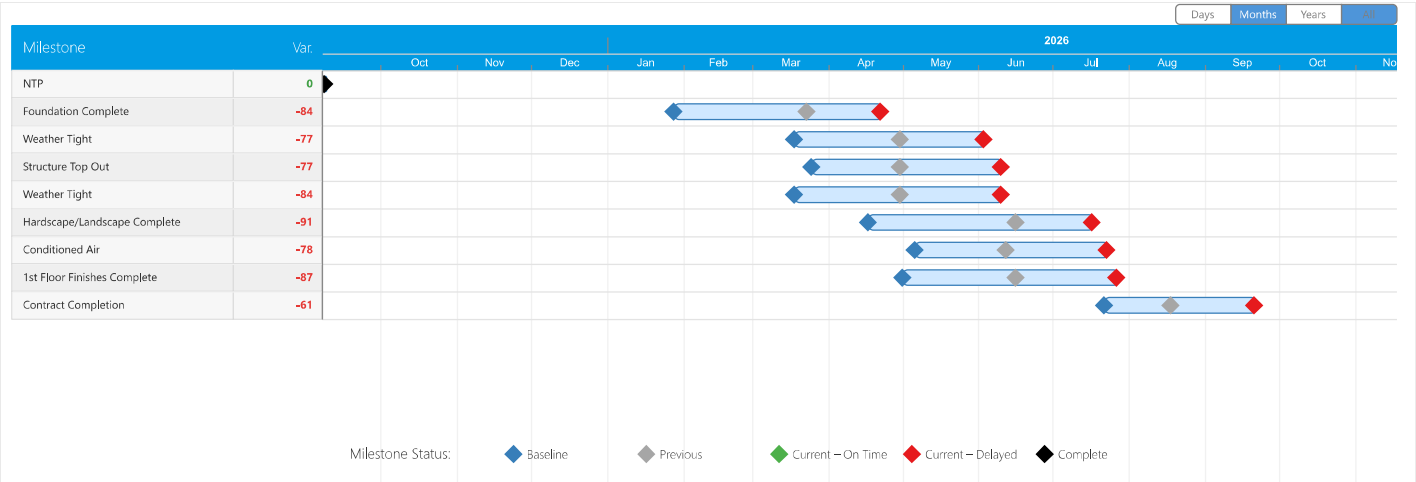

Baseline Variance Trends — Critical Milestones

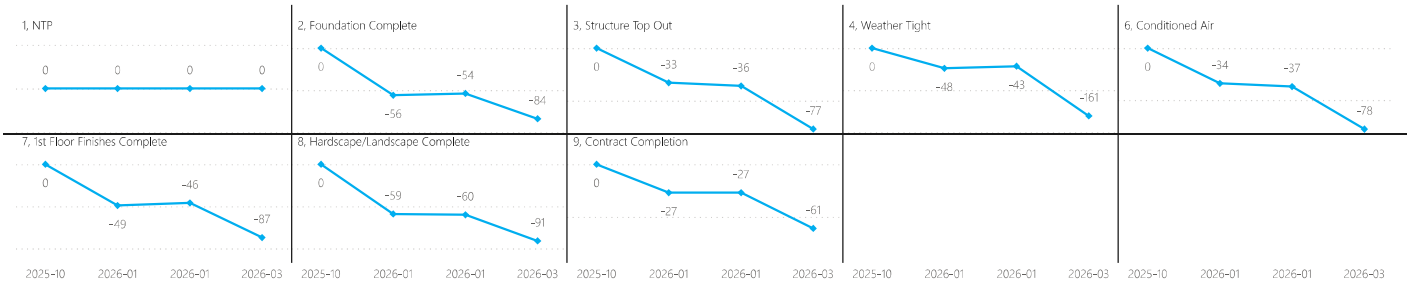

Schedule Performance Summary

Summary: The schedule's overall health is critically compromised, with multiple high-weight metrics (quality, change control, finish performance, and critical path stability) in ALERT status. Risks of delay, execution shortfalls, and uncontrolled scope or logic changes are acute—immediate intervention and robust recovery measures are essential to prevent systemic project failure.

Schedule Validation Score: 67.00 — ALERT

The schedule quality is substantially below industry standards, indicating major logic, constraint, or forecasting integrity issues. Schedule reliability is at risk; a comprehensive technical review and corrective action are required.

Execution Score: 57.00% — WARNING

Schedule execution is suboptimal, with weak alignment between planned and actual activity performance. Enhanced coordination and regular update discipline are recommended to restore schedule effectiveness.

Schedule Change Index: 31.00% — ALERT

Over 31% of activities have experienced logic or date changes since the last update, flagging high volatility and a lack of planning discipline. This level of revision undermines confidence in the current schedule's stability and should be addressed.

Remaining Work Compression: 19.00% — ALERT

Excessive compression (19%) is being applied to remaining activities, increasing the likelihood of resource overload and future execution failures. Realistic replanning and resource leveling should be prioritized.

Finish Variance: 82.00% — ALERT

The project is forecasted to finish nearly 82% later than originally planned, reflecting severe schedule slippage and threat of major deadline overruns. Immediate recovery planning and executive attention are critical.

Critical Path Variance: 73.00% — ALERT

The critical path duration has increased by 73%, indicating significant risk to overall project completion. This suggests major delays on critical tasks and demands urgent focus to mitigate further slippage.

Powered By STELIC
