PETRA GENERAL CONTRACTORS

Meridian, ID - 2026.03.26 - UP03

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**89%**	**259 days**	**Mon 9/8/25**	**Fri 9/11/26**
12	Submittals (numerous)	95%	90 days	Tue 10/14/25	Fri 2/20/26
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	50%	40 days	Thu 10/23/25	Fri 12/19/25
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	25%	40 days	Thu 11/6/25	Tue 1/6/26
21	**TWENTY WORKING DAYS OF WEATHER DELAY**	0%	10 days	Mon 8/31/26	Fri 9/11/26
27	**Substantial Completion**	**0%**	**0 days**	**Fri 9/11/26**	**Fri 9/11/26**
28	Clean Up and Project Close Out	0%	5 days	Wed 8/19/26	Tue 8/25/26
29	Demobilize	0%	3 days	Wed 8/26/26	Fri 8/28/26
30	**SITEWORK**	**50%**	**219 days**	**Mon 9/8/25**	**Fri 7/17/26**
31	**Level of Effort**	**42%**	**131 days**	**Mon 9/8/25**	**Fri 3/13/26**
51	Complete UG Utility Lines, SD Turn Ups, to Building A	0%	1 day	Tue 3/31/26	Tue 3/31/26
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**73%**	**74 days**	**Tue 2/3/26**	**Fri 5/15/26**
60	FRAGNET - Mobilize Crew, Rough Grade Prep, Scarify and Air Dry	50%	1 day	Fri 3/20/26	Fri 3/20/26
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If failed, provide geo grid per RFI 33	0%	3 days	Tue 5/5/26	Thu 5/7/26
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	0%	1 day	Fri 5/8/26	Fri 5/8/26
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	0%	5 days	Mon 5/11/26	Fri 5/15/26
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	0%	5 days	Mon 5/11/26	Fri 5/15/26
69	Storm Drain Lines and Devices - South of Buildings (E-W)	0%	7 days	Wed 4/15/26	Thu 4/23/26
70	Site - Flatwork Sidewalk Prep	0%	8 days	Wed 4/15/26	Fri 4/24/26
71	Storm Drain Lines and Devices - North of Buildings (E-W)	0%	7 days	Fri 4/24/26	Mon 5/4/26
72	Site - Curb and Gutter Prep	0%	8 days	Mon 5/18/26	Thu 5/28/26
73	Site - Base Course Asphalt Prep	0%	8 days	Mon 5/18/26	Thu 5/28/26
74	Site Flatwork and Curb and Gutter - (E-W)	0%	15 days	Fri 5/29/26	Thu 6/18/26
75	Site - Fine Grade Asphalt Prep	0%	3 days	Fri 6/19/26	Tue 6/23/26
76	Asphalt Paving	0%	2 days	Wed 6/24/26	Thu 6/25/26
77	Pavement Markings, Signage & Bumpers	0%	2 days	Fri 6/26/26	Mon 6/29/26
78	Site Fencing Chainlink	0%	5 days	Wed 5/20/26	Wed 5/27/26
79	Gravel Road Finish Grading	0%	5 days	Thu 5/28/26	Wed 6/3/26
80	Landscaping and Irrigation	0%	15 days	Fri 6/26/26	Fri 7/17/26
81	Site Fencing Vinyl	0%	10 days	Fri 6/26/26	Fri 7/10/26
82	Site Fencing Rod Iron and Gates	0%	5 days	Fri 6/26/26	Thu 7/2/26
83	**BUILDING B**	**30%**	**195 days**	**Wed 10/29/25**	**Wed 8/5/26**
94	**STEEL AND METALS**	**63%**	**82 days**	**Mon 1/12/26**	**Tue 5/5/26**
97	Panel Shear Walls, Interior Partition, & Corridor Walls (JANUS)	65%	20 days	Thu 2/26/26	Wed 3/25/26
98	Perimeter Panel Interior Walls (JANUS)	0%	20 days	Wed 4/8/26	Tue 5/5/26
99	**WOOD & FRP**	**0%**	**5 days**	**Tue 4/14/26**	**Mon 4/20/26**
100	Misc Finish Carpentry	0%	5 days	Tue 4/14/26	Mon 4/20/26
101	**ROOF & SIDING**	**30%**	**78 days**	**Fri 1/30/26**	**Tue 5/19/26**
105	CMU Veneer Base Course & Grout	25%	15 days	Tue 3/3/26	Tue 4/7/26
106	Rigid Insulation Behind CMU	0%	5 days	Wed 4/8/26	Tue 4/14/26
107	Rigid Insulation Behind Metal Panels	0%	3 days	Wed 4/15/26	Fri 4/17/26
108	CMU Veneer Remaining	0%	15 days	Wed 4/15/26	Tue 5/5/26

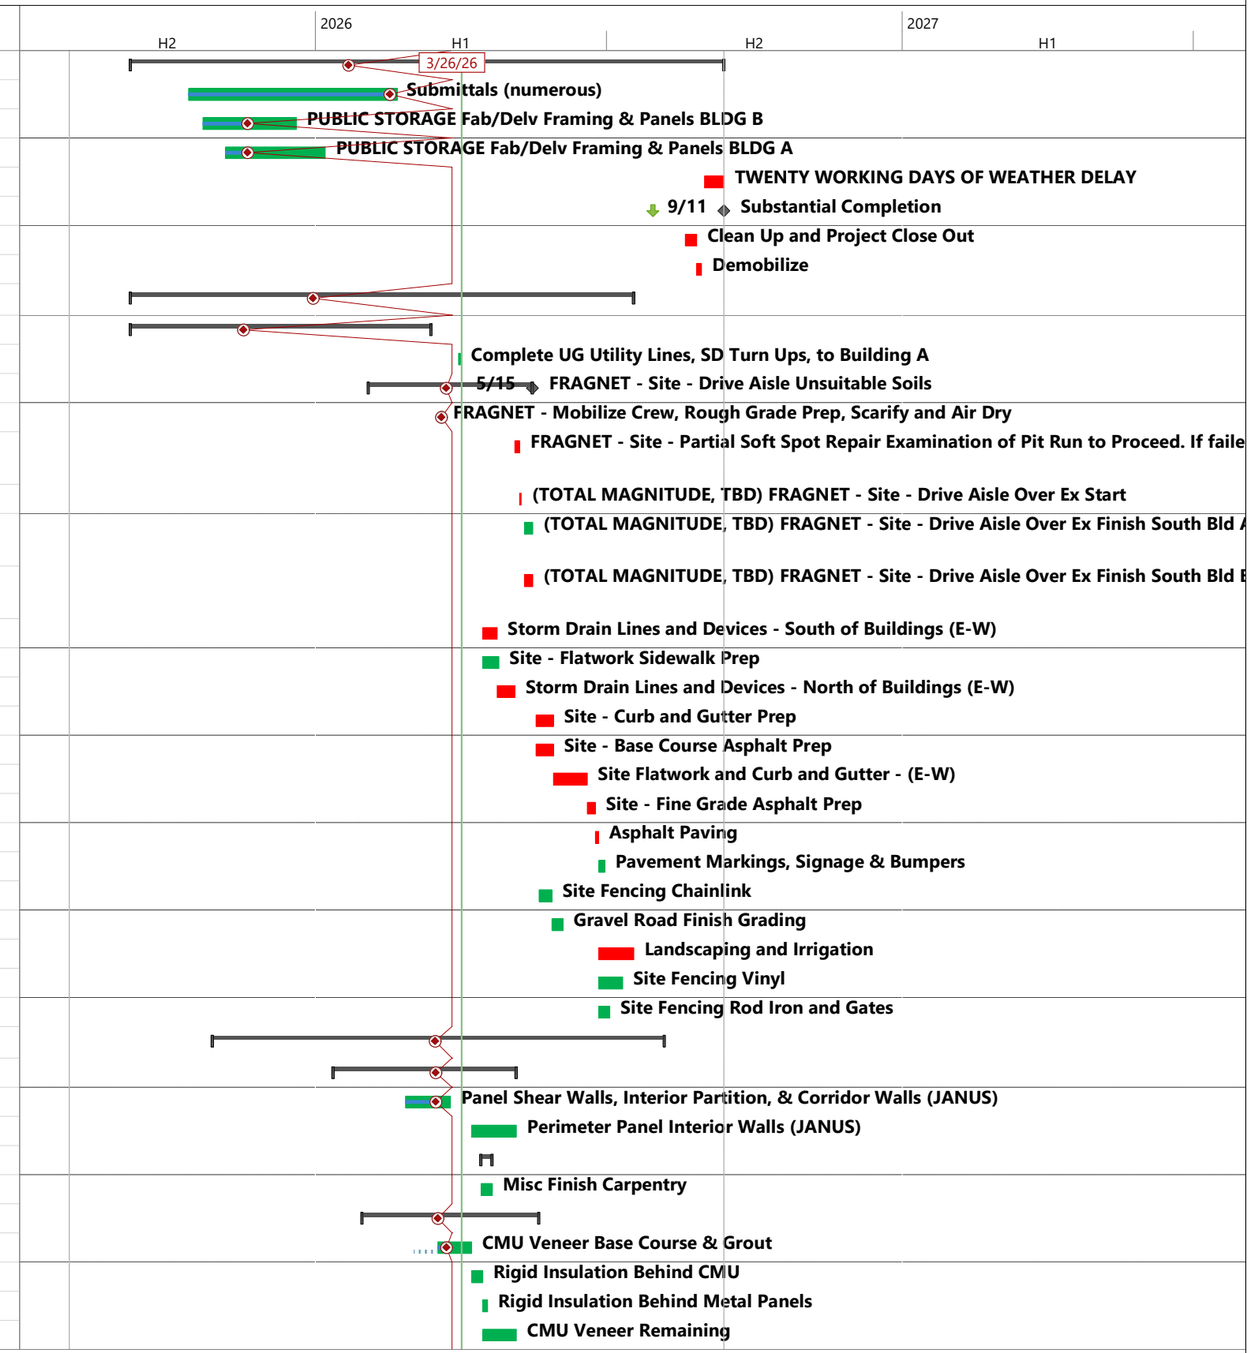

Printed: Thu 4/2/26 3:44 PM

PETRA GENERAL CONTRACTORS

Meridian, ID - 2026.03.26 - UP03

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
109	Exterior Metal Panels (JANUS)	0%	10 days	Wed 5/6/26	Tue 5/19/26
110	Install Roof & Roof Insulation (JANUS)	17%	15 days	Wed 2/25/26	Mon 3/30/26
111	**BLDG B Roofing Complete**	**0%**	**0 days**	**Mon 3/30/26**	**Mon 3/30/26**
112	**DOORS & WINDOWS**	**0%**	**20 days**	**Thu 7/9/26**	**Wed 8/5/26**
113	F&I Storage Unit Doors (JANUS)	0%	20 days	Thu 7/9/26	Wed 8/5/26
114	F&I HM Doors and Hardware (JANUS)	0%	15 days	Thu 7/9/26	Wed 7/29/26
115	**FINISHES**	**0%**	**30 days**	**Tue 3/31/26**	**Mon 5/11/26**
116	Install Gypsum Board	0%	10 days	Tue 3/31/26	Mon 4/13/26
117	Flooring Polished Concrete	0%	5 days	Tue 4/14/26	Mon 4/20/26
118	FRP / Vinyl Base	0%	5 days	Tue 4/21/26	Mon 4/27/26
119	Painting	0%	10 days	Tue 4/28/26	Mon 5/11/26
120	**SPECIALTIES**	**0%**	**23 days**	**Tue 4/14/26**	**Thu 5/14/26**
121	Install Misc Equipment & Lockers	0%	20 days	Tue 4/14/26	Mon 5/11/26
122	Bathroom Accessories	0%	2 days	Tue 4/21/26	Wed 4/22/26
123	Building Interior Signage	0%	3 days	Tue 5/12/26	Thu 5/14/26
124	**FIRE SPRINKLERS**	**13%**	**50 days**	**Mon 2/23/26**	**Fri 5/1/26**
125	Fire Sprinkler System Rough In	20%	28 days	Mon 2/23/26	Fri 4/10/26
126	Fire Sprinkler System Trim Out	0%	15 days	Mon 4/13/26	Fri 5/1/26
127	**PLUMBING**	**16%**	**107 days**	**Thu 11/20/25**	**Thu 4/23/26**
129	Drains, Water, Sewer Lines	0%	15 days	Tue 3/31/26	Mon 4/20/26
130	Bathroom Fixtures	0%	3 days	Tue 4/21/26	Thu 4/23/26
131	Other Plumbing Fixtures	0%	3 days	Tue 4/21/26	Thu 4/23/26
132	**HVAC**	**0%**	**30 days**	**Tue 3/31/26**	**Mon 5/11/26**
133	HVAC Installation	0%	25 days	Tue 3/31/26	Mon 5/4/26
134	HVAC Commisioning & T&B	0%	5 days	Tue 5/5/26	Mon 5/11/26
135	**ELECTRICAL**	**8%**	**149 days**	**Thu 11/20/25**	**Tue 6/23/26**
137	Elect Rough-In	25%	25 days	Mon 3/2/26	Tue 4/7/26
138	New Service Equipment Install, Wire & Inspect	0%	10 days	Tue 3/31/26	Mon 4/13/26
139	Install and Wire Panels	0%	15 days	Tue 4/14/26	Mon 5/4/26
140	**Permanent Power On**	**0%**	**0 days**	**Mon 5/4/26**	**Mon 5/4/26**
142	Electric Lights, Devices and Trim	0%	55 days	Tue 3/31/26	Tue 6/16/26
143	Fire Alarm System	0%	3 days	Tue 5/5/26	Thu 5/7/26
144	Electrical Commissioning	0%	5 days	Wed 6/17/26	Tue 6/23/26
145	**BUILDING A**	**20%**	**145 days**	**Mon 1/26/26**	**Tue 8/18/26**
168	**CONCRETE WORK**	**71%**	**50 days**	**Wed 2/4/26**	**Tue 4/14/26**
172	BLDG A SOG Fine Prep	0%	1 day	Tue 3/31/26	Tue 3/31/26
173	BLDG A Slab On Grade (East)	0%	3 days	Wed 4/1/26	Fri 4/3/26
174	BLDG A Slab On Grade (Center)	0%	3 days	Mon 4/6/26	Wed 4/8/26
175	BLDG A Slab On Grade (West)	0%	4 days	Thu 4/9/26	Tue 4/14/26
176	**BLDG A Slab On Grade Complete**	**0%**	**0 days**	**Tue 4/14/26**	**Tue 4/14/26**
177	**STEEL AND METALS**	**0%**	**67 days**	**Tue 4/21/26**	**Fri 7/24/26**
178	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	0%	25 days	Tue 4/21/26	Tue 5/26/26
179	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	0%	15 days	Wed 5/27/26	Tue 6/16/26
180	Perimeter Panel Interior Walls (JANUS)	0%	15 days	Mon 7/6/26	Fri 7/24/26

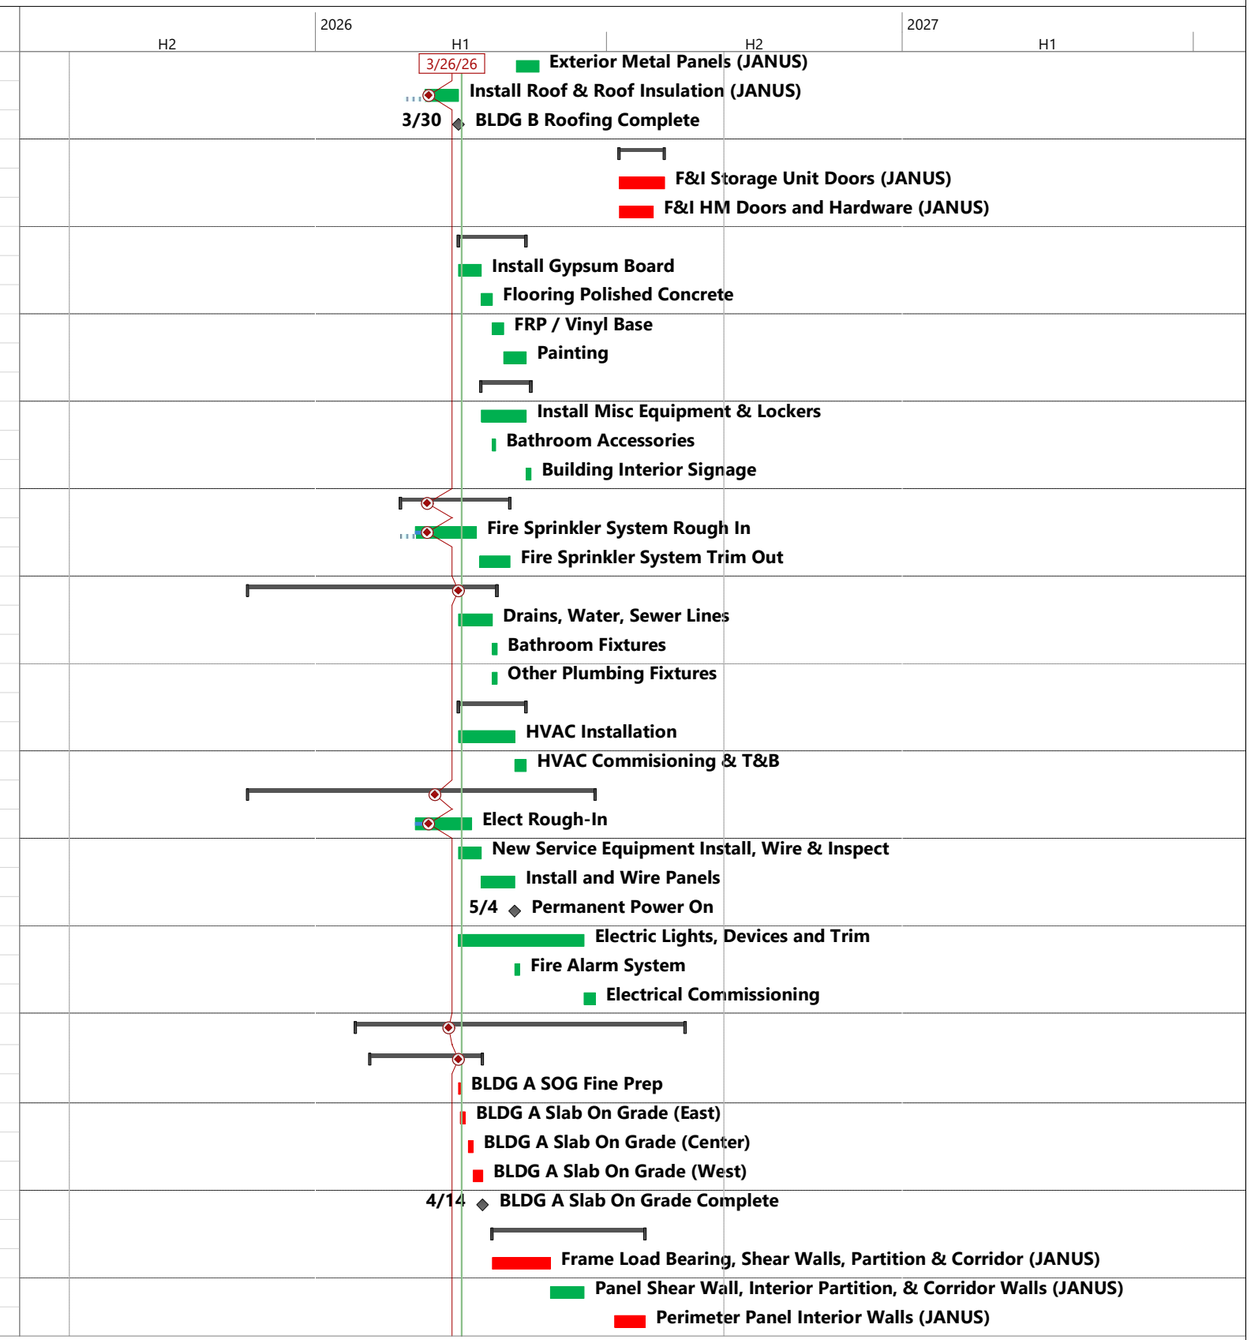

Printed: Thu 4/2/26 3:44 PM

PETRA GENERAL CONTRACTORS

Meridian, ID - 2026.03.26 - UP03

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
181	Canopy Install	0%	8 days	Wed 5/27/26	Fri 6/5/26
182	**WOOD & FRP**	**0%**	**5 days**	**Wed 6/17/26**	**Tue 6/23/26**
183	Misc Finish Carpentry	0%	5 days	Wed 6/17/26	Tue 6/23/26
184	**ROOF & SIDING**	**0%**	**40 days**	**Tue 5/12/26**	**Wed 7/8/26**
185	Exterior Sheathing	0%	10 days	Tue 5/12/26	Tue 5/26/26
186	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	0%	10 days	Tue 5/19/26	Tue 6/2/26
187	Rigid Insulation Behind Metal Panels	0%	3 days	Wed 6/3/26	Fri 6/5/26
188	Rigid Insulation Behind CMU	0%	5 days	Wed 6/3/26	Tue 6/9/26
189	CMU Veneer	0%	15 days	Wed 6/10/26	Tue 6/30/26
190	Exterior Metal Panels (JANUS)	0%	10 days	Wed 6/24/26	Wed 7/8/26
191	Install Roof & Roof Insulation (JANUS)	0%	5 days	Wed 5/27/26	Tue 6/2/26
192	**BLDG A Roofing Complete**	**0%**	**0 days**	**Tue 6/2/26**	**Tue 6/2/26**
193	**DOORS & WINDOWS**	**0%**	**5 days**	**Mon 7/27/26**	**Fri 7/31/26**
194	F&I Storage Unit Doors (JANUS)	0%	5 days	Mon 7/27/26	Fri 7/31/26
195	F&I HM Doors and Hardware (JANUS)	0%	5 days	Mon 7/27/26	Fri 7/31/26
196	**FINISHES**	**0%**	**30 days**	**Wed 6/3/26**	**Wed 7/15/26**
197	Install Gypsum Board	0%	10 days	Wed 6/3/26	Tue 6/16/26
198	Painting	0%	10 days	Wed 6/17/26	Tue 6/30/26
199	Flooring Polished Conc.	0%	5 days	Wed 7/1/26	Wed 7/8/26
200	FRP & Vinyl Base	0%	5 days	Thu 7/9/26	Wed 7/15/26
201	**SPECIALTIES**	**0%**	**22 days**	**Wed 6/17/26**	**Fri 7/17/26**
202	Install Misc Equipment & Lockers	0%	20 days	Wed 6/17/26	Wed 7/15/26
203	Bathroom Accessories- Building A	0%	2 days	Thu 7/16/26	Fri 7/17/26
204	Building Interior Signage	0%	3 days	Wed 7/1/26	Mon 7/6/26
205	**FIRE SPRINKLERS**	**0%**	**30 days**	**Wed 6/3/26**	**Wed 7/15/26**
206	Fire Sprinkler System Rough In	0%	15 days	Wed 6/3/26	Tue 6/23/26
207	Fire Sprinkler System Trim Out	0%	15 days	Wed 6/24/26	Wed 7/15/26
208	**PLUMBING**	**10%**	**96 days**	**Mon 3/9/26**	**Wed 7/22/26**
210	Drains, Water, Sewer Lines	0%	15 days	Wed 6/3/26	Tue 6/23/26
211	Bathroom Fixtures- Building A	0%	10 days	Wed 6/24/26	Wed 7/8/26
212	Other Plumbing Fixtures	0%	10 days	Thu 7/9/26	Wed 7/22/26
213	**HVAC**	**0%**	**30 days**	**Wed 6/3/26**	**Wed 7/15/26**
214	HVAC Installation	0%	20 days	Wed 6/3/26	Tue 6/30/26
215	HVAC Commisioning - Building A	0%	10 days	Wed 7/1/26	Wed 7/15/26
216	**ELECTRICAL**	**0%**	**104 days**	**Tue 3/24/26**	**Tue 8/18/26**
217	Building Rough-in Underground	0%	5 days	Tue 3/24/26	Mon 3/30/26
218	Electrical Rough-In	0%	25 days	Fri 5/29/26	Thu 7/2/26
219	New Service Equipment Install, Wire & Inspect	0%	10 days	Wed 6/3/26	Tue 6/16/26
220	Install and Wire Panels	0%	15 days	Wed 6/17/26	Wed 7/8/26
221	**Permanent Power On- Building A**	**0%**	**0 days**	**Wed 7/8/26**	**Wed 7/8/26**
222	Electric Lights, Devices and Trim	0%	42 days	Fri 6/12/26	Tue 8/11/26
223	Fire Alarm System	0%	5 days	Wed 7/1/26	Wed 7/8/26
224	Electrical Commissioning	0%	5 days	Wed 8/12/26	Tue 8/18/26

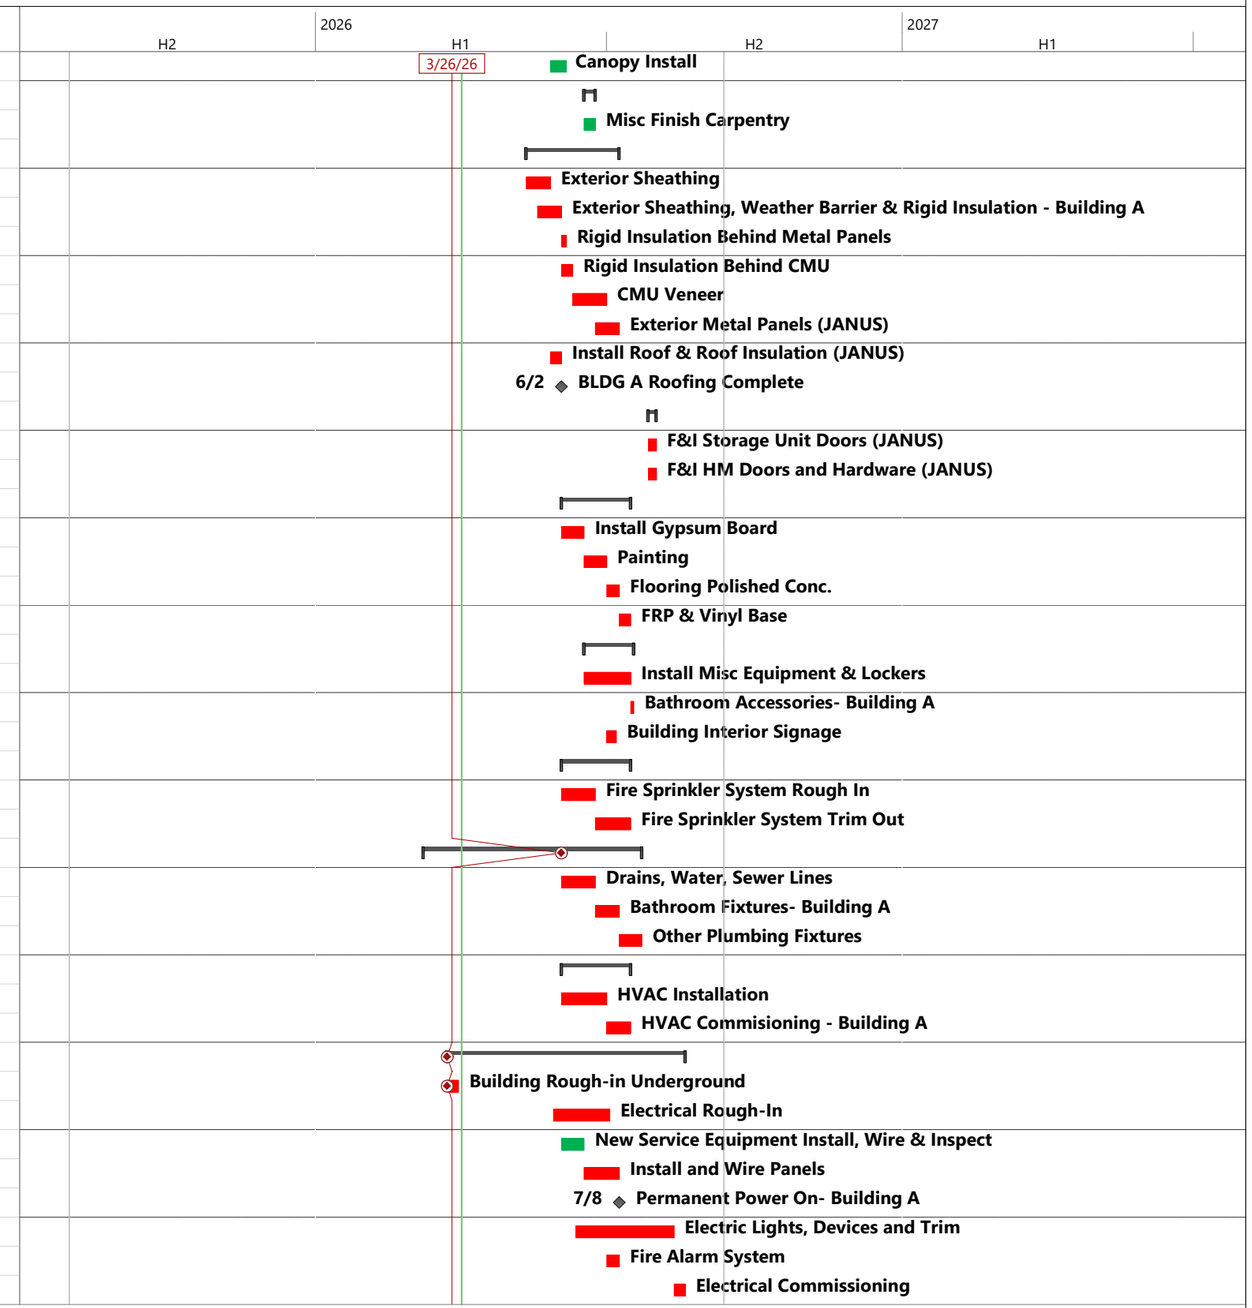

Printed: Thu 4/2/26 3:44 PM
