Public Storage,
Sandhill Road

ID	Task Name	% Complete	Duration	Start	Finish
0	**Overall Construction Schedule**	**56%**	**343 days**	**Wed 7/9/25**	**Fri 10/30/26**
4	**Procurement**	**62%**	**287 days**	**Thu 8/7/25**	**Fri 9/11/26**
86	075423 - TPO Roofing, Shop Drawing, Review/Approval	90%	20 days	Mon 2/23/26	Wed 4/22/26
85	075423 - TPO Roofing, Product Data, Review/Approval	0%	6 days	Mon 3/23/26	Tue 4/28/26
35	055110 - Aluminum Diamond Plate Wainscot, Product Data/Shop Drawings, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
44	064116 - Plastic Laminate Casework, Product Data, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
45	064116 - Plastic Laminate Casework, Shop Drawings, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
46	064116 - Plastic Laminate Casework, Color Samples	90%	20 days	Thu 3/26/26	Wed 4/22/26
51	066400 - FRP Submittals	72%	25 days	Thu 3/26/26	Wed 4/29/26
62	071416 - Cold Fluid Applied Waterproofing, Shop Drawings, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
80	072713 - Modified Bituminous Sheet Air Barriers, Shop Drawing, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
93	076200 - Sheet Metal Flashing and Trim, Shop Drawings, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
94	076200 - Sheet Metal Flashing and Trim, Samples, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
98	077100 - Roof Specialties, Product Data, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
99	077100 - Roof Specialties, Shop Drawing, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
144	089516 - Wall Vents, Product Data, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
145	089516 - Wall Vents, Metal Samples of Vents, for Approval	90%	20 days	Thu 3/26/26	Wed 4/22/26
162	101423 - Interior Signage, Product Data/Shop Drawings, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
163	101423 - Interior Signage, Samples for approval	90%	20 days	Thu 3/26/26	Wed 4/22/26
169	104413 - Fire Extinquishers/Cabinets, Product Data/Shop Drawings, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
178	113100 - Office Appliances, Product Data, Submittal	60%	30 days	Thu 3/26/26	Wed 5/6/26
201	230553 - ID for HVAC Piping & Equipment, Product Data, Submittals	90%	20 days	Thu 3/26/26	Wed 4/22/26
203	230593 - Testing and Balancing, Qualifications Data for TAB Firm	90%	20 days	Thu 3/26/26	Wed 4/22/26
204	230593 - Testing and Balancing, TAB agenda	90%	20 days	Thu 3/26/26	Wed 4/22/26
236	260553 - ID for Electrical Systems, Product Data/ID Schedule, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
261	265100 - LED Interior Lighting, Fabrication/Delivery	23%	80 days	Thu 3/26/26	Wed 7/15/26
264	265600 - Exterior Lighting, Fabrication/Delivery	23%	80 days	Thu 3/26/26	Wed 7/15/26
265	275123 - Intercommunications & PA Systems, Shop Drawings/Product Data, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
267	281300 - Access Control System, Shop Drawings, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
269	282300 - Video Surveillance, Product Data, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
271	282300 - Video Surveillance, Shop Drawings, Submittal	90%	20 days	Thu 3/26/26	Wed 4/22/26
275	283111 - Digital, Addressable Fire Alarm System, Product Data, Submittal to AHJ	90%	20 days	Thu 3/26/26	Wed 4/22/26
277	283111 - Digital, Addressable Fire Alarm System, Shop Drawings, Submittal to AHJ	90%	20 days	Thu 3/26/26	Wed 4/22/26
285	321713 - Parking Bumpers and Bollards, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
287	321723 - Pavement Markings, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
289	321726 - Tactile Warning Surfacing, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
291	321726 - Tactile Warning Surfacing, Color Sample Chart, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
293	323113 - Chain Link Fence, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
295	323113 - Chain Link Fence, Shop Drawings, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
297	323113 - Chain Link Fence, Samples, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
299	323114 - Security Wire Mesh Fences/Gates, Product Data, Submittals	72%	25 days	Thu 3/26/26	Wed 4/29/26
301	323114 - Security Wire Mesh Fences/Gates, Shop Drawings, Submittals	72%	25 days	Thu 3/26/26	Wed 4/29/26
307	328400 - Planting Irrigation, Product Data/Shop Drawings, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
309	329200 - Turf and Grasses, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
311	329300 - Plants, Product Data, Submittal	72%	25 days	Thu 3/26/26	Wed 4/29/26
176	107316 - Metal Canopies, Color Samples, Review/Approval	87%	15 days	Thu 4/2/26	Wed 4/22/26

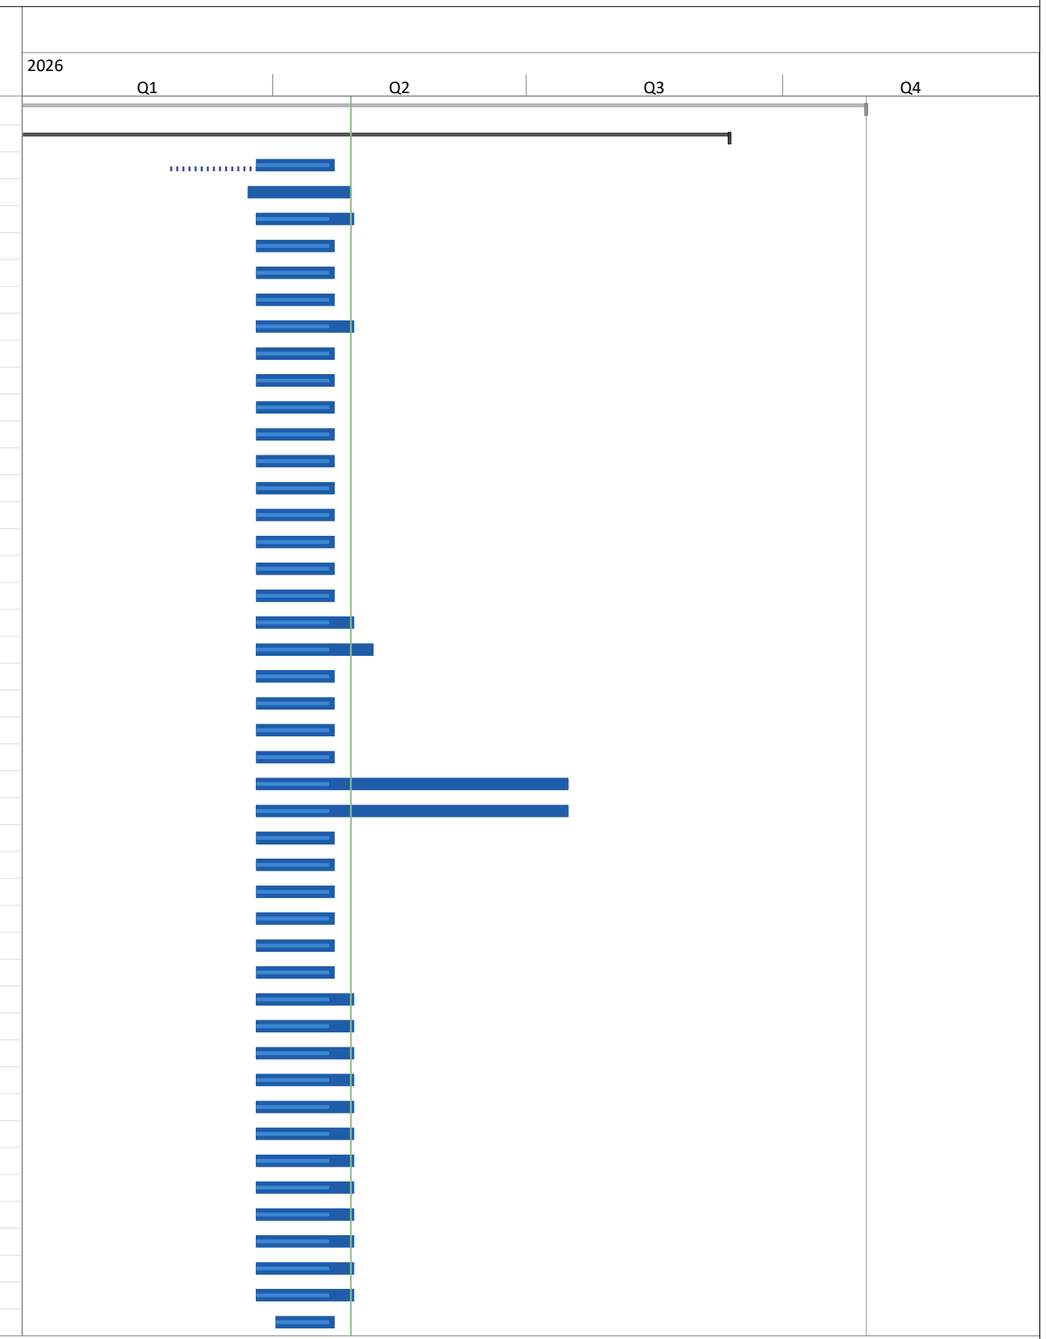

Public Storage,
Sandhill Road

ID	Task Name	% Complete	Duration	Start	Finish
13	033000 - CIP - Construction Joint Layout, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
14	033000 - CIP - Slab on Grade Control Joint Layout, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
41	061000 - Rough Carpentry, Product Data Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
54	071113 - Bituminous Waterproofing, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
58	071326 - Self-Adhering Sheet Waterproofing, Shop Drawings, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
60	071326 - Self-Adhering Sheet Waterproofing, Samples, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
63	071416 - Cold Fluid Applied Waterproofing, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
76	072500 - Weather Barriers, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
78	072500 - Weather Barriers, Shop Drawing, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
81	072713 - Modified Bituminous Sheet Air Barriers, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
88	075423- TPO Roofing, Sample Warranty, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
95	076200 - Sheet Metal Flashing and Trim, Product Data, Review/Approval	80%	10 days	Thu 4/9/26	Wed 4/22/26
114	079200 - Joint Sealants, Initial Samples for Selection, Review/Approval	80%	10 days	Thu 4/9/26	Wed 4/22/26
121	083113 - Access Doors and Frames, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
132	084329 - Sliding Automatic Storm Entrance, Color Sample, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
149	092216 - Non-Structural Metal Framing, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
157	099100 - Painting, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
159	099100- Painting, Initial Paint Selection, Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
233	260519 - Low-Voltage Power Conductors & Cables, Product Data, Review/Approvals	53%	15 days	Thu 4/9/26	Wed 4/29/26
235	260526 - Grounding and Bonding for Electrical, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
241	260923 - Lighting Control Devices, Shop Drawings, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
243	262200 - Low Voltage Transformers, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
245	262200 - Low Voltage Transformers, Shop Drawings, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
252	262726 - Wiring Devices, Product Data, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
258	262913 - Enclosed Controllers, Product Data/Shop Drawing, Review/Approval	53%	15 days	Thu 4/9/26	Wed 4/29/26
73	072410 - Stucco System, Color Samples, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
74	072410 - Stucco System, Shop Drawings, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
105	077200 - Roof Accessories, Product Data, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
106	077200 - Roof Accessories, Shop Drawings, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
107	077200 - Roof Accessories, Design Certifications, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
209	230713 - Duct Insulation, Product Data, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
211	230719 - HVAC Piping Insulation, Product Data, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
214	232300 - Refrigerant Piping, Product Data, Review/Approvals	20%	15 days	Thu 4/16/26	Wed 5/6/26
215	232300 - Refrigerant Piping, Shop Drawings, Review/Approvals	20%	15 days	Thu 4/16/26	Wed 5/6/26
217	233113 - Metal Ducts, Shop Drawings, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
221	233300 - Air Duct Accessories, Shop Drawings, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
227	238126 - Split System Air-Conditioners, Shop Drawings, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
231	238239 - Decentralized HVAC Equipment, Product Data, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
282	321313 - Concrete Paving, Design Mixes, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
284	321313 - Concrete Paving, Product Data, Review/Approval	20%	15 days	Thu 4/16/26	Wed 5/6/26
128	084113 - Aluminum Entrances/Storefront Fabrication/Delivery	5%	40 days	Fri 4/17/26	Thu 6/11/26
143	088000 - Glazing Fabrication/Delivery	3%	60 days	Fri 4/17/26	Thu 7/9/26
140	087111 - Door Hardware, Fabrication/Delivery	5%	20 days	Mon 4/20/26	Fri 5/15/26
47	064116 - Plastic Laminate Casework, Product Data, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
48	064116 - Plastic Laminate Casework, Shop Drawings, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
49	064116 - Plastic Laminate Casework, Color Samples, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26

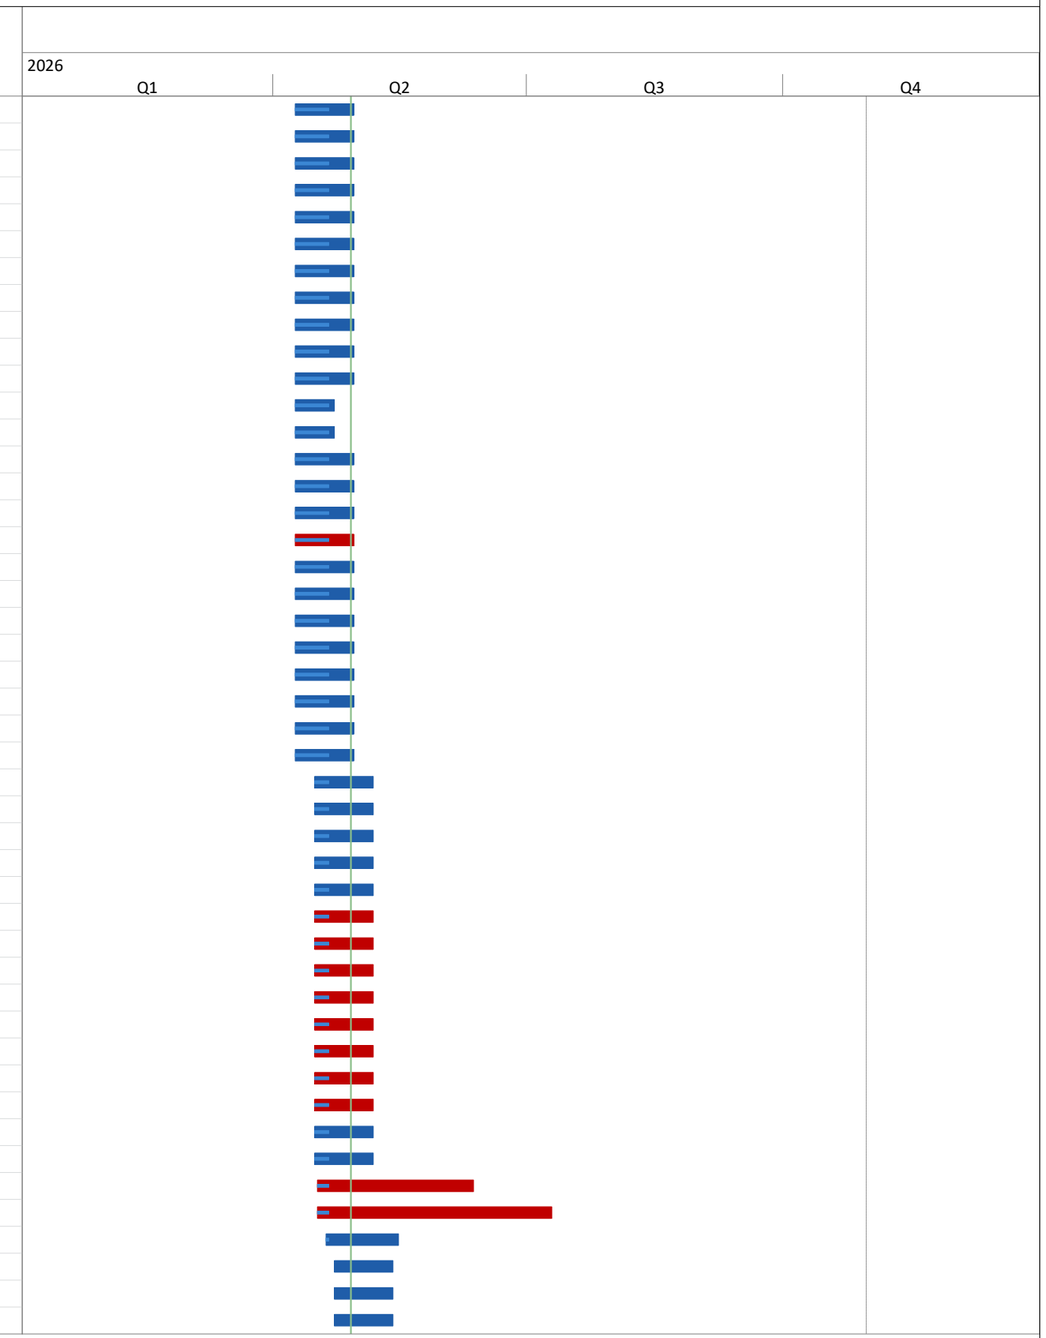

Public Storage,
Sandhill Road

ID	Task Name	% Complete	Duration	Start	Finish
64	071416 - Cold Fluid Applied Waterproofing, Shop Drawings, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
82	072713 - Modified Bituminous Sheet Air Barriers, Shop Drawing, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
96	076200 - Sheet Metal Flashing and Trim, Shop Drawings, Review/Approval	0%	10 days	Thu 4/23/26	Wed 5/6/26
97	076200 - Sheet Metal Flashing and Trim, Samples, Review/Approval	0%	10 days	Thu 4/23/26	Wed 5/6/26
100	077100 - Roof Specialties, Product Data, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
101	077100 - Roof Specialties, Shop Drawing, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
112	079200 - Joint Sealants, Samples for Verificiation	0%	20 days	Thu 4/23/26	Wed 5/20/26
146	089516 - Wall Vents, Product Data, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
147	089516 - Wall Vents, Metal Samples of Vents, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
164	101423 - Interior Signage, Product Data/Shop Drawings, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
165	101423 - Interior Signage, Samples, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
202	230553 - ID for HVAC Piping & Equipment, Product Data, Review/Approve	0%	15 days	Thu 4/23/26	Wed 5/13/26
205	230593 - Testing and Balancing, Qualifications Data, Review/Approval	0%	20 days	Thu 4/23/26	Wed 5/20/26
206	230593 - Testing and Balancing, TAB agenda, Review/Approval	0%	20 days	Thu 4/23/26	Wed 5/20/26
237	260553 - ID for Electrical Systems, Product Data/ID Schedule, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
266	275123 - Intercommunications & PA Systems, Shop Drawings/Product Data, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
268	281300 - Access Control System, Shop Drawings, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
270	282300 - Video Surveillance, Product Data, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
272	282300 - Video Surveillance, Shop Drawings, Review/Approval	0%	15 days	Thu 4/23/26	Wed 5/13/26
276	283111 - Digital, Addressable Fire Alarm System, Product Data, Review/Approval by AHJ	0%	60 days	Thu 4/23/26	Wed 7/15/26
278	283111 - Digital, Addressable Fire Alarm System, Shop Drawings, AHJ Review/Approval	0%	60 days	Thu 4/23/26	Wed 7/15/26
177	107316 - Metal Canopies, Fabrication/Delivery	0%	50 days	Fri 4/24/26	Thu 7/2/26
36	055110 - Aluminum Diamond Plate Wainscot, Product Data/Shop Drawings, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
52	066400 - FRP - Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
160	099100 - Painting, Samples for Verificiation, submittal to Architect	0%	10 days	Thu 4/30/26	Wed 5/13/26
170	104413 - Fire Extinquishers/Cabinets, Product Data/Shop Drawings, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
286	321713 - Parking Bumpers and Bollards, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
288	321723 - Pavement Markings, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
290	321726 - Tactile Warning Surfacing, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
292	321726 - Tactile Warning Surfacing, Color Sample Chart, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
294	323113 - Chain Link Fence, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
296	323113 - Chain Link Fence, Shop Drawings, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
298	323113 - Chain Link Fence, Samples, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
300	323114 - Security Wire Mesh Fences/Gates, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
302	323114 - Security Wire Mesh Fences/Gates, Shop Drawings, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
308	328400 - Planting Irrigation, Product Data/Shop Drawings, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
310	329200 - Turf and Grasses, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
312	329300 - Plants, Product Data, Review/Approval	0%	15 days	Thu 4/30/26	Wed 5/20/26
179	113100 - Office Appliances, Product Data, Review/Approval	0%	15 days	Thu 5/7/26	Wed 5/27/26
89	075423 - TPO Roofing, Closeout Submittal, Maintenance Data	0%	20 days	Tue 5/12/26	Mon 6/8/26
90	075423 - TPO Roofing, Closeout Submittal, Roof Warranty	0%	20 days	Tue 5/12/26	Mon 6/8/26
91	075423 - TPO Roofing, Closeout Submittal, Record Drawings	0%	20 days	Tue 5/12/26	Mon 6/8/26
50	064116 - Plastic Laminate Casework, Fabrication/Delivery	0%	25 days	Thu 5/14/26	Wed 6/17/26

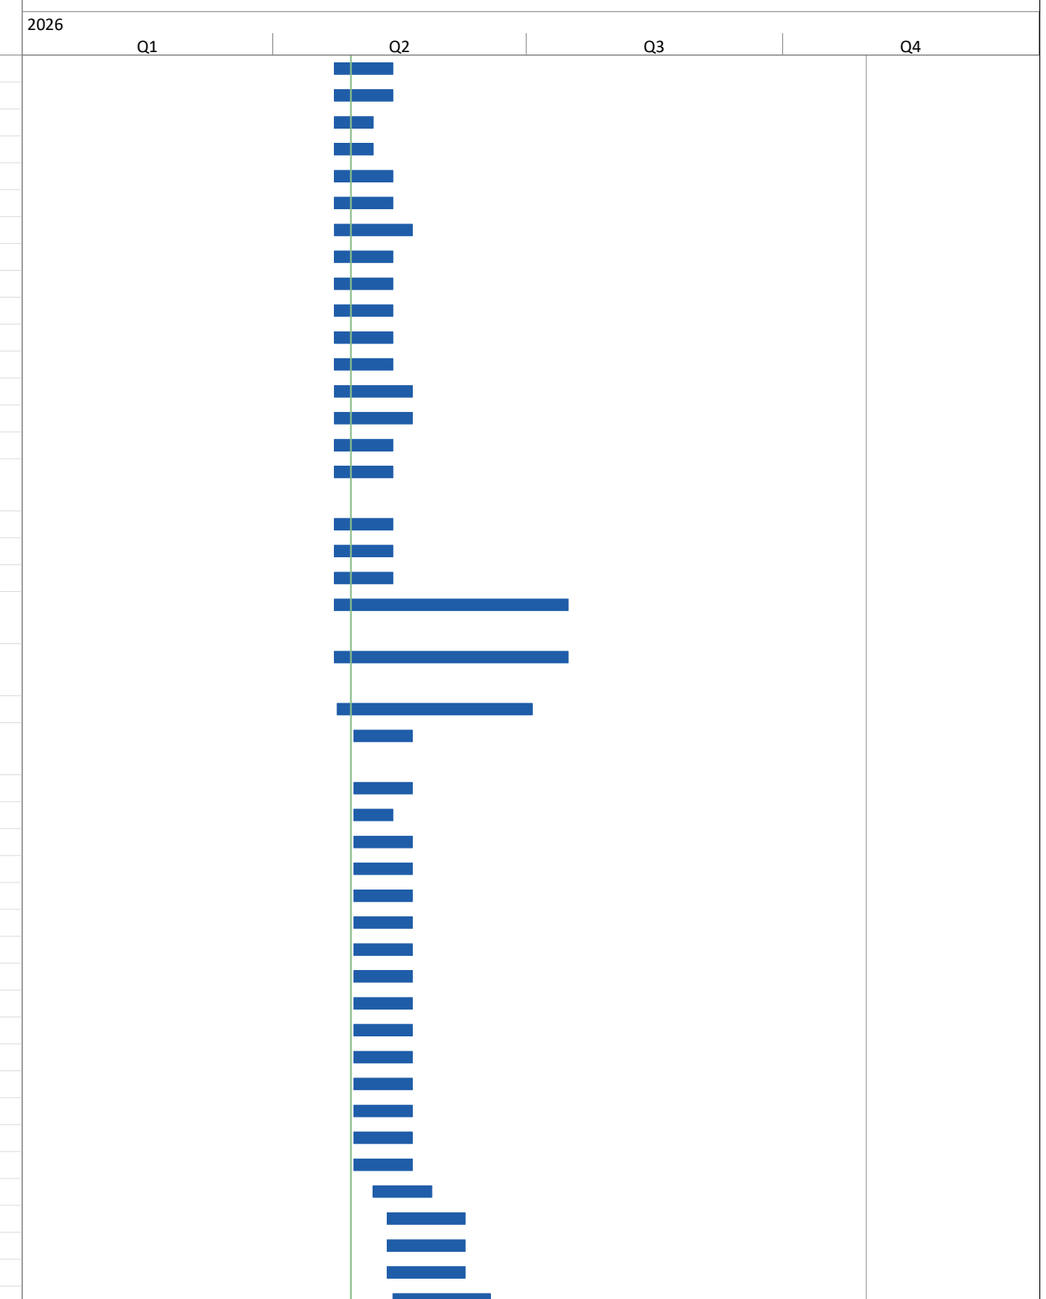

Public Storage,
Sandhill Road

ID	Task Name	% Complete	Duration	Start	Finish
161	099100 - Painting, Samples for Verificaiton, Review/Approval	0%	15 days	Thu 5/14/26	Wed 6/3/26
166	101423 - Interior Signage, Fabrication/Delivery	0%	15 days	Thu 5/14/26	Wed 6/3/26
115	079200 - Joint Sealants, Samples for Verificiation, Review/Approval	0%	20 days	Thu 5/21/26	Wed 6/17/26
207	230593 - Testing and Balancing, Final TAB Report	0%	10 days	Mon 8/31/26	Fri 9/11/26
313	**Pre-Installation Meetings**	**50%**	**173 days**	**Tue 9/23/25**	**Thu 5/21/26**
320	Preinstallation Meeting, Metal Canopies	0%	1 day	Thu 4/23/26	Thu 4/23/26
325	Preinstallation Meeting, TPO Roofing/Sheet Metal Flashing & Trim	0%	1 day	Thu 4/23/26	Thu 4/23/26
326	Preinstallation Meeting, Stucco System	0%	1 day	Thu 5/7/26	Thu 5/7/26
317	Preinstallation Meeting, Cold Fluid Applied Waterproofing	0%	1 day	Thu 5/14/26	Thu 5/14/26
322	Preinstallation Meeting, Fencing	0%	1 day	Thu 5/21/26	Thu 5/21/26
323	Preinstallation Meeting, Security Wire Mesh Fence and Gates	0%	1 day	Thu 5/21/26	Thu 5/21/26
389	**Site Utlities/As-Builts**	**59%**	**215 days**	**Thu 11/20/25**	**Wed 9/16/26**
395	Permanent Power to Building	50%	16 days	Fri 4/17/26	Fri 5/8/26
396	As-Built Drawings for Sanitary and Storm Water	0%	12 days	Tue 9/1/26	Wed 9/16/26
352	**Building Construction**	**28%**	**178 days**	**Wed 12/10/25**	**Fri 8/14/26**
374	3rd floor structure erection & Roof	67%	24 days	Mon 3/30/26	Thu 4/30/26
375	Install TPO Roofing	0%	7 days	Fri 5/1/26	Mon 5/11/26
385	Light gauge office framing	0%	5 days	Fri 5/1/26	Thu 5/7/26
380	Stanley Sliding Door Install	0%	1 day	Tue 5/12/26	Tue 5/12/26
376	**Roofing Complete - Building Dry-In**	0%	0 days	Tue 5/12/26	Tue 5/12/26
386	Elevator #1 Install	0%	20 days	Thu 5/14/26	Wed 6/10/26
377	EIFS/Stucco	0%	35 days	Fri 5/15/26	Thu 7/2/26
387	Elevator #2 install	0%	20 days	Thu 6/11/26	Wed 7/8/26
378	Storefront Frames Install	0%	10 days	Fri 6/12/26	Thu 6/25/26
381	Canopies	0%	8 days	Fri 7/3/26	Tue 7/14/26
379	Storefront Glass Installed	0%	10 days	Fri 7/10/26	Thu 7/23/26
382	Install Metal Coping/Downspouts/Trim	0%	6 days	Fri 7/24/26	Fri 7/31/26
388	Building Façade Complete	0%	0 days	Fri 7/31/26	Fri 7/31/26
383	Exterior Building Caulking	0%	5 days	Mon 8/3/26	Fri 8/7/26
384	Exterior Building Punchlist	0%	5 days	Mon 8/10/26	Fri 8/14/26
397	**Rough-ins and Finishes**	**0%**	**157 days**	**Thu 2/19/26**	**Fri 9/25/26**
398	1st Floor Electrical/Fire Alarm Rough In	0%	7 days	Thu 2/19/26	Tue 5/26/26
399	1st Floor HVAC Rough In	0%	7 days	Tue 2/24/26	Fri 5/15/26
400	1st Floor Sprinkler Rough-in/riser room-1st floor	0%	12 days	Tue 3/3/26	Fri 5/15/26
420	Office Buildout	0%	30 days	Mon 3/16/26	Thu 8/6/26
406	2nd Floor Electrical/Fire Alarm Rough In	0%	15 days	Thu 3/26/26	Wed 6/17/26
411	Install Gear in Electrical Room	0%	7 days	Thu 4/16/26	Mon 5/11/26
405	2nd Floor HVAC Rough In	0%	15 days	Thu 5/7/26	Wed 5/27/26
413	3rd Floor HVAC Rough In	0%	15 days	Thu 5/7/26	Wed 5/27/26
412	Power to elevator machine rooms	0%	2 days	Tue 5/12/26	Wed 5/13/26
414	3rd Floor Electrical/Fire Alarm Rough In	0%	15 days	Tue 5/19/26	Mon 6/8/26
407	2nd Floor Sprinkler Rough-in	0%	7 days	Thu 5/21/26	Fri 5/29/26
401	1st Floor HVAC Trim/Line Set	0%	10 days	Wed 5/27/26	Tue 6/9/26
408	2nd Floor HVAC Trim/Line Sets	0%	10 days	Mon 6/1/26	Fri 6/12/26
415	3rd Floor Sprinkler Rough-in	0%	5 days	Tue 6/9/26	Mon 6/15/26
403	1st Floor Hallway System- by Janus	0%	20 days	Wed 6/10/26	Tue 7/7/26

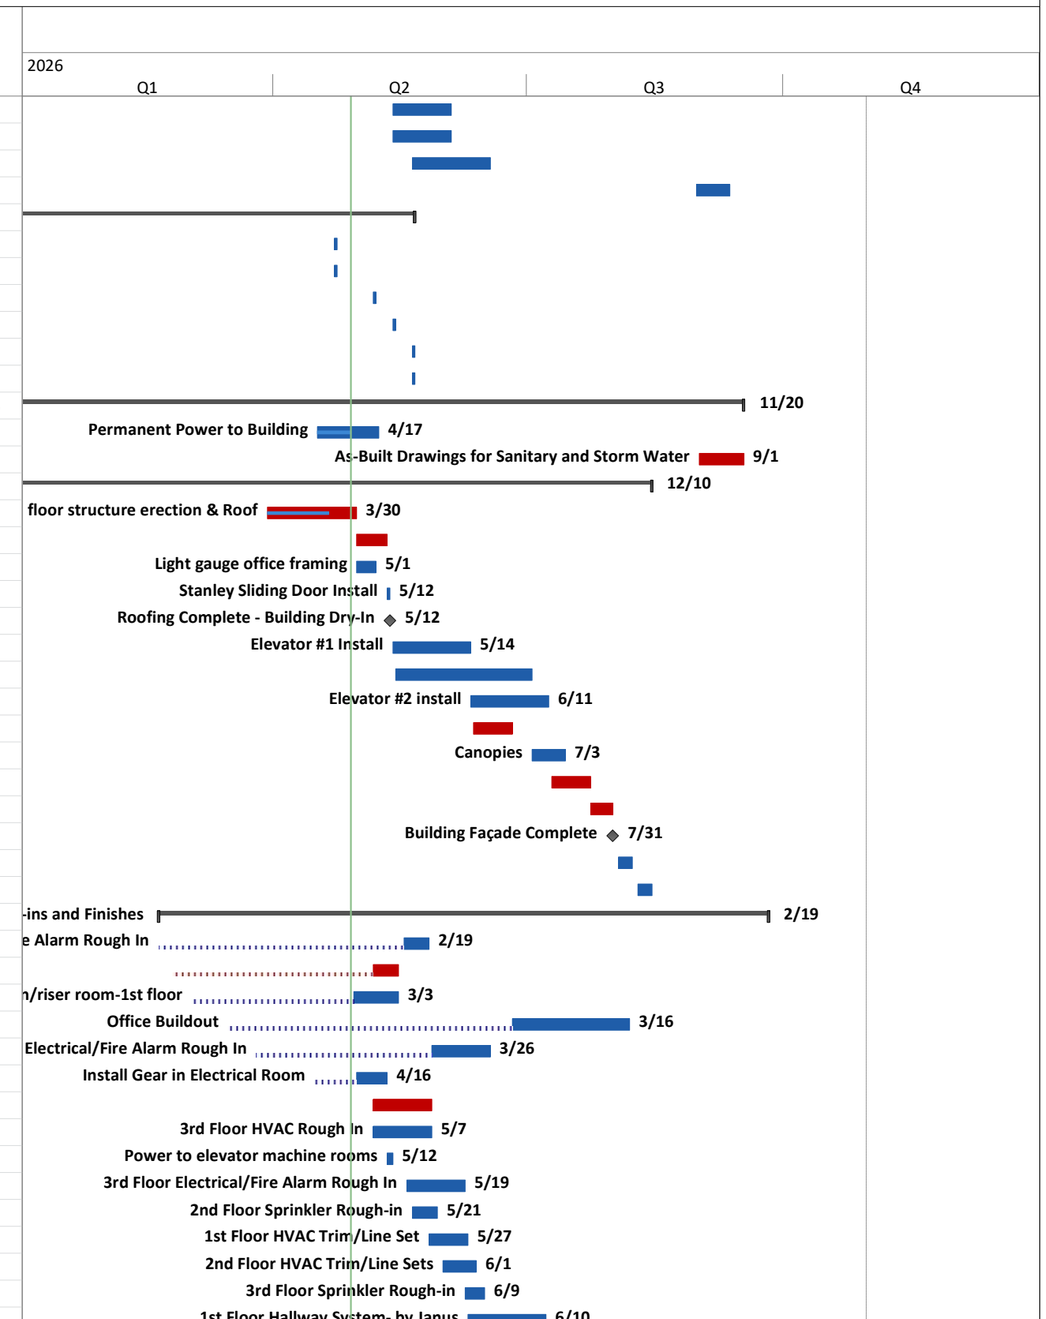

Public Storage,
Sandhill Road
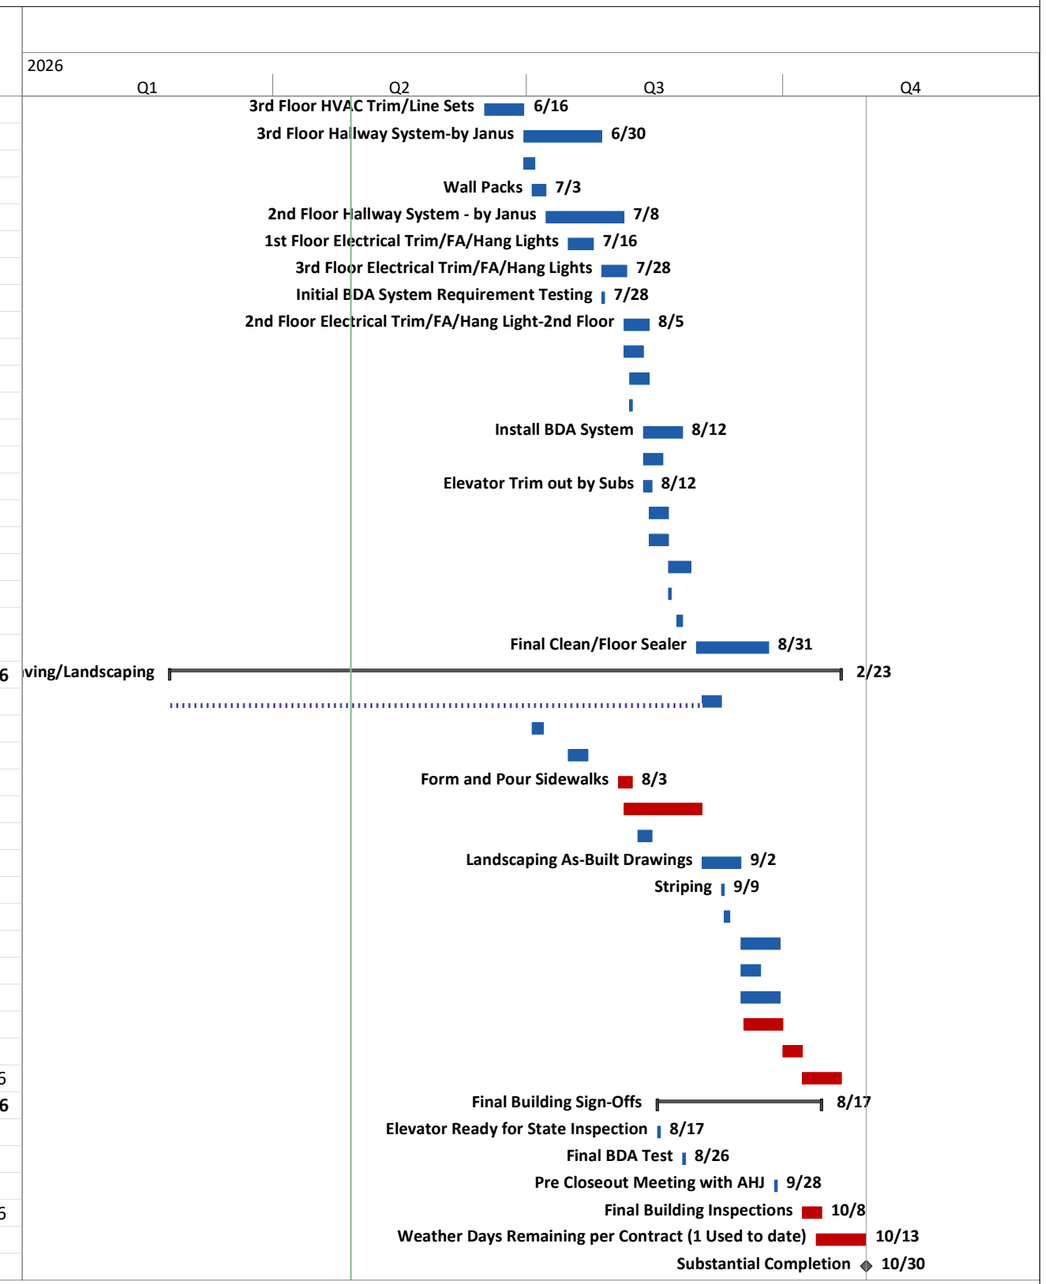
ID	Task Name	% Complete	Duration	Start	Finish
416	3rd Floor HVAC Trim/Line Sets	0%	10 days	Tue 6/16/26	Mon 6/29/26
417	3rd Floor Hallway System-by Janus	0%	20 days	Tue 6/30/26	Mon 7/27/26
429	Install Plumbing Fixtures and Water Heaters	0%	4 days	Tue 6/30/26	Fri 7/3/26
433	Wall Packs	0%	3 days	Fri 7/3/26	Tue 7/7/26
409	2nd Floor Hallway System - by Janus	0%	20 days	Wed 7/8/26	Tue 8/4/26
404	1st Floor Electrical Trim/FA/Hang Lights	0%	7 days	Thu 7/16/26	Fri 7/24/26
418	3rd Floor Electrical Trim/FA/Hang Lights	0%	7 days	Tue 7/28/26	Wed 8/5/26
421	Initial BDA System Requirement Testing	0%	1 day	Tue 7/28/26	Tue 7/28/26
410	2nd Floor Electrical Trim/FA/Hang Light-2nd Floor	0%	7 days	Wed 8/5/26	Thu 8/13/26
419	Install Aluminum Wainscot at Elevator Lobbies	0%	5 days	Wed 8/5/26	Tue 8/11/26
423	1st Floor Punchlist Repairs	0%	5 days	Fri 8/7/26	Thu 8/13/26
431	Install Fire Extinguishers and Cabinets	0%	1 day	Fri 8/7/26	Fri 8/7/26
422	Install BDA System	0%	10 days	Wed 8/12/26	Tue 8/25/26
425	3rd Floor Punchlist Repairs	0%	5 days	Wed 8/12/26	Tue 8/18/26
434	Elevator Trim out by Subs	0%	3 days	Wed 8/12/26	Fri 8/14/26
424	2nd Floor Punchlist Repairs	0%	5 days	Fri 8/14/26	Thu 8/20/26
432	Final Painting, Stairs/Railings/Doors	0%	5 days	Fri 8/14/26	Thu 8/20/26
428	HVAC Startup	0%	6 days	Fri 8/21/26	Fri 8/28/26
430	Install Interior Signage	0%	1 day	Fri 8/21/26	Fri 8/21/26
426	Complete Interior Punchlist Work - All Floors	0%	2 days	Mon 8/24/26	Tue 8/25/26
427	Final Clean/Floor Sealer	0%	20 days	Mon 8/31/26	Fri 9/25/26
435	**Finsh Sitework - Dumpster/Sidewalks/Paving/Landscaping**	**0%**	**173 days**	**Mon 2/23/26**	**Wed 10/21/26**
440	Curb/Asphalt Paving	0%	5 days	Mon 2/23/26	Tue 9/8/26
436	Rough grade for landscaping	0%	2 days	Fri 7/3/26	Mon 7/6/26
437	Install Exterior Lighting in Parking Area	0%	5 days	Thu 7/16/26	Wed 7/22/26
438	Form and Pour Sidewalks	0%	5 days	Mon 8/3/26	Fri 8/7/26
439	Landscaping and Irrigation Installation	0%	20 days	Wed 8/5/26	Tue 9/1/26
441	Install Fencing	0%	5 days	Mon 8/10/26	Fri 8/14/26
443	Landscaping As-Built Drawings	0%	10 days	Wed 9/2/26	Tue 9/15/26
442	Striping	0%	1 day	Wed 9/9/26	Wed 9/9/26
446	Contractor's Letter of Completion	0%	2 days	Thu 9/10/26	Fri 9/11/26
444	Developer's Letter of Dedication	0%	10 days	Wed 9/16/26	Tue 9/29/26
445	Engineer's Certificate of Completion	0%	5 days	Wed 9/16/26	Tue 9/22/26
447	Satisfaction Letter/Email from FDOT and City for Infrastructure	0%	10 days	Wed 9/16/26	Tue 9/29/26
448	SOV for Site Utilites, Water, Wastewater, Reclaimed Water	0%	10 days	Thu 9/17/26	Wed 9/30/26
449	Polk County Final Walkthrough Request	0%	5 days	Thu 10/1/26	Wed 10/7/26
450	Polk County Approval of Site	0%	10 days	Thu 10/8/26	Wed 10/21/26
451	**Final Building Sign-Offs**	**0%**	**43 days**	**Mon 8/17/26**	**Wed 10/14/26**
454	Elevator Ready for State Inspection	0%	1 day	Mon 8/17/26	Mon 8/17/26
453	Final BDA Test	0%	1 day	Wed 8/26/26	Wed 8/26/26
452	Pre Closeout Meeting with AHJ	0%	1 day	Mon 9/28/26	Mon 9/28/26
455	Final Building Inspections	0%	5 days	Thu 10/8/26	Wed 10/14/26
456	**Weather Days Remaining per Contract (1 Used to date)**	0%	14 days	Tue 10/13/26	Fri 10/30/26
457	**Substantial Completion**	0%	0 days	Fri 10/30/26	Fri 10/30/26
