Davenport, FL

Compare Remaining Compression

Report Date: 03/04/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
260129- Davenport - 01/29/2026	**260129- Davenport -03/03/2026**
Data Date: 01/29/2026	Data Date: 03/03/2026
Finish Date: 10/30/2026	Finish Date: 10/30/2026

Remaining Work Compression 59 %

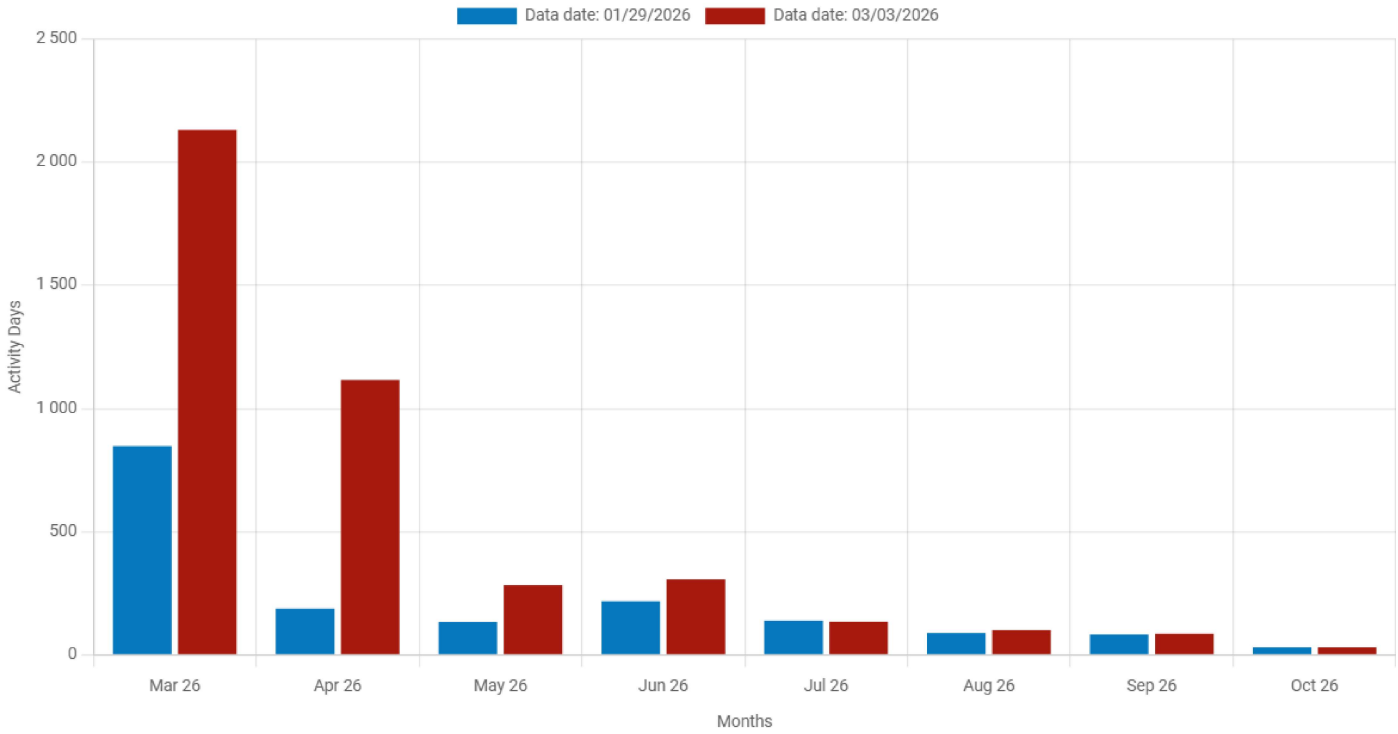

Month	01/29/2026 Activity Days	03/03/2026 Activity Days
Mar 26	848	2132
Apr 26	188	1116
May 26	133	283
Jun 26	217	307
Jul 26	139	134
Aug 26	89	100
Sep 26	83	86
Oct 26	31	31
