ID	Task Name	Duration	Start	Finish	Predecessors	Successors
1	**Frisco Office TI**	**197 days**	**Mon 25/09/08**	**Tue 26/06/09**		
2	**Construction Documents**	**136 days**	**Mon 25/09/08**	**Mon 26/03/16**		
3	CD Kick off and Start	34 days	Mon 25/09/08	Thu 25/10/23		4
4	65% progress set	1 day	Fri 25/10/24	Fri 25/10/24	3	5
5	Owner Drawing review of 65% set	5 days	Mon 25/10/27	Fri 25/10/31	4	6
6	Completon of Bid, Demo and Permit Submital set	10 days	Mon 25/11/03	Fri 25/11/14	5	8;16;12
7	**Plan Check**	**31 days**	**Mon 25/11/17**	**Mon 25/12/29**		
8	**Issue for Interiors Permit (Plan Check)**	**31 days**	**Mon 25/11/17**	**Mon 25/12/29**	**6**	
9	City Permit Review	15 days	Mon 25/11/17	Fri 25/12/05		10
10	Drawing Coordination/City Comments	15 days	Mon 25/12/08	Fri 25/12/26	9	11
11	Receive Interior TI Building Permit	1 day	Mon 25/12/29	Mon 25/12/29	10	34
12	**Issue for Demo Permit**	**16 days**	**Mon 25/11/17**	**Mon 25/12/08**	**6**	
13	Demo Permit Review	15 days	Mon 25/11/17	Fri 25/12/05		14
14	Receive Demo Permit	1 day	Mon 25/12/08	Mon 25/12/08	13	32
15	**Bidding**	20 days	Mon 25/11/17	Fri 25/12/12		
16	Bidding for TI GCs	15 days	Mon 25/11/17	Fri 25/12/05	6	17
17	Award GC Contract	5 days	Mon 25/12/08	Fri 25/12/12	16	32
18	**Procurement of Direct FBO items**	136 days	Mon 25/09/08	Mon 26/03/16		
19	**Furniture**	97 days	Fri 25/10/31	Mon 26/03/16		
20	Select Furniture Vendor	1 day	Fri 25/10/31	Fri 25/10/31		21
21	Review and finalize details for furniture	15 days	Mon 25/11/03	Fri 25/11/21	20	22
22	Furniture Order Due	1 day	Mon 25/11/24	Mon 25/11/24	21	23
23	Furniture Lead Time	80 days	Tue 25/11/25	Mon 26/03/16	22	47
24	**HVAC Equipment**	71 days	Mon 25/10/27	Mon 26/02/02		
25	Order Roof Top HVAC equipment	1 day	Mon 25/10/27	Mon 25/10/27		35;26
26	HVAC Equipment Lead Time	70 days	Tue 25/10/28	Mon 26/02/02	25	35;36
27	**Elevator Modernization**	126 days	Mon 25/09/08	Mon 26/03/02		
28	Contract for Elevator Modernization	1 day	Mon 25/09/08	Mon 25/09/08		29
29	Elevator Equipment Lead Time	100 days	Tue 25/09/09	Mon 26/01/26	28	30
30	Elevator Modernization	25 days	Tue 26/01/27	Mon 26/03/02	29	48
31	**Demolition**	**15 days**	**Mon 25/12/15**	**Fri 26/01/02**		
32	Demo of finishes/Existing	15 days	Mon 25/12/15	Fri 26/01/02	17;14	34
33	**Construction**	112 days	Mon 26/01/05	Tue 26/06/09		
34	Overhead MEP installation	15 days	Mon 26/01/05	Fri 26/01/23	32;11	37
35	Installation of Roof Top HVAC	10 days	Tue 26/02/03	Mon 26/02/16	25;26	38
36	Installation of VAV boxes HVAC rework	10 days	Tue 26/02/03	Mon 26/02/16	26	41
37	Framing one side drywall	15 days	Mon 26/01/26	Fri 26/02/13	34	38

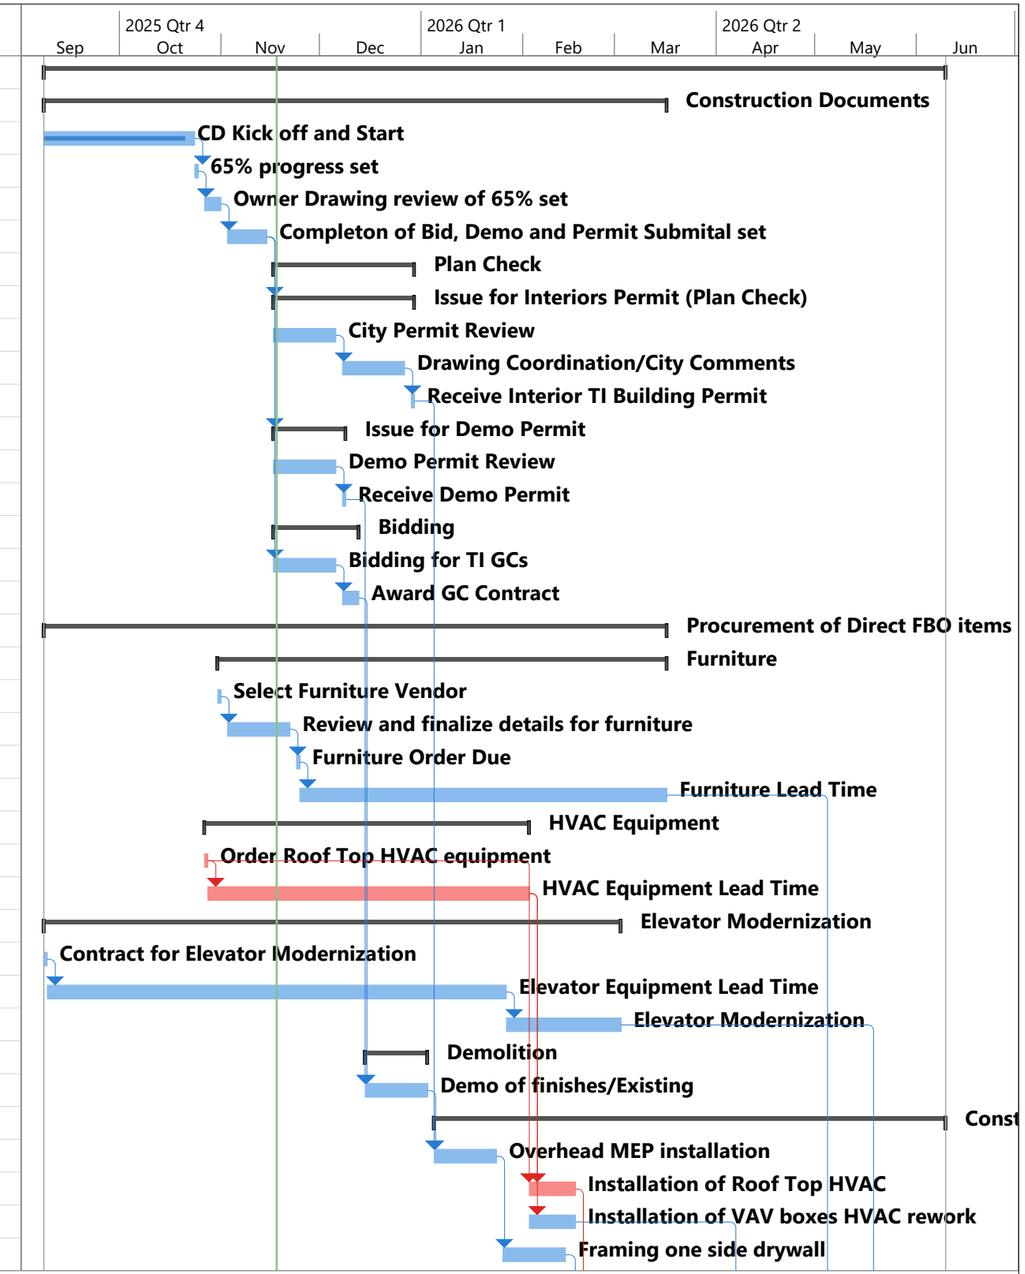

Project: Frisco Master Schedule
Date: Tue 25/11/18

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
Split	Inactive Milestone	Manual Summary	Deadline	
Milestone	Inactive Summary	Start-only	Critical	
Summary	Manual Task	Finish-only	Critical Split	
Project Summary	Duration-only	External Tasks	Progress	

ID	Task Name	Duration	Start	Finish	Predecessors	Successors
38	MEP Rough in Walls and Floors	15 days	Tue 26/02/17	Mon 26/03/09	37;35	39SS+10 days;45;
39	Data and Wiring Low Voltage	10 days	Tue 26/03/03	Mon 26/03/16	38SS+10 days	45;46;40
40	Wall Taping finish	15 days	Tue 26/03/17	Mon 26/04/06	39	44;45;46;41
41	Grid install rework	10 days	Tue 26/04/07	Mon 26/04/20	40;36	42SS+5 days
42	Light fixtures install	10 days	Tue 26/04/14	Mon 26/04/27	41SS+5 days	43
43	Ceiling tile installation	10 days	Tue 26/04/28	Mon 26/05/11	42;46	48;47SS+5 days
44	Millwork and fixtures	15 days	Tue 26/04/07	Mon 26/04/27	40	48
45	AV Equipment Installation	10 days	Tue 26/04/07	Mon 26/04/20	38;39;40	48
46	Security Systems Equipment Installation	10 days	Tue 26/04/07	Mon 26/04/20	38;39;40	48;43
47	Furniture systems installation	10 days	Tue 26/05/05	Mon 26/05/18	23;38;43SS+5 day	48
48	Inspections and Commissioning	10 days	Tue 26/05/19	Mon 26/06/01	47;45;44;43;46;3(	49
49	Final Clean	5 days	Tue 26/06/02	Mon 26/06/08	48	50
50	**Move in**	1 day	Tue 26/06/09	Tue 26/06/09	49	

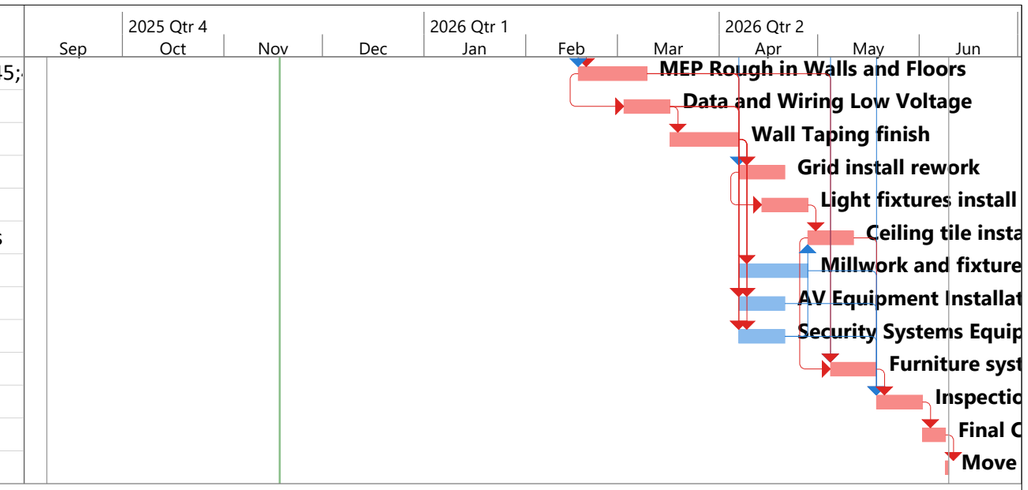

Project: Frisco Master Schedule
Date: Tue 25/11/18

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
Split	Inactive Milestone	Manual Summary	Deadline	
Milestone	Inactive Summary	Start-only	Critical	
Summary	Manual Task	Finish-only	Critical Split	
Project Summary	Duration-only	External Tasks	Progress	
