Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 1/12/2026

Type	Project	Region	Responsible
Construction	Mesa, AZ	West Coast	Josh Pait

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
1/12/2026	4/8/2026	-86 Baseline 34 Previous	Remaining Work Compression: 26% — Normal

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP		12/27/2024	12/27/2024	0	0	Notice To Proceed	On Track – Gaining
Foundation Complete		4/21/2025	4/21/2025	0	0	Pour Slab On Grade South 8"	On Track – Gaining
Structure Top Out		10/6/2025	10/6/2025	0	0	Roof Structural @ Platforms & Screens	On Track – Gaining
Weather Tight		11/12/2025	11/12/2025	0	0	Roof Insulation Cover Board & Membrane	On Track – Gaining
Permanent Power		1/23/2026	2/10/2026	-18	-18	City Of Mesa Work Scope Power To Building	Delayed – Slipping
Hardscape/Landscape Complete		3/23/2026	3/13/2026	10	10	Landscape	On Track – Gaining
Elevator Complete		3/25/2026	3/16/2026	9	9	Elevator Inspection Scheduling And Approval	On Track – Gaining
Contract Completion	1/12/2026	5/12/2026	4/8/2026	-86	34	Building Final	Delayed – Gaining

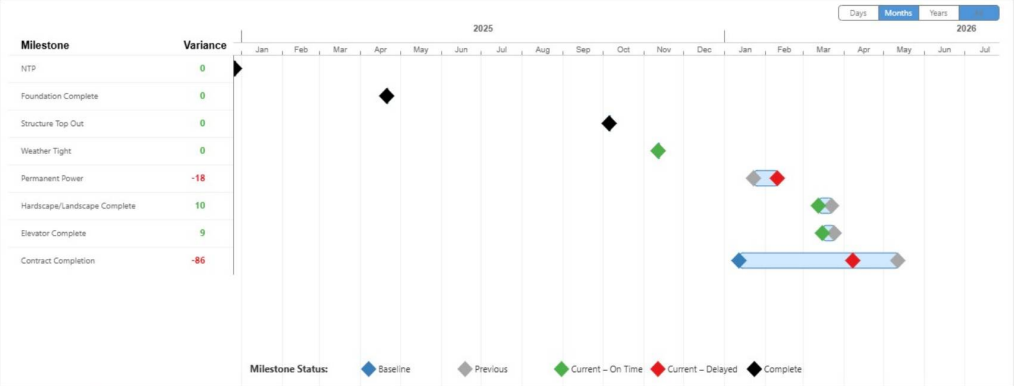

Baseline Variance

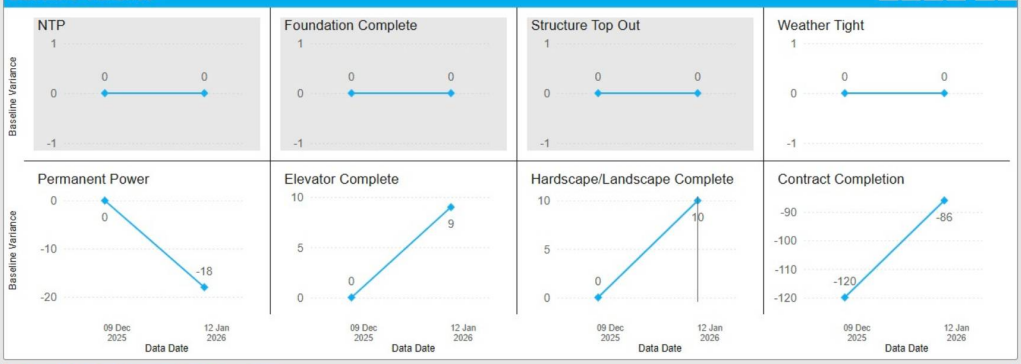

Schedule Performance Summary

Summary

High-risk conditions dominate the schedule, driven by widespread changes, weak schedule quality, ineffective execution, and aggressive compression of remaining activities. These deficiencies severely compromise forecast accuracy and project control; immediate leadership intervention and schedule management reforms should be prioritized.

Execution Score: 0.00% — ALERT
The schedule is not being used effectively to manage real work; actual execution diverges completely from plan, undermining forecasting and control. Urgent corrective action and team retraining are recommended

Remaining Work Compression: 26% — Normal
Excessive compression in the remaining workload increases risk of resource overload and future delays. Review recovery strategies and avoid aggressive re-sequencing unless supported by realistic resource plans.

Schedule Change Index: 100.00% — ALERT
Logic or date changes have impacted all schedule activities, signaling extreme volatility and absence of planning discipline. Investigate for systemic issues such as scope redefinition or mass resequencing.

Schedule Validation Score: 54.00 — ALERT
The schedule does not meet minimum quality standards, indicating poor logic, inadequate forecasting practices, and a high risk of unreliable critical path analysis. Immediate quality remediation is required

Powered By STELIC INSIGHT+ACTION=IMPACT
