	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**231 days**	**255 days**	**-24d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Tue 8/4/26**	**Mon 9/7/26**	**-24d**
2	Notice to Proceed	1 day	1 day	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/8/25	Mon 9/8/25	0d
3	DELAY - PERMIT DELAY	32 days	32 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Wed 10/22/25	Wed 10/22/25	0d
4	Obtain Building Permit	0 days	0 days	0d	Wed 10/22/25	Wed 10/22/25	0d	Wed 10/22/25	Wed 10/22/25	0d
5	ACHD ROW Permit	0 days	0 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 10/29/25	Wed 10/29/25	0d
6	Obtain LDIR Approval to Proceed	0 days	0 days	0d	Mon 10/27/25	Mon 10/27/25	0d	Mon 10/27/25	Mon 10/27/25	0d
7	Receive CAD Base Files from Public Storage	10 days	10 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/22/25	Mon 9/22/25	0d
8	Procure Early Work Subcontractors	5 days	5 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/15/25	Mon 9/15/25	0d
9	Procure Remaining Subcontractors	20 days	20 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 10/13/25	Mon 10/13/25	0d
10	Submittals (SWPPP/NOI)	10 days	10 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/29/25	Mon 9/29/25	0d
11	Submittals (SES /Switchgear)	125 days	125 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Fri 3/13/26	Fri 3/13/26	0d
12	Submittals (numerous)	150 days	150 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Fri 5/15/26	Fri 5/15/26	0d
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	124 days	124 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Mon 4/20/26	Mon 4/20/26	0d
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	108 days	110 days	-2d	Thu 11/6/25	Thu 11/6/25	0d	Fri 4/10/26	Tue 4/14/26	-2d
15	Procure SES's/Switchgears (6 mos ~ 130 WD)	56 days	56 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 1/23/26	Fri 1/23/26	0d
16	Light Fixture Submittal Review and Approval	10 days	10 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Fri 2/6/26	Fri 2/6/26	0d
17	Light Fixture Package Alternate - Fab and Deliver	10 days	10 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Fri 2/20/26	Fri 2/20/26	0d
18	Fire Sprinkler Design and Approval	78 days	78 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 2/4/26	Wed 2/4/26	0d
19	Fire Alarm System Design and Approval	40 days	40 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 12/10/25	Wed 12/10/25	0d
20	ASPHALT BATCH PLANT SHUTDOWN	70 days	70 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Thu 2/26/26	Thu 2/26/26	0d
21	TWENTY WORKING DAYS OF WEATHER DELAY	10 days	10 days	0d	Wed 7/22/26	Tue 8/25/26	-24d	Tue 8/4/26	Mon 9/7/26	-24d
22	WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	2 days	0d	Wed 12/17/25	Wed 12/17/25	0d	Thu 12/18/25	Thu 12/18/25	0d
23	WEATHER DELAY - Rain - Impact SOG B	1 day	1 day	0d	Mon 12/22/25	Mon 12/22/25	0d	Mon 12/22/25	Mon 12/22/25	0d
24	WEATHER DELAY - Rain - Impact SOG B	3 days	3 days	0d	Thu 1/8/26	Thu 1/8/26	0d	Mon 1/12/26	Mon 1/12/26	0d
25	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Wed 2/18/26	Wed 2/18/26	0d
26	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/24/26	Tue 2/24/26	0d	Wed 2/25/26	Wed 2/25/26	0d
27	Substantial Completion	0 days	0 days	0d	Tue 8/4/26	Mon 9/7/26	-24d	Tue 8/4/26	Mon 9/7/26	-24d
28	Clean Up and Project Close Out	5 days	5 days	0d	Tue 6/30/26	Thu 8/13/26	-32d	Tue 7/7/26	Wed 8/19/26	-31d
29	Demobilize	3 days	3 days	0d	Wed 7/8/26	Thu 8/20/26	-31d	Fri 7/10/26	Mon 8/24/26	-31d
30	**SITEWORK**	**212 days**	**219 days**	**-7d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Wed 7/8/26**	**Fri 7/17/26**	**-7d**
31	**Level of Effort**	**131 days**	**131 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 3/13/26**	**Fri 3/13/26**	**0d**
32	Construction Staking & Surveying	90 days	90 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 1/16/26	Fri 1/16/26	0d
33	Inspections and Testing	100 days	100 days	0d	Fri 9/12/25	Fri 9/12/25	0d	Fri 2/13/26	Fri 2/13/26	0d
34	Maintain Erosion Control	120 days	120 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Fri 3/13/26	Fri 3/13/26	0d
35	Erosion Control & SWPP	5 days	5 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/22/25	Mon 9/22/25	0d
36	Mobilization	5 days	5 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/15/25	Mon 9/15/25	0d
37	Site Demolition (Trees,Sawcut, Asphalt, Base)	0 days	0 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 9/12/25	Fri 9/12/25	0d
38	Clear/Grub & Overlot Grading	12 days	12 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Tue 9/23/25	Tue 9/23/25	0d
39	Structure Demo (Partial Building & RV Storage)	5 days	5 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/7/25	Fri 11/7/25	0d
40	Re-Mobilization	4 days	4 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Tue 10/28/25	Tue 10/28/25	0d
41	FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	7 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Thu 11/6/25	Thu 11/6/25	0d
42	Site - Water Line Ten Mile Tie-In	2 days	2 days	0d	Sat 11/8/25	Sat 11/8/25	0d	Tue 11/11/25	Tue 11/11/25	0d
43	Work Week Restriction	5 days	5 days	0d	Fri 11/7/25	Fri 11/7/25	0d	Thu 11/13/25	Thu 11/13/25	0d
44	Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	13 days	0d	Fri 11/14/25	Fri 11/14/25	0d	Thu 12/4/25	Thu 12/4/25	0d
45	DELAY - GIRR License Agreement Approval to Proceed	6 days	6 days	0d	Fri 12/5/25	Fri 12/5/25	0d	Fri 12/12/25	Fri 12/12/25	0d
46	DELAY - RFI #14 - GIRR Separation	4 days	4 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Thu 12/18/25	Thu 12/18/25	0d
47	Storm Drain Lines South	6 days	6 days	0d	Mon 12/22/25	Mon 12/22/25	0d	Tue 12/30/25	Tue 12/30/25	0d
48	Site - Water Line & Fire Lines/Hydrants and Devices Remaining	18 days	18 days	0d	Mon 1/5/26	Mon 1/5/26	0d	Wed 1/28/26	Wed 1/28/26	0d
49	Site - GIRR Piping & Devices	16 days	16 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/2/26	Mon 2/2/26	0d
50	TP DELAY - Site - GIRR Box Delivery and Placement	6 days	6 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Mon 2/2/26	Mon 2/2/26	0d
51	Complete UG Utility Lines, to Building A	1 day	1 day	0d	Fri 3/27/26	Fri 3/27/26	0d	Fri 3/27/26	Fri 3/27/26	0d
52	Gravel Road Rough Grade Prep	8 days	8 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Wed 12/17/25	Wed 12/17/25	0d
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**74 days**	**74 days**	**0d**	**Tue 2/3/26**	**Tue 2/3/26**	**0d**	**Fri 5/15/26**	**Fri 5/15/26**	**0d**
54	FRAGNET - Site - Drive Aisle Over Ex Unsuitable Soil Identified	1 day	1 day	0d	Tue 2/3/26	Tue 2/3/26	0d	Tue 2/3/26	Tue 2/3/26	0d
55	FRAGNET - Site - Drive Aisle Over Ex Discussion and Confirmation on Solution	2 days	2 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/5/26	Thu 2/5/26	0d
56	FRAGNET - Site - Idaho Power - Pivot to Moblize and Peform the UG JT in Drive Ais	15 days	15 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/26/26	Thu 2/26/26	0d
57	FRAGNET - Site - Owner Review of Impact and Discussion with Geo Tech to Identif	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 2/25/26	Wed 2/25/26	0d
58	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
59	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
60	FRAGNET - Mobilize Crew, Rough Grade Prep, Scarify and Air Dry	2 days	2 days	0d	Fri 3/20/26	Fri 3/20/26	0d	Mon 3/23/26	Mon 3/23/26	0d

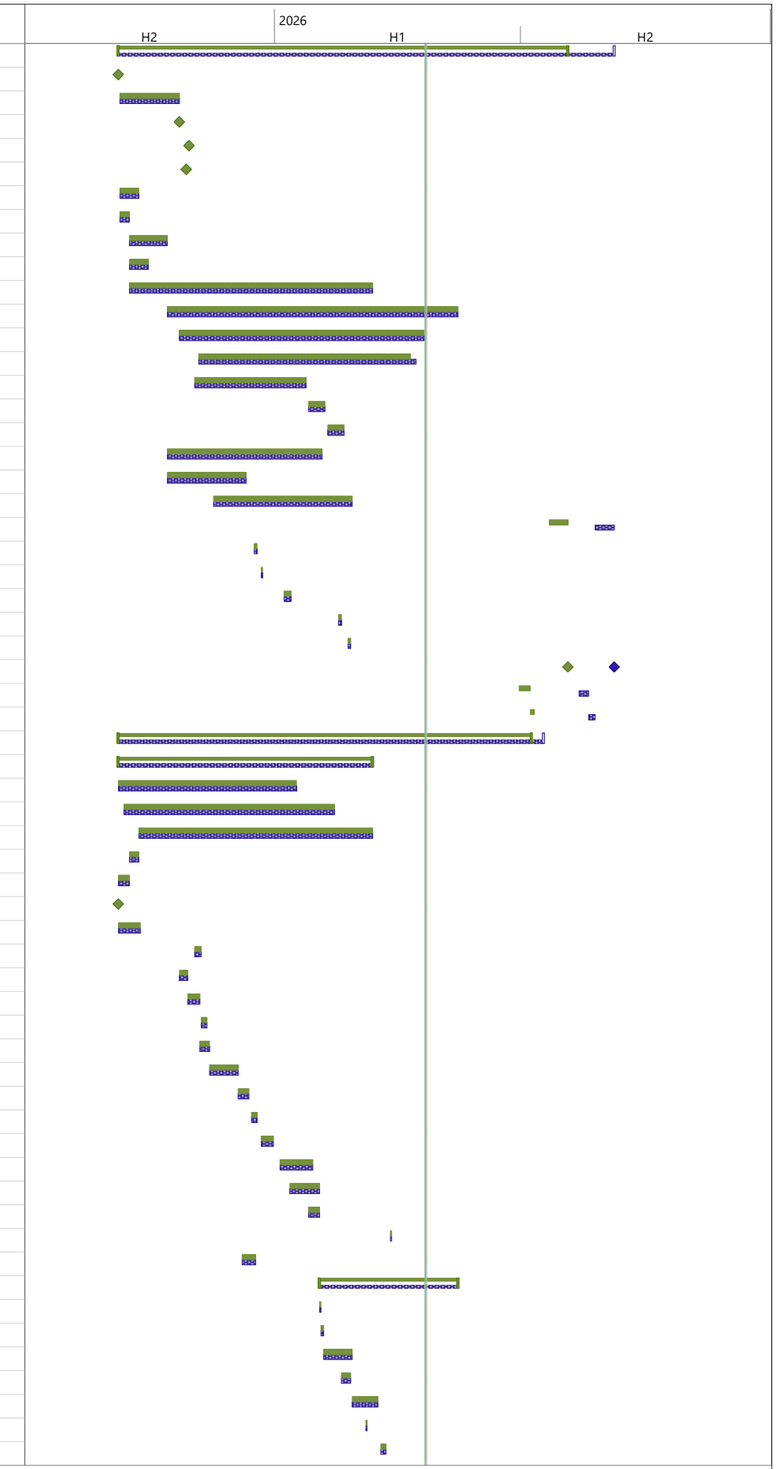

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
61	FRAGNET - Re-Prep, Proof Roll, Confirm Soft Spot Magnitude	1 day	1 day	0d	Mon 3/23/26	Mon 3/23/26	0d	Mon 3/23/26	Mon 3/23/26	0d
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If faile	3 days	3 days	0d	Tue 5/5/26	Tue 5/5/26	0d	Thu 5/7/26	Thu 5/7/26	0d
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	1 day	1 day	0d	Fri 5/8/26	Fri 5/8/26	0d	Fri 5/8/26	Fri 5/8/26	0d
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	5 days	5 days	0d	Mon 5/11/26	Mon 5/11/26	0d	Fri 5/15/26	Fri 5/15/26	0d
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	5 days	5 days	0d	Mon 5/11/26	Mon 5/11/26	0d	Fri 5/15/26	Fri 5/15/26	0d
66	Site - Idaho Power Boring	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Fri 2/27/26	Fri 2/27/26	0d
67	Site - Idaho Power Trench, Conduit and Backfill	5 days	5 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Fri 3/13/26	Fri 3/13/26	0d
68	Site - Idaho Power Transformer Set and Make Live	0 days	0 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Fri 3/13/26	Fri 3/13/26	0d
69	Storm Drain Lines and Devices - South of Buildings (E-W)	7 days	7 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Thu 4/23/26	Thu 4/23/26	0d
70	Site - Flatwork Sidewalk Prep		8 days			Wed 4/15/26			Fri 4/24/26	
71	Site - Flatwork Sidewalk Prep (E-W)	8 days			Wed 4/15/26			Fri 4/24/26		
72	Storm Drain Lines and Devices - North of Buildings (E-W)	7 days	7 days	0d	Fri 4/24/26	Fri 4/24/26	0d	Mon 5/4/26	Mon 5/4/26	0d
73	Site Concrete Flatwork and Curb and Gutter - (E-W) at Buildings	15 days	15 days	0d	Mon 4/27/26	Fri 5/29/26	-24d	Fri 5/15/26	Thu 6/18/26	-24d
74	Site - Base Course Asphalt Prep	8 days	8 days	0d	Mon 5/18/26	Mon 5/18/26	0d	Thu 5/28/26	Thu 5/28/26	0d
75	Site - Curb and Gutter Prep	8 days	8 days	0d	Fri 5/29/26	Mon 5/18/26	9d	Tue 6/9/26	Thu 5/28/26	8d
76	Site - Fine Grade Asphalt Prep	3 days	3 days	0d	Wed 6/10/26	Fri 6/19/26	-7d	Fri 6/12/26	Tue 6/23/26	-7d
77	Asphalt Paving	2 days	2 days	0d	Mon 6/15/26	Wed 6/24/26	-7d	Tue 6/16/26	Thu 6/25/26	-7d
78	Pavement Markings, Signage & Bumpers	2 days	2 days	0d	Wed 6/17/26	Fri 6/26/26	-7d	Thu 6/18/26	Mon 6/29/26	-7d
79	Site Fencing Chainlink	5 days	5 days	0d	Wed 5/20/26	Wed 5/20/26	0d	Wed 5/27/26	Wed 5/27/26	0d
80	Gravel Road Finish Grading	5 days	5 days	0d	Wed 6/10/26	Thu 5/28/26	9d	Tue 6/16/26	Wed 6/3/26	9d
81	Landscaping and Irrigation	15 days	15 days	0d	Wed 6/17/26	Fri 6/26/26	-7d	Wed 7/8/26	Fri 7/17/26	-7d
82	Site Fencing Vinyl	10 days	10 days	0d	Wed 6/17/26	Fri 6/26/26	-7d	Tue 6/30/26	Fri 7/10/26	-8d
83	Site Fencing Rod Iron and Gates	5 days	5 days	0d	Wed 6/17/26	Fri 6/26/26	-7d	Tue 6/23/26	Thu 7/2/26	-7d
84	**BUILDING B**	**162 days**	**191 days**	**-29d**	**Wed 10/29/25**	**Wed 10/29/25**	**0d**	**Thu 6/18/26**	**Thu 7/30/26**	**-30d**
85	BLDG B Foundation Excavation	6 days	6 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 11/5/25	Wed 11/5/25	0d
86	DELAY - BLDG B FOOTING OVER-EX	4 days	4 days	0d	Fri 10/31/25	Fri 10/31/25	0d	Wed 11/5/25	Wed 11/5/25	0d
87	BLDG B SOG Prep	5 days	5 days	0d	Wed 11/26/25	Wed 11/26/25	0d	Thu 12/4/25	Thu 12/4/25	0d
88	FRAGNET - Bldg B Soft Spot Repair	8 days	8 days	0d	Thu 12/4/25	Thu 12/4/25	0d	Mon 12/15/25	Mon 12/15/25	0d
89	BLDG B Backfill Foundations	18 days	18 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 1/9/26	Fri 1/9/26	0d
90	**CONCRETE WORK**	**44 days**	**44 days**	**0d**	**Thu 11/6/25**	**Thu 11/6/25**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**
91	BLDG B Foundation	14 days	14 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Tue 11/25/25	Tue 11/25/25	0d
92	BLDG B Dampproofing	1 day	1 day	0d	Tue 11/18/25	Tue 11/18/25	0d	Wed 11/26/25	Wed 11/26/25	0d
93	BLDG B Slab On Grade	19 days	19 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Mon 1/12/26	Mon 1/12/26	0d
94	BLDG B Slab On Grade Complete	0 days	0 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 1/12/26	Mon 1/12/26	0d
95	**STEEL AND METALS**	**76 days**	**76 days**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 4/27/26**	**Mon 4/27/26**	**0d**
96	Frame Load Bearing Shear Walls, Interior Partitions, & Corridors (JANUS)	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/9/26	Mon 2/9/26	0d
97	FRAGNET - Extended Shear Wall Durations (JANUS)	12 days	12 days	0d	Tue 2/10/26	Tue 2/10/26	0d	Wed 2/25/26	Wed 2/25/26	0d
98	Panel Shear Walls, Interior Partition, & Corridor Walls (JANUS)	20 days	20 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Wed 3/25/26	Wed 3/25/26	0d
99	Perimeter Panel Interior Walls (JANUS)	20 days	20 days	0d	Tue 3/31/26	Tue 3/31/26	0d	Mon 4/27/26	Mon 4/27/26	0d
100	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Thu 4/9/26**	**Thu 4/9/26**	**0d**	**Wed 4/15/26**	**Wed 4/15/26**	**0d**
101	Misc Finish Carpentry	5 days	5 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/15/26	Wed 4/15/26	0d
102	**ROOF & SIDING**	**78 days**	**78 days**	**0d**	**Fri 1/30/26**	**Fri 1/30/26**	**0d**	**Tue 5/19/26**	**Tue 5/19/26**	**0d**
103	Exterior Sheathing	0 days	0 days	0d	Fri 1/30/26	Fri 1/30/26	0d	Mon 2/16/26	Mon 2/16/26	0d
104	Weather Barrier Fluid Applied	8 days	8 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/19/26	Thu 2/19/26	0d
105	Weather Barrier Tyvek	10 days	10 days	0d	Wed 3/4/26	Wed 3/4/26	0d	Tue 3/17/26	Tue 3/17/26	0d
106	CMU Veneer Base Course & Grout	15 days	15 days	0d	Tue 3/3/26	Tue 3/3/26	0d	Tue 4/7/26	Tue 4/7/26	0d
107	Rigid Insulation Behind CMU	5 days	5 days	0d	Wed 4/8/26	Wed 4/8/26	0d	Tue 4/14/26	Tue 4/14/26	0d
108	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Fri 4/17/26	Fri 4/17/26	0d
109	CMU Veneer Remaining	15 days	15 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Tue 5/5/26	Tue 5/5/26	0d
110	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Wed 5/6/26	Wed 5/6/26	0d	Tue 5/19/26	Tue 5/19/26	0d
111	Install Roof & Roof Insulation (JANUS)	12 days	12 days	0d	Wed 2/25/26	Wed 2/25/26	0d	Wed 3/25/26	Wed 3/25/26	0d
112	BLDG B Roofing Complete	0 days	0 days	0d	Wed 3/25/26	Wed 3/25/26	0d	Wed 3/25/26	Wed 3/25/26	0d
113	**DOORS & WINDOWS**	**41 days**	**20 days**	**21d**	**Mon 4/13/26**	**Thu 7/2/26**	**-58d**	**Tue 6/9/26**	**Thu 7/30/26**	**-37d**
114	F&I HM Doors and Hardware (JANUS)	5 days	15 days	-10d	Mon 4/13/26	Thu 7/2/26	-58d	Fri 4/17/26	Thu 7/23/26	-69d
115	F&I Storage Unit Doors (JANUS)	30 days	20 days	10d	Tue 4/28/26	Thu 7/2/26	-47d	Tue 6/9/26	Thu 7/30/26	-37d
116	Install Security Mesh (JANUS)	10 days			Mon 5/18/26			Mon 6/1/26		
117	**FINISHES**	**30 days**	**30 days**	**0d**	**Thu 3/26/26**	**Thu 3/26/26**	**0d**	**Wed 5/6/26**	**Wed 5/6/26**	**0d**
118	Install Gypsum Board	10 days	10 days	0d	Thu 3/26/26	Thu 3/26/26	0d	Wed 4/8/26	Wed 4/8/26	0d
119	Flooring Polished Concrete	5 days	5 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/15/26	Wed 4/15/26	0d
120	FRP / Vinyl Base	5 days	5 days	0d	Thu 4/16/26	Thu 4/16/26	0d	Wed 4/22/26	Wed 4/22/26	0d

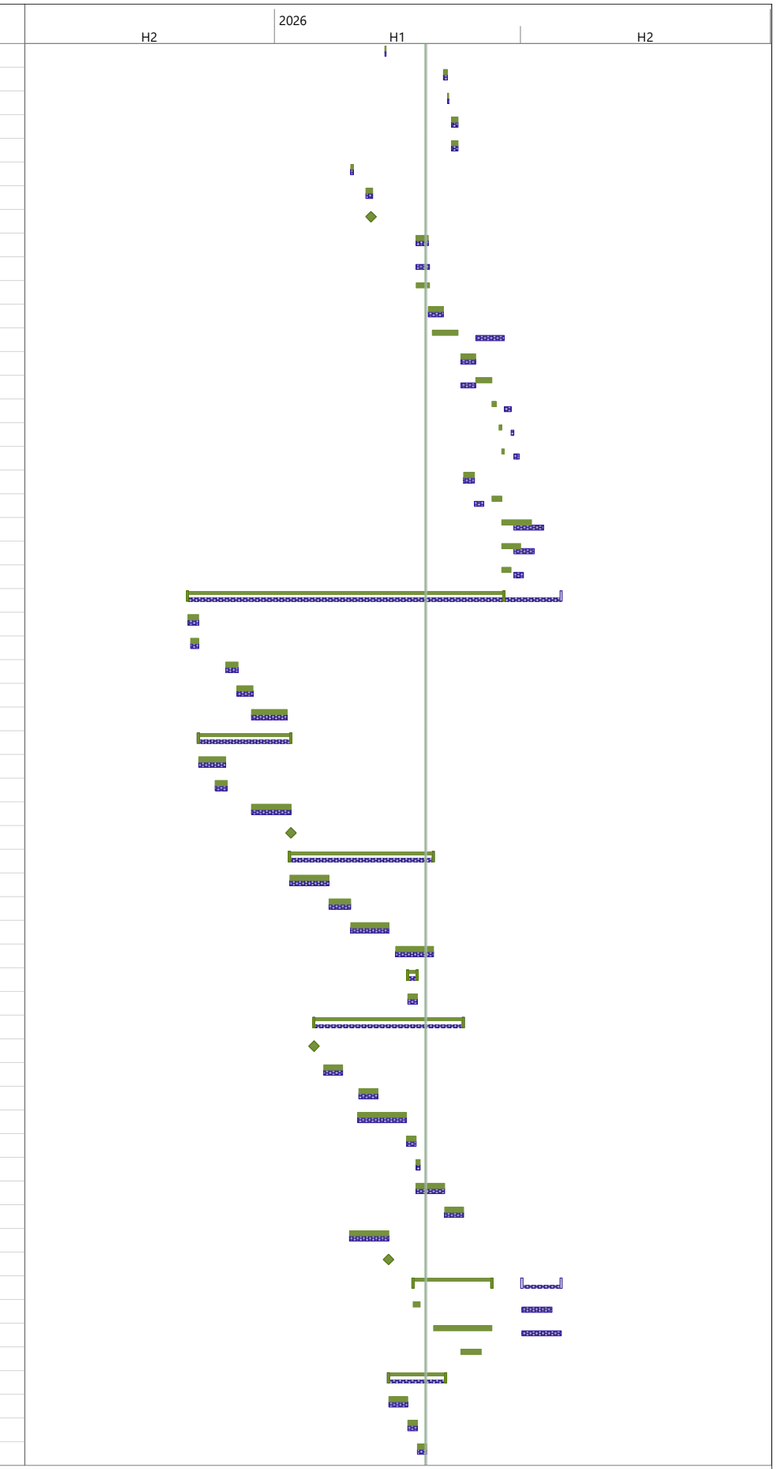

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
121	Painting	10 days	10 days	0d	Thu 4/23/26	Thu 4/23/26	0d	Wed 5/6/26	Wed 5/6/26	0d
122	**SPECIALTIES**	**23 days**	**23 days**	**0d**	**Thu 4/9/26**	**Thu 4/9/26**	**0d**	**Mon 5/11/26**	**Mon 5/11/26**	**0d**
123	Install Misc Equipment & Lockers	20 days	20 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 5/6/26	Wed 5/6/26	0d
124	Bathroom Accessories	2 days	2 days	0d	Thu 4/16/26	Thu 4/16/26	0d	Fri 4/17/26	Fri 4/17/26	0d
125	Building Interior Signage	3 days	3 days	0d	Thu 5/7/26	Thu 5/7/26	0d	Mon 5/11/26	Mon 5/11/26	0d
126	**FIRE SPRINKLERS**	**36.25 days**	**36.25 days**	**0d**	**Mon 2/23/26**	**Mon 2/23/26**	**0d**	**Tue 4/14/26**	**Tue 4/14/26**	**0d**
127	Fire Sprinkler System Rough In	18 days	18 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 3/27/26	Fri 3/27/26	0d
128	Fire Sprinkler System Trim Out	15 days	15 days	0d	Mon 3/2/26	Mon 3/2/26	0d	Tue 4/14/26	Tue 4/14/26	0d
129	**PLUMBING**	**104 days**	**104 days**	**0d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Mon 4/20/26**	**Mon 4/20/26**	**0d**
130	Plumbing Rough-in Underground	4 days	4 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
131	Drains, Water, Sewer Lines	15 days	15 days	0d	Thu 3/26/26	Thu 3/26/26	0d	Wed 4/15/26	Wed 4/15/26	0d
132	Bathroom Fixtures	3 days	3 days	0d	Thu 4/16/26	Thu 4/16/26	0d	Mon 4/20/26	Mon 4/20/26	0d
133	Other Plumbing Fixtures	3 days	3 days	0d	Thu 4/16/26	Thu 4/16/26	0d	Mon 4/20/26	Mon 4/20/26	0d
134	**HVAC**	**63 days**	**94 days**	**-31d**	**Mon 3/16/26**	**Mon 3/16/26**	**0d**	**Thu 6/11/26**	**Mon 7/27/26**	**-32d**
135	HVAC Installation - Start/Partial	4 days	4 days	0d	Mon 3/23/26	Mon 3/23/26	0d	Tue 3/31/26	Tue 3/31/26	0d
136	**FRAGNET - RFI 38 Condenser Unit Relocations**	**55 days**	**63 days**	**-8d**	**Mon 3/23/26**	**Mon 3/23/26**	**0d**	**Mon 6/8/26**	**Thu 6/18/26**	**-8d**
137	FRAGNET - RFI 38 Submitted, Reviewed, Responded, Confirmed Direction for Co	10 days	10 days	0d	Mon 3/23/26	Mon 3/23/26	0d	Wed 4/8/26	Wed 4/8/26	0d
138	FRAGNET - RFI 38 - Cost Impact, Collect, Submit, Confirm CO	2 days	10 days	-8d	Thu 4/9/26	Thu 4/9/26	0d	Fri 4/10/26	Wed 4/22/26	-8d
139	FRAGNET - RFI 38 - Procurement, Re-Route Electrical	8 days	15 days	-7d	Mon 4/13/26	Thu 4/23/26	-8d	Wed 4/22/26	Wed 5/13/26	-15d
140	TBD FRAGNET - RFI 38 - HVAC Set Units, Duct Procurement & Install	0 days	40 days	-40d	Thu 4/9/26	Thu 4/23/26	-10d	Thu 4/9/26	Thu 6/18/26	-51d
141	TBD FRAGNET - RFI 38 - Screen Wall Procurement and Install	40 days	40 days	0d	Mon 4/13/26	Thu 4/23/26	-8d	Mon 6/8/26	Thu 6/18/26	-8d
142	**FRAGNET - RFI 37 - Duct Conflicts**	**29 days**	**57 days**	**-28d**	**Mon 3/16/26**	**Mon 3/16/26**	**0d**	**Thu 4/23/26**	**Wed 6/3/26**	**-29d**
143	RFI 37 - Initiated and Responded	8 days	8 days	0d	Mon 3/16/26	Mon 3/16/26	0d	Wed 3/25/26	Wed 3/25/26	0d
144	RFI 37 - Further Clarification Required, Caught Design Decrepency	2 days	2 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Thu 4/2/26	Thu 4/2/26	0d
145	RFI 37 - Review and Responsed, Close as Directed	5 days	3 days	2d	Fri 4/3/26	Fri 4/3/26	0d	Thu 4/9/26	Tue 4/7/26	2d
146	TBD RFI 37 - Cost Impact Collection and Submission	10 days	10 days	0d	Fri 4/10/26	Wed 4/8/26	2d	Thu 4/23/26	Tue 4/21/26	2d
147	TBD RFI 37 - Procure Remaining Duct Materials	5 days	30 days	-25d	Fri 4/10/26	Wed 4/22/26	-8d	Thu 4/16/26	Wed 6/3/26	-34d
148	HVAC Installation - Remaining	21 days	21 days	0d	Fri 4/17/26	Fri 6/19/26	-45d	Fri 5/15/26	Mon 7/20/26	-46d
149	HVAC Commisioning & T&B	5 days	5 days	0d	Fri 6/5/26	Tue 7/21/26	-32d	Thu 6/11/26	Mon 7/27/26	-32d
150	**ELECTRICAL**	**146 days**	**175 days**	**-29d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Thu 6/18/26**	**Thu 7/30/26**	**-30d**
151	Building Rough-in Underground	0 days	0 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
152	Elect Rough-In Start/Partial	19 days	19 days	0d	Mon 3/2/26	Mon 3/2/26	0d	Mon 3/30/26	Mon 3/30/26	0d
153	Install, Wire & Inspect - Start/Partial	5 days	5 days	0d	Wed 3/25/26	Wed 3/25/26	0d	Wed 4/1/26	Wed 4/1/26	0d
154	Install Wire & Inspect - Remaining	5 days	5 days	0d	Thu 4/23/26	Thu 5/14/26	-15d	Wed 4/29/26	Wed 5/20/26	-15d
155	Install and Wire Panels	3 days	3 days	0d	Thu 4/30/26	Fri 6/19/26	-36d	Mon 5/4/26	Tue 6/23/26	-36d
156	Permanent Power On	0 days	0 days	0d	Thu 6/4/26	Tue 6/23/26	-13d	Thu 6/4/26	Tue 6/23/26	-13d
157	FRAGNET - RFI 35 - Light Fixture Mounting Height Clarification Submitted/Closed,	3 days	3 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Tue 3/17/26	Tue 3/17/26	0d
158	Electric Lights, Devices and Trim	55 days	55 days	0d	Wed 3/25/26	Wed 3/25/26	0d	Thu 6/11/26	Thu 6/11/26	0d
159	Fire Alarm System	3 days	3 days	0d	Mon 5/18/26	Tue 7/21/26	-46d	Wed 5/20/26	Thu 7/23/26	-46d
160	Electrical Commissioning	5 days	5 days	0d	Fri 6/12/26	Fri 7/24/26	-30d	Thu 6/18/26	Thu 7/30/26	-30d
161	**BUILDING A**	**125 days**	**141 days**	**-16d**	**Mon 1/26/26**	**Mon 1/26/26**	**0d**	**Tue 7/21/26**	**Wed 8/12/26**	**-16d**
162	BLDG A Foundation Excavation	24 days	24 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
163	FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day	1 day	0d	Mon 2/2/26	Mon 2/2/26	0d	Mon 2/2/26	Mon 2/2/26	0d
164	BLDG A - Interoir Backfill Foundations	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Tue 3/3/26	Tue 3/3/26	0d
165	**FRAGNET - BLDG A Seepage Bed Pad Over Ex.**	**11 days**	**11 days**	**0d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Thu 3/12/26**	**Thu 3/12/26**	**0d**
166	FRAGNET -Proposed direction received from Owner to perform BLDG A Seepage B	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
167	FRAGNET - Prepare and Submit Pricing for Approval	8 days	8 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/10/26	Tue 3/10/26	0d
168	FRAGNET - Owner Issued CCD 06 on Seepage Bed Cost Impact	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
169	FRAGNET - Mobilize Crew for BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Tue 3/10/26	Tue 3/10/26	0d	Tue 3/10/26	Tue 3/10/26	0d
170	FRAGNET - Start BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Wed 3/11/26	Wed 3/11/26	0d	Wed 3/11/26	Wed 3/11/26	0d
171	FRAGNET - Finish BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Thu 3/12/26	Thu 3/12/26	0d	Thu 3/12/26	Thu 3/12/26	0d
172	BLDG A - Exterior Backfill Foundations	2 days	2 days	0d	Tue 3/10/26	Tue 3/10/26	0d	Wed 3/11/26	Wed 3/11/26	0d
173	BLDG A SOG Rough Grade Prep	2 days	2 days	0d	Wed 3/18/26	Wed 3/18/26	0d	Thu 3/19/26	Thu 3/19/26	0d
174	**FRAGNET - BLDG A Soft Spot Over Ex**	**20 days**	**20 days**	**0d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Wed 3/25/26**	**Wed 3/25/26**	**0d**
175	FRAGNET - Proposed direction received from Owner to perform BLDG A Soft Spot	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
176	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
177	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
178	FRAGNET - Mobilize Crew, SOG Rough Grade Prep, Scarify, Air Dry Pad A	5 days	5 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Thu 3/19/26	Thu 3/19/26	0d
179	FRAGNET - Air Dry Pad A, Re-Prep, Proof Roll to Idendify Soft Spots	2 days	2 days	0d	Fri 3/20/26	Fri 3/20/26	0d	Mon 3/23/26	Mon 3/23/26	0d
180	FRAGNET - Start Soft Spot Repairs	0 days	0 days	0d	Mon 3/23/26	Mon 3/23/26	0d	Mon 3/23/26	Mon 3/23/26	0d

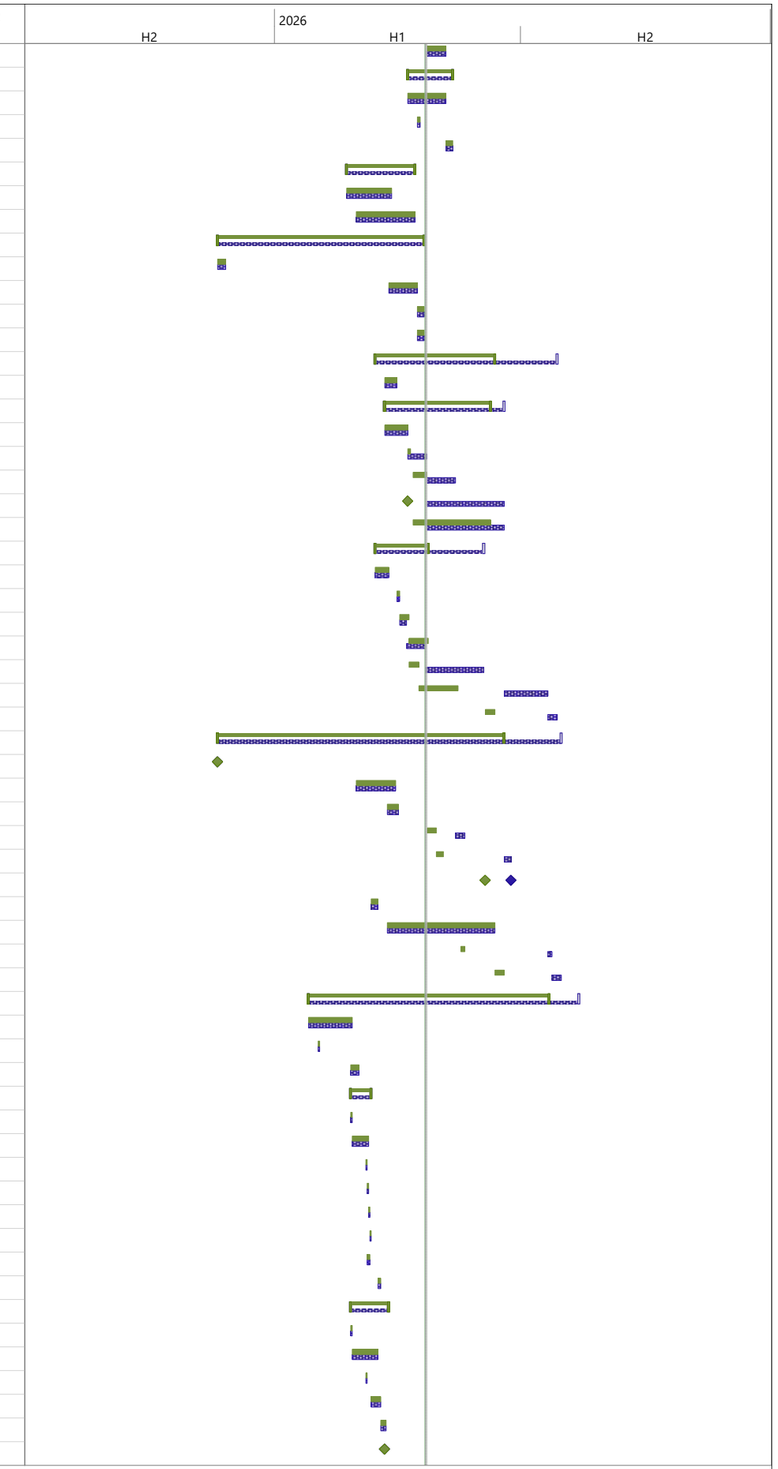
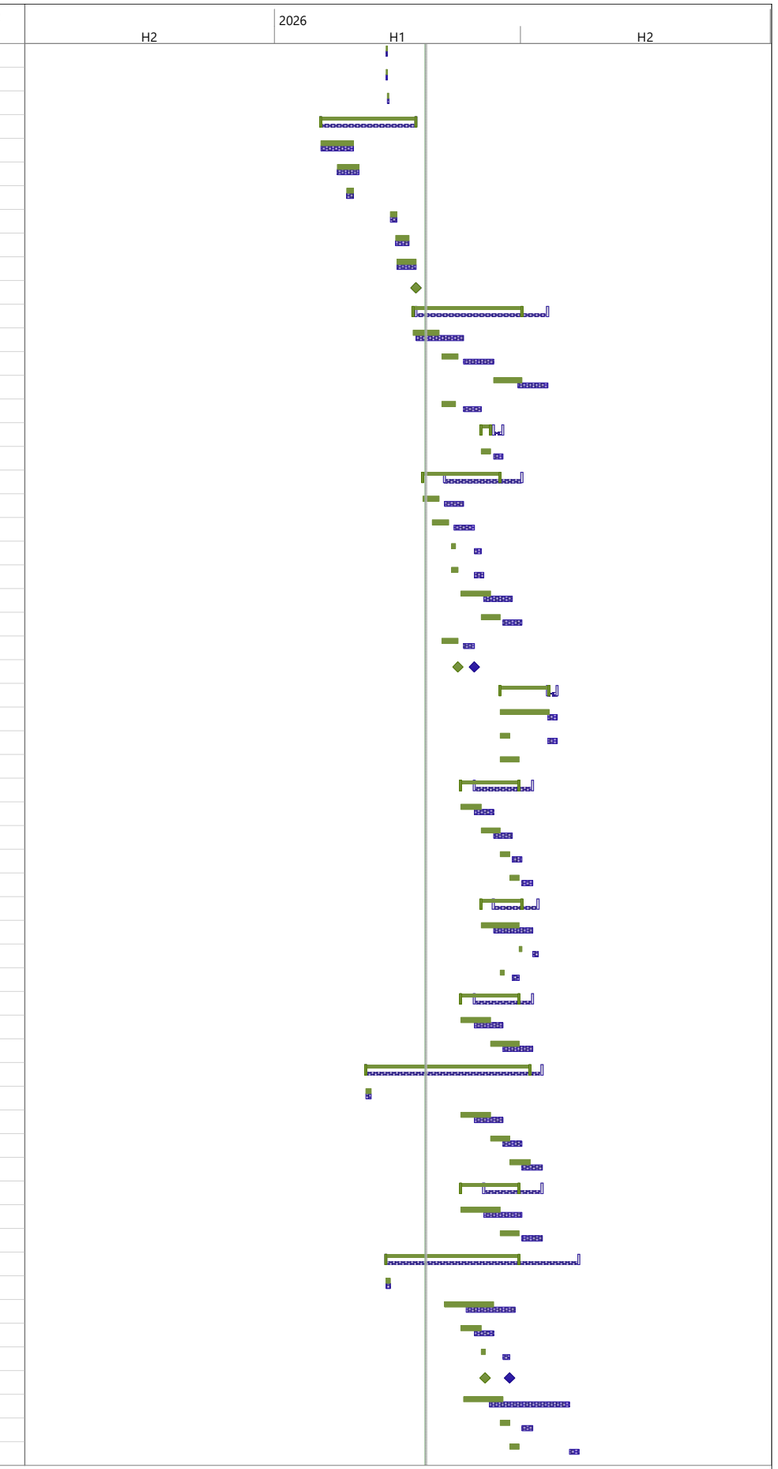
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
181	FRAGNET - Test and Review Compaction Results for Soft Spot - If Approved, Proce	1 day	1 day	0d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/24/26	Tue 3/24/26	0d
182	FRAGNET - Soft Spot Repairs East Area	1 day	1 day	0d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/24/26	Tue 3/24/26	0d
183	FRAGNET - Soft Spot Repairs West Area	1 day	1 day	0d	Wed 3/25/26	Wed 3/25/26	0d	Wed 3/25/26	Wed 3/25/26	0d
184	**CONCRETE WORK**	**50 days**	**50 days**	**0d**	**Wed 2/4/26**	**Wed 2/4/26**	**0d**	**Tue 4/14/26**	**Tue 4/14/26**	**0d**
185	BLDG A Foundation	18 days	18 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Fri 2/27/26	Fri 2/27/26	0d
186	BLDG A Dampproofing	4 days	4 days	0d	Mon 2/16/26	Mon 2/16/26	0d	Tue 3/3/26	Tue 3/3/26	0d
187	BLDG A Exterior Footing Insulation	5 days	5 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 2/27/26	Fri 2/27/26	0d
188	BLDG A SOG Fine Prep	3 days	3 days	0d	Fri 3/27/26	Fri 3/27/26	0d	Tue 3/31/26	Tue 3/31/26	0d
189	BLDG A Slab On Grade (East)	7 days	7 days	0d	Tue 3/31/26	Tue 3/31/26	0d	Thu 4/9/26	Thu 4/9/26	0d
190	BLDG A Slab On Grade (West)	10 days	10 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Tue 4/14/26	Tue 4/14/26	0d
191	BLDG A Slab On Grade Complete	0 days	0 days	0d	Tue 4/14/26	Tue 4/14/26	0d	Tue 4/14/26	Tue 4/14/26	0d
192	**STEEL AND METALS**	**57 days**	**67 days**	**-10d**	**Mon 4/13/26**	**Wed 4/15/26**	**-2d**	**Wed 7/1/26**	**Mon 7/20/26**	**-13d**
193	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	15 days	25 days	-10d	Mon 4/13/26	Wed 4/15/26	-2d	Fri 5/1/26	Tue 5/19/26	-12d
194	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	10 days	15 days	-5d	Mon 5/4/26	Wed 5/20/26	-12d	Fri 5/15/26	Wed 6/10/26	-18d
195	Perimeter Panel Interior Walls (JANUS)	15 days	15 days	0d	Thu 6/11/26	Mon 6/29/26	-12d	Wed 7/1/26	Mon 7/20/26	-13d
196	Canopy Install	8 days	8 days	0d	Mon 5/4/26	Wed 5/20/26	-12d	Wed 5/13/26	Mon 6/1/26	-13d
197	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Tue 6/2/26**	**Thu 6/11/26**	**-7d**	**Mon 6/8/26**	**Wed 6/17/26**	**-7d**
198	Misc Finish Carpentry	5 days	5 days	0d	Tue 6/2/26	Thu 6/11/26	-7d	Mon 6/8/26	Wed 6/17/26	-7d
199	**ROOF & SIDING**	**40 days**	**40 days**	**0d**	**Mon 4/20/26**	**Wed 5/6/26**	**-12d**	**Mon 6/15/26**	**Wed 7/1/26**	**-12d**
200	Exterior Sheathing	10 days	10 days	0d	Mon 4/20/26	Wed 5/6/26	-12d	Fri 5/1/26	Tue 5/19/26	-12d
201	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	10 days	10 days	0d	Mon 4/27/26	Wed 5/13/26	-12d	Fri 5/8/26	Wed 5/27/26	-13d
202	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Mon 5/11/26	Thu 5/28/26	-13d	Wed 5/13/26	Mon 6/1/26	-13d
203	Rigid Insulation Behind CMU	5 days	5 days	0d	Mon 5/11/26	Thu 5/28/26	-13d	Fri 5/15/26	Wed 6/3/26	-13d
204	CMU Veneer	15 days	15 days	0d	Mon 5/18/26	Thu 6/4/26	-13d	Mon 6/8/26	Wed 6/24/26	-12d
205	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Tue 6/2/26	Thu 6/18/26	-12d	Mon 6/15/26	Wed 7/1/26	-12d
206	Install Roof & Roof Insulation (JANUS)	10 days	5 days	5d	Mon 5/4/26	Wed 5/20/26	-12d	Fri 5/15/26	Wed 5/27/26	-8d
207	BLDG A Roofing Complete	0 days	0 days	0d	Fri 5/15/26	Wed 5/27/26	-8d	Fri 5/15/26	Wed 5/27/26	-8d
208	**DOORS & WINDOWS**	**25 days**	**5 days**	**20d**	**Tue 6/16/26**	**Tue 7/21/26**	**-25d**	**Tue 7/21/26**	**Mon 7/27/26**	**-4d**
209	F&I Storage Unit Doors (JANUS)	25 days	5 days	20d	Tue 6/16/26	Tue 7/21/26	-25d	Tue 7/21/26	Mon 7/27/26	-4d
210	F&I HM Doors and Hardware (JANUS)	5 days	5 days	0d	Tue 6/16/26	Tue 7/21/26	-25d	Mon 6/22/26	Mon 7/27/26	-25d
211	Install Security Mesh (JANUS)	10 days			Tue 6/16/26			Mon 6/29/26		
212	**FINISHES**	**30 days**	**30 days**	**0d**	**Mon 5/18/26**	**Thu 5/28/26**	**-8d**	**Mon 6/29/26**	**Thu 7/9/26**	**-8d**
213	Install Gypsum Board	10 days	10 days	0d	Mon 5/18/26	Thu 5/28/26	-8d	Mon 6/1/26	Wed 6/10/26	-7d
214	Painting	10 days	10 days	0d	Tue 6/2/26	Thu 6/11/26	-7d	Mon 6/15/26	Wed 6/24/26	-7d
215	Flooring Polished Conc.	5 days	5 days	0d	Tue 6/16/26	Thu 6/25/26	-7d	Mon 6/22/26	Wed 7/1/26	-7d
216	FRP & Vinyl Base	5 days	5 days	0d	Tue 6/23/26	Thu 7/2/26	-7d	Mon 6/29/26	Thu 7/9/26	-8d
217	**SPECIALTIES**	**22 days**	**22 days**	**0d**	**Tue 6/2/26**	**Thu 6/11/26**	**-7d**	**Wed 7/1/26**	**Mon 7/13/26**	**-8d**
218	Install Misc Equipment & Lockers	20 days	20 days	0d	Tue 6/2/26	Thu 6/11/26	-7d	Mon 6/29/26	Thu 7/9/26	-8d
219	Bathroom Accessories- Building A	2 days	2 days	0d	Tue 6/30/26	Fri 7/10/26	-8d	Wed 7/1/26	Mon 7/13/26	-8d
220	Building Interior Signage	3 days	3 days	0d	Tue 6/16/26	Thu 6/25/26	-7d	Thu 6/18/26	Mon 6/29/26	-7d
221	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**	**Mon 5/18/26**	**Thu 5/28/26**	**-8d**	**Mon 6/29/26**	**Thu 7/9/26**	**-8d**
222	Fire Sprinkler System Rough In	15 days	15 days	0d	Mon 5/18/26	Thu 5/28/26	-8d	Mon 6/8/26	Wed 6/17/26	-7d
223	Fire Sprinkler System Trim Out	15 days	15 days	0d	Tue 6/9/26	Thu 6/18/26	-7d	Mon 6/29/26	Thu 7/9/26	-8d
224	**PLUMBING**	**85 days**	**92 days**	**-7d**	**Mon 3/9/26**	**Mon 3/9/26**	**0d**	**Tue 7/7/26**	**Thu 7/16/26**	**-7d**
225	Plumbing Rough-in Underground	4 days	4 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Thu 3/12/26	Thu 3/12/26	0d
226	Drains, Water, Sewer Lines	15 days	15 days	0d	Mon 5/18/26	Thu 5/28/26	-8d	Mon 6/8/26	Wed 6/17/26	-7d
227	Bathroom Fixtures- Building A	10 days	10 days	0d	Tue 6/9/26	Thu 6/18/26	-7d	Mon 6/22/26	Wed 7/1/26	-7d
228	Other Plumbing Fixtures	10 days	10 days	0d	Tue 6/23/26	Thu 7/2/26	-7d	Tue 7/7/26	Thu 7/16/26	-7d
229	**HVAC**	**30 days**	**30 days**	**0d**	**Mon 5/18/26**	**Thu 6/4/26**	**-13d**	**Mon 6/29/26**	**Thu 7/16/26**	**-13d**
230	HVAC Installation	20 days	20 days	0d	Mon 5/18/26	Thu 6/4/26	-13d	Mon 6/15/26	Wed 7/1/26	-12d
231	HVAC Commisioning - Building A	10 days	10 days	0d	Tue 6/16/26	Thu 7/2/26	-12d	Mon 6/29/26	Thu 7/16/26	-13d
232	**ELECTRICAL**	**69 days**	**100 days**	**-31d**	**Tue 3/24/26**	**Tue 3/24/26**	**0d**	**Mon 6/29/26**	**Wed 8/12/26**	**-32d**
233	Building Rough-in Underground	3 days	3 days	0d	Tue 3/24/26	Tue 3/24/26	0d	Thu 3/26/26	Thu 3/26/26	0d
234	Electrical Rough-In	25 days	25 days	0d	Wed 5/6/26	Fri 5/22/26	-12d	Wed 6/10/26	Fri 6/26/26	-12d
235	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Mon 5/18/26	Thu 5/28/26	-8d	Mon 6/1/26	Wed 6/10/26	-7d
236	Install and Wire Panels	3 days	3 days	0d	Tue 6/2/26	Thu 6/18/26	-12d	Thu 6/4/26	Mon 6/22/26	-12d
237	Permanent Power On- Building A	0 days	0 days	0d	Thu 6/4/26	Mon 6/22/26	-12d	Thu 6/4/26	Mon 6/22/26	-12d
238	Electric Lights, Devices and Trim	20 days	42 days	-22d	Wed 5/20/26	Mon 6/8/26	-13d	Wed 6/17/26	Wed 8/5/26	-35d
239	Fire Alarm System	5 days	5 days	0d	Tue 6/16/26	Thu 7/2/26	-12d	Mon 6/22/26	Thu 7/9/26	-13d
240	Electrical Commissioning	5 days	5 days	0d	Tue 6/23/26	Thu 8/6/26	-32d	Mon 6/29/26	Wed 8/12/26	-32d
