Aventura, FL

Compare Remaining Compression

Report Date: 03/25/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Aventura, FL - 01/16/2026 - BL01	**Aventura, FL - 03/25/2026 - UP01**
Data Date: 01/16/2026	Data Date: 03/25/2026
Finish Date: 06/19/2026	Finish Date: 07/10/2026

Remaining Work Compression 35 %

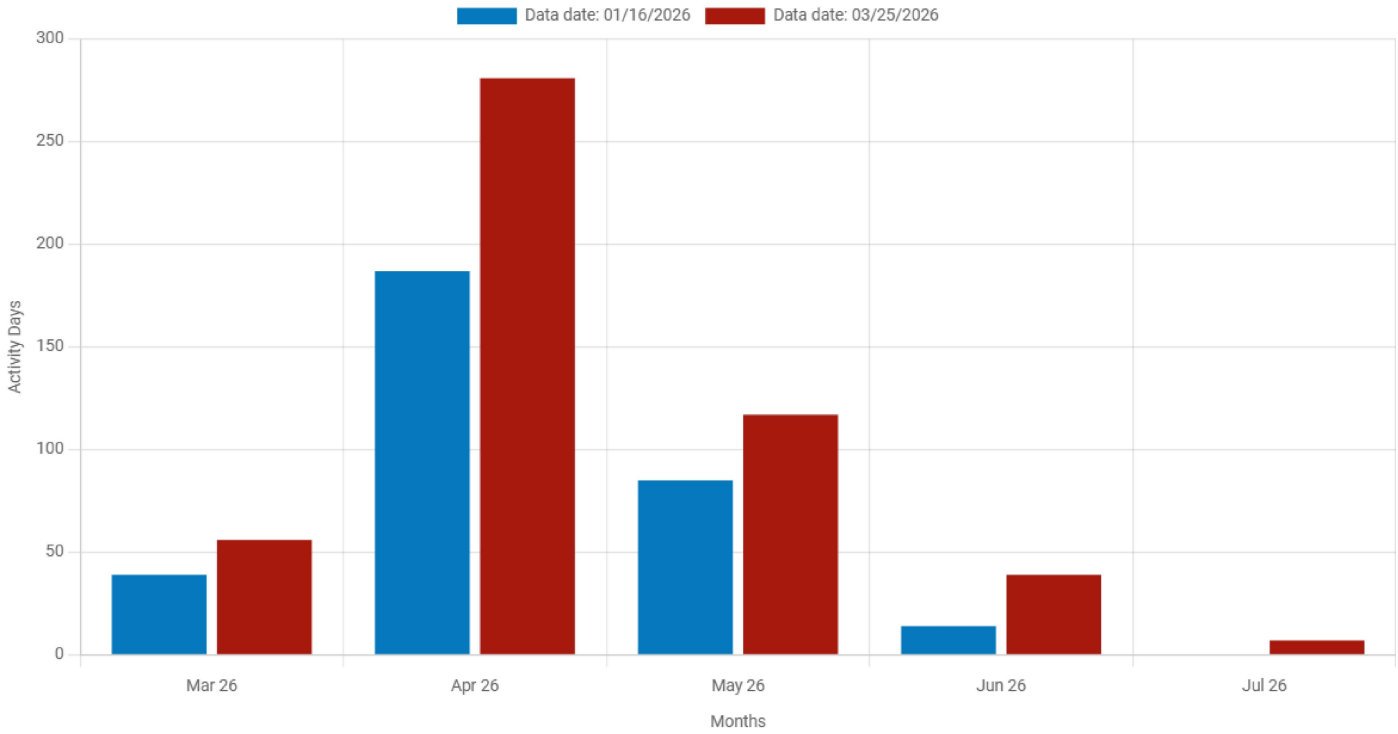

Month	01/16/2026 Activity Days	03/25/2026 Activity Days
Mar 26	39	56
Apr 26	187	281
May 26	85	117
Jun 26	14	39
Jul 26	0	7
