Delray, FL

Compare Remaining Compression

Report Date: 03/25/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Delray, FL - 01/19/2026 - BL01	**Delray, FL - 03/17/2026 - UP01**
Data Date: 01/19/2026	Data Date: 03/25/2026
Finish Date: 07/01/2026	Finish Date: 07/01/2026

Remaining Work Compression -5 %

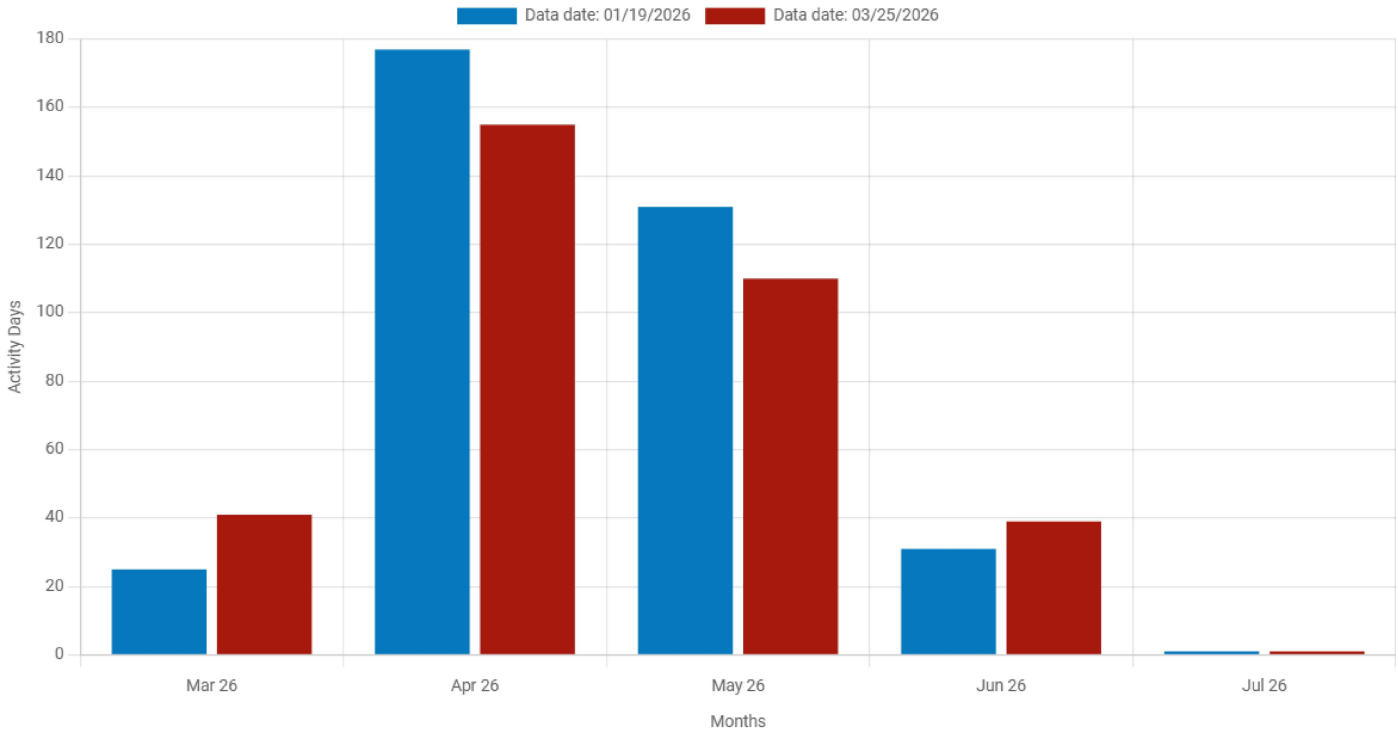

Month	01/19/2026 Activity Days	03/25/2026 Activity Days
Mar 26	25	41
Apr 26	177	155
May 26	131	110
Jun 26	31	39
Jul 26	1	1
