Fairfax, VA

Compare Remaining Compression

Report Date: 02/17/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Fairfax, VA - 12/31/2025	**Fairfax, VA - 01/31/2026**
Data Date: 12/31/2025	Data Date: 01/31/2026
Finish Date: 09/11/2026	Finish Date: 09/04/2026

Remaining Work Compression 11 %

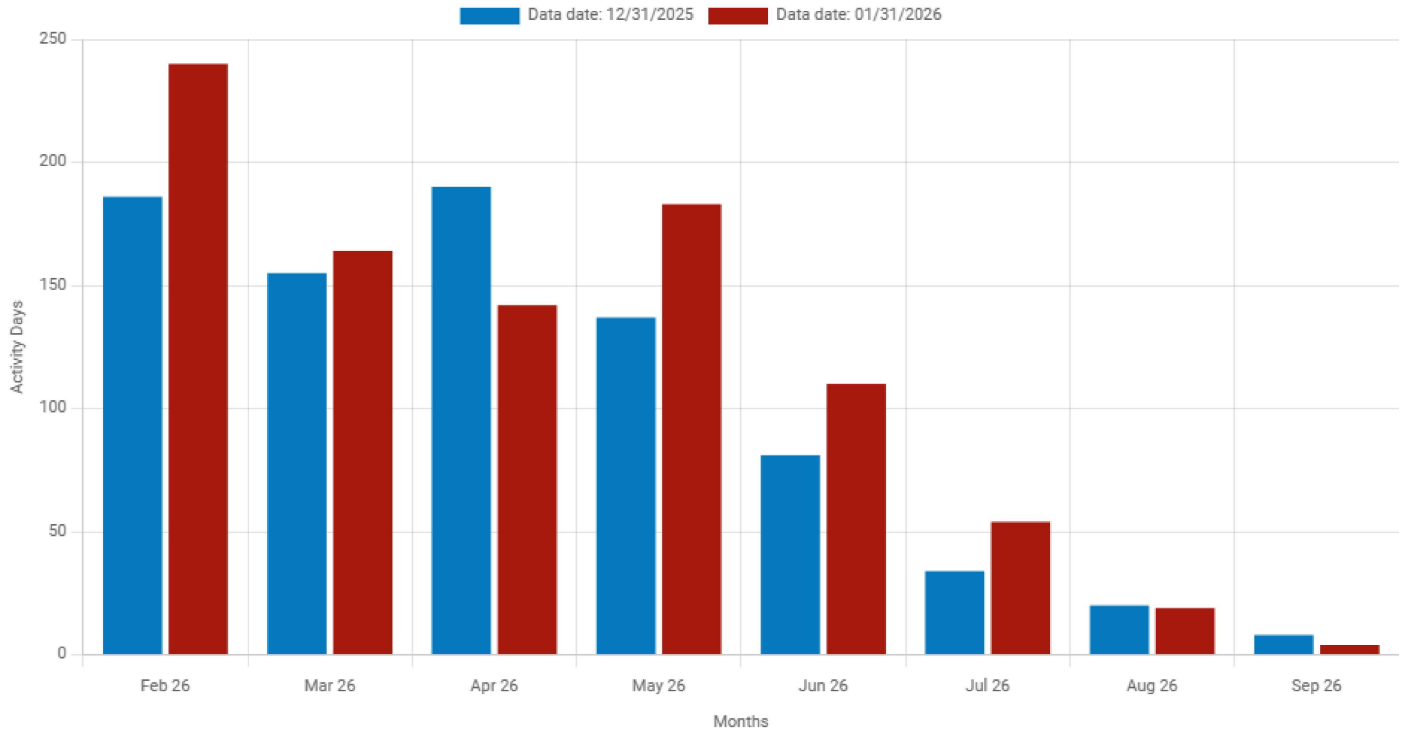

Month	12/31/2025 Activity Days	01/31/2026 Activity Days
Feb 26	186	240
Mar 26	155	164
Apr 26	190	142
May 26	137	183
Jun 26	81	110
Jul 26	34	54
Aug 26	20	19
Sep 26	8	4
