Frisco, TX

Compare Remaining Compression

Report Date: 02/19/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Frisco, TX - 02/03/2026	**Frisco, TX - 02/18/2026**
Data Date: 02/03/2026	Data Date: 02/18/2026
Finish Date: 06/02/2026	Finish Date: 06/04/2026

Remaining Work Compression 23 %

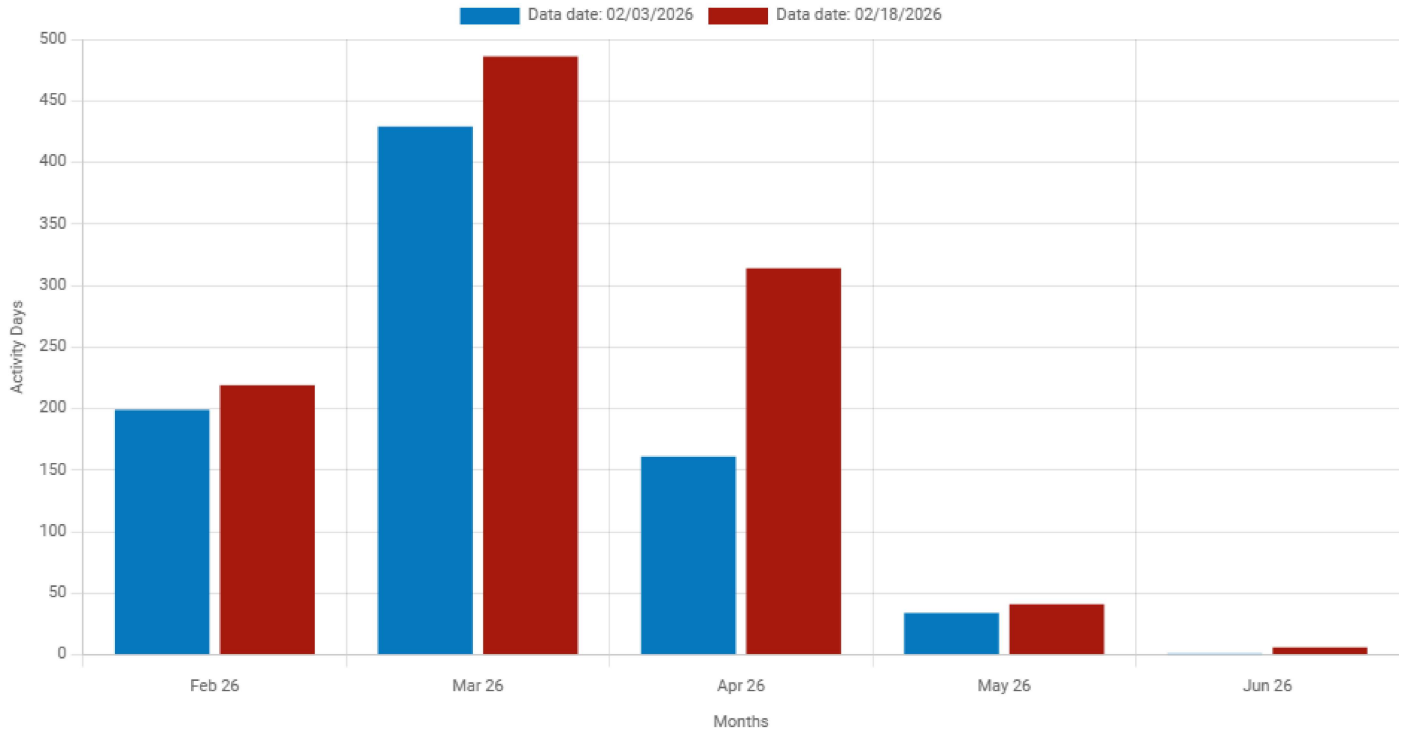

Month	02/03/2026 Activity Days	02/18/2026 Activity Days
Feb 26	199	219
Mar 26	429	486
Apr 26	161	314
May 26	34	41
Jun 26	1	6
