Frisco, TX

Compare Remaining Compression

Report Date: 03/06/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Frisco, TX - 02/18/2026	**Frisco,TX - 03/04/2026**
Data Date: 02/18/2026	Data Date: 03/04/2026
Finish Date: 06/04/2026	Finish Date: 06/04/2026

Remaining Work Compression 7 %

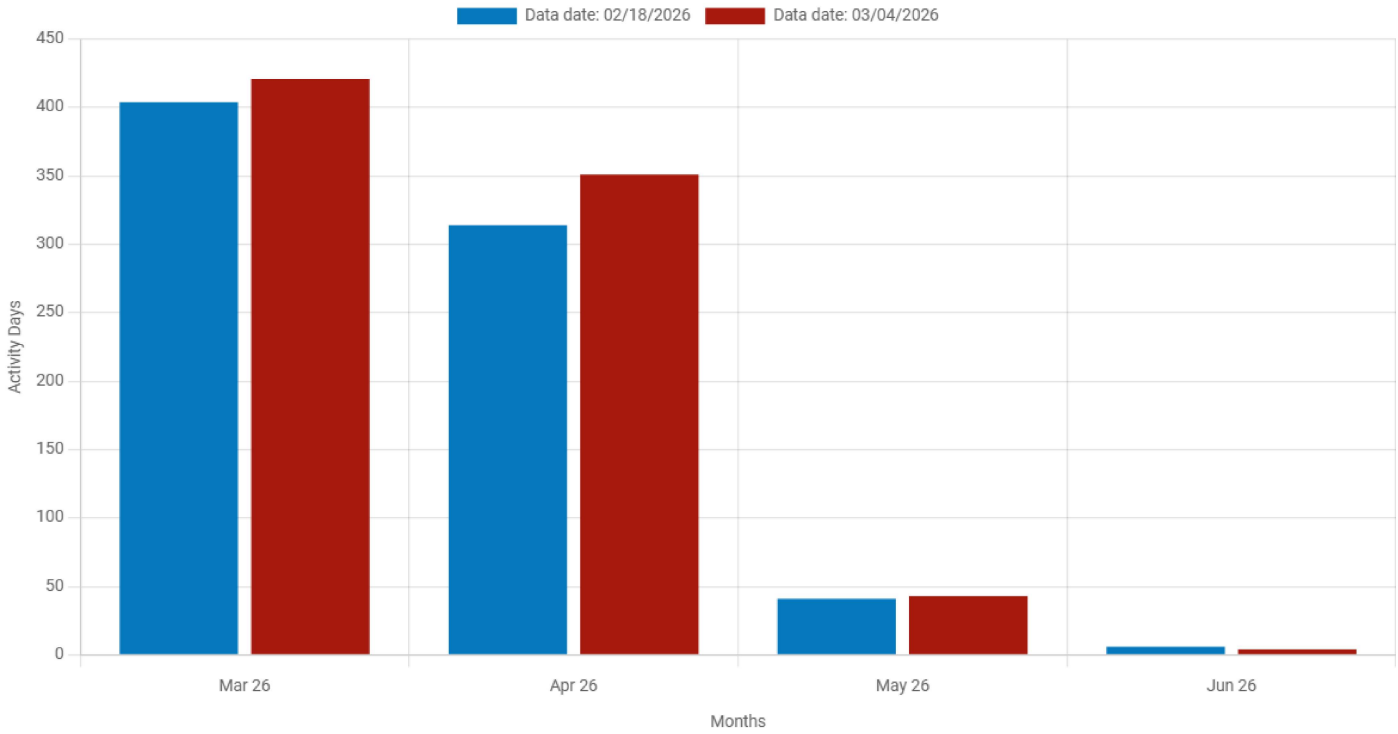

Month	02/18/2026 Activity Days	03/04/2026 Activity Days
Mar 26	404	421
Apr 26	314	351
May 26	41	43
Jun 26	6	4
