	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Frisco Office TI**		**197 days**			**Mon 25/09/08**			**Tue 26/06/09**	
2	**Construction Documents**		**136 days**			**Mon 25/09/08**			**Mon 26/03/16**	
3	CD Kick off and Start		34 days			Mon 25/09/08			Thu 25/10/23	
4	65% progress set		1 day			Fri 25/10/24			Fri 25/10/24	
5	Owner Drawing review of 65% set		5 days			Mon 25/10/27			Fri 25/10/31	
6	Completon of Bid, Demo and Permit Submital set		10 days			Mon 25/11/03			Fri 25/11/14	
7	**Plan Check**		**31 days**			**Mon 25/11/17**			**Mon 25/12/29**	
8	**Issue for Interiors Permit (Plan Check)**		**31 days**			**Mon 25/11/17**			**Mon 25/12/29**	
9	City Permit Review		15 days			Mon 25/11/17			Fri 25/12/05	
10	Drawing Coordination/City Comments		15 days			Mon 25/12/08			Fri 25/12/26	
11	Receive Interior TI Building Permit		1 day			Mon 25/12/29			Mon 25/12/29	
12	**Issue for Demo Permit**		**16 days**			**Mon 25/11/17**			**Mon 25/12/08**	
13	Demo Permit Review		15 days			Mon 25/11/17			Fri 25/12/05	
14	Receive Demo Permit		1 day			Mon 25/12/08			Mon 25/12/08	
15	**Bidding**		**20 days**			**Mon 25/11/17**			**Fri 25/12/12**	
16	Bidding for TI GCs		15 days			Mon 25/11/17			Fri 25/12/05	
17	Award GC Contract		5 days			Mon 25/12/08			Fri 25/12/12	
18	**Procurement of Direct FBO items**		**136 days**			**Mon 25/09/08**			**Mon 26/03/16**	
19	**Furniture**		**97 days**			**Fri 25/10/31**			**Mon 26/03/16**	
20	Select Furniture Vendor		1 day			Fri 25/10/31			Fri 25/10/31	
21	Review and finalize details for furniture		15 days			Mon 25/11/03			Fri 25/11/21	
22	Furniture Order Due		1 day			Mon 25/11/24			Mon 25/11/24	
23	Furniture Lead Time		80 days			Tue 25/11/25			Mon 26/03/16	
24	**HVAC Equipment**		**71 days**			**Mon 25/10/27**			**Mon 26/02/02**	
25	Order Roof Top HVAC equipment		1 day			Mon 25/10/27			Mon 25/10/27	
26	HVAC Equipment Lead Time		70 days			Tue 25/10/28			Mon 26/02/02	
27	**Elevator Modernization**		**126 days**			**Mon 25/09/08**			**Mon 26/03/02**	
28	Contract for Elevator Modernization		1 day			Mon 25/09/08			Mon 25/09/08	
29	Elevator Equipment Lead Time		100 days			Tue 25/09/09			Mon 26/01/26	
30	Elevator Modernization		25 days			Tue 26/01/27			Mon 26/03/02	
31	**Demolition**		**15 days**			**Mon 25/12/15**			**Fri 26/01/02**	
32	Demo of finishes/Existing		15 days			Mon 25/12/15			Fri 26/01/02	
33	**Construction**		**112 days**			**Mon 26/01/05**			**Tue 26/06/09**	
34	Overhead MEP installation		15 days			Mon 26/01/05			Fri 26/01/23	
35	Installation of Roof Top HVAC		10 days			Tue 26/02/03			Mon 26/02/16	
36	Installation of VAV boxes HVAC rework		10 days			Tue 26/02/03			Mon 26/02/16	
37	Framing one side drywall		15 days			Mon 26/01/26			Fri 26/02/13	
38	MEP Rough in Walls and Floors		15 days			Tue 26/02/17			Mon 26/03/09	
39	Data and Wiring Low Voltage		10 days			Tue 26/03/03			Mon 26/03/16	
40	Wall Taping finish		15 days			Tue 26/03/17			Mon 26/04/06	
41	Grid install rework		10 days			Tue 26/04/07			Mon 26/04/20	
42	Light fixtures install		10 days			Tue 26/04/14			Mon 26/04/27	
43	Ceiling tile installation		10 days			Tue 26/04/28			Mon 26/05/11	
44	Millwork and fixtures		15 days			Tue 26/04/07			Mon 26/04/27	
45	AV Equipment Installation		10 days			Tue 26/04/07			Mon 26/04/20	
46	Security Systems Equipment Installation		10 days			Tue 26/04/07			Mon 26/04/20	
47	Furniture systems installation		10 days			Tue 26/05/05			Mon 26/05/18	
48	Inspections and Commissioning		10 days			Tue 26/05/19			Mon 26/06/01	
49	Final Clean		5 days			Tue 26/06/02			Mon 26/06/08	
50	Move in		1 day			Tue 26/06/09			Tue 26/06/09	
51	**Construction Documents**	**50 days**			**Mon 25/09/08**			**Fri 25/11/14**		

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
52	CD Kick off and Start	34 days			Mon 25/09/08			Thu 25/10/23		
53	65% progress set	1 day			Fri 25/10/24			Fri 25/10/24		
54	Owner Drawing review Of 65% set	5 days			Mon 25/10/27			Fri 25/10/31		
55	Completon of Bid, Demo and Permit Submital set	10 days			Mon 25/11/03			Fri 25/11/14		
56	**Plan Check**	**29 days**			**Mon 25/11/17**			**Mon 25/12/29**		
57	**Issue for Interiors Permit (Plan Check)**	**29 days**			**Mon 25/11/17**			**Mon 25/12/29**		
58	City Permit Review	15 days			Mon 25/11/17			Fri 25/12/05		
59	Drawing Coordination/City Comments	13 days			Mon 25/12/08			Wed 25/12/24		
60	Receive interior Tl Building Permit	1 day			Mon 25/12/29			Mon 25/12/29		
61	**Issue for Demo Permit**	**16 days**			**Mon 25/11/17**			**Mon 25/12/08**		
62	Demo Permit Review	15 days			Mon 25/11/17			Fri 25/12/05		
63	Receive Demo Permit	1 day			Mon 25/12/08			Mon 25/12/08		
64	**Bidding**	**19 days**			**Mon 25/11/17**			**Thu 25/12/11**		
65	Bidding for Tl GCs	15 days			Mon 25/11/17			Fri 25/12/05		
66	Award GC Contract	4 days			Mon 25/12/08			Thu 25/12/11		
67	**Contracting**	**16 days**			**Fri 25/12/12**			**Thu 26/01/08**		
68	Execute Demo LOA	1 day			Fri 25/12/12			Fri 25/12/12		
69	Contract Preparation	5 days			Mon 25/12/15			Fri 25/12/19		
70	Contract Negotiation	5 days			Mon 25/12/22			Tue 25/12/30		
71	Contract Execution	5 days			Fri 26/01/02			Thu 26/01/08		
72	**ARCO Procurement**	**69 days**			**Fri 26/01/09**			**Wed 26/04/15**		
73	Submittal Approval	2 wks			Fri 26/01/09			Thu 26/01/22		
74	Light Fixtures	8 wks			Fri 26/01/23			Thu 26/03/19		
75	Millwork Shop Drawings	2,2 wks			Fri 26/01/23			Fri 26/02/06		
76	Millwork Field Measure and Fab	6 wks			Thu 26/03/05			Wed 26/04/15		
77	Flooring - Tile and Carpet	6 wks			Fri 26/01/23			Thu 26/03/05		
78	Frames	6 wks			Fri 26/01/23			Thu 26/03/05		
79	Doors, Hardware	8 wks			Fri 26/01/23			Thu 26/03/19		
80	Appliances	8 wks			Fri 26/01/23			Thu 26/03/19		
81	Ceiling Baffles	10 wks			Fri 26/01/23			Thu 26/04/02		
82	**Procurement Of Direct FBO items**	**136 days**			**Mon 25/09/08**			**Fri 26/03/20**		
83	**Furniture**	**97 days**			**Fri 25/10/31**			**Fri 26/03/20**		
84	Select Furniture Vendor	1 day			Fri 25/10/31			Fri 25/10/31		
85	Review and finalize details for furniture	15 days			Mon 25/11/03			Fri 25/11/21		
86	Furniture Order Due	1 day			Mon 25/11/24			Mon 25/11/24		
87	Furniture Lead Time	80 days			Tue 25/11/25			Fri 26/03/20		
88	**HVAC Equipment**	**71 days**			**Mon 25/10/27**			**Fri 26/02/06**		
89	Order Roof Top HVAC equipment	1 day			Mon 25/10/27			Mon 25/10/27		
90	HVAC Equipment Lead Time	70 days			Tue 25/10/28			Fri 26/02/06		
91	**Elevator Modernization**	**123 days**			**Mon 25/09/08**			**Tue 26/03/03**		
92	Contract for Elevator Modernization	1 day			Mon 25/09/08			Mon 25/09/08		
93	Elevator Equipment Lead Time	97 days			Tue 25/09/09			Tue 26/01/27		
94	Elevator Modernization	25 days			Wed 26/01/28			Tue 26/03/03		
95	**Demolition**	**25 days**			**Mon 25/12/15**			**Thu 26/01/22**		
96	MEP/F Make Safe	3 wks			Mon 25/12/15			Thu 26/01/08		
97	Demolition	5 wks			Mon 25/12/15			Thu 26/01/22		
98	Slab Demo and Coring	3 days			Tue 26/01/20			Thu 26/01/22		
99	**Construction**	**101 days**			**Fri 26/01/09**			**Fri 26/05/29**		
100	Overhead MEP Rough In	30 days			Fri 26/01/09			Thu 26/02/19		
101	Low Voltage Bulk Cabling	20 days			Fri 26/01/30			Thu 26/02/26		
102	Walls - Studs and Track	15 days			Fri 26/01/23			Thu 26/02/12		
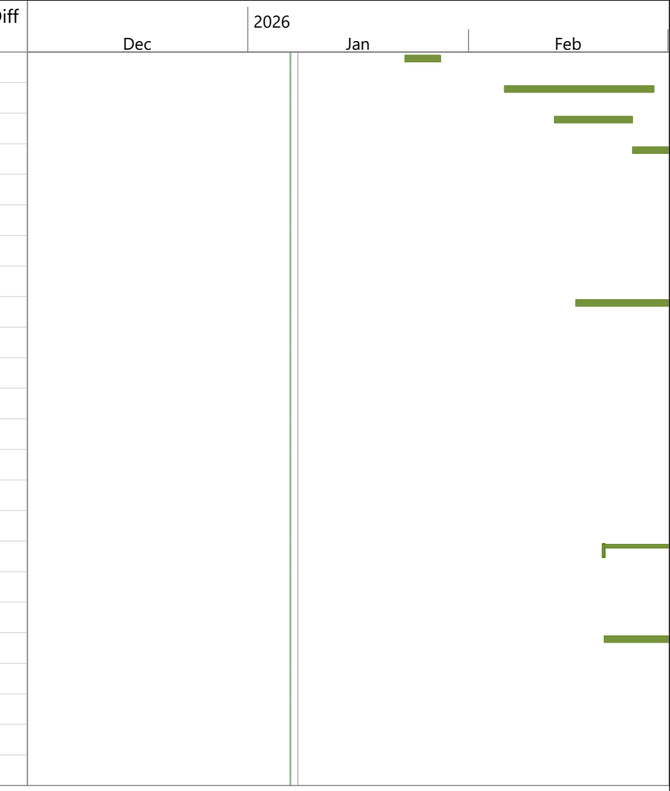
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
103	Underslab MEP	3 days			Fri 26/01/23			Tue 26/01/27		
104	MEP Rough-in Walls	15 days			Fri 26/02/06			Thu 26/02/26		
105	Single Side Drywall	7 days			Fri 26/02/13			Mon 26/02/23		
106	Second Side Drywall	7 days			Tue 26/02/24			Wed 26/03/04		
107	Wall Tape and Bed	12 days			Thu 26/03/05			Fri 26/03/20		
108	Grid Install Rework	10 days			Mon 26/03/16			Fri 26/03/27		
109	Light Fixture Install and Ceiling MEP Finishes	12 days			Mon 26/03/23			Tue 26/04/07		
110	Ceiling Tile Installation	10 days			Wed 26/04/08			Tue 26/04/21		
111	Restroom Renovations	25 days			Mon 26/02/16			Mon 26/03/23		
112	Carpet and Tile Prep and Install	20 days			Mon 26/03/23			Fri 26/04/17		
113	Painting	20 days			Mon 26/03/23			Fri 26/04/17		
114	MEP Trimout	15 days			Mon 26/04/06			Fri 26/04/24		
115	Millwork Install	5 days			Thu 26/04/16			Wed 26/04/22		
116	Inspections and Commissioning	10 days			Mon 26/05/11			Fri 26/05/22		
117	Punch Walk and Corrections	5 days			Mon 26/05/11			Fri 26/05/15		
118	Final Clean	5 days			Mon 26/05/25			Fri 26/05/29		
119	**Install of Owner Provided Equipment/Vendors**	**56 days**			**Fri 26/02/20**			**Fri 26/05/08**		
120	Confirm Weather For RTU Replacements	1 day			Mon 26/03/02			Mon 26/03/02		
121	RTU Replacement	3 days			Tue 26/03/03			Thu 26/03/05		
122	VAV Replacements	15 days			Fri 26/02/20			Thu 26/03/12		
123	AV Equipment Installation	10 days			Mon 26/03/23			Fri 26/04/03		
124	Security Systems Equipment Installation	10 days			Mon 26/03/23			Fri 26/04/03		
125	Furniture Systems Installation	10 days			Mon 26/04/27			Fri 26/05/08		
126	Move in	1 day			Mon 26/06/01			Mon 26/06/01
