Meridian, ID

Compare Remaining Compression

Report Date: 03/26/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Meridian, MS -01/30/2026	**Meridian - 03/20/2026 - UP02**
Data Date: 01/30/2026	Data Date: 03/12/2026
Finish Date: 08/18/2026	Finish Date: 09/21/2026

Remaining Work Compression 19 %

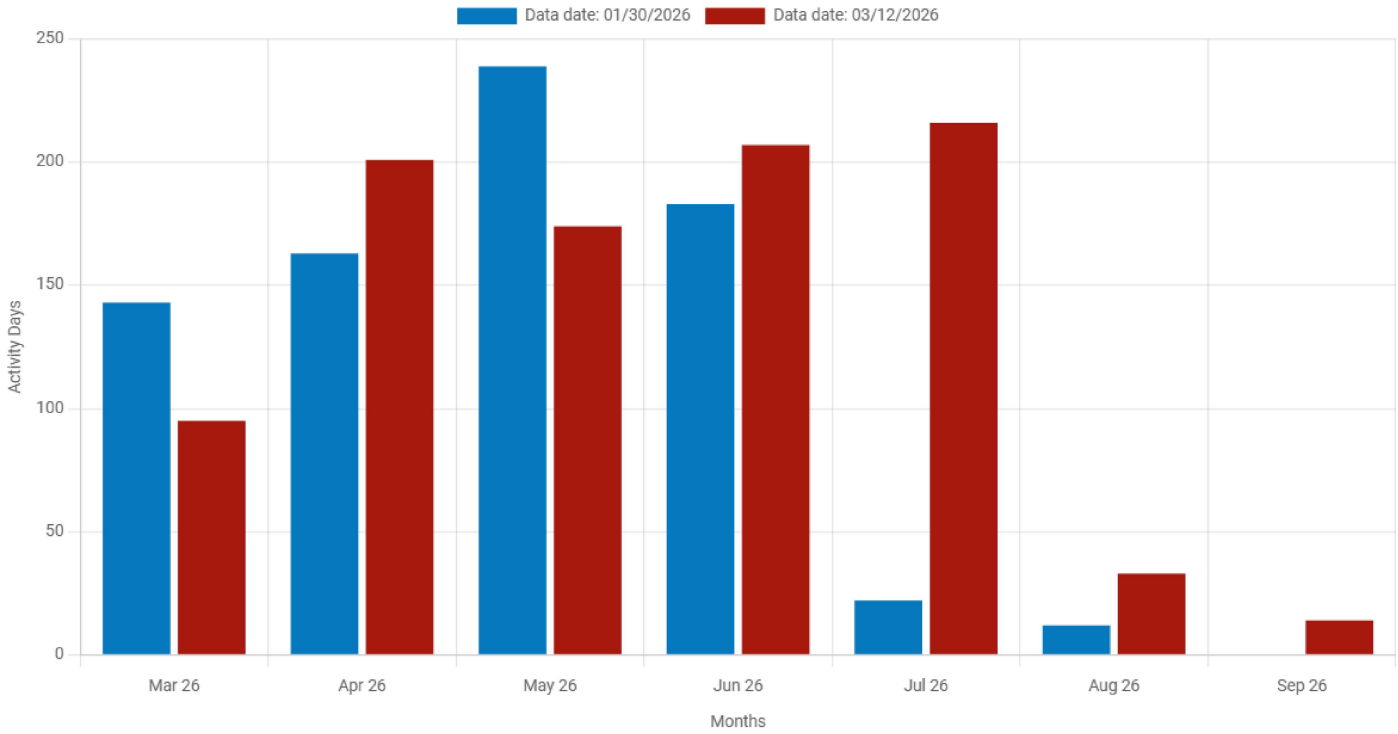

Month	01/30/2026 Activity Days	03/12/2026 Activity Days
Mar 26	143	95
Apr 26	163	201
May 26	239	174
Jun 26	183	207
Jul 26	22	216
Aug 26	12	33
Sep 26	0	14
