	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**259 days**	**265 days**	**-6d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 9/11/26**	**Mon 9/21/26**	**-6d**
2	Notice to Proceed	1 day	1 day	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/8/25	Mon 9/8/25	0d
3	DELAY - PERMIT DELAY	32 days	32 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Wed 10/22/25	Wed 10/22/25	0d
4	Obtain Building Permit	0 days	0 days	0d	Wed 10/22/25	Wed 10/22/25	0d	Wed 10/22/25	Wed 10/22/25	0d
5	ACHD ROW Permit	0 days	0 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 10/29/25	Wed 10/29/25	0d
6	Obtain LDIR Approval to Proceed	0 days	0 days	0d	Mon 10/27/25	Mon 10/27/25	0d	Mon 10/27/25	Mon 10/27/25	0d
7	Receive CAD Base Files from Public Storage	10 days	10 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/22/25	Mon 9/22/25	0d
8	Procure Early Work Subcontractors	5 days	5 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/15/25	Mon 9/15/25	0d
9	Procure Remaining Subcontractors	20 days	20 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 10/13/25	Mon 10/13/25	0d
10	Submittals (SWPPP/NOI)	10 days	10 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/29/25	Mon 9/29/25	0d
11	Submittals (SES /Switchgear)	125 days	125 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Fri 3/13/26	Fri 3/13/26	0d
12	Submittals (numerous)	90 days	90 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Fri 2/20/26	Fri 2/20/26	0d
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	40 days	40 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Fri 12/19/25	Fri 12/19/25	0d
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	40 days	40 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Tue 1/6/26	Tue 1/6/26	0d
15	Procure SES's/Switchgears (6 mos ~ 130 WD)	56 days	56 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 1/23/26	Fri 1/23/26	0d
16	Light Fixture Submittal Review and Approval	10 days	10 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Fri 2/6/26	Fri 2/6/26	0d
17	Light Fixture Package Alternate - Fab and Deliver	10 days	10 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Fri 2/20/26	Fri 2/20/26	0d
18	Fire Sprinkler Design and Approval	78 days	78 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 2/4/26	Wed 2/4/26	0d
19	Fire Alarm System Design and Approval	40 days	40 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 12/10/25	Wed 12/10/25	0d
20	ASPHALT BATCH PLANT SHUTDOWN	70 days	70 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Thu 2/26/26	Thu 2/26/26	0d
21	TWENTY WORKING DAYS OF WEATHER DELAY	10 days	10 days	0d	Mon 8/31/26	Tue 9/8/26	-6d	Fri 9/11/26	Mon 9/21/26	-6d
22	WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	2 days	0d	Wed 12/17/25	Wed 12/17/25	0d	Thu 12/18/25	Thu 12/18/25	0d
23	WEATHER DELAY - Rain - Impact SOG B	1 day	1 day	0d	Mon 12/22/25	Mon 12/22/25	0d	Mon 12/22/25	Mon 12/22/25	0d
24	WEATHER DELAY - Rain - Impact SOG B	3 days	3 days	0d	Thu 1/8/26	Thu 1/8/26	0d	Mon 1/12/26	Mon 1/12/26	0d
25	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Wed 2/18/26	Wed 2/18/26	0d
26	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/24/26	Tue 2/24/26	0d	Wed 2/25/26	Wed 2/25/26	0d
27	Substantial Completion	0 days	0 days	0d	Fri 9/11/26	Mon 9/21/26	-6d	Fri 9/11/26	Mon 9/21/26	-6d
28	Clean Up and Project Close Out	5 days	5 days	0d	Wed 8/19/26	Thu 8/27/26	-6d	Tue 8/25/26	Wed 9/2/26	-6d
29	Demobilize	3 days	3 days	0d	Wed 8/26/26	Thu 9/3/26	-6d	Fri 8/28/26	Mon 9/7/26	-6d
30	**SITEWORK**	**219 days**	**219 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 7/17/26**	**Fri 7/17/26**	**0d**
31	**Level of Effort**	**131 days**	**131 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 3/13/26**	**Fri 3/13/26**	**0d**
32	Construction Staking & Surveying	90 days	90 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 1/16/26	Fri 1/16/26	0d
33	Inspections and Testing	100 days	100 days	0d	Fri 9/12/25	Fri 9/12/25	0d	Fri 2/13/26	Fri 2/13/26	0d
34	Maintain Erosion Control	120 days	120 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Fri 3/13/26	Fri 3/13/26	0d
35	Erosion Control & SWPP	5 days	5 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/22/25	Mon 9/22/25	0d
36	Mobilization	5 days	5 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/15/25	Mon 9/15/25	0d
37	Site Demolition (Trees,Sawcut, Asphalt, Base)	0 days	0 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 9/12/25	Fri 9/12/25	0d
38	Clear/Grub & Overlot Grading	12 days	12 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Tue 9/23/25	Tue 9/23/25	0d
39	Structure Demo (Partial Building & RV Storage)	5 days	5 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/7/25	Fri 11/7/25	0d
40	Re-Mobilization	4 days	4 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Tue 10/28/25	Tue 10/28/25	0d
41	FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	7 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Thu 11/6/25	Thu 11/6/25	0d
42	Site - Water Line Ten Mile Tie-In	2 days	2 days	0d	Sat 11/8/25	Sat 11/8/25	0d	Tue 11/11/25	Tue 11/11/25	0d
43	Work Week Restriction	5 days	5 days	0d	Fri 11/7/25	Fri 11/7/25	0d	Thu 11/13/25	Thu 11/13/25	0d
44	Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	13 days	0d	Fri 11/14/25	Fri 11/14/25	0d	Thu 12/4/25	Thu 12/4/25	0d
45	DELAY - GIRR License Agreement Approval to Proceed	6 days	6 days	0d	Fri 12/5/25	Fri 12/5/25	0d	Fri 12/12/25	Fri 12/12/25	0d
46	DELAY - RFI #14 - GIRR Separation	4 days	4 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Thu 12/18/25	Thu 12/18/25	0d
47	Storm Drain Lines South	6 days	6 days	0d	Mon 12/22/25	Mon 12/22/25	0d	Tue 12/30/25	Tue 12/30/25	0d
48	Site - Water Line & Fire Lines/Hydrants and Devices Remaining	18 days	18 days	0d	Mon 1/5/26	Mon 1/5/26	0d	Wed 1/28/26	Wed 1/28/26	0d
49	Site - GIRR Piping & Devices	16 days	16 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/2/26	Mon 2/2/26	0d
50	TP DELAY - Site - GIRR Box Delivery and Placement	6 days	6 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Mon 2/2/26	Mon 2/2/26	0d
51	Complete UG Utility Lines, SD Turn Ups, to Building A	1 day	5 days	-4d	Tue 3/31/26	Thu 5/14/26	-32d	Tue 3/31/26	Wed 5/20/26	-36d
52	Gravel Road Rough Grade Prep	8 days	8 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Wed 12/17/25	Wed 12/17/25	0d
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**74 days**	**53 days**	**21d**	**Tue 2/3/26**	**Tue 2/3/26**	**0d**	**Fri 5/15/26**	**Thu 4/16/26**	**21d**
54	FRAGNET - Site - Drive Aisle Over Ex Unsuitable Soil Identified	1 day	1 day	0d	Tue 2/3/26	Tue 2/3/26	0d	Tue 2/3/26	Tue 2/3/26	0d
55	FRAGNET - Site - Drive Aisle Over Ex Discussion and Confirmation on Solution	2 days	2 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/5/26	Thu 2/5/26	0d
56	FRAGNET - Site - Idaho Power - Pivot to Moblize and Peform the UG JT in Drive Aisle	15 days	15 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/26/26	Thu 2/26/26	0d
57	FRAGNET - Site - Owner Review of Impact and Discussion with Geo Tech to Identify Alternative Solutions More Econamical	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 2/25/26	Wed 2/25/26	0d

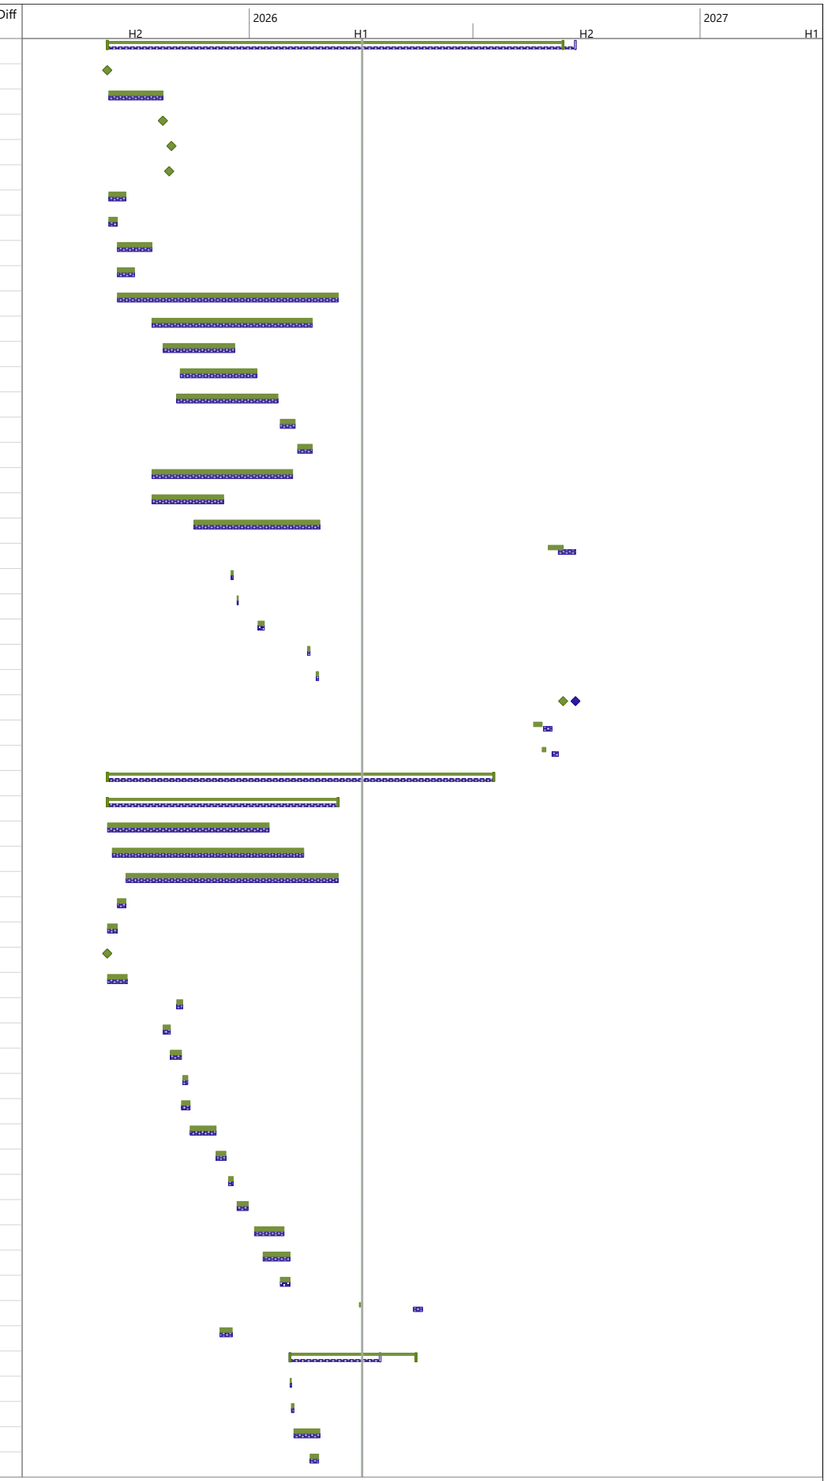

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
58	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
59	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
60	FRAGNET - Mobilize Crew, Rough Grade Prep, Scarify and Air Dry	1 day	1 day	0d	Fri 3/20/26	Fri 3/20/26	0d	Fri 3/20/26	Fri 3/20/26	0d
61	FRAGNET - Re-Prep, Proof Roll, Confirm Soft Spot Magnitude	1 day	1 day	0d	Mon 3/23/26	Mon 3/23/26	0d	Mon 3/23/26	Mon 3/23/26	0d
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If failed, provide geo grid per RFI 33	3 days	3 days	0d	Tue 5/5/26	Tue 3/24/26	30d	Thu 5/7/26	Thu 3/26/26	30d
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	1 day	1 day	0d	Fri 5/8/26	Thu 4/9/26	21d	Fri 5/8/26	Thu 4/9/26	21d
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	5 days	5 days	0d	Mon 5/11/26	Fri 4/10/26	21d	Fri 5/15/26	Thu 4/16/26	21d
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	5 days	5 days	0d	Mon 5/11/26	Fri 4/10/26	21d	Fri 5/15/26	Thu 4/16/26	21d
66	Site - Idaho Power Boring	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Fri 2/27/26	Fri 2/27/26	0d
67	Site - Idaho Power Trench, Conduit and Backfill	5 days	5 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Fri 3/13/26	Fri 3/13/26	0d
68	Site - Idaho Power Transformer Set and Make Live	0 days	0 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Fri 3/13/26	Fri 3/13/26	0d
69	Storm Drain Lines and Devices - South of Buildings (E-W)	7 days			Wed 4/15/26			Thu 4/23/26		
70	Site - Flatwork Sidewalk Prep	8 days			Wed 4/15/26			Fri 4/24/26		
71	Storm Drain Lines and Devices - North of Buildings (E-W)	7 days	15 days	-8d	Fri 4/24/26	Thu 4/23/26	1d	Mon 5/4/26	Wed 5/13/26	-7d
72	Site - Curb and Gutter Prep	8 days			Mon 5/18/26			Thu 5/28/26		
73	Site - Base Course Asphalt Prep	8 days	8 days	0d	Mon 5/18/26	Thu 4/23/26	17d	Thu 5/28/26	Mon 5/4/26	18d
74	Site Flatwork and Curb and Gutter - (E-W)	15 days			Fri 5/29/26			Thu 6/18/26		
75	Site - Fine Grade Asphalt Prep	3 days	3 days	0d	Fri 6/19/26	Fri 6/12/26	5d	Tue 6/23/26	Tue 6/16/26	5d
76	Asphalt Paving	2 days	2 days	0d	Wed 6/24/26	Wed 6/17/26	5d	Thu 6/25/26	Thu 6/18/26	5d
77	Pavement Markings, Signage & Bumpers	2 days	2 days	0d	Fri 6/26/26	Fri 6/19/26	5d	Mon 6/29/26	Mon 6/22/26	5d
78	Site Fencing Chainlink	5 days	5 days	0d	Wed 5/20/26	Fri 6/19/26	-22d	Wed 5/27/26	Thu 6/25/26	-21d
79	Gravel Road Finish Grading	5 days	5 days	0d	Thu 5/28/26	Thu 5/14/26	10d	Wed 6/3/26	Wed 5/20/26	10d
80	Site Flatwork and Curb and Gutter		15 days			Thu 5/21/26			Thu 6/11/26	
81	Landscaping and Irrigation	15 days	15 days	0d	Fri 6/26/26	Fri 6/19/26	5d	Fri 7/17/26	Fri 7/10/26	5d
82	Site Fencing Vinyl	10 days	10 days	0d	Fri 6/26/26	Fri 6/26/26	0d	Fri 7/10/26	Fri 7/10/26	0d
83	Site Fencing Rod Iron and Gates	5 days	5 days	0d	Fri 6/26/26	Mon 7/13/26	-11d	Thu 7/2/26	Fri 7/17/26	-11d
84	**BUILDING B**	**195 days**	**193 days**	**2d**	**Wed 10/29/25**	**Wed 10/29/25**	**0d**	**Wed 8/5/26**	**Mon 8/3/26**	**2d**
85	BLDG B Foundation Excavation	6 days	6 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 11/5/25	Wed 11/5/25	0d
86	DELAY - BLDG B FOOTING OVER-EX	4 days	4 days	0d	Fri 10/31/25	Fri 10/31/25	0d	Wed 11/5/25	Wed 11/5/25	0d
87	BLDG B SOG Prep	5 days	5 days	0d	Wed 11/26/25	Wed 11/26/25	0d	Thu 12/4/25	Thu 12/4/25	0d
88	FRAGNET - Bldg B Soft Spot Repair	8 days	8 days	0d	Thu 12/4/25	Thu 12/4/25	0d	Mon 12/15/25	Mon 12/15/25	0d
89	BLDG B Backfill Foundations	18 days	18 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 1/9/26	Fri 1/9/26	0d
90	**CONCRETE WORK**	**44 days**	**44 days**	**0d**	**Thu 11/6/25**	**Thu 11/6/25**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**
91	BLDG B Foundation	14 days	14 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Tue 11/25/25	Tue 11/25/25	0d
92	BLDG B Dampproofing	1 day	1 day	0d	Tue 11/18/25	Tue 11/18/25	0d	Wed 11/26/25	Wed 11/26/25	0d
93	BLDG B Slab On Grade	19 days	19 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Mon 1/12/26	Mon 1/12/26	0d
94	BLDG B Slab On Grade Complete	0 days	0 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 1/12/26	Mon 1/12/26	0d
95	**STEEL AND METALS**	**82 days**	**108.5 day**	**-26.5d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Tue 5/5/26**	**Fri 6/12/26**	**-27.5d**
96	Frame Load Bearing Shear Walls, Interior Partitions, & Corridors (JANUS)	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/9/26	Mon 2/9/26	0d
97	FRAGNET - Extended Shear Wall Durations (JANUS)	12 days	30 days	-18d	Tue 2/10/26	Tue 2/10/26	0d	Wed 2/25/26	Mon 3/23/26	-18d
98	Frame & Panel Partition & Corridor Walls (JANUS)		20 days			Thu 5/14/26			Fri 6/12/26	
99	Panel Shear Walls, Interior Partition, & Corridor Walls (JANUS)	20 days			Thu 2/26/26			Wed 3/25/26		
100	Perimeter Panel Interior Walls (JANUS)	20 days			Wed 4/8/26			Tue 5/5/26		
101	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Tue 4/14/26**	**Thu 4/23/26**	**-7.5d**	**Mon 4/20/26**	**Thu 4/30/26**	**-7.5d**
102	Misc Finish Carpentry	5 days	5 days	0d	Tue 4/14/26	Thu 4/23/26	-7.5d	Mon 4/20/26	Thu 4/30/26	-7.5d
103	**ROOF & SIDING**	**78 days**	**78 days**	**0d**	**Fri 1/30/26**	**Fri 1/30/26**	**0d**	**Tue 5/19/26**	**Tue 5/19/26**	**0d**
104	Exterior Sheathing	0 days	0 days	0d	Fri 1/30/26	Fri 1/30/26	0d	Mon 2/16/26	Mon 2/16/26	0d
105	Weather Barrier Fluid Applied	8 days	8 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/19/26	Thu 2/19/26	0d
106	Weather Barrier Tyvek	10 days	10 days	0d	Wed 3/4/26	Wed 3/4/26	0d	Tue 3/17/26	Tue 3/17/26	0d
107	CMU Veneer Base Course & Grout	15 days	15 days	0d	Tue 3/3/26	Tue 3/3/26	0d	Tue 4/7/26	Tue 4/7/26	0d
108	Rigid Insulation Behind CMU	5 days	5 days	0d	Wed 4/8/26	Wed 4/8/26	0d	Tue 4/14/26	Tue 4/14/26	0d
109	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Fri 4/17/26	Fri 4/17/26	0d
110	CMU Veneer Remaining	15 days	15 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Tue 5/5/26	Tue 5/5/26	0d
111	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Wed 5/6/26	Wed 5/6/26	0d	Tue 5/19/26	Tue 5/19/26	0d
112	Install Roof & Roof Insulation (JANUS)	15 days	15 days	0d	Wed 2/25/26	Wed 2/25/26	0d	Mon 3/30/26	Thu 4/9/26	-7.5d
113	BLDG B Roofing Complete	0 days	0 days	0d	Mon 3/30/26	Thu 4/9/26	-7.5d	Mon 3/30/26	Thu 4/9/26	-7.5d
114	**DOORS & WINDOWS**	**20 days**	**20 days**	**0d**	**Thu 7/9/26**	**Tue 7/7/26**	**2d**	**Wed 8/5/26**	**Mon 8/3/26**	**2d**

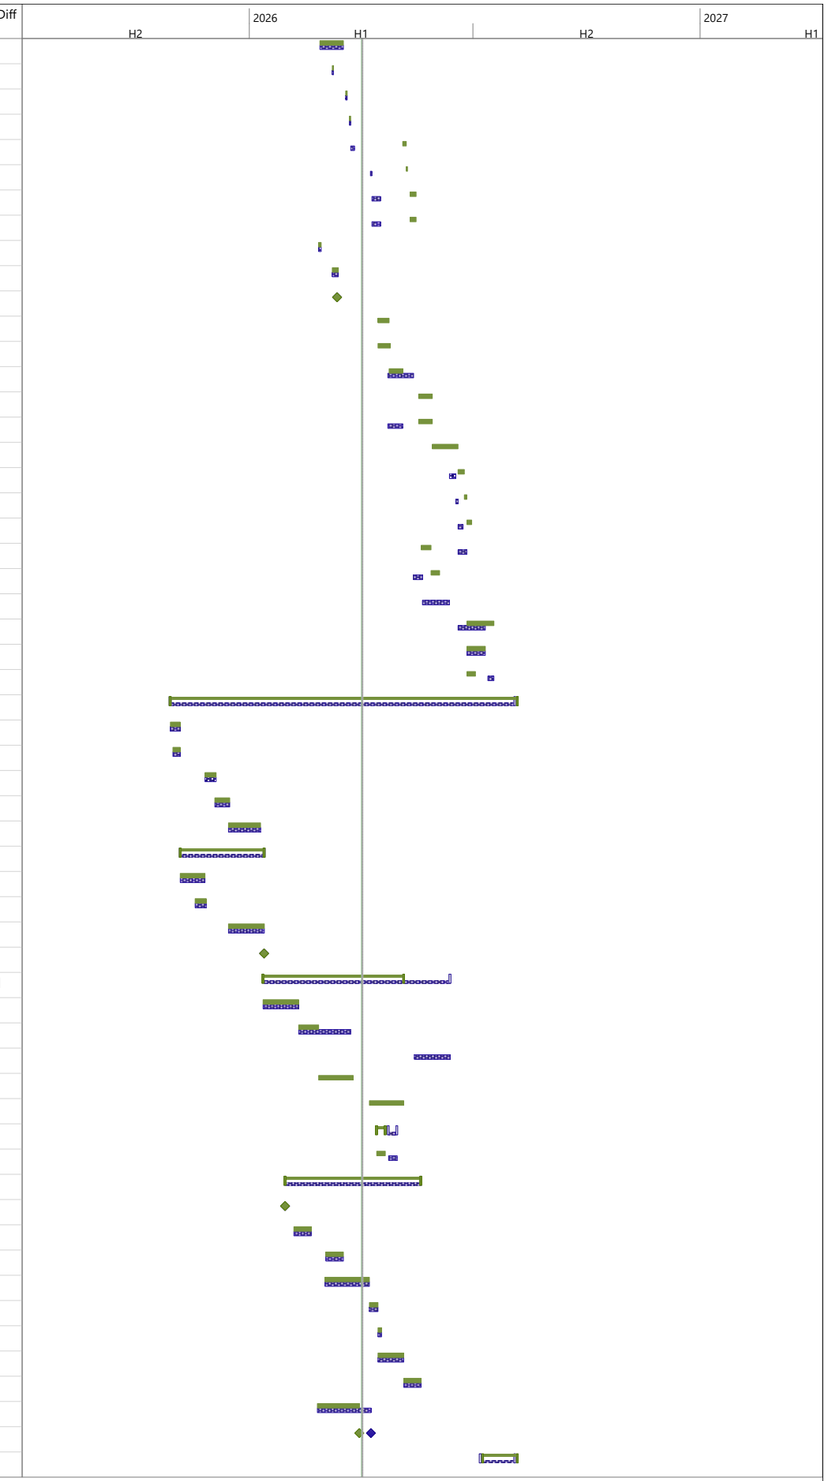

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
115	F&I Storage Unit Doors (JANUS)	20 days	20 days	0d	Thu 7/9/26	Tue 7/7/26	2d	Wed 8/5/26	Mon 8/3/26	2d
116	F&I HM Doors and Hardware (JANUS)	15 days	15 days	0d	Thu 7/9/26	Tue 7/7/26	2d	Wed 7/29/26	Mon 7/27/26	2d
117	**FINISHES**	**30 days**	**30 days**	**0d**	**Tue 3/31/26**	**Thu 4/9/26**	**-7.5d**	**Mon 5/11/26**	**Thu 5/21/26**	**-7.5d**
118	Install Gypsum Board	10 days	10 days	0d	Tue 3/31/26	Thu 4/9/26	-7.5d	Mon 4/13/26	Thu 4/23/26	-7.5d
119	Flooring Polished Concrete	5 days	5 days	0d	Tue 4/14/26	Thu 4/23/26	-7.5d	Mon 4/20/26	Thu 4/30/26	-7.5d
120	FRP / Vinyl Base	5 days	5 days	0d	Tue 4/21/26	Thu 4/30/26	-7.5d	Mon 4/27/26	Thu 5/7/26	-7.5d
121	Painting	10 days	10 days	0d	Tue 4/28/26	Thu 5/7/26	-7.5d	Mon 5/11/26	Thu 5/21/26	-7.5d
122	**SPECIALTIES**	**23 days**	**23 days**	**0d**	**Tue 4/14/26**	**Thu 4/23/26**	**-7.5d**	**Thu 5/14/26**	**Wed 5/27/26**	**-8.5d**
123	Install Misc Equipment & Lockers	20 days	20 days	0d	Tue 4/14/26	Thu 4/23/26	-7.5d	Mon 5/11/26	Thu 5/21/26	-7.5d
124	Bathroom Accessories	2 days	2 days	0d	Tue 4/21/26	Thu 4/30/26	-7.5d	Wed 4/22/26	Mon 5/4/26	-7.5d
125	Building Interior Signage	3 days	3 days	0d	Tue 5/12/26	Thu 5/21/26	-7.5d	Thu 5/14/26	Wed 5/27/26	-8.5d
126	**FIRE SPRINKLERS**	**50 days**	**50 days**	**0d**	**Mon 2/23/26**	**Mon 2/23/26**	**0d**	**Fri 5/1/26**	**Fri 5/1/26**	**0d**
127	Fire Sprinkler System Rough In	28 days	28 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 4/10/26	Fri 4/10/26	0d
128	Fire Sprinkler System Trim Out	15 days	15 days	0d	Mon 4/13/26	Mon 4/13/26	0d	Fri 5/1/26	Fri 5/1/26	0d
129	**PLUMBING**	**107 days**	**114.5 day**	**-7.5d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Thu 4/23/26**	**Tue 5/5/26**	**-7.5d**
130	Plumbing Rough-in Underground	4 days	4 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
131	Drains, Water, Sewer Lines	15 days	15 days	0d	Tue 3/31/26	Thu 4/9/26	-7.5d	Mon 4/20/26	Thu 4/30/26	-7.5d
132	Bathroom Fixtures	3 days	3 days	0d	Tue 4/21/26	Thu 4/30/26	-7.5d	Thu 4/23/26	Tue 5/5/26	-7.5d
133	Other Plumbing Fixtures	3 days	3 days	0d	Tue 4/21/26	Thu 4/30/26	-7.5d	Thu 4/23/26	Tue 5/5/26	-7.5d
134	**HVAC**	**30 days**	**30 days**	**0d**	**Tue 3/31/26**	**Thu 4/9/26**	**-7.5d**	**Mon 5/11/26**	**Thu 5/21/26**	**-7.5d**
135	HVAC Installation	25 days	25 days	0d	Tue 3/31/26	Thu 4/9/26	-7.5d	Mon 5/4/26	Thu 5/14/26	-7.5d
136	HVAC Commisioning & T&B	5 days	5 days	0d	Tue 5/5/26	Thu 5/14/26	-7.5d	Mon 5/11/26	Thu 5/21/26	-7.5d
137	**ELECTRICAL**	**149 days**	**156.5 day**	**-7.5d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Tue 6/23/26**	**Mon 7/6/26**	**-8.5d**
138	Building Rough-in Underground	0 days	0 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
139	Elect Rough-In	25 days	25 days	0d	Mon 3/2/26	Mon 3/2/26	0d	Tue 4/7/26	Tue 4/7/26	0d
140	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Tue 3/31/26	Thu 4/9/26	-7.5d	Mon 4/13/26	Thu 4/23/26	-7.5d
141	Install and Wire Panels	15 days	15 days	0d	Tue 4/14/26	Thu 4/23/26	-7.5d	Mon 5/4/26	Thu 5/14/26	-7.5d
142	Permanent Power On	0 days	0 days	0d	Mon 5/4/26	Thu 5/14/26	-7.5d	Mon 5/4/26	Thu 5/14/26	-7.5d
143	FRAGNET - RFI 35 - Light Fixture Mounting Height Clarification Submitted/Closed,	3 days	3 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Tue 3/17/26	Tue 3/17/26	0d
144	Electric Lights, Devices and Trim	55 days	55 days	0d	Tue 3/31/26	Thu 4/9/26	-7.5d	Tue 6/16/26	Fri 6/26/26	-7.5d
145	Fire Alarm System	3 days	3 days	0d	Tue 5/5/26	Thu 5/14/26	-7.5d	Thu 5/7/26	Tue 5/19/26	-7.5d
146	Electrical Commissioning	5 days	5 days	0d	Wed 6/17/26	Fri 6/26/26	-7.5d	Tue 6/23/26	Mon 7/6/26	-8.5d
147	**BUILDING A**	**145 days**	**151 days**	**-6d**	**Mon 1/26/26**	**Mon 1/26/26**	**0d**	**Tue 8/18/26**	**Wed 8/26/26**	**-6d**
148	BLDG A Foundation Excavation	24 days	24 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
149	FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day	1 day	0d	Mon 2/2/26	Mon 2/2/26	0d	Mon 2/2/26	Mon 2/2/26	0d
150	BLDG A - Interoir Backfill Foundations	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Tue 3/3/26	Tue 3/3/26	0d
151	**FRAGNET - BLDG A Seepage Bed Pad Over Ex.**	**11 days**	**11 days**	**0d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Thu 3/12/26**	**Thu 3/12/26**	**0d**
152	FRAGNET -Proposed direction received from Owner to perform BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
153	FRAGNET - Prepare and Submit Pricing for Approval	8 days	8 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/10/26	Tue 3/10/26	0d
154	FRAGNET - Owner Issued CCD 06 on Seepage Bed Cost Impact	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
155	FRAGNET - Mobilize Crew for BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Tue 3/10/26	Tue 3/10/26	0d	Tue 3/10/26	Tue 3/10/26	0d
156	FRAGNET - Start BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Wed 3/11/26	Wed 3/11/26	0d	Wed 3/11/26	Wed 3/11/26	0d
157	FRAGNET - Finish BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Thu 3/12/26	Thu 3/12/26	0d	Thu 3/12/26	Thu 3/12/26	0d
158	BLDG A - Exterior Backfill Foundations	2 days	2 days	0d	Tue 3/10/26	Tue 3/10/26	0d	Wed 3/11/26	Wed 3/11/26	0d
159	BLDG A SOG Rough Grade Prep	2 days	2 days	0d	Wed 3/18/26	Wed 3/18/26	0d	Thu 3/19/26	Thu 3/19/26	0d
160	**FRAGNET - BLDG A Soft Spot Over Ex**	**20 days**	**30 days**	**-10d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Wed 3/25/26**	**Wed 4/8/26**	**-10d**
161	FRAGNET - Proposed direction received from Owner to perform BLDG A Soft Spot Repairs Using Only Pit Run	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
162	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
163	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
164	FRAGNET - Mobilize Crew, SOG Rough Grade Prep, Scarify, Air Dry Pad A	5 days	5 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Thu 3/19/26	Thu 3/19/26	0d
165	FRAGNET - Air Dry Pad A, Re-Prep, Proof Roll to Idendify Soft Spots	2 days	7 days	-5d	Fri 3/20/26	Fri 3/20/26	0d	Mon 3/23/26	Mon 3/30/26	-5d
166	FRAGNET - Start Soft Spot Repairs	0 days	1 day	-1d	Mon 3/23/26	Tue 3/31/26	-6d	Mon 3/23/26	Tue 3/31/26	-6d
167	FRAGNET - Test and Review Compaction Results for Soft Spot - If Approved, Proceed with Direction Further	1 day	1 day	0d	Tue 3/24/26	Wed 4/1/26	-6d	Tue 3/24/26	Wed 4/1/26	-6d
168	FRAGNET - Soft Spot Repairs East Area	1 day	5 days	-4d	Tue 3/24/26	Thu 4/2/26	-7d	Tue 3/24/26	Wed 4/8/26	-11d
169	FRAGNET - Soft Spot Repairs West Area	1 day	5 days	-4d	Wed 3/25/26	Thu 4/2/26	-6d	Wed 3/25/26	Wed 4/8/26	-10d
170	**CONCRETE WORK**	**50 days**	**56 days**	**-6d**	**Wed 2/4/26**	**Wed 2/4/26**	**0d**	**Tue 4/14/26**	**Wed 4/22/26**	**-6d**
171	BLDG A Foundation	18 days	18 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Fri 2/27/26	Fri 2/27/26	0d

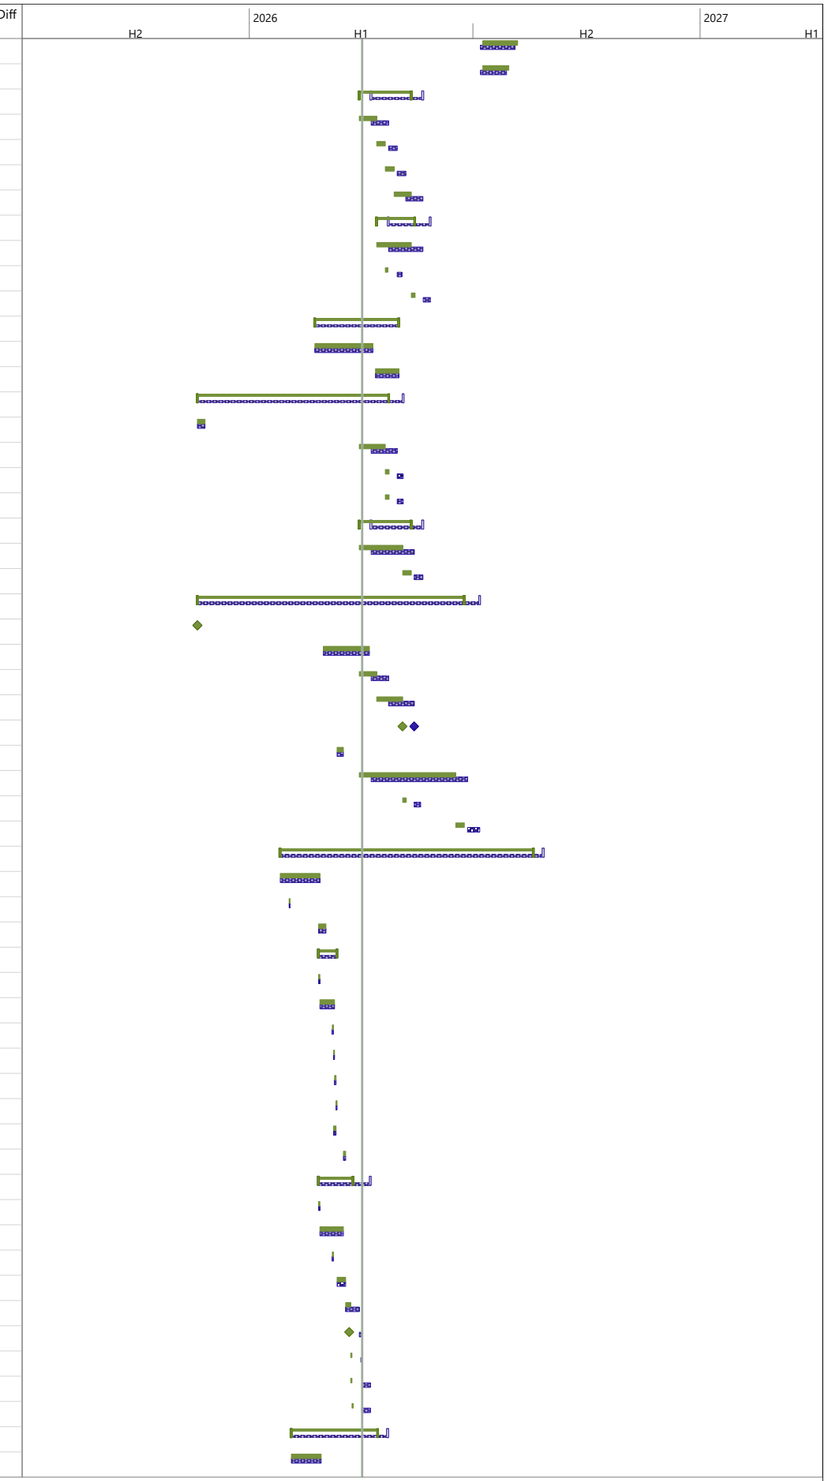
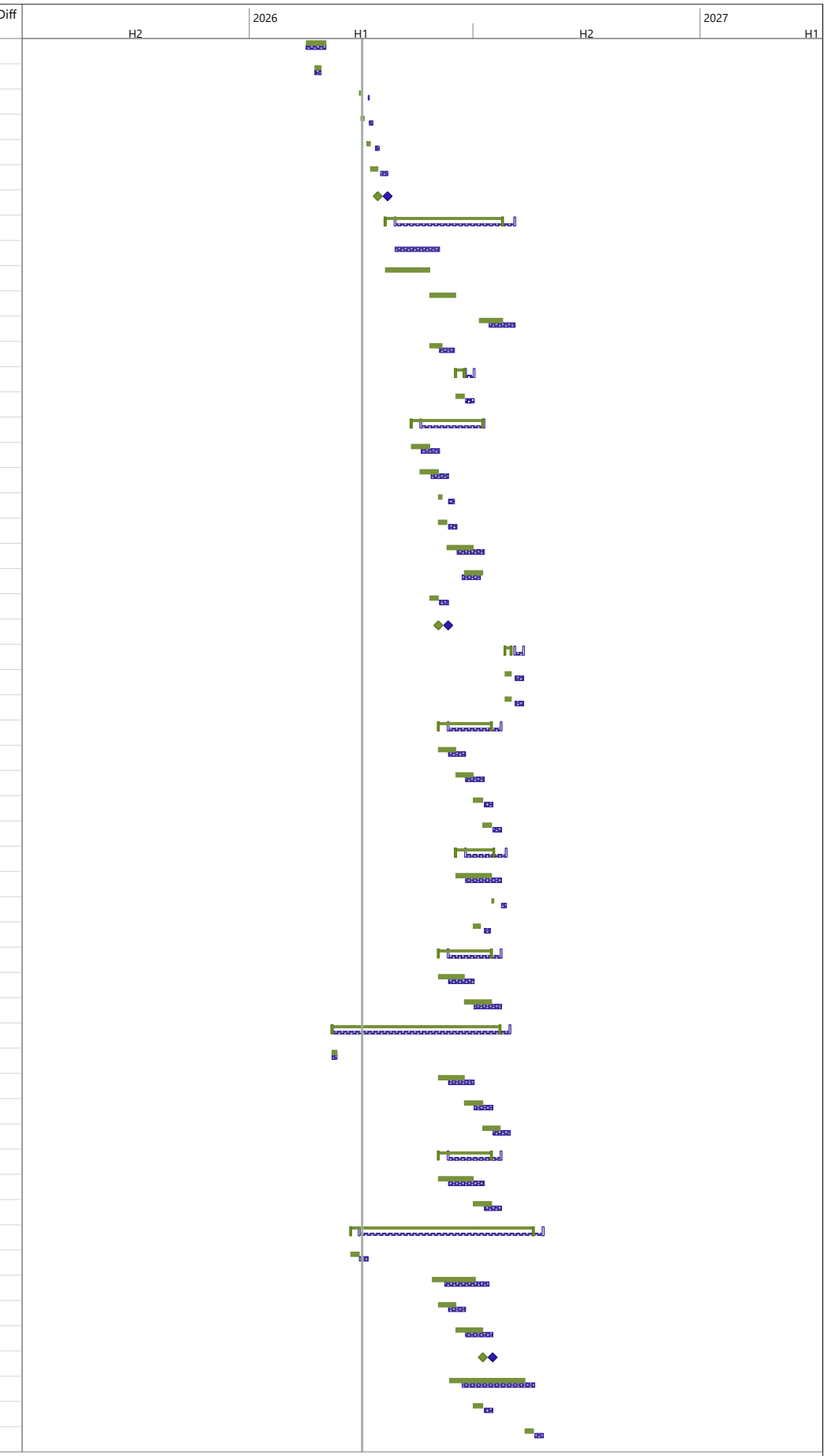
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
172	BLDG A Dampproofing	4 days	4 days	0d	Mon 2/16/26	Mon 2/16/26	0d	Tue 3/3/26	Tue 3/3/26	0d
173	BLDG A Exterior Footing Insulation	5 days	5 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 2/27/26	Fri 2/27/26	0d
174	BLDG A SOG Fine Prep	1 day	1 day	0d	Tue 3/31/26	Tue 4/7/26	-5d	Tue 3/31/26	Tue 4/7/26	-5d
175	BLDG A Slab On Grade (East)	3 days	3 days	0d	Wed 4/1/26	Wed 4/8/26	-5d	Fri 4/3/26	Fri 4/10/26	-5d
176	BLDG A Slab On Grade (Center)	3 days	3 days	0d	Mon 4/6/26	Mon 4/13/26	-5d	Wed 4/8/26	Wed 4/15/26	-5d
177	BLDG A Slab On Grade (West)	4 days	4 days	0d	Thu 4/9/26	Fri 4/17/26	-6d	Tue 4/14/26	Wed 4/22/26	-6d
178	BLDG A Slab On Grade Complete	0 days	0 days	0d	Tue 4/14/26	Wed 4/22/26	-6d	Tue 4/14/26	Wed 4/22/26	-6d
179	**STEEL AND METALS**	**67 days**	**67 days**	**0d**	**Tue 4/21/26**	**Wed 4/29/26**	**-6d**	**Fri 7/24/26**	**Mon 8/3/26**	**-6d**
180	Frame & Panel Load Bearing & Shear Walls (JANUS)		25 days			Wed 4/29/26			Wed 6/3/26	
181	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	25 days			Tue 4/21/26			Tue 5/26/26		
182	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	15 days			Wed 5/27/26			Tue 6/16/26		
183	Perimeter Panel Interior Walls (JANUS)	15 days	15 days	0d	Mon 7/6/26	Tue 7/14/26	-6d	Fri 7/24/26	Mon 8/3/26	-6d
184	Canopy Install	8 days	8 days	0d	Wed 5/27/26	Thu 6/4/26	-6d	Fri 6/5/26	Mon 6/15/26	-6d
185	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Wed 6/17/26**	**Thu 6/25/26**	**-6d**	**Tue 6/23/26**	**Wed 7/1/26**	**-6d**
186	Misc Finish Carpentry	5 days	5 days	0d	Wed 6/17/26	Thu 6/25/26	-6d	Tue 6/23/26	Wed 7/1/26	-6d
187	**ROOF & SIDING**	**40 days**	**35 days**	**5d**	**Tue 5/12/26**	**Wed 5/20/26**	**-6d**	**Wed 7/8/26**	**Thu 7/9/26**	**-1d**
188	Exterior Sheathing	10 days	10 days	0d	Tue 5/12/26	Wed 5/20/26	-6d	Tue 5/26/26	Wed 6/3/26	-6d
189	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	10 days	10 days	0d	Tue 5/19/26	Thu 5/28/26	-7d	Tue 6/2/26	Wed 6/10/26	-6d
190	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Fri 6/5/26	Mon 6/15/26	-6d
191	Rigid Insulation Behind CMU	5 days	5 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/9/26	Wed 6/17/26	-6d
192	CMU Veneer	15 days	15 days	0d	Wed 6/10/26	Thu 6/18/26	-6d	Tue 6/30/26	Thu 7/9/26	-7d
193	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Wed 6/24/26	Mon 6/22/26	2d	Wed 7/8/26	Mon 7/6/26	2d
194	Install Roof & Roof Insulation (JANUS)	5 days	5 days	0d	Wed 5/27/26	Thu 6/4/26	-6d	Tue 6/2/26	Wed 6/10/26	-6d
195	BLDG A Roofing Complete	0 days	0 days	0d	Tue 6/2/26	Wed 6/10/26	-6d	Tue 6/2/26	Wed 6/10/26	-6d
196	**DOORS & WINDOWS**	**5 days**	**5 days**	**0d**	**Mon 7/27/26**	**Tue 8/4/26**	**-6d**	**Fri 7/31/26**	**Mon 8/10/26**	**-6d**
197	F&I Storage Unit Doors (JANUS)	5 days	5 days	0d	Mon 7/27/26	Tue 8/4/26	-6d	Fri 7/31/26	Mon 8/10/26	-6d
198	F&I HM Doors and Hardware (JANUS)	5 days	5 days	0d	Mon 7/27/26	Tue 8/4/26	-6d	Fri 7/31/26	Mon 8/10/26	-6d
199	**FINISHES**	**30 days**	**30 days**	**0d**	**Wed 6/3/26**	**Thu 6/11/26**	**-6d**	**Wed 7/15/26**	**Thu 7/23/26**	**-6d**
200	Install Gypsum Board	10 days	10 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/16/26	Wed 6/24/26	-6d
201	Painting	10 days	10 days	0d	Wed 6/17/26	Thu 6/25/26	-6d	Tue 6/30/26	Thu 7/9/26	-7d
202	Flooring Polished Conc.	5 days	5 days	0d	Wed 7/1/26	Fri 7/10/26	-7d	Wed 7/8/26	Thu 7/16/26	-6d
203	FRP & Vinyl Base	5 days	5 days	0d	Thu 7/9/26	Fri 7/17/26	-6d	Wed 7/15/26	Thu 7/23/26	-6d
204	**SPECIALTIES**	**22 days**	**22 days**	**0d**	**Wed 6/17/26**	**Thu 6/25/26**	**-6d**	**Fri 7/17/26**	**Mon 7/27/26**	**-6d**
205	Install Misc Equipment & Lockers	20 days	20 days	0d	Wed 6/17/26	Thu 6/25/26	-6d	Wed 7/15/26	Thu 7/23/26	-6d
206	Bathroom Accessories- Building A	2 days	2 days	0d	Thu 7/16/26	Fri 7/24/26	-6d	Fri 7/17/26	Mon 7/27/26	-6d
207	Building Interior Signage	3 days	3 days	0d	Wed 7/1/26	Fri 7/10/26	-7d	Mon 7/6/26	Tue 7/14/26	-6d
208	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**	**Wed 6/3/26**	**Thu 6/11/26**	**-6d**	**Wed 7/15/26**	**Thu 7/23/26**	**-6d**
209	Fire Sprinkler System Rough In	15 days	15 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/23/26	Wed 7/1/26	-6d
210	Fire Sprinkler System Trim Out	15 days	15 days	0d	Wed 6/24/26	Thu 7/2/26	-6d	Wed 7/15/26	Thu 7/23/26	-6d
211	**PLUMBING**	**96 days**	**102 days**	**-6d**	**Mon 3/9/26**	**Mon 3/9/26**	**0d**	**Wed 7/22/26**	**Thu 7/30/26**	**-6d**
212	Plumbing Rough-in Underground	4 days	4 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Thu 3/12/26	Thu 3/12/26	0d
213	Drains, Water, Sewer Lines	15 days	15 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/23/26	Wed 7/1/26	-6d
214	Bathroom Fixtures- Building A	10 days	10 days	0d	Wed 6/24/26	Thu 7/2/26	-6d	Wed 7/8/26	Thu 7/16/26	-6d
215	Other Plumbing Fixtures	10 days	10 days	0d	Thu 7/9/26	Fri 7/17/26	-6d	Wed 7/22/26	Thu 7/30/26	-6d
216	**HVAC**	**30 days**	**30 days**	**0d**	**Wed 6/3/26**	**Thu 6/11/26**	**-6d**	**Wed 7/15/26**	**Thu 7/23/26**	**-6d**
217	HVAC Installation	20 days	20 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/30/26	Thu 7/9/26	-7d
218	HVAC Commisioning - Building A	10 days	10 days	0d	Wed 7/1/26	Fri 7/10/26	-7d	Wed 7/15/26	Thu 7/23/26	-6d
219	**ELECTRICAL**	**104 days**	**105 days**	**-1d**	**Tue 3/24/26**	**Tue 3/31/26**	**-5d**	**Tue 8/18/26**	**Wed 8/26/26**	**-6d**
220	Building Rough-in Underground	5 days	5 days	0d	Tue 3/24/26	Tue 3/31/26	-5d	Mon 3/30/26	Mon 4/6/26	-5d
221	Electrical Rough-In	25 days	25 days	0d	Fri 5/29/26	Mon 6/8/26	-6d	Thu 7/2/26	Mon 7/13/26	-7d
222	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Wed 6/3/26	Thu 6/11/26	-6d	Tue 6/16/26	Wed 6/24/26	-6d
223	Install and Wire Panels	15 days	15 days	0d	Wed 6/17/26	Thu 6/25/26	-6d	Wed 7/8/26	Thu 7/16/26	-6d
224	Permanent Power On- Building A	0 days	0 days	0d	Wed 7/8/26	Thu 7/16/26	-6d	Wed 7/8/26	Thu 7/16/26	-6d
225	Electric Lights, Devices and Trim	42 days	42 days	0d	Fri 6/12/26	Mon 6/22/26	-6d	Tue 8/11/26	Wed 8/19/26	-6d
226	Fire Alarm System	5 days	5 days	0d	Wed 7/1/26	Fri 7/10/26	-7d	Wed 7/8/26	Thu 7/16/26	-6d
227	Electrical Commissioning	5 days	5 days	0d	Wed 8/12/26	Thu 8/20/26	-6d	Tue 8/18/26	Wed 8/26/26	-6d
