# Mt Juliet, TN

## Compare Remaining Compression

*Report Date: 01/27/2026*

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

### Schedules Analyzed

| A Earlier Data Date | B Later Data Date |
|---|---|
| **Mt. Juliet, TN - 12/02/2025** | **Mt. Juliet, TN -01/27/2026** |
| Data Date: 12/01/2025 | Data Date: 01/02/2026 |
| Finish Date: 11/03/2027 | Finish Date: 11/04/2027 |

## Remaining Work Compression 1 %

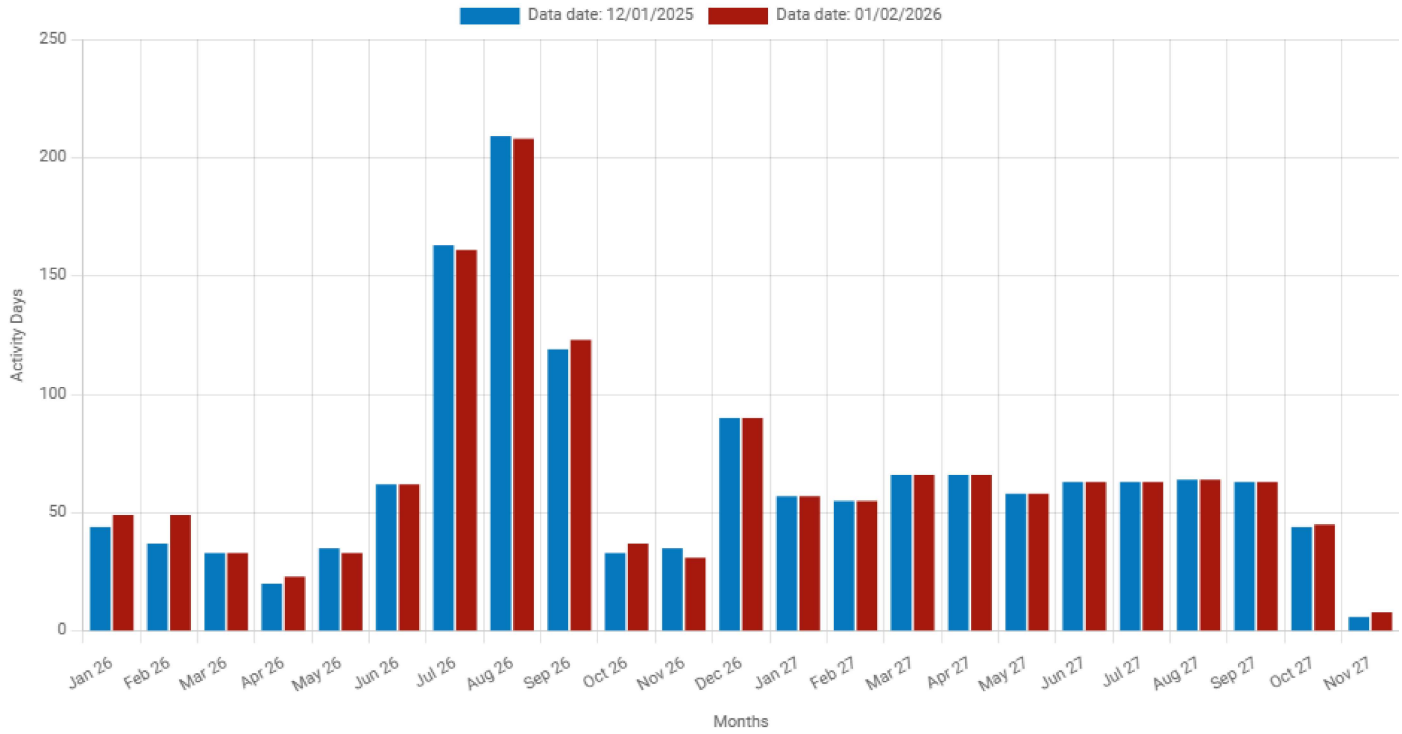


| Month | 12/01/2025 Activity Days | 01/02/2026 Activity Days |
|---|---|---|
| Jan 26 | 44 | 49 |
| Feb 26 | 37 | 49 |
| Mar 26 | 33 | 33 |
| Apr 26 | 20 | 23 |
| May 26 | 35 | 33 |
| Jun 26 | 62 | 62 |
| Jul 26 | 163 | 161 |
| Aug 26 | 209 | 208 |
| Sep 26 | 119 | 123 |
| Oct 26 | 33 | 37 |

| Month | 12/01/2025<br>Activity Days | 01/02/2026<br>Activity Days |
|---|---|---|
| Nov 26 | 35 | 31 |
| Dec 26 | 90 | 90 |
| Jan 27 | 57 | 57 |
| Feb 27 | 55 | 55 |
| Mar 27 | 66 | 66 |
| Apr 27 | 66 | 66 |
| May 27 | 58 | 58 |
| Jun 27 | 63 | 63 |
| Jul 27 | 63 | 63 |
| Aug 27 | 64 | 64 |
| Sep 27 | 63 | 63 |
| Oct 27 | 44 | 45 |
| Nov 27 | 6 | 8 |
