Mt Juliet, TN

Compare Remaining Compression

Report Date: 03/03/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Mt. Juliet, TN -01/27/2026	**Mt. Juliet, TN - 03/02/2026**
Data Date: 01/02/2026	Data Date: 01/31/2026
Finish Date: 11/04/2027	Finish Date: 11/15/2027

Remaining Work Compression 25 %

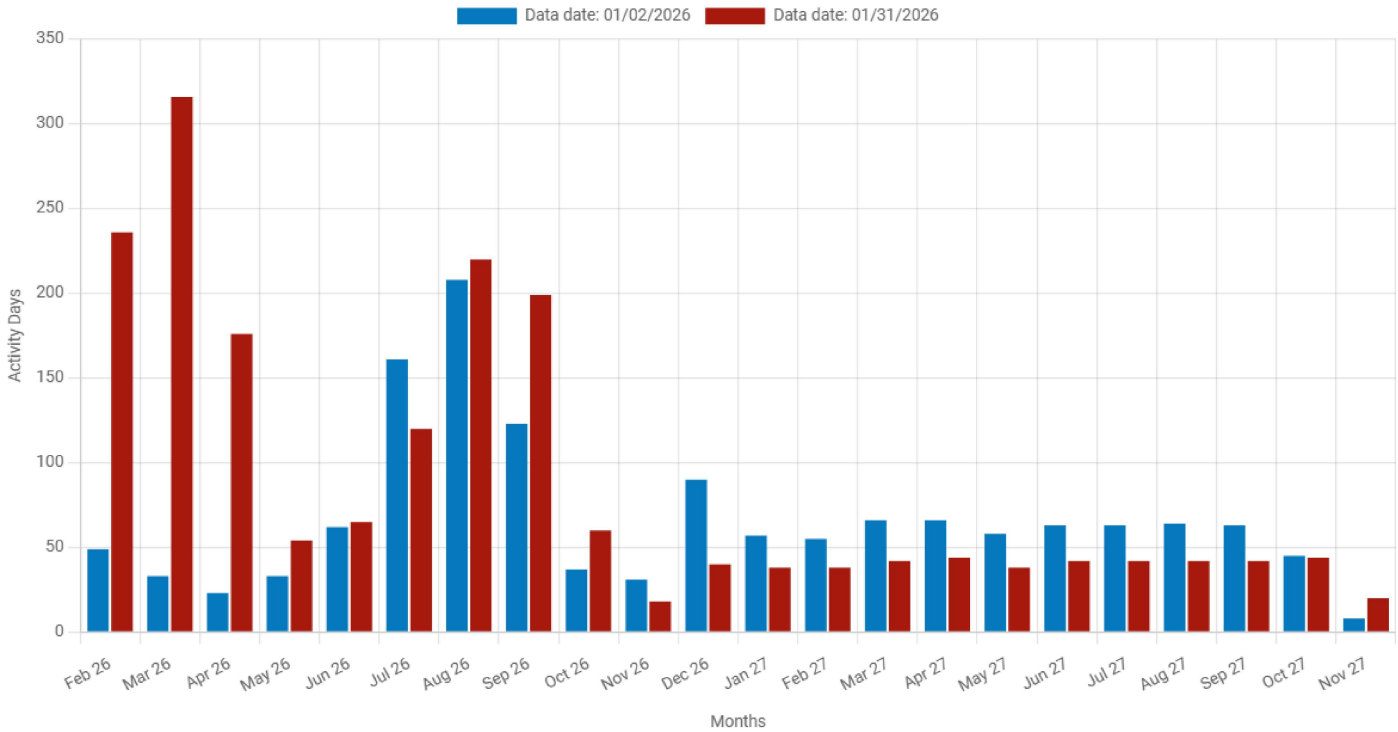

Month	01/02/2026 Activity Days	01/31/2026 Activity Days
Feb 26	49	236
Mar 26	33	316
Apr 26	23	176
May 26	33	54
Jun 26	62	65
Jul 26	161	120
Aug 26	208	220
Sep 26	123	199
Oct 26	37	60
Nov 26	31	18

Month	01/02/2026 Activity Days	01/31/2026 Activity Days
Dec 26	90	40
Jan 27	57	38
Feb 27	55	38
Mar 27	66	42
Apr 27	66	44
May 27	58	38
Jun 27	63	42
Jul 27	63	42
Aug 27	64	42
Sep 27	63	42
Oct 27	45	44
Nov 27	8	20
