Mt Juliet, TN

Compare Remaining Compression

Report Date: 03/11/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Mt. Juliet, TN - 03/02/2026	**Mt. Juliet, TN - 03/10/2026**
Data Date: 01/31/2026	Data Date: 02/24/2026
Finish Date: 11/15/2027	Finish Date: 11/12/2027

Remaining Work Compression 5 %

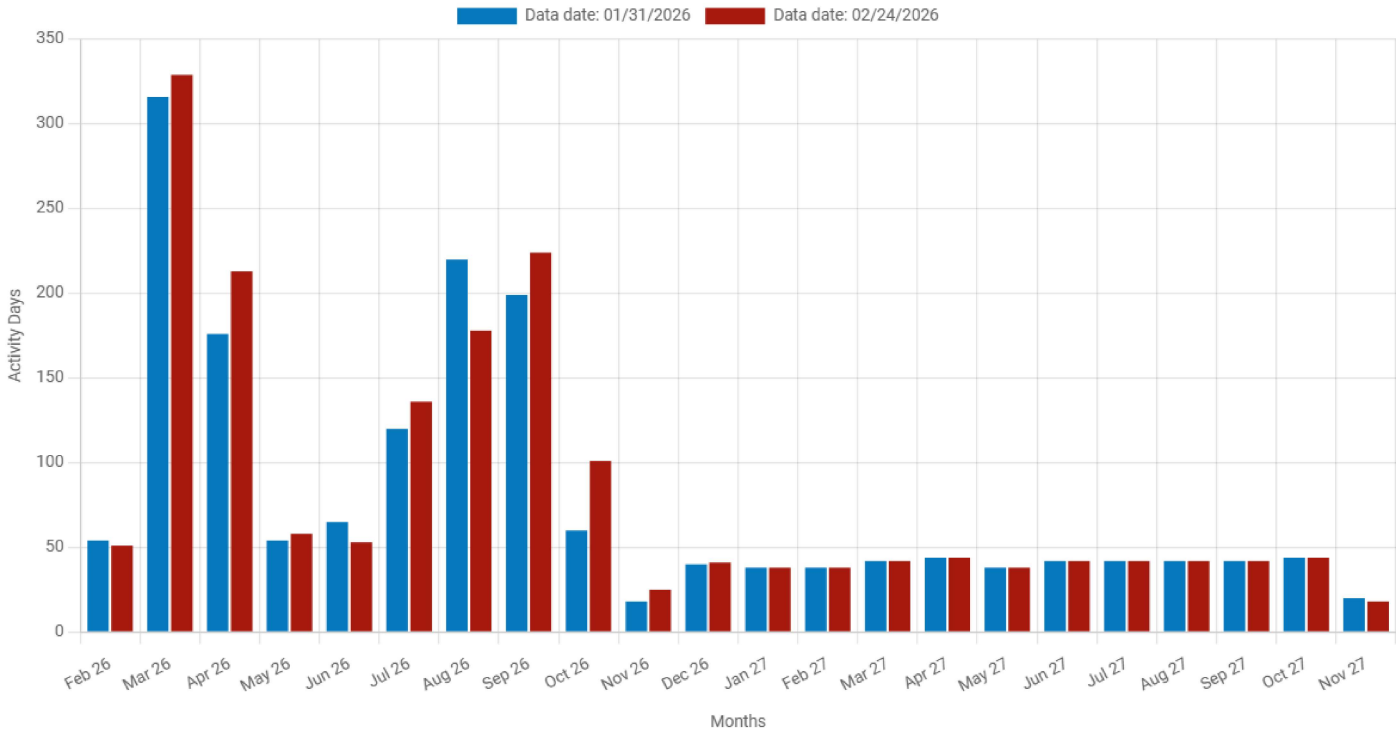

Month	01/31/2026 Activity Days	02/24/2026 Activity Days
Feb 26	54	51
Mar 26	316	329
Apr 26	176	213
May 26	54	58
Jun 26	65	53
Jul 26	120	136
Aug 26	220	178
Sep 26	199	224
Oct 26	60	101
Nov 26	18	25

Month	01/31/2026 Activity Days	02/24/2026 Activity Days
Dec 26	40	41
Jan 27	38	38
Feb 27	38	38
Mar 27	42	42
Apr 27	44	44
May 27	38	38
Jun 27	42	42
Jul 27	42	42
Aug 27	42	42
Sep 27	42	42
Oct 27	44	44
Nov 27	20	18
