Selma, AL

Compare Remaining Compression

Report Date: 02/06/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Selma, AL - 12/08/2025	**Selma, AL - 01/31/2026**
Data Date: 12/08/2025	Data Date: 01/31/2026
Finish Date: 10/09/2026	Finish Date: 10/09/2026

Remaining Work Compression -1 %

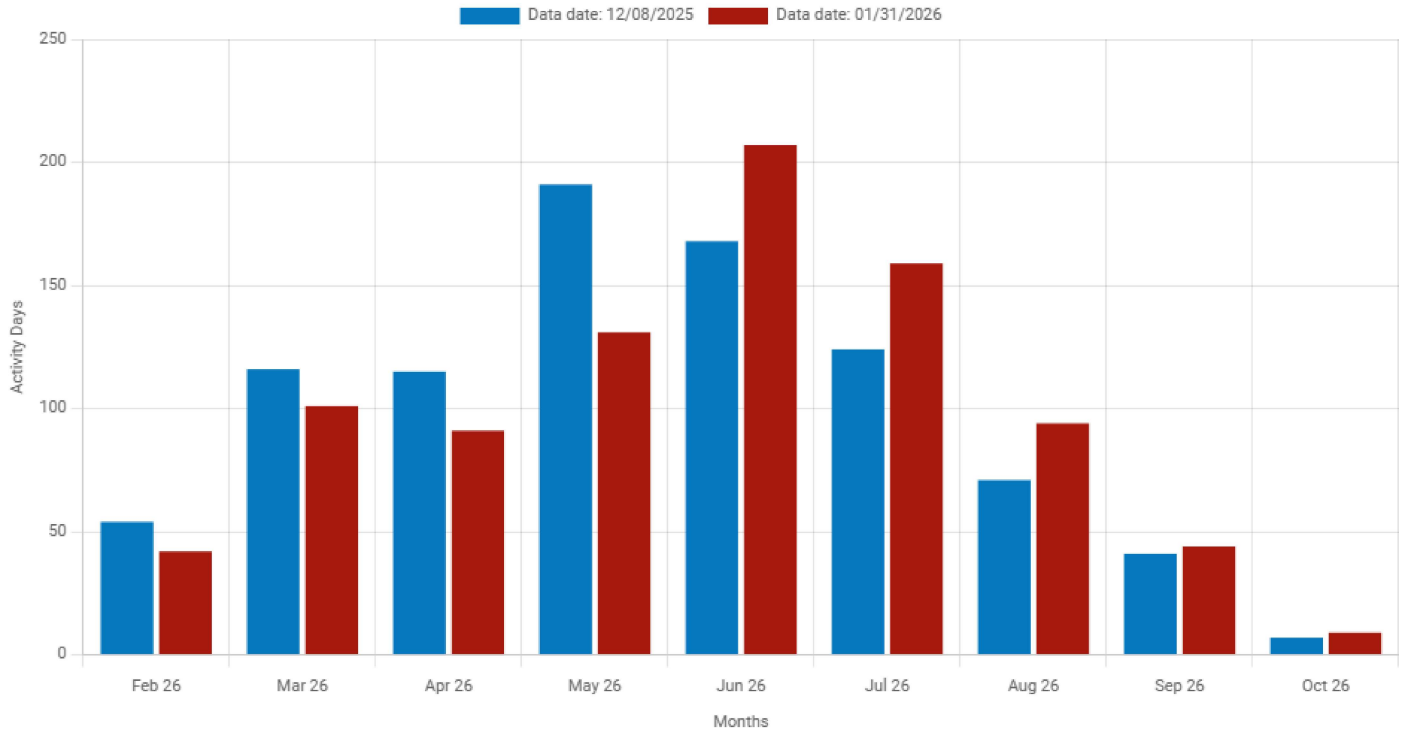

Month	12/08/2025 Activity Days	01/31/2026 Activity Days
Feb 26	54	42
Mar 26	116	101
Apr 26	115	91
May 26	191	131
Jun 26	168	207
Jul 26	124	159
Aug 26	71	94
Sep 26	41	44
Oct 26	7	9
