Selma, NC

Compare Remaining Compression

Report Date: 03/30/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Selma, NC - 03/04/2026	**Selma, NC - 03/27/2026**
Data Date: 03/04/2026	Data Date: 03/27/2026
Finish Date: 10/09/2026	Finish Date: 10/09/2026

Remaining Work Compression 2 %

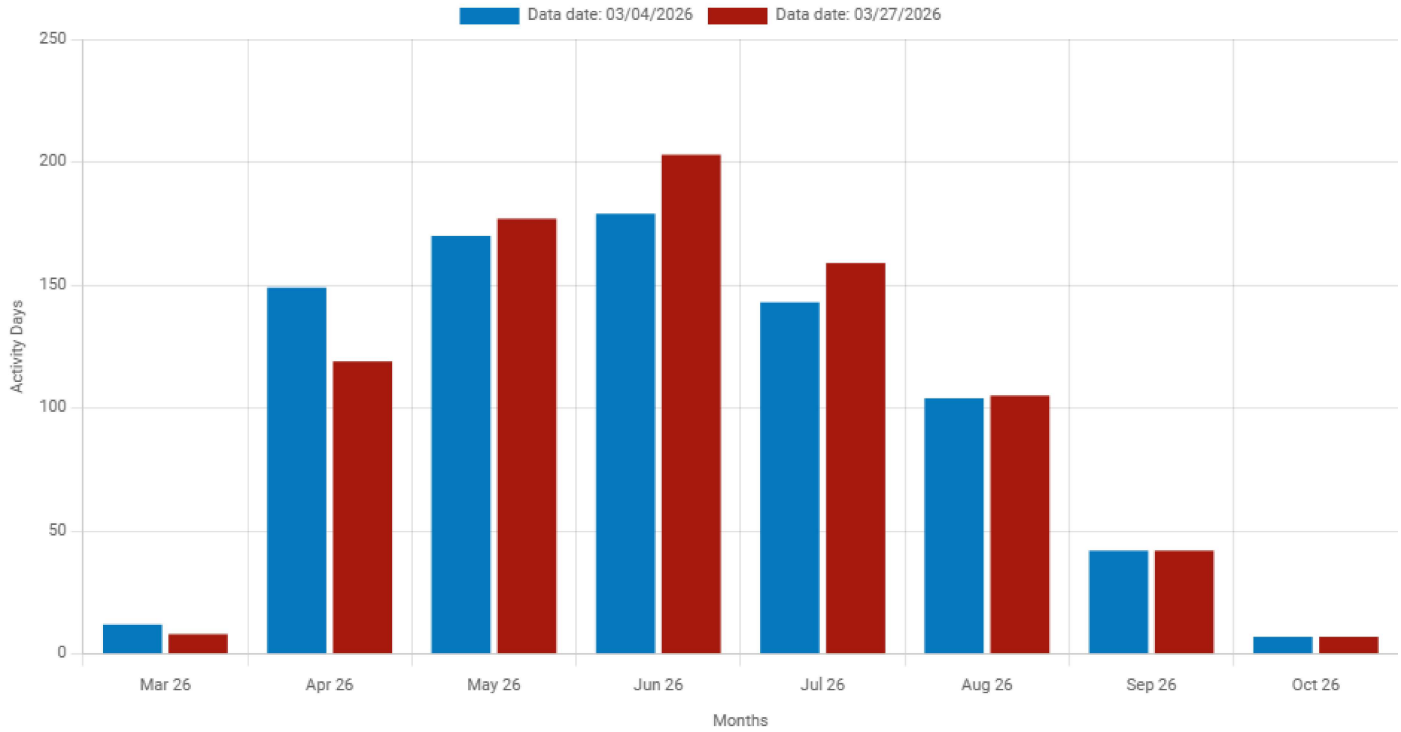

Month	03/04/2026 Activity Days	03/27/2026 Activity Days
Mar 26	12	8
Apr 26	149	119
May 26	170	177
Jun 26	179	203
Jul 26	143	159
Aug 26	104	105
Sep 26	42	42
Oct 26	7	7
