Colorado Springs, CO

Compare Remaining Compression

Report Date: 04/02/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Colorado Springs, CO - 01/30/2026	**Colorado Springs, CO - 04/01/2026**
Data Date: 01/30/2026	Data Date: 04/01/2026
Finish Date: 03/05/2026	Finish Date: 05/21/2026

Remaining Work Compression 100%

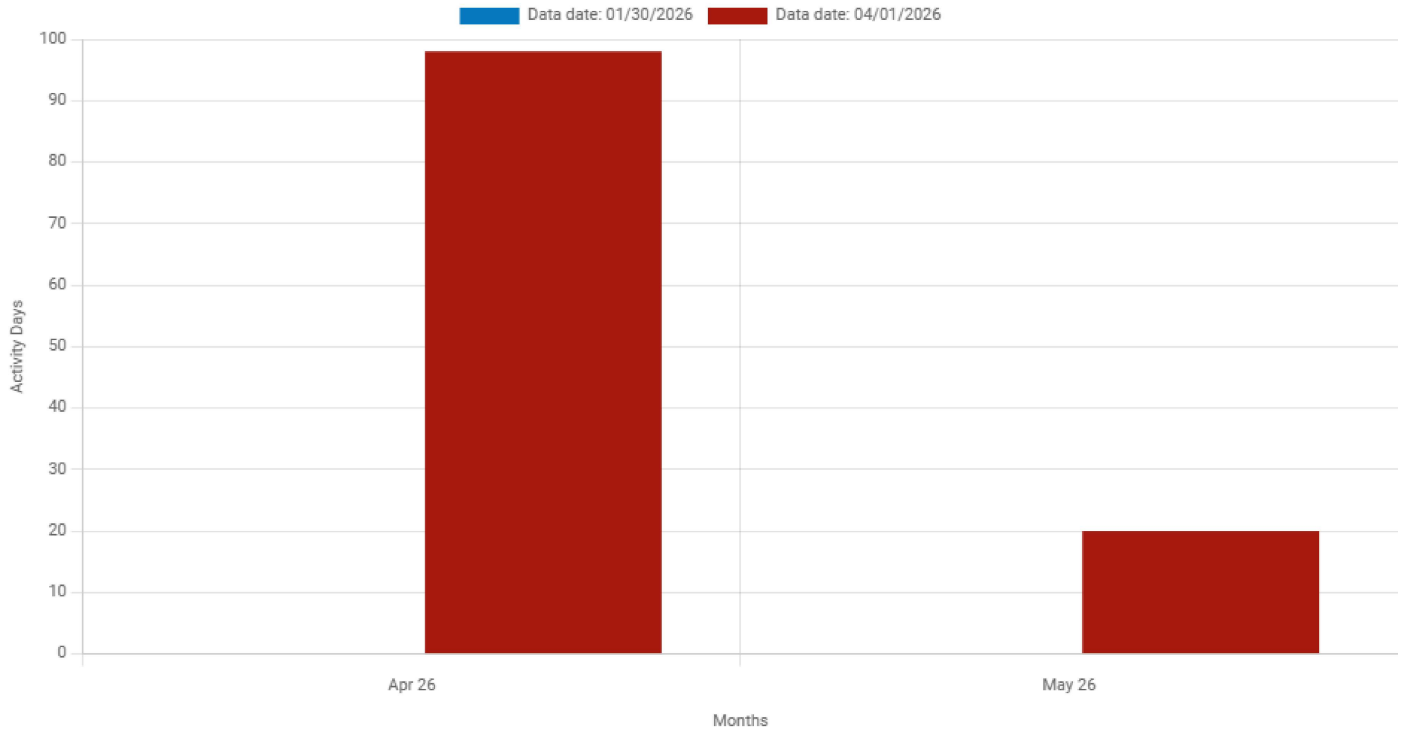

Month	01/30/2026 Activity Days	04/01/2026 Activity Days
Apr 26	0	98
May 26	0	20
