Fairfax, VA

Compare Remaining Compression

Report Date: 01/19/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Fairfax, VA - 10/31/2025	**Fairfax, VA - 12/31/2025**
Data Date: 10/31/2025	Data Date: 12/31/2025
Finish Date: 09/15/2026	Finish Date: 09/11/2026

Remaining Work Compression 22 %

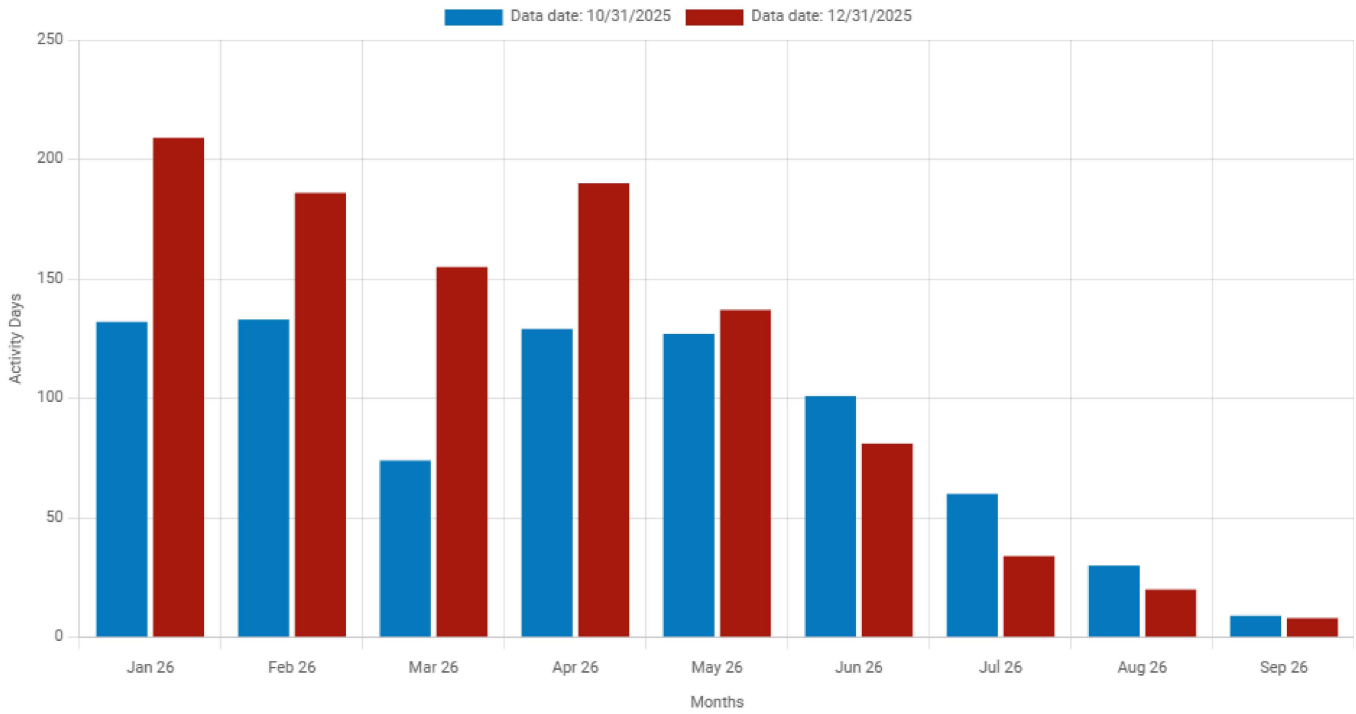

Month	10/31/2025 Activity Days	12/31/2025 Activity Days
Jan 26	132	209
Feb 26	133	186
Mar 26	74	155
Apr 26	129	190
May 26	127	137
Jun 26	101	81
Jul 26	60	34
Aug 26	30	20
Sep 26	9	8
