ID		Task Mode	Task Name	Duration	% Complete	Start	Finish	2 A
1			**Four Corners**	**300 days**	**0%**	**Fri 25/09/26**	**Fri 26/11/20**	
2			**Land Acquisition**	**0 days**	**0%**	**Tue 25/10/07**	**Tue 25/10/07**	
3			Purchase Property	0 days	0%	Tue 25/10/07	Tue 25/10/07	
4			**Design Documents**	**64 days**	**0%**	**Fri 25/09/26**	**Thu 25/12/25**	
5			**Civil**	**12 days**	**0%**	**Fri 25/09/26**	**Wed 25/10/1**	
6			60% CDs - Civil	0 days	0%	Fri 25/09/26	Fri 25/09/26	
7			90% CDs - Civil	0 days	0%	Wed 25/10/1	Wed 25/10/1	
8			**Architecture**	**45 days**	**0%**	**Fri 25/10/24**	**Thu 25/12/25**	
9			Kick off Meeting - Architecture	0 days	0%	Fri 25/10/24	Fri 25/10/24	
10			35% CDs - Architecture	15 days	0%	Fri 25/10/24	Thu 25/11/13	
11			90% CDs - Architecture	30 days	0%	Fri 25/11/14	Thu 25/12/25	
12			90% CDs - Architecture Complete	0 days	0%	Thu 25/12/25	Thu 25/12/25	
13			**Permitting**	**288 days**	**0%**	**Wed 25/10/1**	**Fri 26/11/20**	
14			**Lake County Site Plan Review**	**148 days**	**0%**	**Wed 25/10/1**	**Fri 26/05/08**	
15			1st Submittal/Sufficency Review	18 days	0%	Wed 25/10/1	Fri 25/11/07	
16			1st Review	30 days	0%	Mon 25/11/1	Fri 25/12/19	
17			1st Round Plan Revisions	20 days	0%	Mon 25/12/2	Fri 26/01/16	
18			2nd Submittal	0 days	0%	Fri 26/01/16	Fri 26/01/16	
19			2nd Review	30 days	0%	Mon 26/01/1	Fri 26/02/27	
20			2nd Round Plan Revisions	15 days	0%	Mon 26/03/0	Fri 26/03/20	
21			3rd Submittal	0 days	0%	Fri 26/03/20	Fri 26/03/20	
22			3rd Review & Approval	20 days	0%	Mon 26/03/2	Fri 26/04/17	
23			Site Placard Issued	15 days	0%	Mon 26/04/2	Fri 26/05/08	

Project: Four Corners - 102425
Date: Tue 25/11/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	% Complete	Start	Finish	2 A
24			**SWFWMD Storm Water Review**	**75 days**	**0%**	**Wed 25/10/1**	**Tue 26/01/2**	
25			1st Submittal	5 days	0%	Wed 25/10/1	Tue 25/10/21	
26			1st Review	30 days	0%	Wed 25/10/2	Tue 25/12/02	
27			1st Round Plan Revisions	15 days	0%	Wed 25/12/0	Tue 25/12/23	
28			2nd Review / Approval	25 days	0%	Wed 25/12/2	Tue 26/01/27	
29			**Building Permit**	**155 days**	**0%**	**Mon 26/04/2**	**Fri 26/11/20**	
30			Building Permit Review - 1st Round	45 days	0%	Mon 26/04/2	Fri 26/06/19	
31			Revise Plans per AHJ & Peer Review Comments	10 days	0%	Mon 26/06/2	Fri 26/07/03	
32			Building Permit Review - 2nd Round	45 days	0%	Mon 26/07/0	Fri 26/09/04	
33			Revise Plans per AHJ Comments	10 days	0%	Mon 26/09/0	Fri 26/09/18	
34			Building Permit Review - 3rd Round	45 days	0%	Mon 26/09/2	Fri 26/11/20	
35			Building Permit Approval	0 days	0%	Fri 26/11/20	Fri 26/11/20	
36			**GC Selection Process**	**61 days**	**0%**	**Mon 26/07/0**	**Mon 26/09/2**	
37			Compile Bid Set	1 day	0%	Mon 26/07/0	Mon 26/07/0	
38			Issue RFP	1 wk	0%	Tue 26/07/07	Mon 26/07/1	
39			GC Bid Period	4 wks	0%	Tue 26/07/14	Mon 26/08/1	
40			Bid Walk	0 days	0%	Mon 26/08/1	Mon 26/08/1	
41			Compile REIC 3 Package	2 wks	0%	Tue 26/08/11	Mon 26/08/2	
42			REIC 3 Memo Approval	5 days	0%	Tue 26/08/25	Mon 26/08/3	
43			eBuilder Budget Approval	10 days	0%	Tue 26/09/01	Mon 26/09/1	
44			GC Contract Issuance	2 wks	0%	Tue 26/09/15	Mon 26/09/2	

Project: Four Corners - 102425
Date: Tue 25/11/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

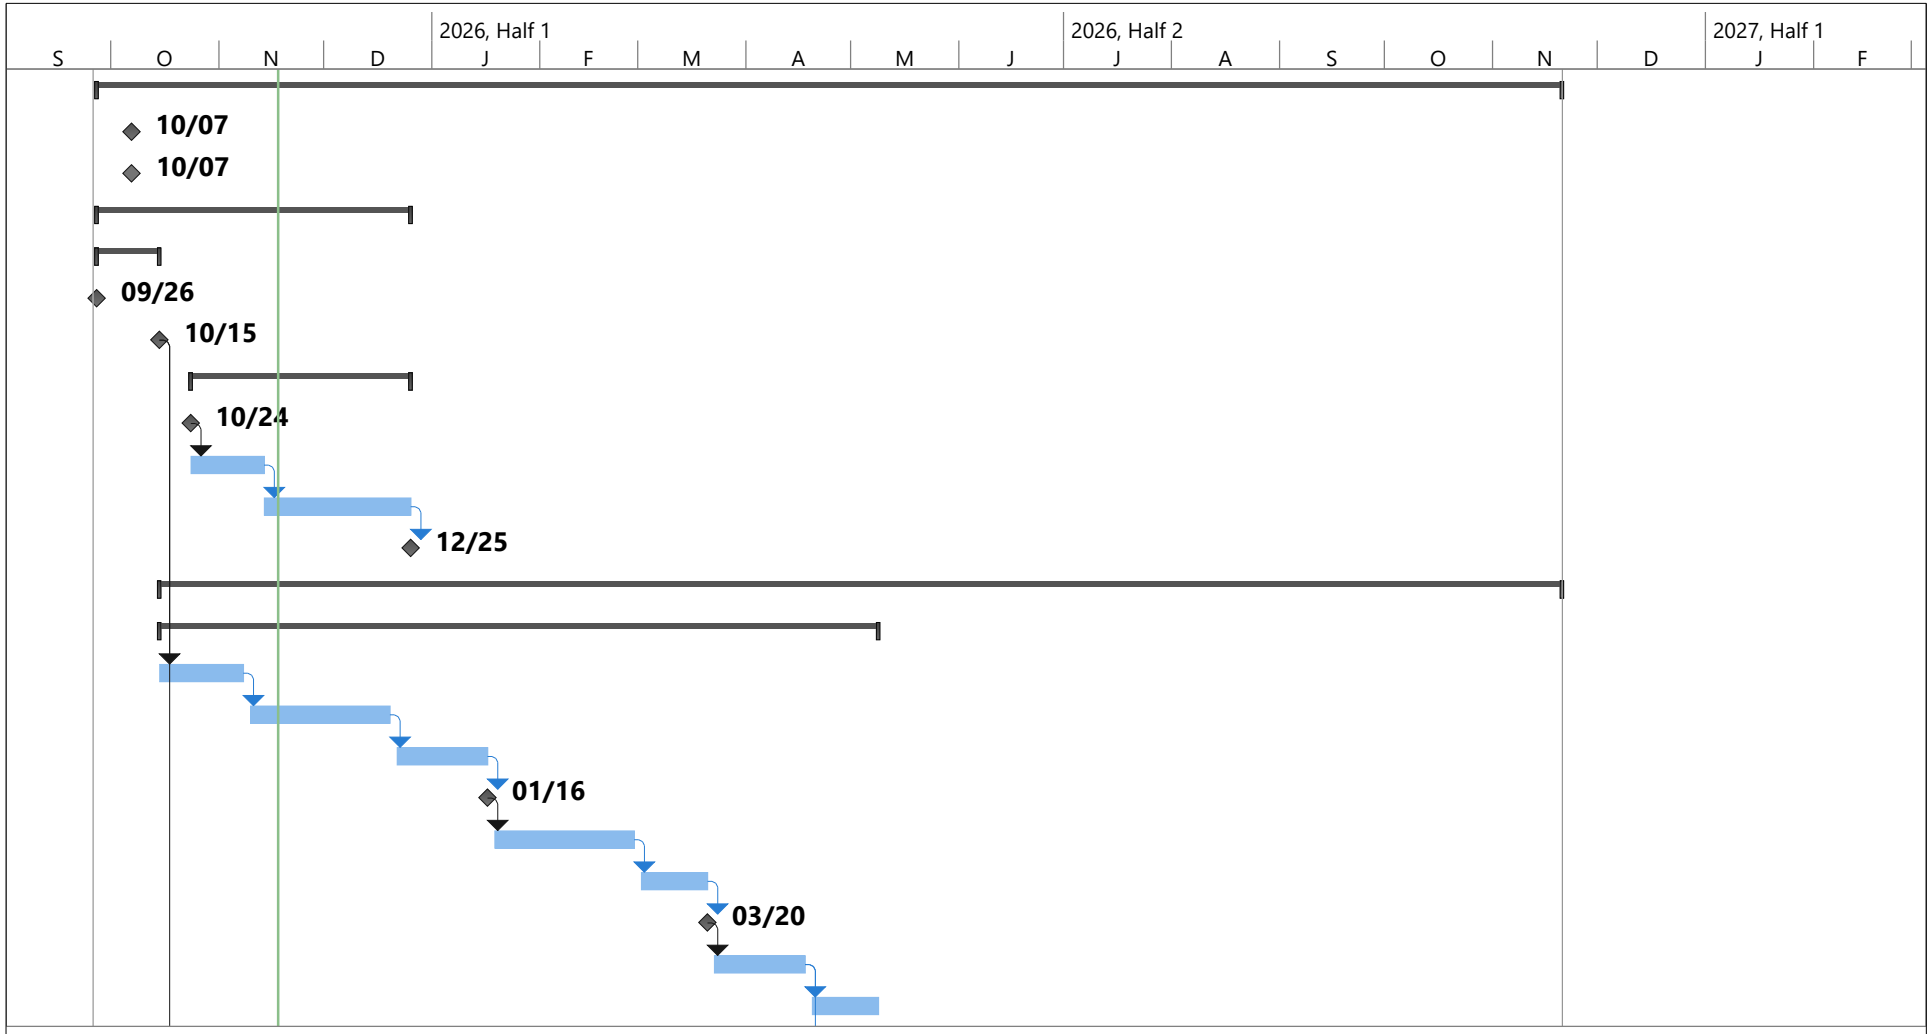

Project: Four Corners - 102425
Date: Tue 25/11/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

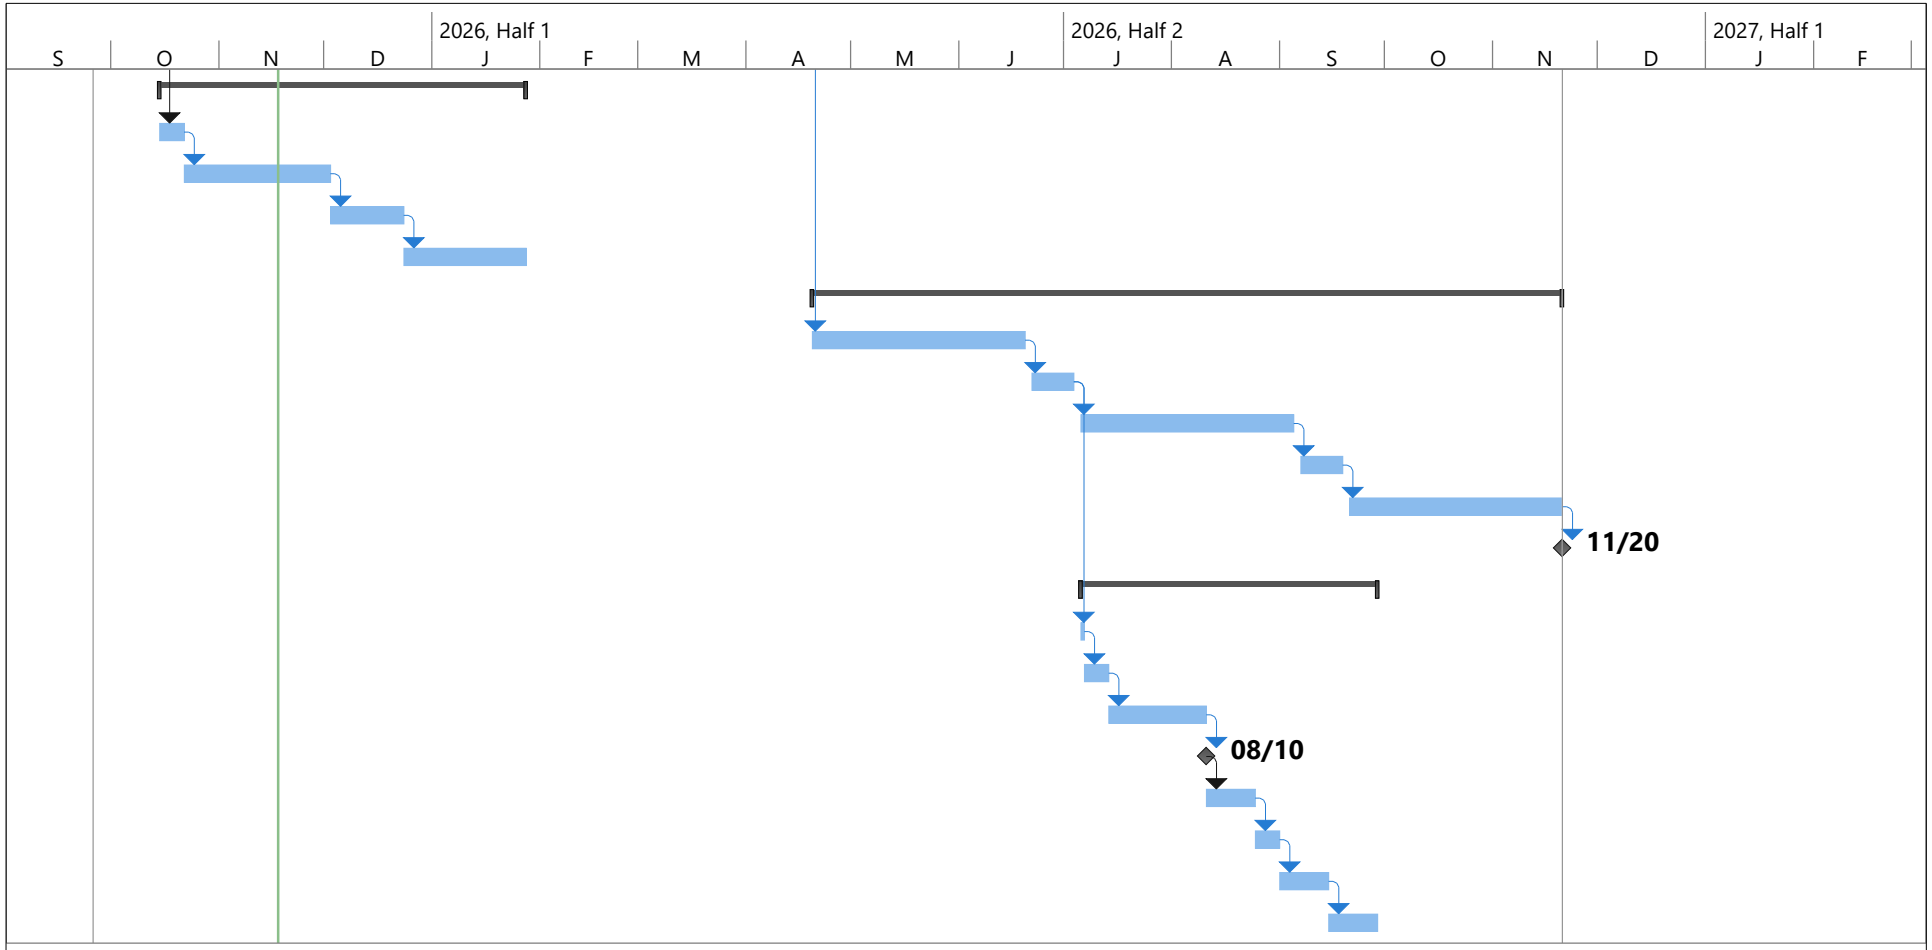

Project: Four Corners - 102425
Date: Tue 25/11/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
