Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 12/1/2025

Type	Project	Region	Responsible
Construction	Mt Juliet, TN	Central	Brendan Blair

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
30 Nov 2026	16 Dec 2026	-16 Baseline 0 Previous	Remaining Work Compression: 2%— Normal

Milestone Variance

First Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	11 Sep 2025	9/11/2025	9/11/2025	0	0	Notice to Proceed	On Track – Gaining
Foundation Complete	16 Feb 2026	2/3/2026	2/4/2026	12	-1	Footings & Foundation CIP Walls (includes elevator pit)	On Track – Slipping
Structure Top Out	05 Jun 2026	5/22/2026	5/26/2026	10	-4	Structure Complete	On Track – Slipping
Weather Tight	14 Jul 2026	6/30/2026	7/1/2026	13	-1	Building Dry In	On Track – Slipping
Elevator Complete	17 Sep 2026	9/3/2026	9/28/2026	-11	-25	Evelvator Installation (incl. Equipment Room Buildout)	Delayed – Slipping
Hardscape/Landscape Complete	26 Oct 2026	11/16/2026	11/17/2026	-22	-1	Final Owner Punch List	Delayed – Slipping
Project Substantial Completion	30 Nov 2026	12/16/2026	12/16/2026	-16	0	Project Sustainability Complete - After Weather Impacts	Delayed – Gaining

Baseline Variance

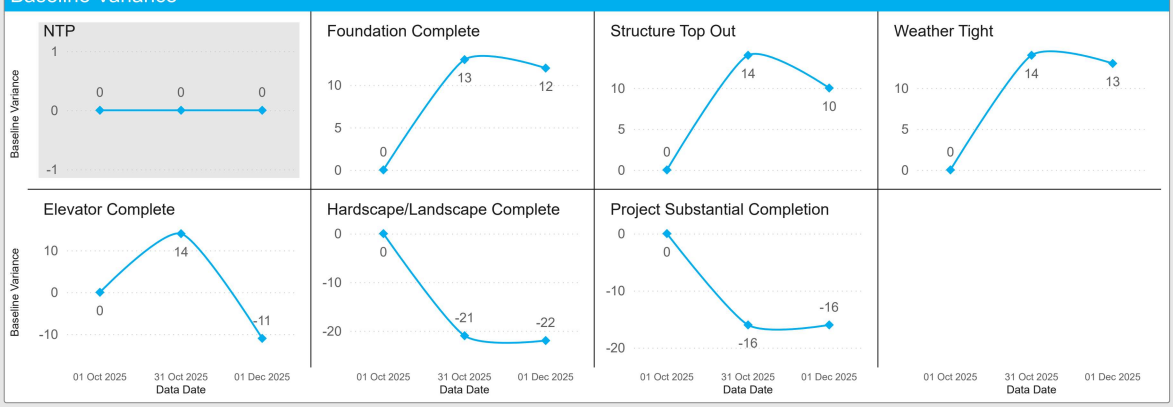

Schedule Performance Summary

Summary

The current project schedule reveals significant issues with schedule quality and execution, all of which are contributing to substantial delays and instability. The critical task now is to undertake a thorough analysis of the reasons behind these deviations and to implement corrective measures urgently to steer the project back on course. Immediate attention to the schedule validation, finish variance, and critical path variance can contribute significantly to recovering the timeline and avoiding further slippage.

Schedule Health Score: Score: 73 — Alert
The schedule's overall quality and technical soundness fall significantly below industry standards, indicating potential issues in forecasting and critical path integrity. This requires immediate comprehensive review and remediation to enhance reliability.

Finish Variance: 63% — Alert
The project is currently projected to finish significantly later than planned, jeopardizing the ability to meet original deadlines. Immediate revisiting of project scheduling and resource allocation is necessary to mitigate further delays.

Critical Path Variance: 73% — Alert
The critical path duration has slipped considerably from the baseline, suggesting major schedule disruptions that could further delay project completion. Swift action is required to analyze the reasons behind these delays and adjust the schedule accordingly.

Execution Score: 38 — Alert
Project activities are not aligning with the planned schedule, indicating poor execution practices and potential for further project delays. Enhancing daily management and oversight of schedule adherence is crucial.

Remaining Work Compression: 2%— Normal
Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea… by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedule Change Index: 6% — Warning
The schedule has undergone more changes than is typically recommended, pointing to possible planning and stability issues. Monitoring and possibly revising the planning process may help stabilize the schedule.

Powered By STELIC INSIGHT • ACTION • IMPACT
