Executive Landing Page

Public Storage Dashboard

Data Date: 2026/02/03

Type	Project	Region	Responsible
Construction	Frisco, TX	Central	Matthew Hobson

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
6/1/2026	6/2/2026	-1 Baseline -1 Previous	Remaining Work Compression: 55% — ALERT

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	1/8/2026	1/8/2026	1/8/2026	0	0	Contract Execution	On Track – Gaining
Elevator Complete	3/3/2026	3/3/2026	3/30/2026	-27	-27	Elevator Modernization	Delayed – Slipping
Contract Completion	6/1/2026	6/1/2026	6/2/2026	-1	-1	Move In	Delayed – Slipping

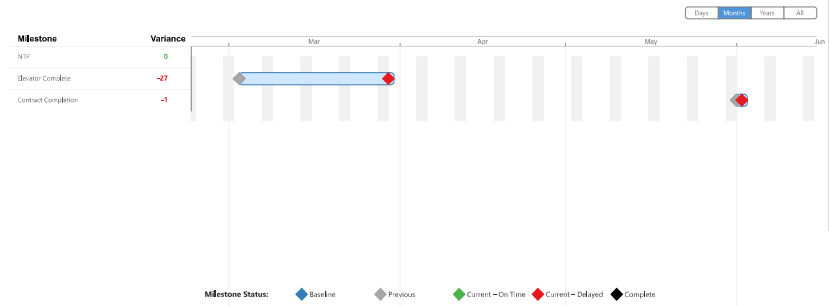

Baseline Variance

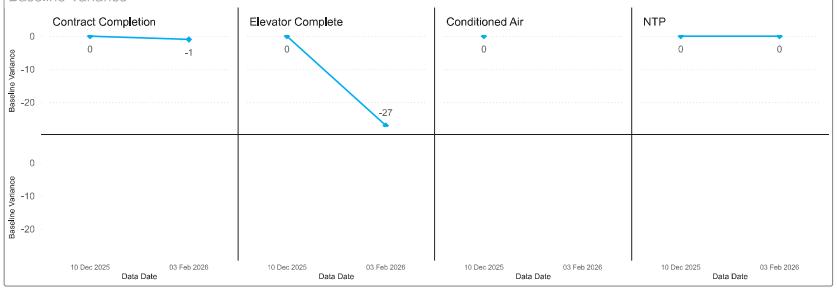

Schedule Performance Summary

Summary

This schedule exhibits severe technical, planning, and execution deficiencies, exposing the project to major delivery risks and loss of control. Immediate intervention is required to stabilize planning processes, improve schedule quality, and restore disciplined execution; failure to act will likely result in compounding delays and contract performance threats.

Execution Score: 0,00 — ALERT

There is an extreme breakdown in schedule-driven execution, with minimal or no evidence that planned activities are being started or completed as expected. This presents high risk of unmanaged work and continued slippage unless urgent corrective action is taken.

Remaining Work Compression: 55% — ALERT

Over half of the remaining activities are compressed relative to their original durations, suggesting unsustainable acceleration that is likely to impact quality and increase the risk of failure to deliver.

Schedule Change Index: 100,00 — ALERT

All activities have experienced logic or date changes since the last update, signaling extreme schedule volatility. Such wholesale changes undermine forecast reliability and call for improved planning discipline and change management.

Schedule Validation Score: 53,00 — ALERT

The SV Score is critically low, indicating significant deficiencies in schedule logic, technical soundness, or adherence to industry best practices. Immediate in-depth review and remediation of schedule quality are necessary to restore reliability.

Powered By STELIC INSIGHT+ACTION=IMPACT
