San Diego, CA

Compare Remaining Compression

Report Date: 12/22/2025

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
32504 IMI Engineering-Master Schedule 2-13-25 - GW	**32504 IMI Engineering-Master Schedule 2-13-25 - GW**
Data Date: 05/27/2025	Data Date: 12/09/2025
Finish Date: 10/23/2026	Finish Date: 11/03/2026

Remaining Work Compression -17 %

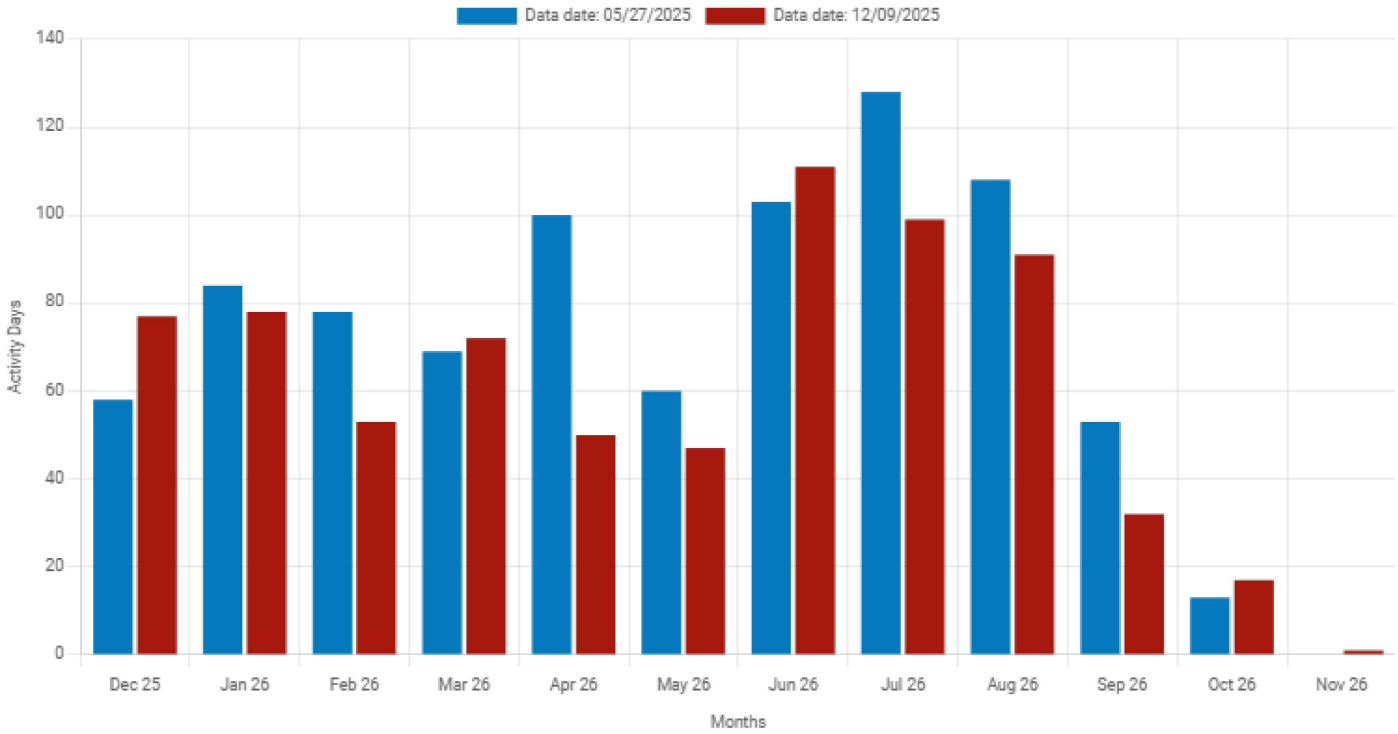

Month	05/27/2025 Activity Days	12/09/2025 Activity Days
Dec 25	58	77
Jan 26	84	78
Feb 26	78	53
Mar 26	69	72
Apr 26	100	50
May 26	60	47
Jun 26	103	111
Jul 26	128	99
Aug 26	108	91
Sep 26	53	32

Month	05/27/2025	12/09/2025
	Activity Days	Activity Days
Oct 26	13	17
Nov 26	0	1
