	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Contract Administration**	**40 days**	**40 days**	**0d**	**Wed 7/9/25**	**Wed 7/9/25**	**0d**	**Tue 9/2/25**	**Tue 9/2/25**	**0d**
2	Notice to Proceed	34 days	34 days	0d	Wed 7/9/25	Wed 7/9/25	0d	Mon 8/25/25	Mon 8/25/25	0d
3	Mobilization	1 day	1 day	0d	Tue 8/26/25	Tue 8/26/25	0d	Tue 9/2/25	Tue 9/2/25	0d
4	**Procurement**	**291 days**	**296 days**	**-5d**	**Thu 8/7/25**	**Thu 8/7/25**	**0d**	**Thu 9/17/26**	**Thu 9/24/26**	**-5d**
5	033000 - CIP - Product Data/Material Certificates, Submittal	1 day	1 day	0d	Mon 8/11/25	Mon 8/11/25	0d	Wed 8/13/25	Wed 8/13/25	0d
6	033000 - CIP - Design Mixtures for Concrete, Submittal	0 days	0 days	0d	Thu 8/7/25	Thu 8/7/25	0d	Fri 8/8/25	Fri 8/8/25	0d
7	033000 - CIP - Rebar Shop Drawings, Submittal	0 days	0 days	0d	Thu 8/7/25	Thu 8/7/25	0d	Fri 8/8/25	Fri 8/8/25	0d
8	033000 - CIP - Construction Joint Layout, Submittal	10 days	10 days	0d	Tue 3/3/26	Mon 12/22/25	51d	Mon 3/16/26	Fri 1/2/26	51d
9	033000 - CIP - Slab on Grade Control Joint Layout, Submittal	10 days	11 days	-1d	Tue 3/3/26	Thu 8/7/25	148d	Mon 3/16/26	Thu 8/21/25	147d
10	033000 - CIP - Product Data/Material Certificates, Review/Approval	15 days	11 days	4d	Tue 3/3/26	Thu 8/7/25	148d	Mon 3/23/26	Thu 8/21/25	152d
11	033000 - CIP - Design Mixtures for Concrete, Review/Approval	2 days	2 days	0d	Fri 8/8/25	Fri 8/8/25	0d	Mon 8/25/25	Mon 8/25/25	0d
12	033000 - CIP - Rebar Shop Drawings, Review/Approval	31 days	31 days	0d	Fri 8/8/25	Fri 8/8/25	0d	Mon 9/22/25	Mon 9/22/25	0d
13	033000 - CIP - Construction Joint Layout, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Mon 1/5/26	51d	Mon 4/6/26	Fri 1/23/26	51d
14	033000 - CIP - Slab on Grade Control Joint Layout, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Mon 1/5/26	51d	Mon 4/6/26	Fri 1/23/26	51d
15	033300 - Concrete Sealing, Product Data, F-01 Finish, Submittals	2 days	2 days	0d	Tue 1/27/26	Mon 1/19/26	6d	Wed 1/28/26	Tue 1/20/26	6d
16	033300 - Concrete Polishing, Product Data FF-02, Submittals	2 days	2 days	0d	Tue 1/27/26	Mon 1/19/26	6d	Wed 1/28/26	Tue 1/20/26	6d
17	033300 - Concrete Sealing, Product Data, F-01 Finish, Review/Approval	15 days	15 days	0d	Tue 3/3/26	Wed 1/28/26	24d	Mon 3/23/26	Tue 2/17/26	24d
18	033300 - Concrete Polishing, Product Data FF-02, Review/Approval	15 days	15 days	0d	Tue 3/3/26	Wed 1/28/26	24d	Mon 3/23/26	Tue 2/17/26	24d
19	042000 - Unit Masonry, Product Data, Masonry Accessories, Submittal	0 days	0 days	0d	Thu 8/7/25	Thu 8/7/25	0d	Fri 8/8/25	Fri 8/8/25	0d
20	042000 - Unit Masonry, Product Data, Masonry Accessories, Review/Approval	0 days	0 days	0d	Thu 8/14/25	Thu 8/14/25	0d	Wed 9/10/25	Wed 9/10/25	0d
21	042000 Unit Masonry, Grout Mix, Submittal	0 days	0 days	0d	Thu 8/7/25	Thu 8/7/25	0d	Fri 8/8/25	Fri 8/8/25	0d
22	042000 Unit Masonry, Grout Mix, Review/Approval	0 days	0 days	0d	Tue 10/7/25	Tue 10/7/25	0d	Fri 10/10/25	Fri 10/10/25	0d
23	051200 - Structural Steel Framing, Shop Drawings, Submittal	1 day	1 day	0d	Fri 9/26/25	Fri 9/26/25	0d	Fri 9/26/25	Fri 9/26/25	0d
24	051200 - Structural Steel Framing, Shop Drawings, Review/Approval	15 days	15 days	0d	Mon 9/29/25	Mon 9/29/25	0d	Fri 10/17/25	Fri 10/17/25	0d
25	054000 - Cold Formed Metal Framing, Product Data, Submittal	2 days	11 days	-9d	Tue 9/23/25	Wed 9/10/25	9d	Wed 9/24/25	Wed 9/24/25	0d
26	054000 - Cold Formed Metal Framing, Product Data, Review/Approval	0 days	0 days	0d	Thu 9/25/25	Thu 9/25/25	0d	Fri 9/26/25	Fri 9/26/25	0d
27	054000 - Cold Formed Metal Framing, Shop Drawings, Submittal	2 days	11 days	-9d	Thu 9/25/25	Wed 9/10/25	11d	Fri 9/26/25	Wed 9/24/25	2d
28	054000 - Cold Formed Metal Framing, Shop Drawings, Review/Approval	0 days	0 days	0d	Mon 9/29/25	Mon 9/29/25	0d	Fri 10/17/25	Fri 10/17/25	0d
29	055000 - Metal Fabricators, Shop Drawings, Submittal	20 days	2 days	18d	Mon 9/1/25	Thu 10/30/25	-43d	Sun 9/28/25	Fri 10/31/25	-25d
30	055000 - Metal Fabricators, Shop Drawings, Review/Approval	14 days	29 days	-15d	Mon 9/29/25	Fri 10/31/25	-24d	Thu 10/16/25	Thu 12/11/25	-40d
31	055000 - Metal Fabricators, Fabrication/Delivery	57 days	30 days	27d	Fri 10/17/25	Mon 12/15/25	-41d	Mon 1/5/26	Wed 3/11/26	-47d
32	055100/055116 - Metal Stair, Shop Drawings, Submittal	2 days	2 days	0d	Thu 10/30/25	Thu 10/30/25	0d	Fri 10/31/25	Fri 10/31/25	0d
33	055100/055116 - Metal Stair, Shop Drawings, Review/Approval	0 days	0 days	0d	Mon 11/3/25	Fri 10/31/25	1d	Thu 12/11/25	Thu 12/11/25	0d
34	055100/055116 - Metal Stair, Shop Drawings, Fabrication/Delivery	25 days	25 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Mon 4/6/26	Wed 3/4/26	23d
35	055110 - Aluminum Diamond Plate Wainscot, Product Data/Shop Drawings, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
36	055110 - Aluminum Diamond Plate Wainscot, Product Data/Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
37	055213 - Pipe and Tube Railings, Shop Drawings, Submittal	2 days	2 days	0d	Thu 10/30/25	Thu 10/30/25	0d	Fri 10/31/25	Fri 10/31/25	0d
38	055213 - Pipe and Tube Railings, Shop Drawings, Review/Approval	0 days	0 days	0d	Mon 11/3/25	Fri 10/31/25	1d	Thu 12/11/25	Thu 12/11/25	0d
39	055213 - Pipe and Tube Railings, Shop Drawings, Fabrication/Delivery	25 days	25 days	0d	Tue 3/3/26	Mon 12/15/25	56d	Mon 4/6/26	Wed 3/4/26	23d
40	061000 - Rough Carpentry, Product Data Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
41	061000 - Rough Carpentry, Product Data Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
42	061600 - Sheathing, Product Data Submittals	2 days	10 days	-8d	Mon 2/2/26	Thu 1/29/26	2d	Tue 2/3/26	Wed 2/11/26	-6d
43	061600 - Sheathing, Product Data Review/Approval	15 days	15 days	0d	Wed 2/4/26	Thu 2/12/26	-6d	Mon 3/23/26	Wed 3/4/26	13d
44	064116 - Plastic Laminate Casework, Product Data, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 4/9/26	-27d	Mon 3/30/26	Wed 5/6/26	-27d
45	064116 - Plastic Laminate Casework, Shop Drawings, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
46	064116 - Plastic Laminate Casework, Color Samples	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
47	064116 - Plastic Laminate Casework, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 5/7/26	-27d	Mon 4/20/26	Wed 5/27/26	-27d
48	064116 - Plastic Laminate Casework, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
49	064116 - Plastic Laminate Casework, Color Samples, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
50	064116 - Plastic Laminate Casework, Fabrication/Delivery	25 days	25 days	0d	Tue 4/21/26	Thu 5/28/26	-27d	Mon 5/25/26	Wed 7/1/26	-27d
51	066400 - FRP Submittals	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
52	066400 - FRP - Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d

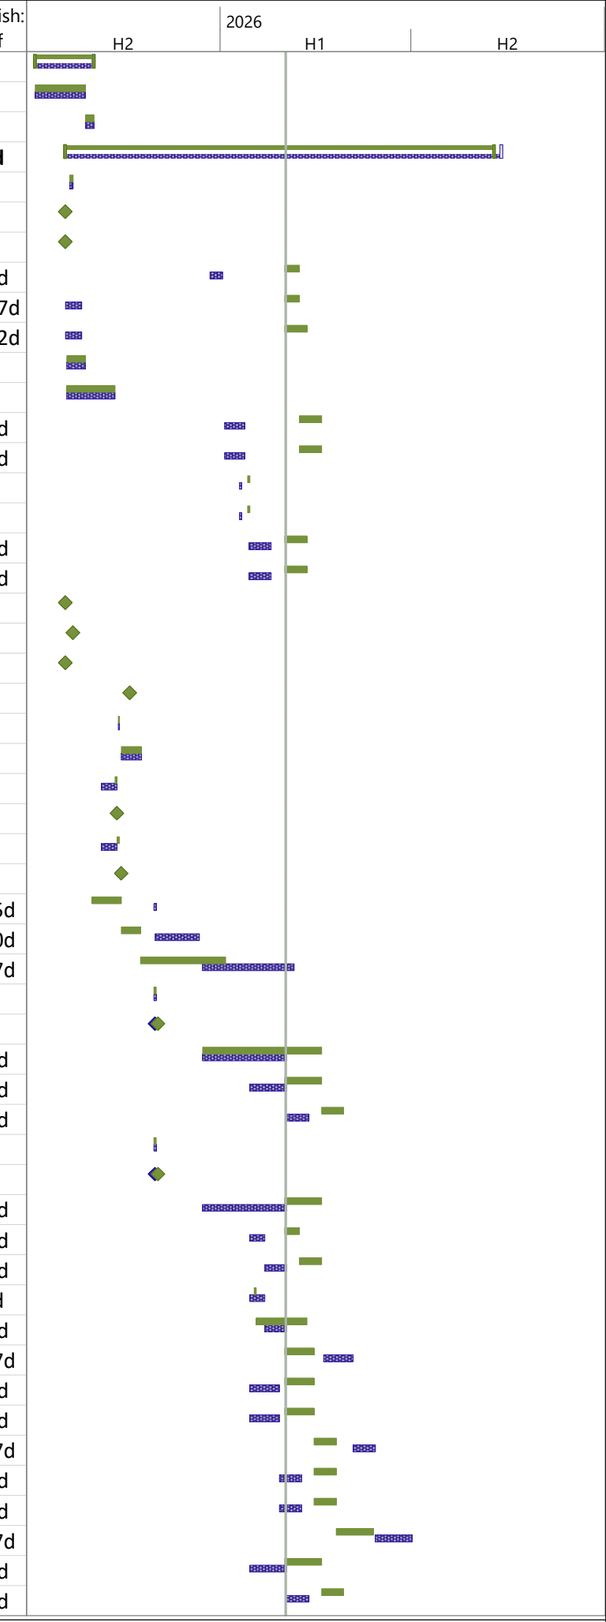

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
53	071113 - Bituminous Waterproofing, Product Data Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
54	071113 - Bituminous Waterproofing, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
55	071326 - Self-Adhering Sheet Waterproofing, Product Data Submittal	1 day	1 day	0d	Wed 9/17/25	Wed 9/17/25	0d	Wed 9/17/25	Wed 9/17/25	0d
56	071326 - Self-Adhering Sheet Waterproofing, Product Data Review/Approval	6 days	6 days	0d	Wed 9/24/25	Wed 9/24/25	0d	Wed 10/1/25	Wed 10/1/25	0d
57	071326 - Self-Adhering Sheet Waterproofing, Shop Drawings, Submittal	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
58	071326 - Self-Adhering Sheet Waterproofing, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
59	071326 - Self-Adhering Sheet Waterproofing, Samples, Submittal	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
60	071326 - Self-Adhering Sheet Waterproofing, Samples, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
61	071416 - Cold Fluid Applied Waterproofing, Product Data Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
62	071416 - Cold Fluid Applied Waterproofing, Shop Drawings, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
63	071416 - Cold Fluid Applied Waterproofing, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
64	071416 - Cold Fluid Applied Waterproofing, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
65	072100 - Thermal Insulation, Product Data Submittals	2 days	10 days	-8d	Mon 2/2/26	Thu 1/29/26	2d	Tue 2/3/26	Wed 2/11/26	-6d
66	072100 - Thermal Insulation, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/3/26	Thu 2/12/26	13d	Mon 3/23/26	Wed 3/4/26	13d
67	072410 - Stucco System, Product Data, Submittals	6 days	6 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Mon 11/24/25	Mon 11/24/20	0d
68	072410 - Stucco System, Manufacturers Standard Warranty, Submittal	6 days	6 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Mon 11/24/25	Mon 11/24/20	0d
69	072410 - Stucco System, Color Samples for Architect Approval	15 days	6 days	9d	Tue 3/3/26	Mon 11/17/25	76d	Mon 3/23/26	Mon 2/2/26	35d
70	072410 - Stucco System, Shop Drawings for Approval	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
71	072410 - Stucco System, Product Data, Review/Approval	15 days	14 days	1d	Tue 3/3/26	Mon 11/24/25	71d	Mon 3/23/26	Thu 12/11/25	72d
72	072410 - Stucco System, Manufacturers Standard Warranty, Review/Approval	15 days	13 days	2d	Tue 3/3/26	Mon 11/24/25	71d	Mon 3/23/26	Thu 12/11/25	72d
73	072410 - Stucco System, Color Samples, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Tue 2/3/26	35d	Mon 4/13/26	Mon 2/23/26	35d
74	072410 - Stucco System, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
75	072500 - Weather Barriers, Product Data, Submittal	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
76	072500 - Weather Barriers, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
77	072500 - Weather Barriers, Shop Drawings, Submittal	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
78	072500 - Weather Barriers, Shop Drawing, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
79	072713 - Modified Bituminous Sheet Air Barriers, Product Data, Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
80	072713 - Modified Bituminous Sheet Air Barriers, Shop Drawing, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
81	072713 - Modified Bituminous Sheet Air Barriers, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
82	072713 - Modified Bituminous Sheet Air Barriers, Shop Drawing, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
83	075423 - TPO Roofing, Product Data, Submittals	3 days	3 days	0d	Wed 11/12/25	Wed 11/12/25	0d	Fri 11/14/25	Fri 11/14/25	0d
84	075423 - TPO Roofing, Shop Drawing, Submittals	20 days	3 days	17d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/30/26	Fri 11/14/25	96d
85	075423 - TPO Roofing, Product Data, Review/Approval	1 day	27 days	-26d	Mon 11/17/25	Mon 11/17/25	0d	Tue 1/27/26	Tue 2/17/26	-14.5
86	075423 - TPO Roofing, Shop Drawing, Review/Approval	15 days	52 days	-37d	Tue 3/31/26	Mon 11/17/25	96d	Mon 4/20/26	Thu 3/5/26	32d
87	075423 - TPO Roofing, Sample Warranty, Submittal	10 days	3 days	7d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/16/26	Fri 11/14/25	86d
88	075423- TPO Roofing, Sample Warranty, Review/Approval	15 days	52 days	-37d	Tue 3/17/26	Mon 11/17/25	86d	Mon 4/6/26	Thu 3/5/26	22d
89	075423 - TPO Roofing, Closeout Submittal, Maintenance Data	20 days	20 days	0d	Mon 6/1/26	Wed 6/3/26	-2d	Fri 6/26/26	Tue 6/30/26	-2d
90	075423 - TPO Roofing, Closeout Submittal, Roof Warranty	20 days	20 days	0d	Mon 6/1/26	Wed 6/3/26	-2d	Fri 6/26/26	Tue 6/30/26	-2d
91	075423 - TPO Roofing, Closeout Submittal, Record Drawings	20 days	20 days	0d	Mon 6/1/26	Wed 6/3/26	-2d	Fri 6/26/26	Tue 6/30/26	-2d
92	076200 - Sheet Metal Flashing and Trim, Product Data, Submittals	10 days	3 days	7d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/16/26	Fri 11/14/25	86d
93	076200 - Sheet Metal Flashing and Trim, Shop Drawings, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
94	076200 - Sheet Metal Flashing and Trim, Samples, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
95	076200 - Sheet Metal Flashing and Trim, Product Data, Review/Approval	10 days	52 days	-42d	Tue 3/17/26	Mon 11/17/25	86d	Mon 3/30/26	Thu 3/5/26	17d
96	076200 - Sheet Metal Flashing and Trim, Shop Drawings, Review/Approval	20 days	20 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/27/26	Wed 3/25/26	23d
97	076200 - Sheet Metal Flashing and Trim, Samples, Review/Approval	20 days	20 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/27/26	Wed 3/25/26	23d
98	077100 - Roof Specialties, Product Data, Submittals	20 days	3 days	17d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/30/26	Fri 11/14/25	96d
99	077100 - Roof Specialties, Shop Drawing, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
100	077100 - Roof Specialties, Product Data, Review/Approval	15 days	52 days	-37d	Tue 3/31/26	Mon 11/17/25	96d	Mon 4/20/26	Thu 3/5/26	32d
101	077100 - Roof Specialties, Shop Drawing, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
102	077200 - Roof Accessories, Product Data, Submittals	15 days	3 days	12d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/23/26	Fri 11/14/25	91d
103	077200 - Roof Accessories, Shop Drawings, Submittal	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
104	077200 - Roof Accessories, Design Certifications, Submittal	15 days	3 days	12d	Tue 3/3/26	Wed 11/12/25	79d	Mon 3/23/26	Fri 11/14/25	91d

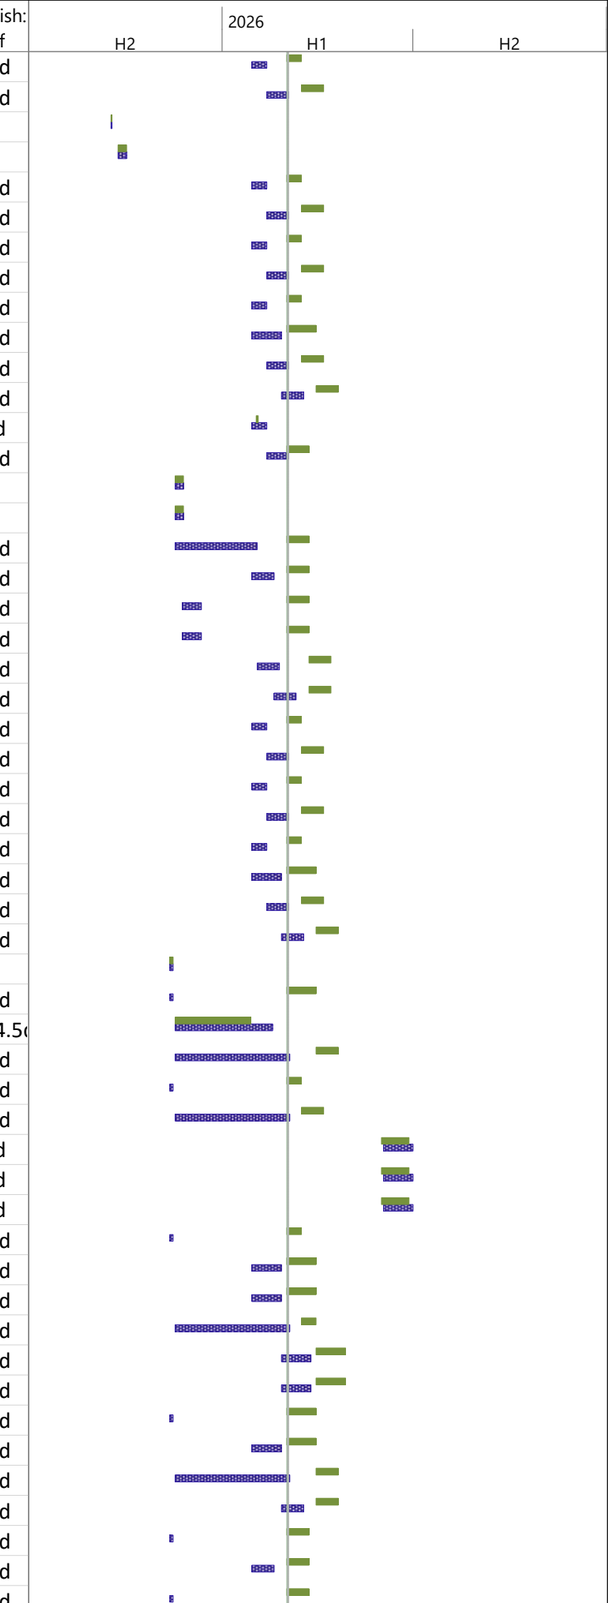

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
105	077200 - Roof Accessories, Product Data, Review/Approval	15 days	52 days	-37d	Tue 3/24/26	Mon 11/17/25	91d	Mon 4/13/26	Thu 3/5/26	27d
106	077200 - Roof Accessories, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
107	077200 - Roof Accessories, Design Certifications, Review/Approval	15 days	52 days	-37d	Tue 3/24/26	Mon 11/17/25	91d	Mon 4/13/26	Thu 3/5/26	27d
108	078413 - Penetration Firestopping, Product Data, Submittals	2 days	2 days	0d	Mon 10/20/25	Mon 10/20/25	0d	Tue 10/21/25	Tue 10/21/25	0d
109	078413 - Penetration Firestopping, Product Data, Review/Approval	11 days	16 days	-5d	Wed 10/22/25	Wed 10/22/25	0d	Wed 11/5/25	Wed 11/12/2	-5d
110	079200 - Joint Sealants, Product Data, Submittal	2 days	2 days	0d	Tue 10/21/25	Tue 10/21/25	0d	Wed 10/22/25	Wed 10/22/2	0d
111	079200 - Joint Sealants, Initial Samples for Selection	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
112	079200 - Joint Sealants, Samples for Verificiation	20 days	20 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/27/26	Wed 3/25/26	23d
113	079200 - Joint Sealants, Product Data, Review/Approval	15 days	15 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Wed 11/12/25	Wed 11/12/2	0d
114	079200 - Joint Sealants, Initial Samples for Selection, Review/Approval	10 days	10 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 3/30/26	Wed 2/25/26	23d
115	079200 - Joint Sealants, Samples for Verificiation, Review/Approval	20 days	20 days	0d	Tue 4/28/26	Thu 3/26/26	23d	Mon 5/25/26	Wed 4/22/26	23d
116	081113 - Hollow Metal Doors and Frames, Product Data Submittal	6 days	6 days	0d	Mon 8/25/25	Mon 8/25/25	0d	Tue 9/2/25	Tue 9/2/25	0d
117	081113 - Hollow Metal Doors and Frames, Shop Drawings, Submittal	6 days	6 days	0d	Mon 8/25/25	Mon 8/25/25	0d	Tue 9/2/25	Tue 9/2/25	0d
118	081113 - Hollow Metal Doors and Frames, Product Data, Review/Approval	0 days	0 days	0d	Wed 9/3/25	Wed 9/3/25	0d	Thu 10/9/25	Thu 10/9/25	0d
119	081113 - Hollow Metal Doors and Frames, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
120	083113 - Access Doors and Frames, Product Data, Submittal	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
121	083113 - Access Doors and Frames, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
122	084113 - Aluminum Framed Entrances and Storefronts, Product Data, Submittal	84 days	84 days	0d	Mon 9/15/25	Mon 9/15/25	0d	Thu 1/8/26	Thu 1/8/26	0d
123	084113 - Aluminum Framed Entrances/Storefronts, Shop Drawings, Submittal	84 days	84 days	0d	Mon 9/15/25	Mon 9/15/25	0d	Thu 1/8/26	Thu 1/8/26	0d
124	084113 - Aluminum Framing Samples, for review	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
125	084113 - Aluminum Framed Entrances and Storefronts, Product Data, Review/Approval	3 days	15 days	-12d	Thu 1/8/26	Thu 1/8/26	0d	Wed 3/4/26	Mon 2/9/26	17d
126	084113 - Aluminum Framed Entrances/Storefronts, Shop Drawings, Review/Approval	0 days	30 days	-30d	Thu 1/8/26	Mon 9/15/25	83d	Thu 1/29/26	Thu 2/19/26	-15d
127	084113 - Aluminum Framing Samples, Review/Approval	5 days	15 days	-10d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/6/26	Wed 3/18/26	13d
128	084113 - Aluminum Entrances/Storefront Fabrication/Delivery	40 days	45 days	-5d	Wed 4/8/26	Fri 3/20/26	13d	Tue 6/2/26	Thu 5/21/26	8d
129	084329 - Sliding Automatic Storm Entrances, Shop Drawing, Submittals	0 days	0 days	0d	Tue 1/6/26	Mon 9/15/25	81d	Wed 1/7/26	Thu 1/8/26	-1d
130	084329 - Sliding Automatic Storm Entrance, Color Sample, for Approval	10 days	25 days	-15d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 3/4/26	8d
131	084329 - Sliding Automatic Storm Entrances, Shop Drawing, Review/Approval	16 days	15 days	1d	Thu 1/8/26	Fri 1/9/26	-1d	Thu 3/12/26	Mon 2/9/26	23.5d
132	084329 - Sliding Automatic Storm Entrance, Color Sample, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 3/5/26	8d	Mon 4/6/26	Wed 3/25/26	8d
133	087111 - Door Hardware, Product Data, Submittal	6 days	6 days	0d	Mon 8/25/25	Mon 8/25/25	0d	Tue 9/2/25	Tue 9/2/25	0d
134	087111 - Door Hardware Schedule for Approval	9.5 days	7.5 days	2d	Wed 9/3/25	Wed 9/3/25	0d	Wed 3/4/26	Fri 10/31/25	88d
135	087111 - Door Hardware, Maintenance Data for Closeout	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
136	087111 - Door Hardware, Warranties	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
137	087111 - Door Hardware, Product Data, Review/Approval	38 days	36.1 days	1.9d	Wed 9/3/25	Wed 9/3/25	0d	Wed 3/4/26	Fri 10/31/25	87.9d
138	087111 - Door Hardware Schedule, Review/Approval	15 days	0 days	15d	Thu 3/5/26	Wed 9/3/25	131d	Wed 3/25/26	Fri 10/31/25	103d
139	087111 - Door Hardware, Qualification Data, Review/Approval	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
140	087111 - Door Hardware, Fabrication/Delivery	20 days	20 days	0d	Thu 3/26/26	Thu 1/29/26	40d	Wed 4/22/26	Wed 2/25/26	40d
141	088000 - Glazing, Product Data and Glazing Schedule, Submittal	2 days	2 days	0d	Wed 1/7/26	Tue 1/6/26	1d	Thu 1/8/26	Wed 1/7/26	1d
142	088000 - Glazing, Product Data and Glazing Schedule, Review/Approval	15 days	15 days	0d	Fri 1/9/26	Thu 1/8/26	1d	Thu 3/12/26	Mon 2/9/26	23d
143	088000 - Glazing Fabrication/Delivery	60 days	40 days	20d	Wed 4/8/26	Fri 3/20/26	13d	Tue 6/30/26	Thu 5/14/26	33d
144	089516 - Wall Vents, Product Data, Submittal	20 days	2 days	18d	Tue 3/3/26	Wed 12/10/25	59d	Mon 3/30/26	Thu 12/11/25	77d
145	089516 - Wall Vents, Metal Samples of Vents, for Approval	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
146	089516 - Wall Vents, Product Data, Review/Approval	15 days	33 days	-18d	Tue 3/31/26	Fri 12/12/25	77d	Mon 4/20/26	Fri 2/20/26	41.5d
147	089516 - Wall Vents, Metal Samples of Vents, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
148	092216 - Non-Structural Metal Framing, Product Data, Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
149	092216 - Non-Structural Metal Framing, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
150	092900 - Gypsum Board, Product Data, Submittals	1 day	10 days	-9d	Sun 2/1/26	Thu 1/29/26	2d	Mon 2/2/26	Wed 2/11/26	-7d
151	092900 - Gypsum Board, Product Data, Review/Approval	15 days	15 days	0d	Tue 2/3/26	Thu 2/12/26	-7d	Mon 3/23/26	Wed 3/4/26	13d
152	095113 - Acoustical Panel Ceilings, Product Data, Submittals	1 day	10 days	-9d	Sun 2/1/26	Thu 1/29/26	2d	Mon 2/2/26	Wed 2/11/26	-7d
153	095113 - Acoustical Panel Ceilings, Product Data, Review/Approval	15 days	15 days	0d	Tue 2/3/26	Thu 2/12/26	-7d	Mon 3/23/26	Wed 3/4/26	13d
154	096513 - Resilient Base and Accessories, Product Data, Submittals	2 days	2 days	0d	Mon 1/26/26	Mon 1/19/26	5d	Tue 1/27/26	Tue 1/20/26	5d
155	096513 - Resilient Base and Accessories, Product Data, Review/Approval	15 days	15 days	0d	Wed 1/28/26	Wed 1/28/26	0d	Mon 3/23/26	Tue 2/17/26	24d
156	099100 - Painting, Product Data, Submittals	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d

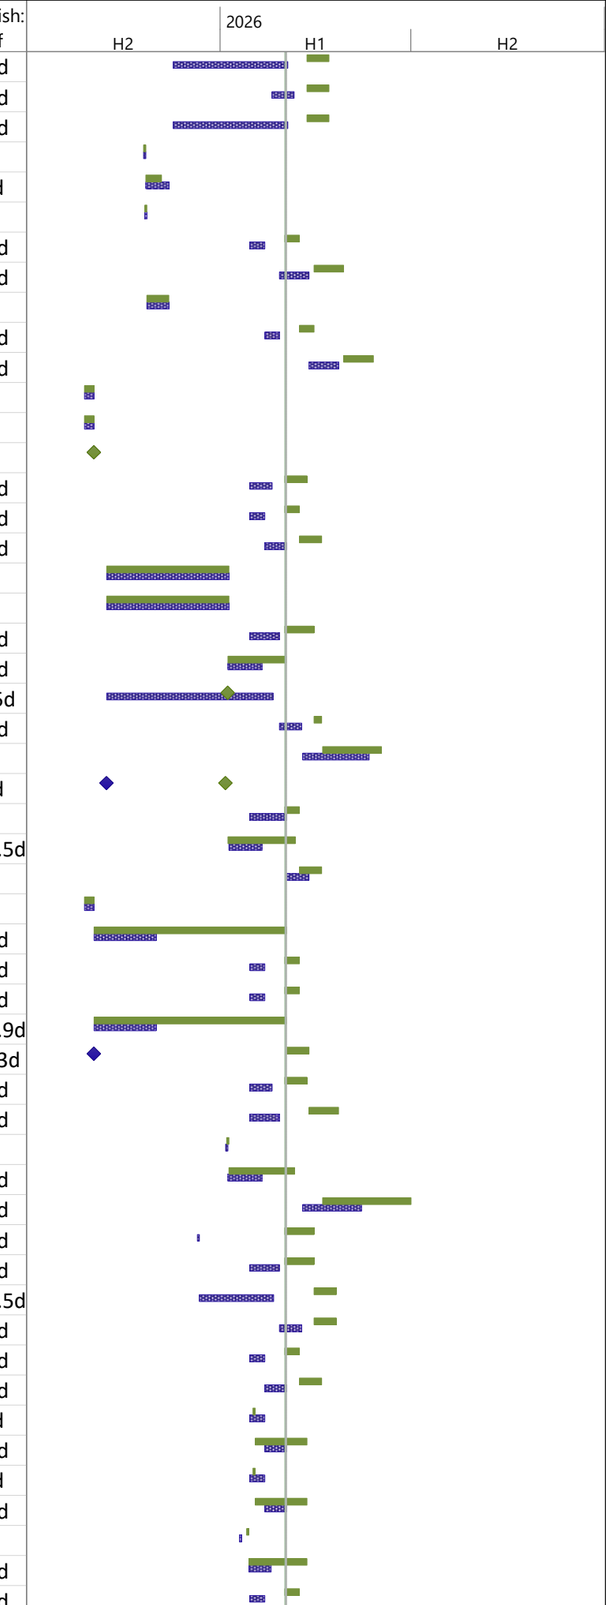

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
157	099100 - Painting, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
158	099100 - Painting, Samples for Initial Selection	10 days	10 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/16/26	Wed 2/11/26	23d
159	099100- Painting, Initial Paint Selection, Approval	15 days	15 days	0d	Tue 3/17/26	Thu 2/12/26	23d	Mon 4/6/26	Wed 3/4/26	23d
160	099100 - Painting, Samples for Verificiation, submittal to Architect	10 days	10 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/20/26	Wed 3/18/26	23d
161	099100 - Painting, Samples for Verificaiton, Review/Approval	15 days	15 days	0d	Tue 4/21/26	Thu 3/19/26	23d	Mon 5/11/26	Wed 4/8/26	23d
162	101423 - Interior Signage, Product Data/Shop Drawings, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
163	101423 - Interior Signage, Samples for approval	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
164	101423 - Interior Signage, Product Data/Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
165	101423 - Interior Signage, Samples, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
166	101423 - Interior Signage, Fabrication/Delivery	15 days	15 days	0d	Tue 4/21/26	Thu 3/19/26	23d	Mon 5/11/26	Wed 4/8/26	23d
167	102800 - Toilet Accessories, Product Data/Equipment Schedule, Submittal	2 days	4 days	-2d	Mon 1/26/26	Mon 1/19/26	5d	Tue 1/27/26	Thu 1/22/26	3d
168	102800 - Toilet Accessories, Product Data, Review/Approval	15 days	15 days	0d	Wed 1/28/26	Wed 1/28/26	0d	Mon 3/23/26	Wed 2/18/26	23d
169	104413 - Fire Extinquishers/Cabinets, Product Data/Shop Drawings, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
170	104413 - Fire Extinquishers/Cabinets, Product Data/Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
171	107316 - Metal Canopies, Product Data, Submittal	2 days	2 days	0d	Mon 1/19/26	Mon 1/19/26	0d	Tue 1/20/26	Tue 1/20/26	0d
172	107316 - Metal Canopies, Shop Drawings, for Approval	2 days	2 days	0d	Mon 1/19/26	Mon 1/19/26	0d	Tue 1/20/26	Tue 1/20/26	0d
173	107316 - Metal Canopies, Color Samples	5 days	20 days	-15d	Tue 3/3/26	Mon 1/19/26	31d	Mon 3/9/26	Fri 2/13/26	16d
174	107316 - Metal Canopies, Product Data, Review/Approval	12 days	15 days	-3d	Wed 1/21/26	Wed 1/21/26	0d	Thu 2/5/26	Tue 2/10/26	-3d
175	107316 - Metal Canopies, Shop Drawings, Review/Approval	12 days	15 days	-3d	Wed 1/21/26	Wed 1/21/26	0d	Wed 3/18/26	Tue 2/10/26	26d
176	107316 - Metal Canopies, Color Samples, Review/Approval	15 days	15 days	0d	Tue 3/10/26	Mon 1/19/26	36d	Mon 3/30/26	Fri 3/6/26	16d
177	107316 - Metal Canopies, Fabrication/Delivery	50 days	60 days	-10d	Wed 4/1/26	Tue 3/10/26	16d	Tue 6/9/26	Mon 6/1/26	6d
178	113100 - Office Appliances, Product Data, Submittal	30 days	30 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/13/26	Wed 3/11/26	23d
179	113100 - Office Appliances, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/14/26	Thu 3/12/26	23d	Mon 5/4/26	Wed 4/1/26	23d
180	142123 - Hydraulic Passenger Elevators, Product Data, Submittal	3 days	3 days	0d	Mon 8/18/25	Mon 8/18/25	0d	Wed 8/20/25	Wed 8/20/25	0d
181	142123 - Hydraulic Elevator, Shop Drawings, Submittal	3 days	3 days	0d	Mon 8/18/25	Mon 8/18/25	0d	Wed 8/20/25	Wed 8/20/25	0d
182	142123 - Hydraulic Elevator, Color Chart/Samples, for approval	3 days	3 days	0d	Mon 8/18/25	Mon 8/18/25	0d	Wed 8/20/25	Wed 8/20/25	0d
183	142123 - Hydraulic Passenger Elevators, Product Data, Review/Approval	4 days	4 days	0d	Thu 8/21/25	Thu 8/21/25	0d	Tue 8/26/25	Tue 8/26/25	0d
184	142123 - Hydraulic Elevator, Shop Drawings, Review/Approval	4 days	4 days	0d	Thu 8/21/25	Thu 8/21/25	0d	Tue 8/26/25	Tue 8/26/25	0d
185	142123 - Hydraulic Elevator, Color Chart/Samples, Review/Approval	4 days	4 days	0d	Thu 8/21/25	Thu 8/21/25	0d	Tue 8/26/25	Tue 8/26/25	0d
186	142123 - Hydraulic Elevators, Fabrication/Delivery	80 days	60 days	20d	Wed 8/27/25	Wed 8/27/25	0d	Mon 6/22/26	Wed 4/22/26	43d
187	211000 - Wet Pipe Fire Protection System, Product Data, Submittals	2 days	2 days	0d	Thu 10/30/25	Thu 10/30/25	0d	Fri 10/31/25	Fri 10/31/25	0d
188	211000 - Wet Pipe Fire Protection, Sprinkler Shop Drawings, for Approval	2 days	2 days	0d	Thu 10/30/25	Thu 10/30/25	0d	Fri 10/31/25	Fri 10/31/25	0d
189	211000 - Wet Pipe Fire Protection System, Product Data, Review/Approval	12 days	12 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Tue 11/18/25	Tue 11/18/25	0d
190	211000 - Wet Pipe Fire Protection, Sprinkler Shop Drawings, Review/Approval	12 days	12 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Tue 11/18/25	Tue 11/18/25	0d
191	220000 - Plumbing Submittals, Product Data, Submittals	2 days	2 days	0d	Fri 9/19/25	Fri 9/19/25	0d	Mon 9/22/25	Mon 9/22/25	0d
192	220000 - Plumbing Submittals, Product Data, Review/Approval	37 days	37 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Wed 11/12/25	Wed 11/12/20	0d
193	221429 - Sump Pumps, Product Data, Submittals	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
194	221429 - Sump Pumps, Product Data, Review/Approval	13 days	13 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Wed 10/8/25	Wed 10/8/25	0d
195	223300 - Electric Domestic Water Heaters, Product Data/Shop Drawing, Submittal	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
196	223300 - Electric Domestic Water Heaters, Product Data/Shop Drawing, Review/Approval	13 days	13 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Wed 10/8/25	Wed 10/8/25	0d
197	224000 - Public Plumbing Fixtures, Product Data, Submittal	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
198	224000 - Public Plumbing Fixtures, Product Data, Review/Approval	12.5 days	12.5 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Wed 11/12/25	Wed 11/12/20	0d
199	224700 - Drinking Fountain and Water Coolers, Product Data, Submittal	2 days	2 days	0d	Fri 9/19/25	Fri 9/19/25	0d	Mon 9/22/25	Mon 9/22/25	0d
200	224700 - Drinking Fountain and Water Coolers, Product Data, Review/Approval	37 days	37 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Wed 11/12/25	Wed 11/12/20	0d
201	230553 - ID for HVAC Piping & Equipment, Product Data, Submittals	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
202	230553 - ID for HVAC Piping & Equipment, Product Data, Review/Approve	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
203	230593 - Testing and Balancing, Qualifications Data for TAB Firm	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
204	230593 - Testing and Balancing, TAB agenda	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
205	230593 - Testing and Balancing, Qualifications Data, Review/Approval	20 days	20 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/27/26	Wed 3/25/26	23d
206	230593 - Testing and Balancing, TAB agenda, Review/Approval	20 days	20 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/27/26	Wed 3/25/26	23d
207	230593 - Testing and Balancing, Final TAB Report	10 days	10 days	0d	Fri 9/4/26	Fri 9/11/26	-5d	Thu 9/17/26	Thu 9/24/26	-5d
208	230713 - Duct Insulation, Product Data, Submittals	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d

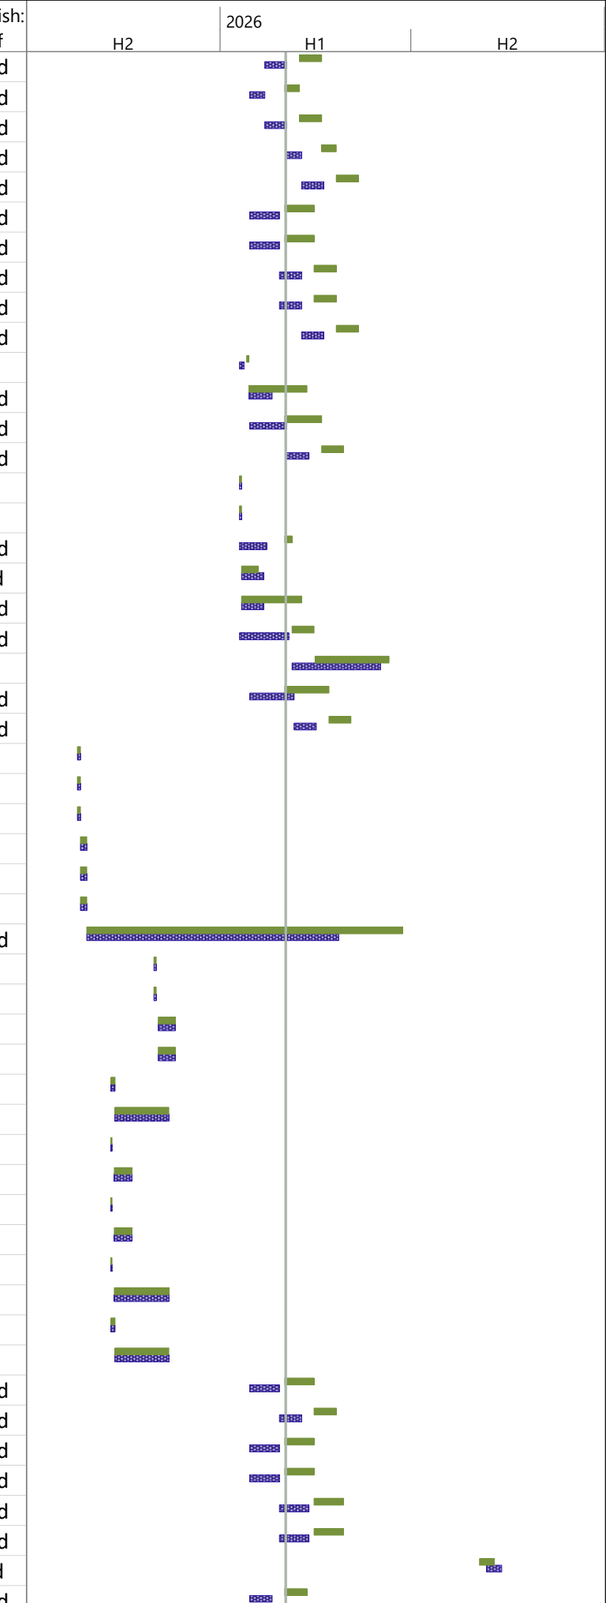

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
209	230713 - Duct Insulation, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
210	230719 - HVAC Piping Insulation, Product Data, Submittals	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
211	230719 - HVAC Piping Insulation, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
212	232300 - Refrigerant Piping, Product Data, Submittals	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
213	232300 - Refrigerant Piping, Shop Drawings, Submittals	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
214	232300 - Refrigerant Piping, Product Data, Review/Approvals	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
215	232300 - Refrigerant Piping, Shop Drawings, Review/Approvals	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
216	233113 - Metal Ducts, Shop Drawings, Submittal	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
217	233113 - Metal Ducts, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
218	233300 - Air Duct Accessories, Product Data, Submittals	2 days	2 days	0d	Mon 10/20/25	Mon 10/20/25	0d	Tue 10/21/25	Tue 10/21/25	0d
219	233300 - Air Duct Accessories, Shop Drawings, Submittal	15 days			Tue 3/3/26			Mon 3/23/26		
220	233300 - Air Duct Accessories, Product Data, Review/Approval	13 days	13 days	0d	Wed 10/22/25	Wed 10/22/25	0d	Fri 11/7/25	Fri 11/7/25	0d
221	233300 - Air Duct Accessories, Shop Drawings, Review/Approval	15 days			Tue 3/24/26			Mon 4/13/26		
222	233713 - Diffusers, Registers and Grilles, Product Data, Submittals	2 days	2 days	0d	Fri 2/20/26	Thu 12/11/25	51d	Mon 2/23/26	Fri 12/12/25	51d
223	233713 - Diffusers, Registers and Grilles, Product Data, Review/Approval	15 days	32 days	-17d	Tue 2/24/26	Mon 12/15/25	51d	Mon 3/23/26	Thu 2/19/26	22d
224	238126 - Split System Air-Conditioners, Product Data, Submittals	2 days	2 days	0d	Thu 12/11/25	Thu 12/11/25	0d	Fri 12/12/25	Fri 12/12/25	0d
225	238126 - Split System Air-Conditioners, Shop Drawings, Submittal	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
226	238126 - Split System Air-Conditioners, Product Data, Review/Approval	32 days	32 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Tue 1/27/26	Tue 1/27/26	0d
227	238126 - Split System Air-Conditioners, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
228	238136 - VRF System, Product Data, Submittals	2 days	2 days	0d	Tue 3/3/26	Thu 12/11/25	58d	Wed 3/4/26	Fri 12/12/25	58d
229	238136 - VRF System, Shop Drawing, Review/Approval	15 days	32 days	-17d	Thu 3/5/26	Mon 12/15/25	58d	Wed 3/25/26	Tue 1/27/26	41d
230	238239 - Decentralized HVAC Equipment, Product Data, Submittal	15 days	2 days	13d	Tue 3/3/26	Thu 12/11/25	58d	Mon 3/23/26	Fri 12/12/25	71d
231	238239 - Decentralized HVAC Equipment, Product Data, Review/Approval	15 days	32 days	-17d	Tue 3/24/26	Mon 12/15/25	71d	Mon 4/13/26	Thu 2/19/26	37d
232	260519 - Low-Voltage Power Conductors & Cables, Product Data, Submittals	10 days			Tue 3/3/26			Mon 3/16/26		
233	260519 - Low-Voltage Power Conductors & Cables, Product Data, Review/Approvals	15 days			Tue 3/17/26			Mon 4/6/26		
234	260526 - Grounding and Bonding for Electrical, Product Data, Submittal	10 days			Tue 3/3/26			Mon 3/16/26		
235	260526 - Grounding and Bonding for Electrical, Product Data, Review/Approval	15 days	17 days	-2d	Tue 3/17/26	Tue 10/28/25	100d	Mon 4/6/26	Wed 11/19/29	8d
236	260553 - ID for Electrical Systems, Product Data/ID Schedule, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
237	260553 - ID for Electrical Systems, Product Data/ID Schedule, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
238	260923 - Lighting Control Devices, Product Data, Submital	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
239	260923 - Lighting Control Devices, Product Data, Review/Approval	15 days	15 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Fri 10/10/25	Fri 10/10/25	0d
240	260923 - Lighting Control Devices, Shop Drawings, Submital	10 days	1 day	9d	Tue 3/3/26	Fri 9/19/25	117d	Mon 3/16/26	Fri 9/19/25	126d
241	260923 - Lighting Control Devices, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/17/26	Mon 9/22/25	126d	Mon 4/6/26	Fri 10/10/25	126d
242	262200 - Low Voltage Transformers, Product Data, Submital	10 days	3 days	7d	Tue 3/3/26	Thu 10/23/25	93d	Mon 3/16/26	Mon 10/27/2	100d
243	262200 - Low Voltage Transformers, Product Data, Review/Approval	15 days	17 days	-2d	Tue 3/17/26	Tue 10/28/25	100d	Mon 4/6/26	Wed 11/19/29	8d
244	262200 - Low Voltage Transformers, Shop Drawings, Submital	10 days	3 days	7d	Tue 3/3/26	Thu 10/23/25	93d	Mon 3/16/26	Mon 10/27/2	100d
245	262200 - Low Voltage Transformers, Shop Drawings, Review/Approval	15 days	17 days	-2d	Tue 3/17/26	Tue 10/28/25	100d	Mon 4/6/26	Wed 11/19/29	8d
246	262416 - Panelboards, Product Data, Submittal	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
247	262416 - Panelboard, Product Data, Review/Approval	14 days	14 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Thu 10/9/25	Thu 10/9/25	0d
248	262416 - Panelboard, Shop Drawings/Schedules, Submittal	2 days	2 days	0d	Fri 10/24/25	Fri 10/24/25	0d	Mon 10/27/25	Mon 10/27/2	0d
249	262416 - Panelboard, Shop Drawings/Schedules, Review/Approal	17 days	17 days	0d	Tue 10/28/25	Tue 10/28/25	0d	Wed 11/19/25	Wed 11/19/2	0d
250	262416 - Panelboard, Release for Fabrication	3 days	1 day	2d	Thu 11/20/25	Thu 11/20/25	0d	Thu 3/5/26	Thu 11/20/25	75d
251	262726 - Wiring Devices, Product Data, Submittal	10 days			Tue 3/3/26			Mon 3/16/26		
252	262726 - Wiring Devices, Product Data, Review/Approval	15 days			Tue 3/17/26			Mon 4/6/26		
253	262813 - Fuses, Product Data, Submittal	2 days			Fri 10/24/25			Mon 10/27/25		
254	262813 -Fuses, Product Data, Review/Approval	17 days			Tue 10/28/25			Wed 11/19/25		
255	262816 - Enclosed Switches & Circuit Breakers, Product Data, Submittal	2 days	2 days	0d	Fri 10/24/25	Fri 10/24/25	0d	Mon 10/27/25	Mon 10/27/2	0d
256	262816 - Enclosed Switches & Circuit Breakers, Product Data, Review/Approval	17 days	17 days	0d	Tue 10/28/25	Tue 10/28/25	0d	Wed 11/19/25	Wed 11/19/2	0d
257	262913 - Enclosed Controllers, Product Data/Shop Drawing, Submittal	10 days			Tue 3/3/26			Mon 3/16/26		
258	262913 - Enclosed Controllers, Product Data/Shop Drawing, Review/Approval	15 days			Tue 3/17/26			Mon 4/6/26		
259	265100 - LED Interior Lighting, Product Data, Submittal	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
260	265100 - LED Interior Lighting, Product Data, Review/Approval	0 days	0 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Fri 11/7/25	Fri 11/7/25	0d

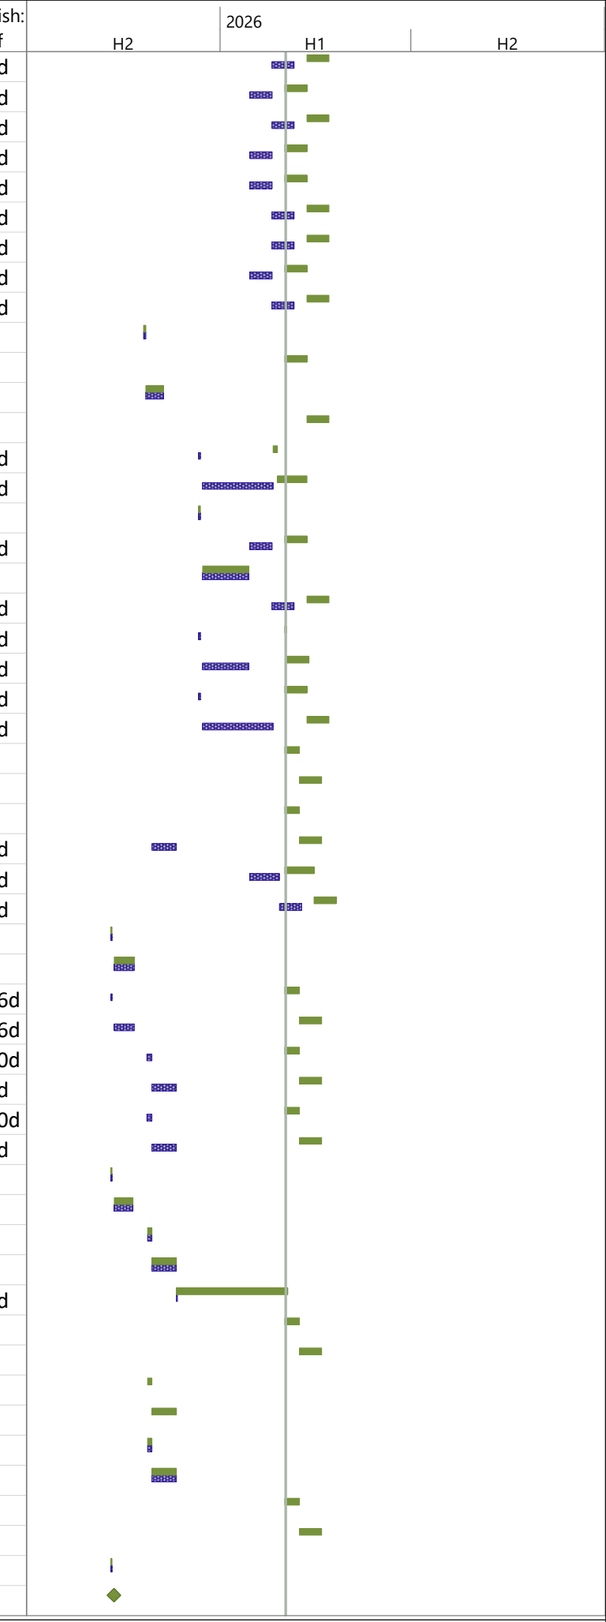

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
261	265100 - LED Interior Lighting, Fabrication/Delivery	80 days	55 days	25d	Tue 3/3/26	Mon 11/10/25	81d	Mon 6/22/26	Fri 1/23/26	106d
262	265600 - Exterior Lighting, Product Data, Submittal	1 day	1 day	0d	Fri 9/19/25	Fri 9/19/25	0d	Fri 9/19/25	Fri 9/19/25	0d
263	265600 - Exterior Lighting, Product Data, Review/Approval	0 days	0 days	0d	Mon 9/22/25	Mon 9/22/25	0d	Fri 11/7/25	Fri 11/7/25	0d
264	265600 - Exterior Lighting, Fabrication/Delivery	80 days	80 days	0d	Tue 3/3/26	Mon 11/10/25	81d	Mon 6/22/26	Wed 5/20/26	23d
265	275123 - Intercommunications & PA Systems, Shop Drawings/Product Data, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
266	275123 - Intercommunications & PA Systems, Shop Drawings/Product Data, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
267	281300 - Access Control System, Shop Drawings, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
268	281300 - Access Control System, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
269	282300 - Video Surveillance, Product Data, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
270	282300 - Video Surveillance, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
271	282300 - Video Surveillance, Shop Drawings, Submittal	20 days	20 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/30/26	Wed 2/25/26	23d
272	282300 - Video Surveillance, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 3/31/26	Thu 2/26/26	23d	Mon 4/20/26	Wed 3/18/26	23d
273	283111 - Digital, Addressable Fire Alarm System, Product Data, to EOR	0 days	15 days	-15d	Mon 1/5/26	Thu 2/19/26	-33d	Wed 2/11/26	Wed 3/11/26	-20d
274	283111 - Digital, Addressable Fire Alarm System, Shop Drawings, to EOR Review/Approval	4 days	15 days	-11d	Wed 2/11/26	Thu 2/19/26	-6d	Fri 3/6/26	Wed 3/11/26	-3d
275	283111 - Digital, Addressable Fire Alarm System, Product Data, Submittal to AHJ	20 days	10 days	10d	Tue 3/3/26	Mon 12/8/25	61d	Mon 3/30/26	Fri 12/19/25	71d
276	283111 - Digital, Addressable Fire Alarm System, Product Data, Review/Approval by AHJ	60 days	15 days	45d	Tue 3/31/26	Mon 12/22/25	71d	Mon 6/22/26	Wed 2/18/26	88d
277	283111 - Digital, Addressable Fire Alarm System, Shop Drawings, Submittal to AHJ	20 days	10 days	10d	Tue 3/3/26	Mon 12/8/25	61d	Mon 3/30/26	Fri 12/19/25	71d
278	283111 - Digital, Addressable Fire Alarm System, Shop Drawings, AHJ Review/Approval	60 days	15 days	45d	Tue 3/31/26	Mon 12/22/25	71d	Mon 6/22/26	Wed 2/18/26	88d
279	321216 - Asphalt Paving, Design Mix, Submittal	2 days	10 days	-8d	Tue 2/17/26	Thu 1/29/26	13d	Wed 2/18/26	Wed 2/11/26	5d
280	321216 - Asphalt Paving, Design Mix, Review/Approval	1 day	15 days	-14d	Thu 2/19/26	Thu 2/12/26	5d	Thu 2/19/26	Wed 3/4/26	-9d
281	321313 - Concrete Paving, Design Mixes, Submittal	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
282	321313 - Concrete Paving, Design Mixes, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
283	321313 - Concrete Paving, Product Data, Submittals	15 days	15 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 3/23/26	Wed 2/18/26	23d
284	321313 - Concrete Paving, Product Data, Review/Approval	15 days	15 days	0d	Tue 3/24/26	Thu 2/19/26	23d	Mon 4/13/26	Wed 3/11/26	23d
285	321713 - Parking Bumpers and Bollards, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
286	321713 - Parking Bumpers and Bollards, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
287	321723 - Pavement Markings, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
288	321723 - Pavement Markings, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
289	321726 - Tactile Warning Surfacing, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
290	321726 - Tactile Warning Surfacing, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
291	321726 - Tactile Warning Surfacing, Color Sample Chart, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
292	321726 - Tactile Warning Surfacing, Color Sample Chart, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
293	323113 - Chain Link Fence, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
294	323113 - Chain Link Fence, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
295	323113 - Chain Link Fence, Shop Drawings, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
296	323113 - Chain Link Fence, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
297	323113 - Chain Link Fence, Samples, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
298	323113 - Chain Link Fence, Samples, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
299	323114 - Security Wire Mesh Fences/Gates, Product Data, Submittals	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
300	323114 - Security Wire Mesh Fences/Gates, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
301	323114 - Security Wire Mesh Fences/Gates, Shop Drawings, Submittals	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
302	323114 - Security Wire Mesh Fences/Gates, Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
303	323119 - Decorative Metal Fences & Gates, Product Data, Submittal	3 days	3 days	0d	Mon 10/13/25	Mon 10/13/25	0d	Wed 10/15/25	Wed 10/15/20	0d
304	323119 - Decorative Metal Fences & Gates, Product Data, Review/Approval	15 days	15 days	0d	Wed 10/15/25	Wed 10/15/25	0d	Mon 3/23/26	Wed 2/18/26	23d
305	323119 - Decorative Metal Fences & Gates, Shop Drawings, Submittal	1 day	1 day	0d	Mon 10/13/25	Mon 10/13/25	0d	Mon 10/13/25	Mon 10/13/20	0d
306	323119 - Decorative Metal Fences & Gates, Shop Drawings, Review/Approval	15 days	15 days	0d	Wed 10/15/25	Wed 10/15/25	0d	Mon 3/23/26	Wed 2/18/26	23d
307	328400 - Planting Irrigation, Product Data/Shop Drawings, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
308	328400 - Planting Irrigation, Product Data/Shop Drawings, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
309	329200 - Turf and Grasses, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
310	329200 - Turf and Grasses, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d
311	329300 - Plants, Product Data, Submittal	25 days	25 days	0d	Tue 3/3/26	Thu 1/29/26	23d	Mon 4/6/26	Wed 3/4/26	23d
312	329300 - Plants, Product Data, Review/Approval	15 days	15 days	0d	Tue 4/7/26	Thu 3/5/26	23d	Mon 4/27/26	Wed 3/25/26	23d

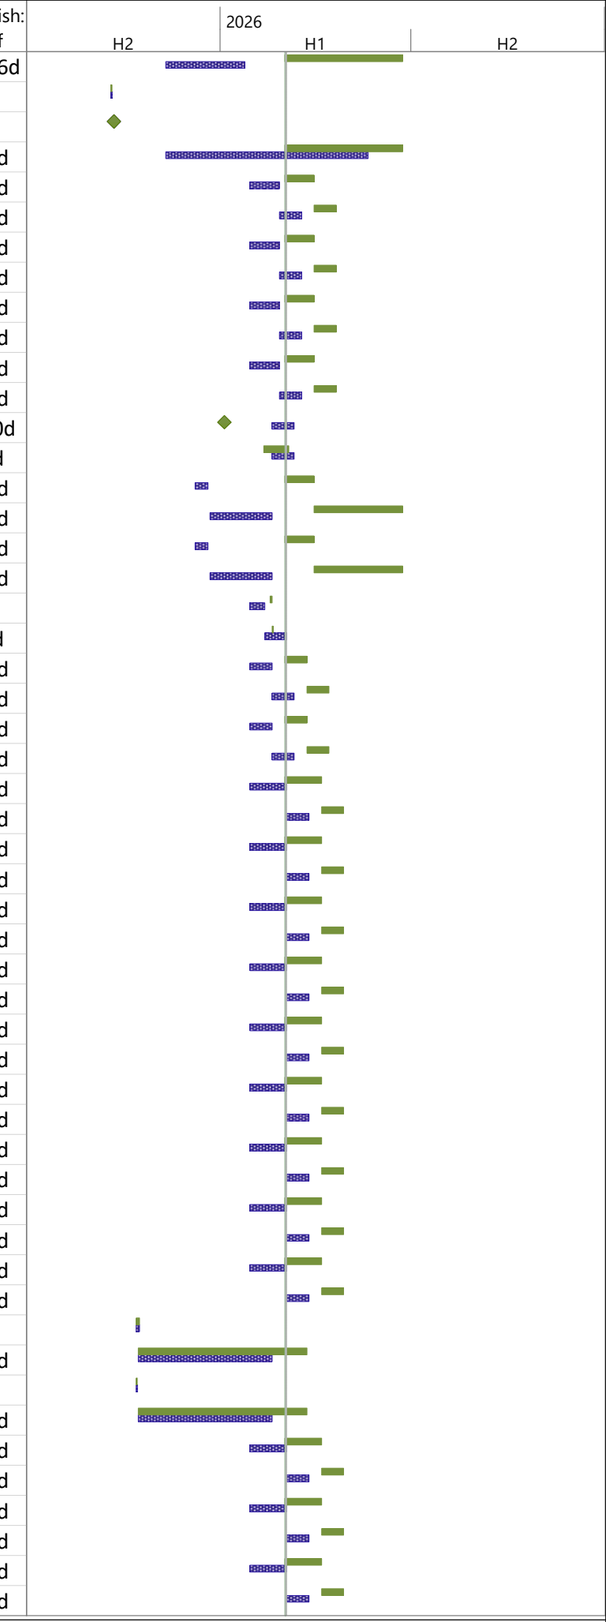

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
313	**Pre-Installation Meetings**	**157 days**	**134 days**	**23d**	**Tue 9/23/25**	**Tue 9/23/25**	**0d**	**Wed 4/29/26**	**Fri 3/27/26**	**23d**
314	Preinstallation Meeting for CIP Concrete	0 days	0 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Thu 10/23/25	Thu 10/23/25	0d
315	Preinstallation Meeting, Cold Formed Metal Framing	1 day	1 day	0d	Tue 12/16/25	Tue 12/16/25	0d	Tue 12/16/25	Tue 12/16/25	0d
316	Preinstallation Meeting, Bituminous and Self-Adhering Waterproofing	0 days	0 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Tue 9/23/25	Tue 9/23/25	0d
317	Preinstallation Meeting, Cold Fluid Applied Waterproofing	1 day	1 day	0d	Tue 4/21/26	Thu 3/19/26	23d	Tue 4/21/26	Thu 3/19/26	23d
318	Preinstallation Meeting, Hollow Metal Doors and Frames	1 day	1 day	0d	Tue 3/24/26	Thu 2/19/26	23d	Tue 3/24/26	Thu 2/19/26	23d
319	Preinstallation Meeting, Aluminum Frames and Storefronts	1 day	1 day	0d	Tue 4/7/26	Thu 3/19/26	13d	Tue 4/7/26	Thu 3/19/26	13d
320	Preinstallation Meeting, Metal Canopies	1 day	1 day	0d	Tue 3/31/26	Mon 3/9/26	16d	Tue 3/31/26	Mon 3/9/26	16d
321	Preinstallation Meeting, Hydraulic Passenger Elevator	1 day	1 day	0d	Tue 3/3/26	Thu 1/29/26	23d	Tue 3/3/26	Thu 1/29/26	23d
322	Preinstallation Meeting, Fencing	1 day	1 day	0d	Tue 4/28/26	Thu 3/26/26	23d	Tue 4/28/26	Thu 3/26/26	23d
323	Preinstallation Meeting, Security Wire Mesh Fence and Gates	1 day	1 day	0d	Tue 4/28/26	Thu 3/26/26	23d	Tue 4/28/26	Thu 3/26/26	23d
324	Preinstallation Meeting, Decorative Metal Fences and Gates	1 day	1 day	0d	Tue 3/24/26	Thu 2/19/26	23d	Tue 3/24/26	Thu 2/19/26	23d
325	Preinstallation Meeting, TPO Roofing/Sheet Metal Flashing & Trim	1 day	1 day	0d	Tue 4/28/26	Thu 3/26/26	23d	Tue 4/28/26	Thu 3/26/26	23d
326	Preinstallation Meeting, Stucco System	1 day	1 day	0d	Wed 4/29/26	Fri 3/27/26	23d	Wed 4/29/26	Fri 3/27/26	23d
327	Preinstallation Meeting, Architectural Concrete Sealing & Polishing	1 day	1 day	0d	Wed 3/25/26	Fri 2/20/26	23d	Wed 3/25/26	Fri 2/20/26	23d
328	**Sitework**	**164 days**	**145 days**	**19d**	**Thu 7/24/25**	**Thu 7/24/25**	**0d**	**Tue 3/10/26**	**Wed 2/11/26**	**19d**
329	Complete Erosion Control Install	4 days	4 days	0d	Thu 7/24/25	Thu 7/24/25	0d	Mon 9/8/25	Mon 9/8/25	0d
330	Silt Fence Inspection	1 day	1 day	0d	Tue 9/9/25	Tue 9/9/25	0d	Tue 9/9/25	Tue 9/9/25	0d
331	Clear and Grub	0 days	0 days	0d	Wed 9/3/25	Wed 9/3/25	0d	Thu 9/18/25	Thu 9/18/25	0d
332	Install Temporary Fencing	1 day	1 day	0d	Fri 10/3/25	Fri 10/3/25	0d	Fri 10/3/25	Fri 10/3/25	0d
333	Mass Grade Site	14 days	14 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Wed 10/8/25	Wed 10/8/25	0d
334	Construct Retention Pond	3 days	3 days	0d	Fri 10/10/25	Fri 10/10/25	0d	Thu 3/5/26	Mon 2/2/26	23d
335	Storm Sewer	0 days	6 days	-6d	Fri 11/14/25	Fri 11/14/25	0d	Fri 2/27/26	Thu 2/5/26	16d
336	Sanitary Sewer, Fire Line and domestic water	6 days	10 days	-4d	Fri 11/14/25	Fri 11/14/25	0d	Tue 3/10/26	Wed 2/11/26	19d
337	Grade for building pad	1 day	1 day	0d	Wed 10/1/25	Wed 10/1/25	0d	Wed 10/8/25	Wed 10/8/25	0d
338	**Building Pad Construction**	**43 days**	**43 days**	**0d**	**Thu 10/9/25**	**Thu 10/9/25**	**0d**	**Mon 12/8/25**	**Mon 12/8/25**	**0d**
339	Survey and Form Perimeter Walls of Building	10 days	10 days	0d	Thu 10/9/25	Thu 10/9/25	0d	Wed 10/22/25	Wed 10/22/25	0d
340	Concrete Footings for Columns	10 days	10 days	0d	Tue 10/28/25	Tue 10/28/25	0d	Fri 12/5/25	Fri 12/5/25	0d
341	Excavation for Elevator Pits	0 days	0 days	0d	Tue 10/28/25	Tue 10/28/25	0d	Fri 11/7/25	Fri 11/7/25	0d
342	Waterproofing of Below Elevator Pit Floors	3 days	3 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Mon 11/10/25	Mon 11/10/25	0d
343	Construct Concrete Elevator Pit Floors and Sump Pits	0 days	0 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Fri 11/7/25	Fri 11/7/25	0d
344	Form and Pour Elevator Pit Walls	2 days	2 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Fri 11/7/25	Fri 11/7/25	0d
345	Underslab Plumbing Rough	0 days	0 days	0d	Tue 11/11/25	Tue 11/11/25	0d	Fri 11/21/25	Fri 11/21/25	0d
346	Fine Grade SOG-Place Stone	0 days	0 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Mon 11/24/25	Mon 11/24/25	0d
347	Underslab Electrical Rough	0 days	0 days	0d	Thu 10/30/25	Thu 10/30/25	0d	Fri 12/5/25	Fri 12/5/25	0d
348	Vapor Barrier/Rebar for Slab on Grade	9 days	9 days	0d	Tue 11/11/25	Tue 11/11/25	0d	Fri 12/5/25	Fri 12/5/25	0d
349	Pour First Half of Slab on Grade	0 days	0 days	0d	Sat 11/22/25	Sat 11/22/25	0d	Sat 11/22/25	Sat 11/22/25	0d
350	Pour Second Half of Slab on Grade	0 days	0 days	0d	Sat 12/6/25	Sat 12/6/25	0d	Sat 12/6/25	Sat 12/6/25	0d
351	Backfill Around Slab on Grade	1 day	1 day	0d	Mon 12/8/25	Mon 12/8/25	0d	Mon 12/8/25	Mon 12/8/25	0d
352	**Building Construction**	**179 days**	**172 days**	**7d**	**Wed 12/10/25**	**Wed 12/10/25**	**0d**	**Mon 8/17/26**	**Thu 8/6/26**	**7d**
353	Hollow metal frames to job site for CMU	0 days	0 days	0d	Wed 12/10/25	Wed 12/10/25	0d	Wed 12/10/25	Wed 12/10/25	0d
354	Construct First Lift of Elevators/Stair Tower CMU	0 days	0 days	0d	Thu 12/11/25	Thu 12/11/25	0d	Wed 12/31/25	Fri 1/9/26	-7d
355	Construct Exterior CMU Walls - SOG to 2nd Floor	0 days	10 days	-10d	Thu 12/11/25	Thu 12/11/25	0d	Thu 1/15/26	Wed 2/11/26	-19d
356	Install Hollow Metal Frames in CMU - 1st Floor	1 day	1 day	0d	Wed 12/10/25	Wed 12/10/25	0d	Wed 12/10/25	Wed 12/10/25	0d
357	Grout First Lift of CMU at Elevators/Stair Towers	1 day	1 day	0d	Wed 12/31/25	Wed 12/31/25	0d	Wed 12/31/25	Wed 12/31/25	0d
358	Construct Second Lift of Elevators/Stair Tower CMU	8 days	8 days	0d	Thu 1/15/26	Thu 1/15/26	0d	Thu 3/12/26	Mon 2/9/26	23d
359	Install Hollow Metal Frames in Stair Towers - 2nd Floor	1 day	1 day	0d	Wed 2/25/26	Thu 1/29/26	19d	Wed 2/25/26	Thu 1/29/26	19d
360	Grout Second Lift of CMU at Elevators/Stair Towers	1 day	2 days	-1d	Thu 2/19/26	Fri 1/30/26	14d	Thu 2/26/26	Mon 2/2/26	18d
361	Construct Final Lift of Elevators/Stair Tower CMU	8 days	8 days	0d	Tue 3/3/26	Tue 2/3/26	20d	Thu 3/12/26	Thu 2/12/26	20d
362	Install Hollow Metal Frame in Stair Towers - 3rd Floor	1 day	1 day	0d	Tue 3/3/26	Tue 2/3/26	20d	Tue 3/3/26	Tue 2/3/26	20d
363	Grout Final Lift of CMU at Elevators/Stair Towers	2 days	2 days	0d	Tue 3/24/26	Thu 3/12/26	8d	Wed 3/25/26	Fri 3/13/26	8d
364	1st floor structure erection/decking	5 days	7 days	-2d	Wed 1/7/26	Wed 1/7/26	0d	Thu 2/12/26	Fri 2/20/26	-6d

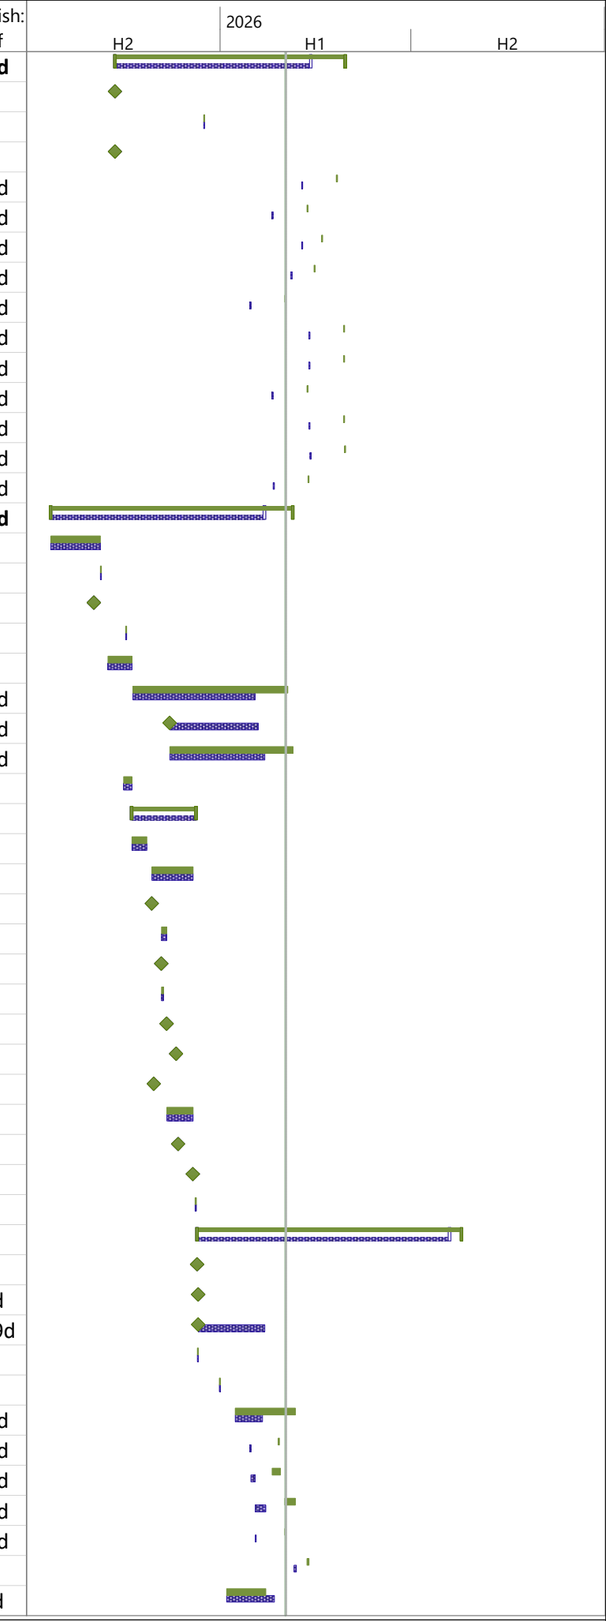

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
365	2nd floor SOD-Prep/wire install/Pour	8 days	7 days	1d	Wed 1/21/26	Tue 1/20/26	1d	Sat 2/21/26	Mon 2/9/26	9d
366	2nd floor SOD-Pour Completed	0 days	0 days	0d	Sat 2/21/26	Mon 2/9/26	9d	Sat 2/21/26	Mon 2/9/26	9d
367	Construct Exterior CMU Walls - 2nd to 3rd floor	10 days	15 days	-5d	Thu 1/15/26	Thu 1/15/26	0d	Mon 3/16/26	Mon 3/9/26	5d
368	2nd floor-structure erection	12 days	25 days	-13d	Mon 2/16/26	Mon 2/23/26	-5d	Wed 3/18/26	Fri 3/27/26	-7d
369	3rd floor-SOD prep/wire install/Pour	7 days	7 days	0d	Thu 3/19/26	Thu 3/26/26	-5d	Fri 3/27/26	Fri 4/3/26	-5d
370	3rd floor-SOD Pour Completed	0 days	0 days	0d	Fri 3/27/26	Fri 4/3/26	-5d	Fri 3/27/26	Fri 4/3/26	-5d
371	Install stairs in stair towers	7 days	7 days	0d	Tue 4/7/26	Mon 3/16/26	16d	Wed 4/15/26	Tue 3/24/26	16d
372	Install Railings	8 days	8 days	0d	Thu 4/16/26	Wed 3/25/26	16d	Mon 4/27/26	Fri 4/3/26	16d
373	3rd Floor - Construct CMU walls from 3rd Floor to Roof	15 days	15 days	0d	Mon 4/6/26	Mon 4/13/26	-5d	Fri 4/24/26	Fri 5/1/26	-5d
374	3rd floor structure erection & Roof	25 days	25 days	0d	Thu 4/16/26	Mon 4/20/26	-2d	Wed 5/20/26	Fri 5/22/26	-2d
375	Install TPO Roofing	7 days	7 days	0d	Thu 5/21/26	Mon 5/25/26	-2d	Fri 5/29/26	Tue 6/2/26	-2d
376	Roofing Complete - Building Dry-In	0 days	0 days	0d	Mon 6/1/26	Wed 6/3/26	-2d	Mon 6/1/26	Wed 6/3/26	-2d
377	EIFS/Stucco	35 days	35 days	0d	Thu 5/21/26	Mon 5/25/26	-2d	Wed 7/8/26	Fri 7/10/26	-2d
378	Storefront Frames Install	10 days	10 days	0d	Wed 6/3/26	Thu 6/4/26	-1d	Tue 6/16/26	Wed 6/17/26	-1d
379	Storefront Glass Installed	10 days	10 days	0d	Wed 7/1/26	Thu 7/2/26	-1d	Tue 7/14/26	Wed 7/15/26	-1d
380	Stanley Sliding Door Install	1 day	1 day	0d	Mon 6/1/26	Wed 6/3/26	-2d	Mon 6/1/26	Wed 6/3/26	-2d
381	Canopies	8 days	8 days	0d	Thu 6/18/26	Mon 6/22/26	-2d	Mon 6/29/26	Wed 7/1/26	-2d
382	Install Metal Coping/Downspouts/Trim	6 days	6 days	0d	Wed 7/15/26	Thu 7/16/26	-1d	Wed 7/22/26	Thu 7/23/26	-1d
383	Exterior Building Caulking	5 days	5 days	0d	Thu 7/23/26	Fri 7/24/26	-1d	Wed 7/29/26	Thu 7/30/26	-1d
384	Exterior Building Punchlist	5 days	5 days	0d	Thu 7/30/26	Fri 7/31/26	-1d	Wed 8/5/26	Thu 8/6/26	-1d
385	Light gauge office framing	5 days	5 days	0d	Thu 5/21/26	Mon 5/25/26	-2d	Wed 5/27/26	Fri 5/29/26	-2d
386	Elevator #1 Install	20 days	20 days	0d	Tue 6/23/26	Fri 6/5/26	12d	Mon 7/20/26	Thu 7/2/26	12d
387	Elevator #2 install	20 days	20 days	0d	Tue 7/21/26	Fri 7/3/26	12d	Mon 8/17/26	Thu 7/30/26	12d
388	Building Façade Complete	0 days	0 days	0d	Wed 7/22/26	Thu 7/23/26	-1d	Wed 7/22/26	Thu 7/23/26	-1d
389	**Site Utlities/As-Builts**	**216 days**	**223 days**	**-7d**	**Thu 11/20/25**	**Mon 11/17/25**	**3d**	**Thu 9/17/26**	**Wed 9/23/26**	**-4d**
390	Electrical Gear Procurement	0 days	20 days	-20d	Thu 11/20/25	Mon 11/17/25	3d	Fri 1/30/26	Wed 2/25/26	-18d
391	Procure Transformer	60 days	15 days	45d	Wed 2/18/26	Mon 2/9/26	7d	Mon 5/25/26	Fri 2/27/26	61d
392	Install Primary Power Conduits to Transformer	17 days	10 days	7d	Fri 1/23/26	Wed 3/4/26	-28d	Mon 2/16/26	Tue 3/17/26	-21d
393	Install Secondary Power Conduits from Building to Transfomer	0 days	0 days	0d	Mon 1/5/26	Mon 12/22/25	10d	Mon 2/2/26	Mon 12/22/2	31d
394	Survey for Transformer Pad		1 day			Thu 1/29/26			Thu 1/29/26	
395	Grade for Transformer Pad		2 days			Fri 1/30/26			Mon 2/2/26	
396	Construct or Set Transformer Pad		4 days			Tue 2/3/26			Fri 2/6/26	
397	Set Transformer	5 days	2 days	3d	Tue 5/26/26	Mon 3/2/26	61d	Mon 6/1/26	Tue 3/3/26	64d
398	Permanent Power to Building	10 days	10 days	0d	Tue 6/2/26	Wed 3/18/26	54d	Mon 6/15/26	Tue 3/31/26	54d
399	As-Built Drawings for Sanitary and Storm		12 days			Tue 9/8/26			Wed 9/23/26	
400	As-Built Drawings for Sanitary and Storm Water	12 days			Wed 9/2/26			Thu 9/17/26		
401	**Rough-ins and Finishes**	**161 days**	**134 days**	**27d**	**Thu 2/19/26**	**Mon 4/6/26**	**-32d**	**Thu 10/1/26**	**Thu 10/8/26**	**-5d**
402	1st Floor Electrical/Fire Alarm Rough In	15 days	15 days	0d	Thu 2/19/26	Wed 4/29/26	-49d	Mon 5/25/26	Tue 5/19/26	4d
403	1st Floor HVAC Rough In	15 days	15 days	0d	Tue 2/24/26	Mon 4/6/26	-29d	Mon 5/4/26	Fri 4/24/26	6d
404	1st Floor Sprinkler Rough-in/riser room-1st floor	12 days	12 days	0d	Tue 3/3/26	Mon 4/20/26	-34d	Wed 4/22/26	Tue 5/5/26	-9d
405	1st Floor HVAC Trim/Line Set	10 days	10 days	0d	Tue 5/26/26	Wed 5/20/26	4d	Mon 6/8/26	Tue 6/2/26	4d
406	1st Floor Plumbing rough walls	5 days	5 days	0d	Tue 6/9/26	Mon 6/1/26	6d	Mon 6/15/26	Fri 6/5/26	6d
407	1st Floor Hallway System- by Janus	20 days	20 days	0d	Tue 6/16/26	Mon 6/8/26	6d	Mon 7/13/26	Fri 7/3/26	6d
408	1st Floor Electrical Trim/FA/Hang Lights	7 days	7 days	0d	Tue 7/14/26	Mon 7/6/26	6d	Wed 7/22/26	Tue 7/14/26	6d
409	2nd Floor HVAC Rough In	15 days	15 days	0d	Thu 5/21/26	Mon 5/25/26	-2d	Wed 6/10/26	Fri 6/12/26	-2d
410	2nd Floor Electrical/Fire Alarm Rough In	15 days	15 days	0d	Thu 6/11/26	Mon 6/15/26	-2d	Wed 7/1/26	Fri 7/3/26	-2d
411	2nd Floor Sprinkler Rough-in	7 days	7 days	0d	Thu 6/4/26	Mon 6/8/26	-2d	Fri 6/12/26	Tue 6/16/26	-2d
412	2nd Floor HVAC Trim/Line Sets	10 days	10 days	0d	Mon 6/15/26	Wed 6/17/26	-2d	Fri 6/26/26	Tue 6/30/26	-2d
413	2nd Floor Hallway System - by Janus	20 days	20 days	0d	Tue 7/14/26	Mon 7/6/26	6d	Mon 8/10/26	Fri 7/31/26	6d
414	2nd Floor Electrical Trim/FA/Hang Light-2nd Floor	7 days	7 days	0d	Tue 8/11/26	Mon 8/3/26	6d	Wed 8/19/26	Tue 8/11/26	6d
415	Install Gear in Electrical Room	10 days	10 days	0d	Mon 6/1/26	Wed 6/3/26	-2d	Fri 6/12/26	Tue 6/16/26	-2d
416	Power to elevator machine rooms	2 days	2 days	0d	Tue 6/16/26	Wed 6/3/26	9d	Wed 6/17/26	Thu 6/4/26	9d

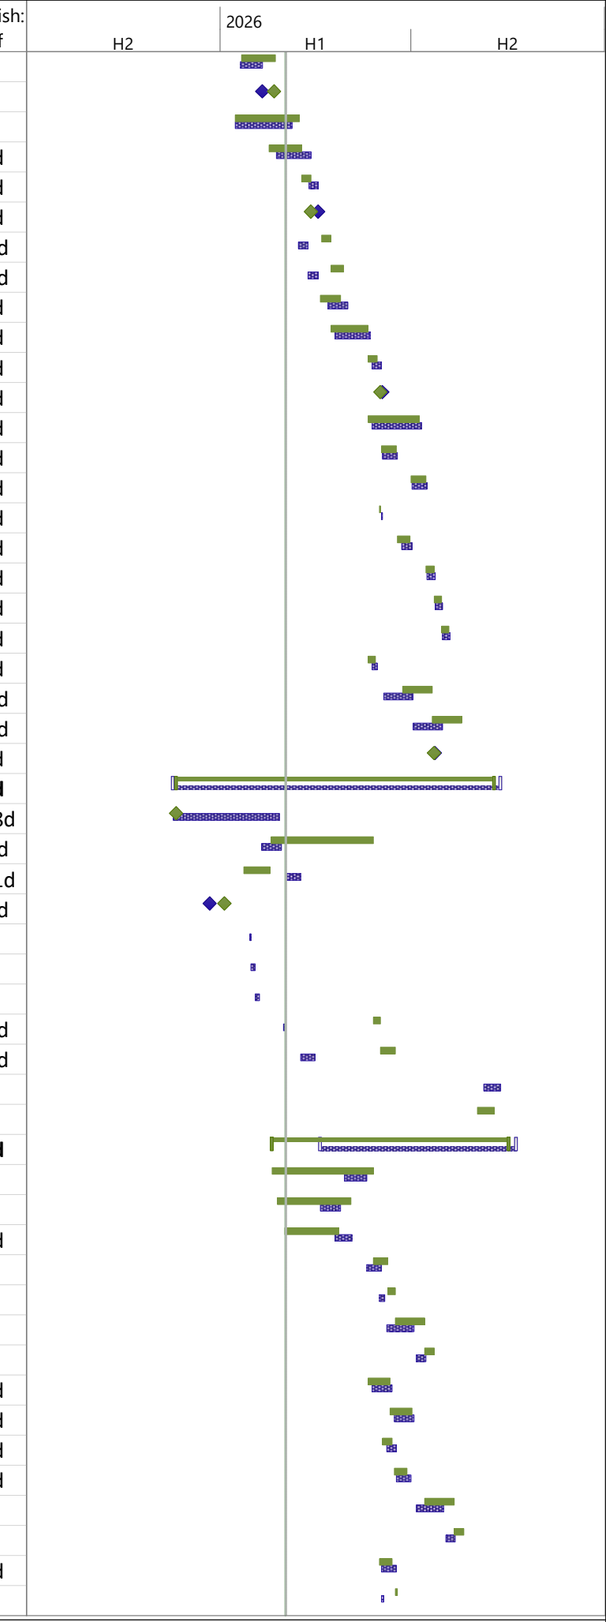
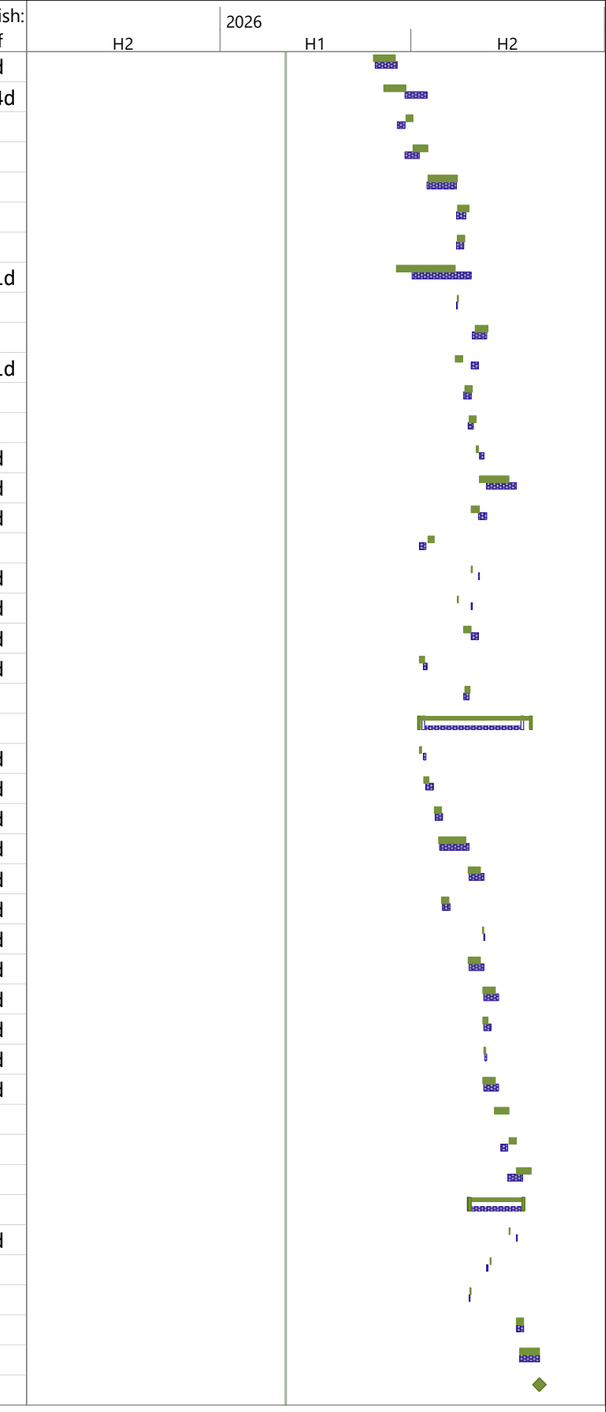
	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
417	3rd Floor HVAC Rough In	15 days	15 days	0d	Tue 5/26/26	Thu 5/28/26	-2d	Mon 6/15/26	Wed 6/17/26	-2d
418	3rd Floor Electrical/Fire Alarm Rough In	15 days	15 days	0d	Fri 6/5/26	Thu 6/25/26	-14d	Thu 6/25/26	Wed 7/15/26	-14d
419	3rd Floor Sprinkler Rough-in	5 days	5 days	0d	Fri 6/26/26	Thu 6/18/26	6d	Thu 7/2/26	Wed 6/24/26	6d
420	3rd Floor HVAC Trim/Line Sets	10 days	10 days	0d	Fri 7/3/26	Thu 6/25/26	6d	Thu 7/16/26	Wed 7/8/26	6d
421	3rd Floor Hallway System-by Janus	20 days	20 days	0d	Fri 7/17/26	Thu 7/16/26	1d	Thu 8/13/26	Wed 8/12/26	1d
422	3rd Floor Electrical Trim/FA/Hang Lights	7 days	7 days	0d	Fri 8/14/26	Thu 8/13/26	1d	Mon 8/24/26	Fri 8/21/26	1d
423	Install Aluminum Wainscot at Elevator Lobbies	5 days	5 days	0d	Fri 8/14/26	Thu 8/13/26	1d	Thu 8/20/26	Wed 8/19/26	1d
424	Office Buildout	40 days	40 days	0d	Wed 6/17/26	Thu 7/2/26	-11d	Tue 8/11/26	Wed 8/26/26	-11d
425	Initial BDA System Requirement Testing	1 day	1 day	0d	Fri 8/14/26	Thu 8/13/26	1d	Fri 8/14/26	Thu 8/13/26	1d
426	Install BDA System	10 days	10 days	0d	Mon 8/31/26	Fri 8/28/26	1d	Fri 9/11/26	Thu 9/10/26	1d
427	1st Floor Punchlist Repairs	5 days	5 days	0d	Wed 8/12/26	Thu 8/27/26	-11d	Tue 8/18/26	Wed 9/2/26	-11d
428	2nd Floor Punchlist Repairs	5 days	5 days	0d	Fri 8/21/26	Thu 8/20/26	1d	Thu 8/27/26	Wed 8/26/26	1d
429	3rd Floor Punchlist Repairs	5 days	5 days	0d	Tue 8/25/26	Mon 8/24/26	1d	Mon 8/31/26	Fri 8/28/26	1d
430	Complete Interior Punchlist Work - All Floors	2 days	2 days	0d	Tue 9/1/26	Fri 9/4/26	-3d	Wed 9/2/26	Mon 9/7/26	-3d
431	Final Clean/Floor Sealer	20 days	20 days	0d	Fri 9/4/26	Fri 9/11/26	-5d	Thu 10/1/26	Thu 10/8/26	-5d
432	HVAC Startup	6 days	6 days	0d	Thu 8/27/26	Thu 9/3/26	-5d	Thu 9/3/26	Thu 9/10/26	-5d
433	Install Plumbing Fixtures and Water Heaters	4 days	4 days	0d	Fri 7/17/26	Thu 7/9/26	6d	Wed 7/22/26	Tue 7/14/26	6d
434	Install Interior Signage	1 day	1 day	0d	Thu 8/27/26	Thu 9/3/26	-5d	Thu 8/27/26	Thu 9/3/26	-5d
435	Install Fire Extinguishers and Cabinets	1 day	1 day	0d	Fri 8/14/26	Thu 8/27/26	-9d	Fri 8/14/26	Thu 8/27/26	-9d
436	Final Painting, Stairs/Railings/Doors	5 days	5 days	0d	Thu 8/20/26	Thu 8/27/26	-5d	Wed 8/26/26	Wed 9/2/26	-5d
437	Wall Packs	3 days	3 days	0d	Thu 7/9/26	Mon 7/13/26	-2d	Mon 7/13/26	Wed 7/15/26	-2d
438	Elevator Trim out by Subs	3 days	3 days	0d	Fri 8/21/26	Thu 8/20/26	1d	Tue 8/25/26	Mon 8/24/26	1d
439	**Finsh Sitework - Dumpster/Sidewalks/Paving/Landscaping**	**76 days**	**68 days**	**8d**	**Thu 7/9/26**	**Mon 7/13/26**	**-2d**	**Thu 10/22/26**	**Wed 10/14/2**	**6d**
440	Rough grade for landscaping	2 days	2 days	0d	Thu 7/9/26	Mon 7/13/26	-2d	Fri 7/10/26	Tue 7/14/26	-2d
441	Install Exterior Lighting in Parking Area	5 days	5 days	0d	Mon 7/13/26	Wed 7/15/26	-2d	Fri 7/17/26	Tue 7/21/26	-2d
442	Form and Pour Sidewalks	5 days	5 days	0d	Thu 7/23/26	Fri 7/24/26	-1d	Wed 7/29/26	Thu 7/30/26	-1d
443	Landscaping and Irrigation Installation	20 days	20 days	0d	Mon 7/27/26	Tue 7/28/26	-1d	Fri 8/21/26	Mon 8/24/26	-1d
444	Curb/Asphalt Paving	10 days	10 days	0d	Mon 8/24/26	Tue 8/25/26	-1d	Fri 9/4/26	Mon 9/7/26	-1d
445	Install Fencing	5 days	5 days	0d	Thu 7/30/26	Fri 7/31/26	-1d	Wed 8/5/26	Thu 8/6/26	-1d
446	Striping	1 day	1 day	0d	Mon 9/7/26	Tue 9/8/26	-1d	Mon 9/7/26	Tue 9/8/26	-1d
447	Landscaping As-Built Drawings	10 days	10 days	0d	Mon 8/24/26	Tue 8/25/26	-1d	Fri 9/4/26	Mon 9/7/26	-1d
448	Developer's Letter of Dedication	10 days	10 days	0d	Mon 9/7/26	Tue 9/8/26	-1d	Fri 9/18/26	Mon 9/21/26	-1d
449	Engineer's Certificate of Completion	5 days	5 days	0d	Mon 9/7/26	Tue 9/8/26	-1d	Fri 9/11/26	Mon 9/14/26	-1d
450	Contractor's Letter of Completion	2 days	2 days	0d	Tue 9/8/26	Wed 9/9/26	-1d	Wed 9/9/26	Thu 9/10/26	-1d
451	Satisfaction Letter/Email from FDOT and City for Infrastructure	10 days	10 days	0d	Mon 9/7/26	Tue 9/8/26	-1d	Fri 9/18/26	Mon 9/21/26	-1d
452	SOV for Site Utilites, Water, Wastewater, Reclaimed Water	10 days			Fri 9/18/26			Thu 10/1/26		
453	Polk County Final Walkthrough Request	5 days	5 days	0d	Fri 10/2/26	Thu 9/24/26	6d	Thu 10/8/26	Wed 9/30/26	6d
454	Polk County Approval of Site	10 days	10 days	0d	Fri 10/9/26	Thu 10/1/26	6d	Thu 10/22/26	Wed 10/14/2	6d
455	**Final Building Sign-Offs**	**37 days**	**38 days**	**-1d**	**Wed 8/26/26**	**Tue 8/25/26**	**1d**	**Thu 10/15/26**	**Thu 10/15/2**	**0d**
456	Pre Closeout Meeting with AHJ	1 day	1 day	0d	Fri 10/2/26	Fri 10/9/26	-5d	Fri 10/2/26	Fri 10/9/26	-5d
457	Final BDA Test	1 day	1 day	0d	Mon 9/14/26	Fri 9/11/26	1d	Mon 9/14/26	Fri 9/11/26	1d
458	Elevator Ready for State Inspection	1 day	1 day	0d	Wed 8/26/26	Tue 8/25/26	1d	Wed 8/26/26	Tue 8/25/26	1d
459	Final Building Inspections	5 days	5 days	0d	Fri 10/9/26	Fri 10/9/26	0d	Thu 10/15/26	Thu 10/15/2	0d
460	Weather Days per Contract (20 Calendar Days)	15 days	15 days	0d	Mon 10/12/26	Mon 10/12/26	0d	Fri 10/30/26	Fri 10/30/26	0d
461	Substantial Completion	0 days	0 days	0d	Fri 10/30/26	Fri 10/30/26	0d	Fri 10/30/26	Fri 10/30/26	0d
