Willis, TX

Compare Remaining Compression

Report Date: 03/17/2026

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedules Analyzed

A Earlier Data Date	B Later Data Date
Willis, TX - 02/05/2026	**Willis, TX - 03/05/2026**
Data Date: 02/05/2026	Data Date: 03/17/2026
Finish Date: 08/03/2026	Finish Date: 08/31/2026

Remaining Work Compression 4 %

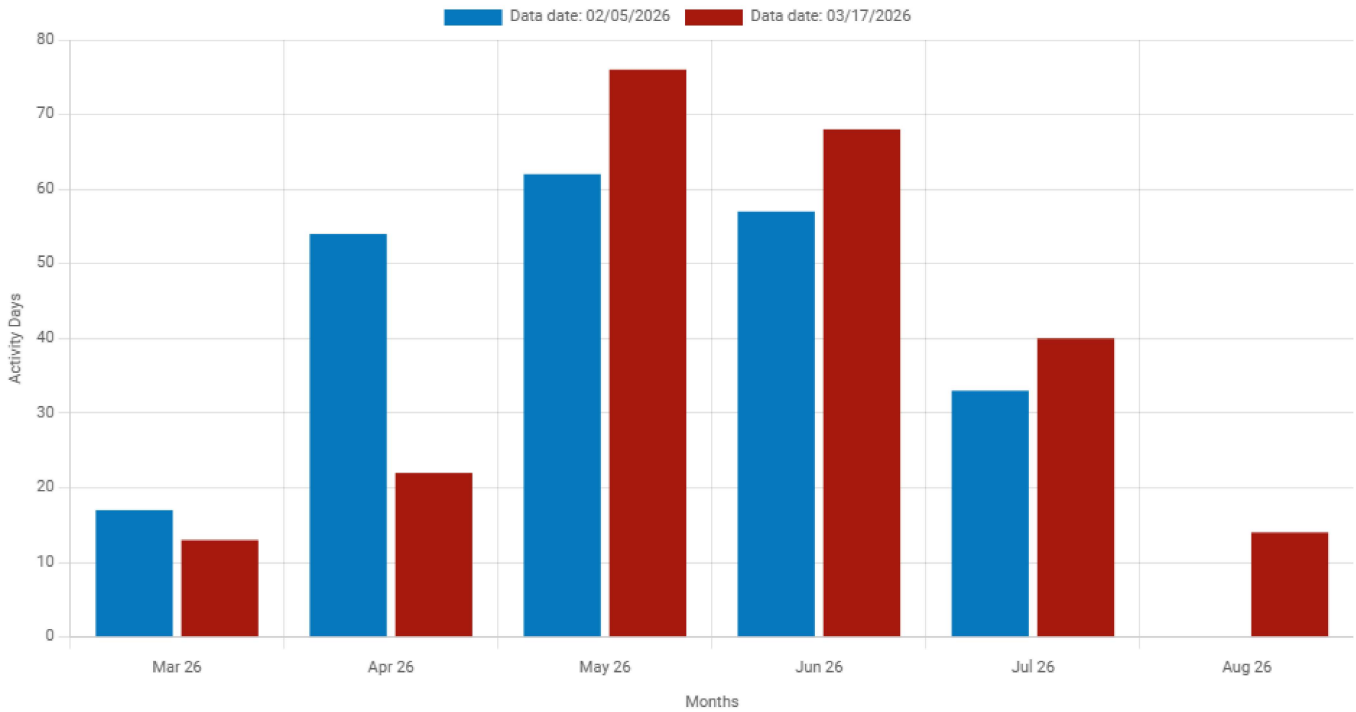

Month	02/05/2026 Activity Days	03/17/2026 Activity Days
Mar 26	17	13
Apr 26	54	22
May 26	62	76
Jun 26	57	68
Jul 26	33	40
Aug 26	0	14
