Executive Landing Page | Landing Page

Public Storage Dashboard

Data Date: 3/17/2026

Type	Project	Region	Responsible
Construction	Aventura, FL	East Coast	Tracy Girard

Baseline Completion Date	Current Completion Date	Schedule Variance	Work Compression
5/21/2026	6/15/2026	-25 days Prev: 0 days | Trend: -25 days ▼ Worsening	Remaining Work Compression: 35.00% — ALERT

Critical Path Status & Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	3/21/2025	3/21/2025	3/21/2025	0	0	Mobilization	On Track – Gaining
Foundation Complete	6/10/2025	6/10/2025	6/10/2025	0	0	Prep & Pour 2	On Track – Gaining
Structure Top Out	10/14/2025	10/14/2025	10/14/2025	0	0	Pour 4Th, 5Th Floor Slab And Roof Deck	On Track – Gaining
Weather Tight	2/4/2026	2/4/2026	2/6/2026	-2	-2	Install Roofing	Delayed – Slipping
Conditioned Air	2/19/2026	2/19/2026	2/23/2026	-4	-4	Mep Hookup Hvac Units	Delayed – Slipping
Permanent Power	3/25/2026	3/25/2026	4/22/2026	-28	-28	Install Electric Meter	Delayed – Slipping
Finishes Complete	2/23/2026	2/23/2026	4/27/2026	-63	-63	Install Doors & Hardware	Delayed – Slipping
Elevator Complete	4/29/2026	4/29/2026	5/8/2026	-9	-9	Install Elevators	Delayed – Slipping
Hardscape/Landscape Complete	5/22/2026	5/22/2026	5/22/2026	0	0	Jet Vac	On Track – Gaining
Contract Completion	5/21/2026	5/21/2026	6/15/2026	-25	-25	Obtain Certificate Of Completion	Delayed – Slipping

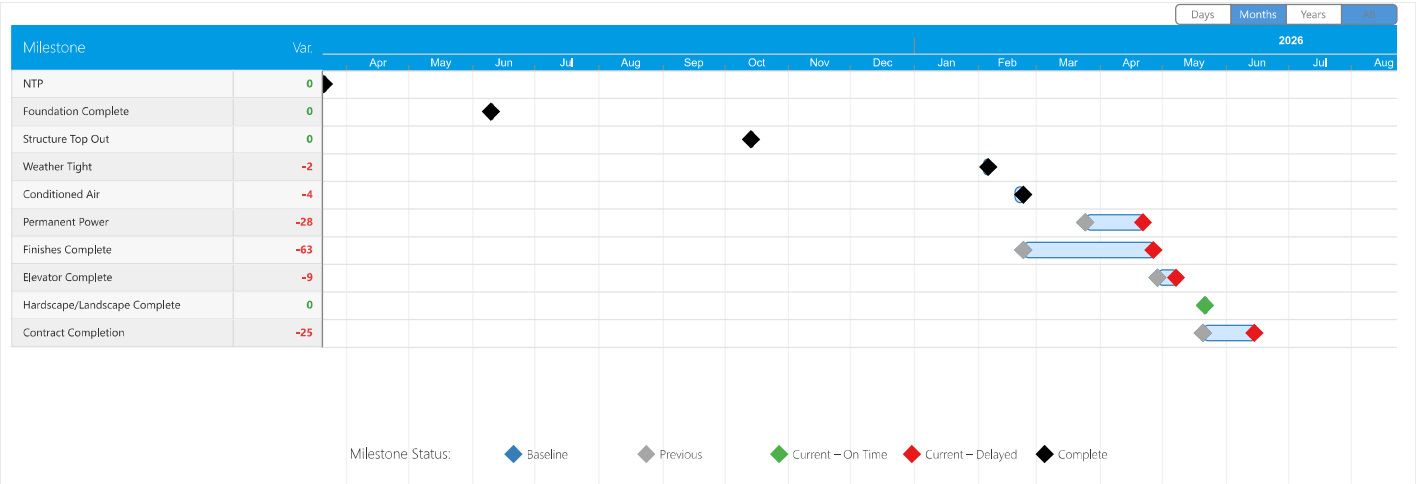

Baseline Variance Trends — Critical Milestones

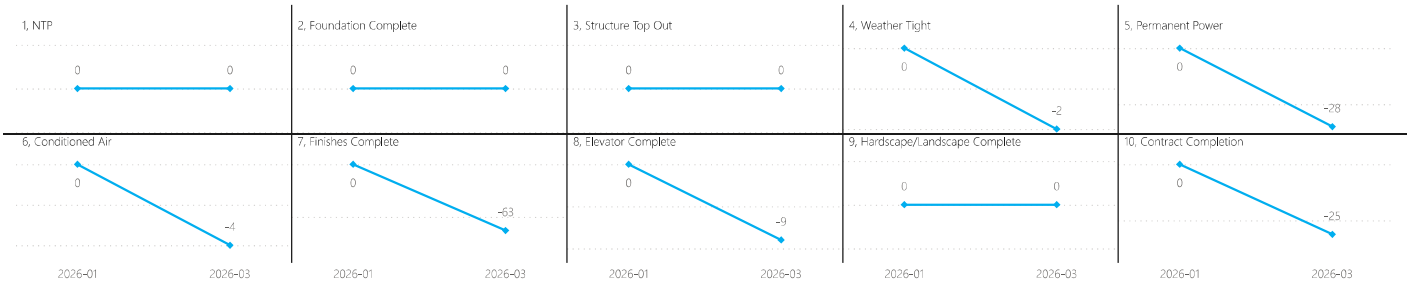

Schedule Performance Summary

Summary: Several key performance indicators are in ALERT status, including core metrics of schedule quality, change frequency, finish slippage, execution, and compression. These results signal extreme risk of project delay, un… forecasting, and compromised execution. Immediate management attention, comprehensive schedule review, and cross-functional recovery actions are strongly recommended to restore schedule control and credibility.

Schedule Change Index: 17.00% — ALERT

Over 17% of activities changed since the last update, demonstrating high schedule volatility. This level of fluctuation undermines reliability—root causes and management controls should be evaluated.

Critical Path Variance: 13.00% — WARNING

The current critical path is 13% longer than baseline, which may lead to project-wide delays if not addressed. Causes should be investigated and mitigation planned.

Finish Variance: 30.00% — ALERT

The project is over 30% behind its planned finish, suggesting significant risk of missing deadlines. Recovery strategies and stakeholder notifications are critical.

Schedule Validation Score: 45.00 — ALERT

The schedule's technical quality is substantially below industry standards, indicating numerous logic errors or structural issues. Immediate action is needed to review and correct foundational schedule integrity problems.

Execution Score: 22.00% — ALERT

Execution discipline is very weak; the schedule is not being effectively used for day-to-day management. Urgent corrective action and team retraining are required.

Remaining Work Compression: 35.00% — ALERT

Aggressive compression of remaining work is present, vastly exceeding thresholds and risking infeasible workloads or rework. A review of schedule logic and recovery planning is advised.

Powered By STELIC
