Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 1/30/2026

Type	Project	Region	Responsible
Construction	Meridian, MS	Central	Josh Pait

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
8/18/2026	6/2/2024	807 Baseline 807 Previous	Remaining Work Compression 7%

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
Contract Completion	8/18/2026	8/18/2026	6/2/2024	807	807	Substantial Completion	On Track – Gaining
NTP	9/8/2025	9/8/2025	6/2/2024	463	463	Notice To Proceed	On Track – Gaining
1st Floor Finishes Complete	3/23/2026	3/23/2026	2/9/2026	42	42	Bathroom Accessories	On Track – Gaining
1st Floor Finishes Complete	3/23/2026	6/19/2026	2/9/2026	42	130	Bathroom Accessories	On Track – Gaining
Foundation Complete	3/25/2026	3/25/2026	2/9/2026	44	44	Bldg A Slab On Grade Complete	On Track – Gaining
Hardscape/Landscape Complete	6/15/2026	6/15/2026	2/9/2026	126	126	Site Fencing Rod Iron And Gates	On Track – Gaining
Permanent Power	4/17/2026	4/17/2026	2/9/2026	67	67	Permanent Power On	On Track – Gaining
Permanent Power	6/10/2026	6/10/2026	2/9/2026	121	121	Permanent Power On	On Track – Gaining
Structure Top Out	4/27/2026	4/27/2026	2/9/2026	77	77	Bldg A Roofing Complete	On Track – Gaining

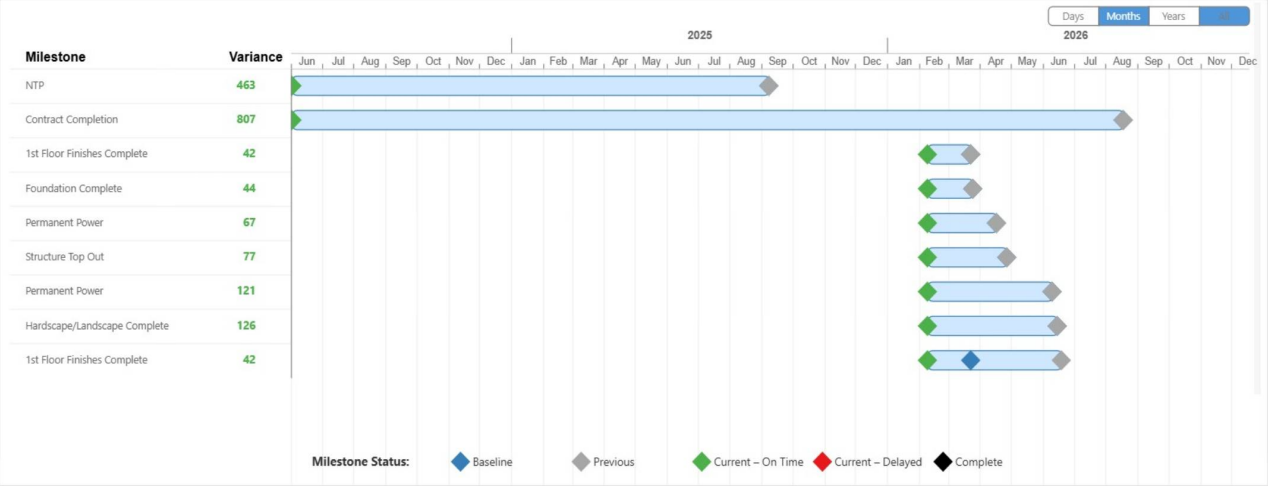

Baseline Variance

Schedule Performance Summary

Summary

With three critical parameters in ALERT—schedule validation, execution, and schedule change index—the project faces elevated schedule risk and diminished reliability of forecasts. Immediate actions must focus on technical schedule quality improvement, re-establishing disciplined short-term planning, and restoring network stability to prevent further schedule erosion and downstream performance failures.

Execution Score: 40.00% — ALERT

Execution score reflects substantial execution discipline gaps, with poor planning and updating of near-term activities. Targeted interventions to improve short-term schedule management and team engagement are highly recommended.

Remaining Work Compression 7%

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea... by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedule Change Index: 20.00% — ALERT

There is excessive schedule volatility, as more than 20% of activities were changed since the previous update. This high degree of modifications undermines schedule stability and may signal inadequate planning or scope control.

Schedule Validation Score: 58.00% — ALERT

The schedule validation score is critically low, indicating significant weaknesses in schedule logic, excessive constraints, or other technical deficiencies. Immediate schedule clean-up and adherence to best practices are required to restore forecasting reliability.

Microsoft Power BI
